Pacoima Spreading Grounds Basin Enhancement Project Air Quality Monitoring Program Summary Report for June 2024

1. Background

- During the month of June 2024, real-time monitoring of air pollutants through four monitoring locations (Figure 1) for the Pacoima Spreading Grounds Basin Enhancement Project (Project) was conducted for the staging activities and active hauling.
- ightharpoonup Results indicated average ambient PM₁₀ concentration of 31 34 μ g/m³ for all four (4) stations.
- ➤ Comparison of upwind and downwind stations at the Pacoima project site with nearest South Coast Air Quality Management District (AQMD) monitoring station (Reseda) PM_{2.5} showed similar trends with higher peaks during the first half of the month at the Pacoima site (Figure 2).
- ➤ Active hauling was complete on June 19th. On-site operations and maintenance continued through the end of the month.

2. Field Activity Summary

- ➤ The following field activities were continued/initiated:
 - Hauling operations of Basin 3 and East Settling Basin
 - o Grading operations at Basin 5
 - Installation of perimeter fencing
 - Removal of sound wall barriers

3. Air Monitoring Summary

- > During staging and hauling activities, real-time monitoring of air pollutants for the Project was conducted and included:
 - ➤ Continuous 24 hours per day PM₁₀ monitoring at all four stations and meteorological parameters at two stations (one upwind and one downwind) for entire month.
 - Monitoring of ozone and NO₂ at two stations (one upwind and one downwind) continuously.

4. Compliance Summary

➤ Air monitoring data for PM₁₀ concentrations were in compliance with SCAQMD Rule 403 for the month of June 2024.

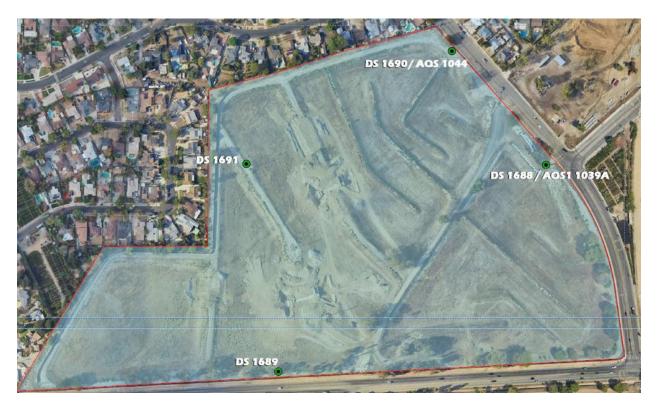


Figure 1. Pacoima Spreading Grounds air monitoring stations for the Northern site. DS: Dust Sentry.
