

E. SACRAMENTO ST & RAYMOND LN POLE # 2335246E

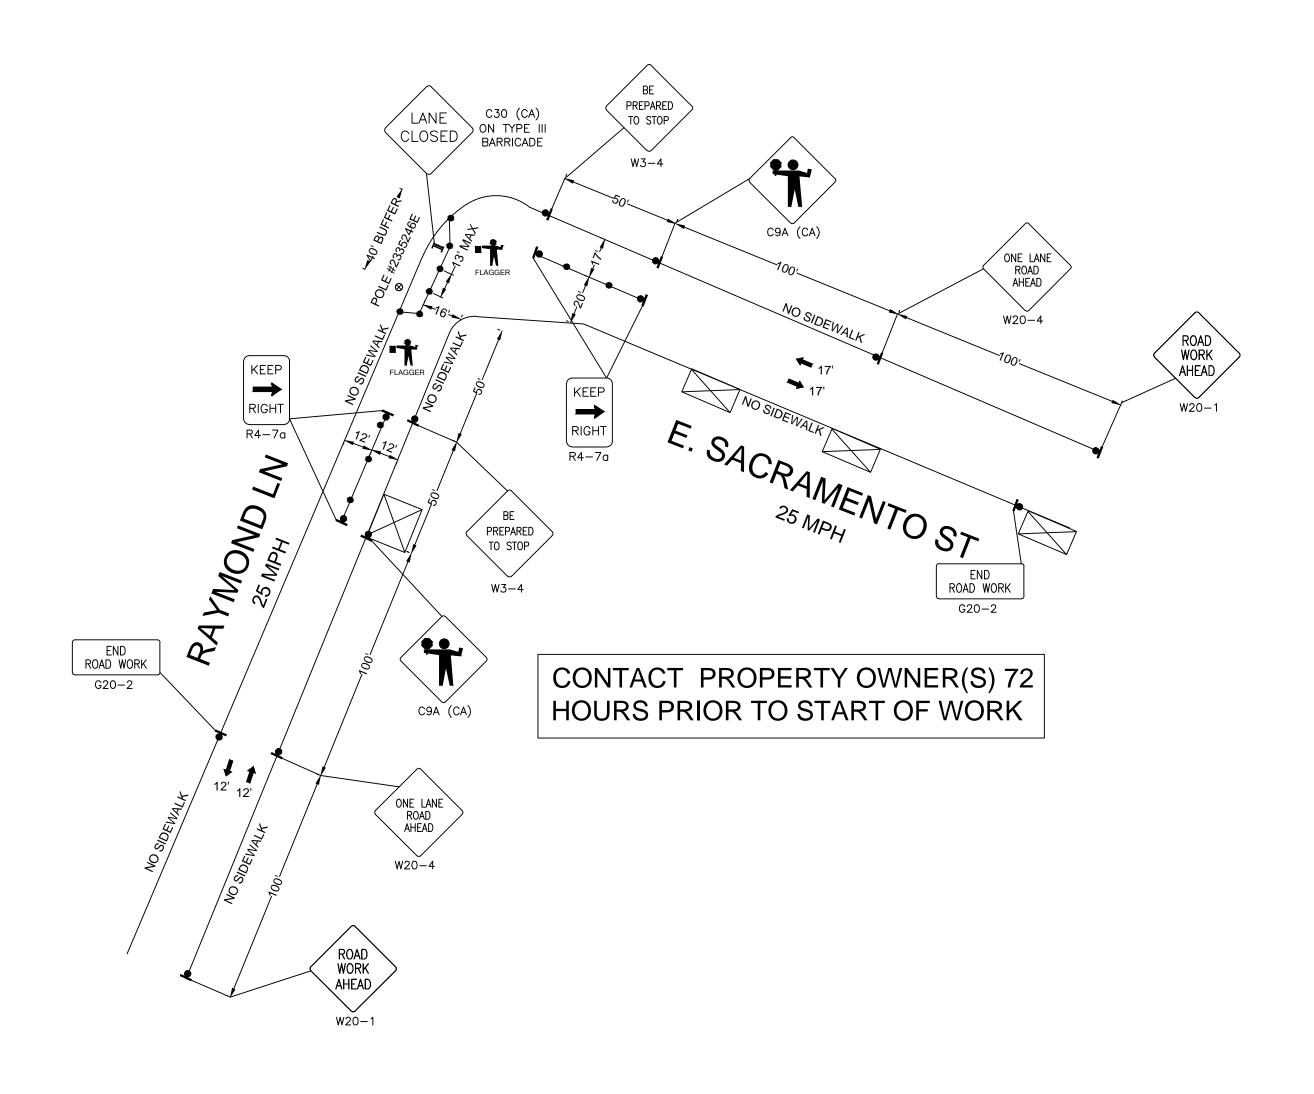

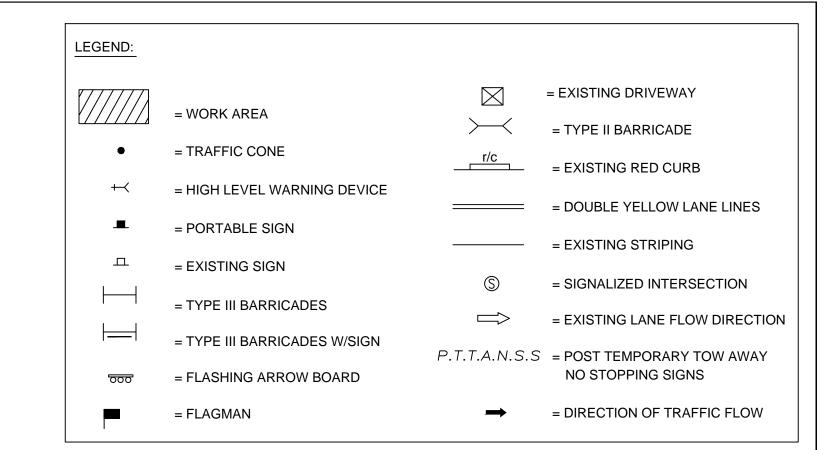

VICINITY MAP (N.T.S.)

POLE # 2335246E **WORK AREA** E.WOODBURY RD

TRAFFIC CONTROL PLANS GENERAL NOTES

- TRAFFIC CONTROL DEVICES (MUTCD) LATEST EDITION.
- 2. ALL STRIPING AND MARKINGS DOES CONFORM TO THE STATE OF CALIFORNIA, STANDARD PLANS AND SPECIFICATIONS, INCLUDING STANDARD PLAN A-20, DETAILS.
- THE CONTRACTOR SHALL PROVIDE FOR ACCESS TO ALL ADJACENT PROPERTIES, AND DRIVEWAYS AT ALL TIME.
- 4. FLASHING YELLOW BEACONS, TYPE "B", SHALL BE USED ON ALL W20-1 SIGNS AND ON ALL TYPE Ⅲ BARRICADES GUARDING THE WORK AREA OVERNIGHT.
- 5. ALL SIGNS SHALL BE REFLECTORIZED AND STANDARD SIZE.
- ALL TUBULAR DELINEATORS AND CONES SHALL BE 28" MINIMUM HEIGHT, REFLECTORIZED AND MAINTAINED ERECT IN THE INDICATED POSITION AT ALL TIMES, AND SHALL BE REPAIRED, REPLACED, OR CLEANED AS NECESSARY TO PRESERVE THEIR APPEARANCE AND CONTINUITY, AND SHALL INCLUDE A 12" HIGH-INTENSITY REFLECTORIZED SLEEVE, IF USED DURING NIGHT-TIME HOURS.
- THE CONTRACTOR SHALL MAINTAIN, ON A CONTINUOUS BASIS, ALL SIGNS, DELINEATORS, BARRICADES, ETC., TO ENSURE PROPER FLOW AND SAFETY OF TRAFFIC DURING CONSTRUCTION.

- ALL WORK AND MATERIALS DOES COMPLY WITH THE CALIFORNIA MANUAL ON UNIFORM 8. THE CONTRACTOR SHALL HAVE ALL SIGNS, DELINEATORS, BARRICADES, ETC., PROPERLY INSTALLED PRIOR TO COMMENCING CONSTRUCTION.
 - 9. CONSTRUCTION OPERATIONS SHALL BE CONDUCTED IN SUCH A MANNER AS TO CAUSE AS LITTLE INCONVENIENCE AS POSSIBLE TO ABUTTING PROPERTY OWNERS.
 - 10. ADDITIONAL TRAFFIC CONTROLS, TRAFFIC SIGNS, OR BARRICADING MAY BE REQUIRED IN THE FIELD. THE CONTRACTOR SHALL BE RESPONSIBLE FOR THE PLACEMENT OF ANY ADDITIONAL DEVICES NECESSARY TO ASSURE SAFETY TO THE PUBLIC AT ALL TIMES DURING CONSTRUCTION.
 - 11. EXACT LOCATION AND TYPE OF CONSTRUCTION SIGNS SHALL BE DIRECTED BY THE ENGINEER BASED UPON CONSTRUCTION CONDITIONS.
 - 12. MOVE DELINEATORS AND/OR CONES TO SIDEWALK DURING NON-WORKING HOURS. REMOVE BARRICADES ETC. FROM TRAVEL LANE.
 - 13. REMOVE OR TURN OFF SIGNS DURING NON-WORK HOURS.
 - 14. ALL CONFLICTING LINES, EXISTING CURB PAINT, AND MARKINGS SHALL BE REMOVED BY WET SANDBLASTING OR OTHER APPROVED METHOD PRIOR TO INSTALLATION OF NEW/TEMPORARY STRIPING. ALL CONFLICTING RAISED PAVEMENT MARKERS SHALL BE REMOVED. PAVEMENT THAT IS DAMAGED DUE TO REMOVAL OF MARKERS SHALL BE REPAIRED TO THE SATISFACTION OF THE CITY ENGINEER AND/OR STATE INSPECTOR.



WORK HOURS: 9:00 A.M. TO 3:30 P.M. MONDAY TO FRIDAY

AT&TID JOHN JOHNSTON

	600 E GREEN ST, ROOM 300 PASADENA, CA 91101-2020	DRAW CHEC APPRO
CHC Cor	nsulting, LLC	

600 E GREEN S1, ROOM 300 PASADENA, CA 91101-2020	DA	TE	RI
CHC Consulting, LLC			
1700 E. Garry Ave. , Suite 210			
Santa Ana, CA 92705 (949) 250-0004 / FAX (949) 250-0006	SCALE	1"	= 4

					TELEPHONE NUMBER
	DRAWN	3-13	3-15	JMM	626-817-4258
1		_			EMAIL ADDRESS
L	CHECKE	D			JJ1823@ATT.COM
ı					FACILITY ENGINEER
	APPROV	ED			STEVEN SAUSER
	DATE REVISION				TELEPHONE NUMBER
			SION2		949-313-6110
					GEOCO
					K107
					CENTRAL OFFICE
					LAKE_PASADENA
					UNDERGROUND CONSTRUCTION ROUTINE ORDER/ESTIMATE NUMBER
20	SCALE		THO	MAS GUIDE	A004IBC
26	1" = 40'			535-H6	A004IBC
	FILE NAME:			DRAWING:	
	A004IBC TG535-H6 POLE ACCESS TCP.DWG			∣ 1/1 ∣	
	_				
