

## AUTHORIZATION FOR JOINT POLE TRANSACTION

J.P. FORM 2-1 Preliminary 1/95

Date Prepared 04/25/2014

This authorization is in accordance with Joint Pole Agreement and Routine. The undersigned have agreed on joint work as specified hereon.

Date Sent \_\_\_\_\_ Confirming Agreement N/A In Field \_\_\_\_\_ By Telephone \_\_\_\_\_ Est. Const. Start \_\_\_\_\_ No. of Pages 1 J.P. Auth.No. E6044-406055647

UTILITY	REPRESENTATIVE	DISTRICT-DIVISION-EXCHANGE	APPROVED	TAXING INSTRUCTIONS	ACCOUNTING DATA
E	RICARDO ESPINOS	SOUTH BAY	MICHAEL FULLER	TORRANCE	TD828496
HLA					

POLE NO.	Pole Length Anchor Size	Year Set	Record				Proposed				Item No.	LOCATION AND NATURE OF WORK If not in accordance with Joint Pole agreement and routine-state reasons.		
			Pole Trt Class	120V	L		2.4KV	L						
			Anchor Direct.	E	HLA			E	HLA					
2094699E	45	80	FT		24			PTD					E TO REPLACE POLE PER SEC 7.3, 10.8, 19.4 W/S BANDINI ST 175' S/O C/L FIFTH ST	1 2
			CL4											3
														4
2094699E	45	14	FT					38-14	24-1				W/S BANDINI ST. 174' C/L FIFTH ST	5
			CL3					2			83		NO CHARGE TO HLA SOLE BENEFIT E	6
								1/2(1)			13B			7
														8
														9
														10
														11
														12
														13

POLE LEGEND: L = LOWER CUT  
P = PULL C(XX) = FOOTAGE CUT  
PB = PULL BUTT SCZ = SAFETY CLEARANCE ZONE  
T = TRANSPORT  
S = SALVAGE ANCHOR LEGEND:  
D = DISPOSE AR = ANCHOR/ARM REMOVED  
TN = TENANT AT = ANCHOR/ARM TRANSFERRED

Show Quantity of  
Items to be billed  
in the Column of  
Party to be Paid.

GEOGRAPHICAL LOCATION

SAN PEDRO

COMMUNITY

APR 25 2014

SENT TO JPA

VP/J.P.-03

Rev. Jan 2010

GAFFEY 2.4KVA % GAFFEY PT SUB

**FINAL DESIGN**  
APPROVED FOR CONSTRUCTION






T.L.M. DATA:			
EXIST.	SIZE	KVA	CUST % LOAD
0	0	0	0
PROP.	75	29.25	5 39.0%
VOLTAGE DROP: 0.96			
FLICKER FACTOR: 4.76			
PR. CIRCUIT: GAFFEY 1 2.4KV			

TD828496 - PREVENTIVE MAINT - NEW BUSINESS DRIVEN

SCOPE: INSTALL 75KVA TRANSFORMER  
POLE REPLACEMENT  
DUE TO FAIL VD/FL FOR NEW SFR

RELATED WORK ORDERS: TD831212  
TD831195

PROJECT REQUIREMENTS	
EDISON EASEMENT REQ'D	<input checked="" type="checkbox"/>
PRD. BR. REQ'D	<input checked="" type="checkbox"/>
PERMIT REQ'D	<input checked="" type="checkbox"/>
PERMIT TYPE:	
OUTAGE REQ'D	<input checked="" type="checkbox"/>
TRAFFIC CONTROL REQ'D	<input checked="" type="checkbox"/>
PED. TRAFFIC CONTROL REQ'D	<input checked="" type="checkbox"/>
CONVEYANCE LETTER REQ'D	<input checked="" type="checkbox"/>

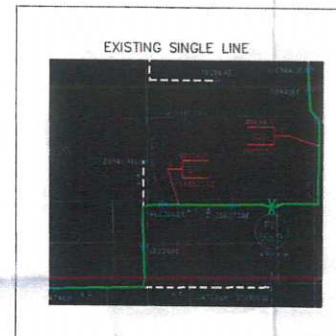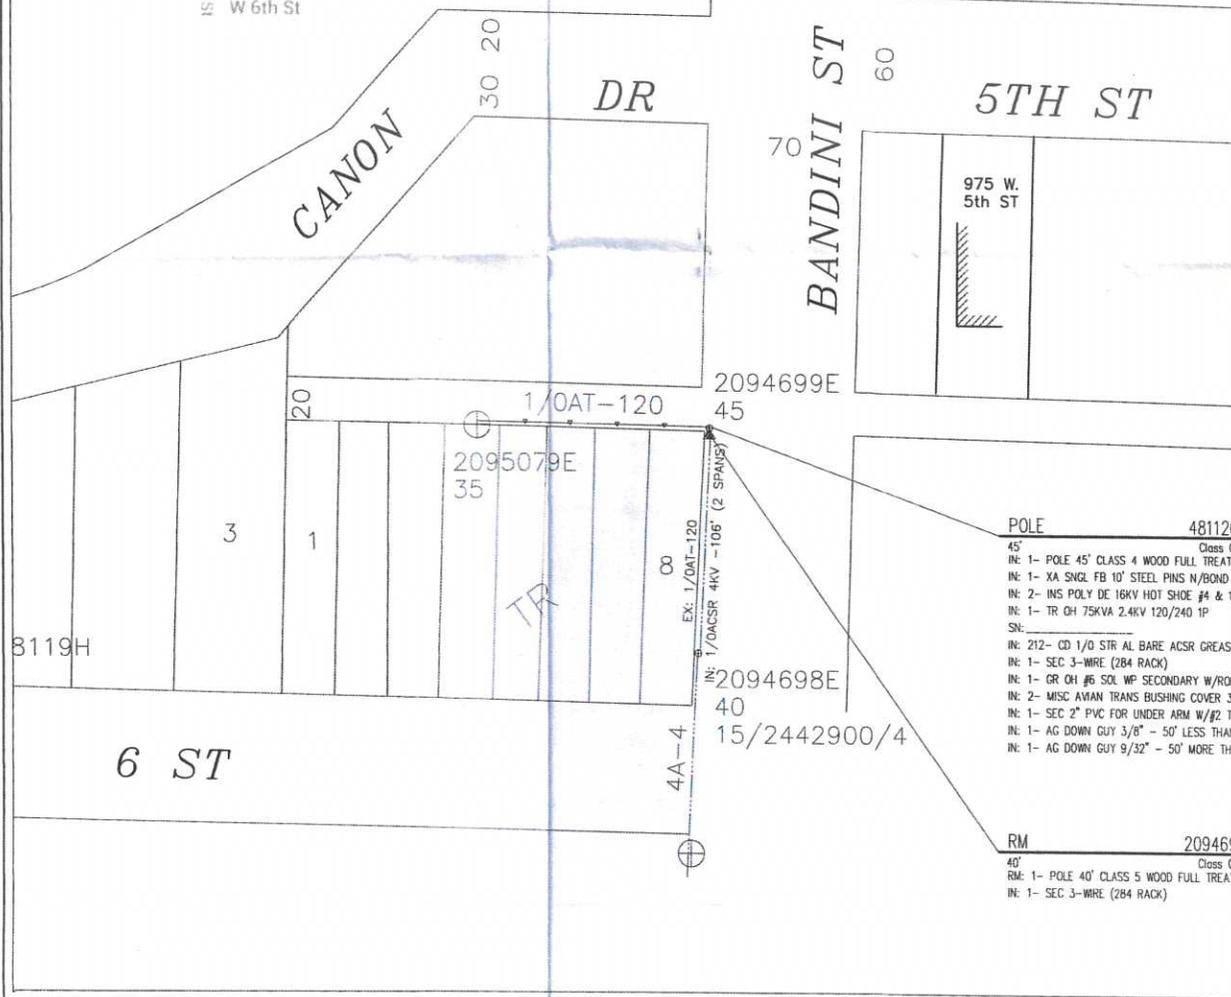

- POLE 4811204E** (2)
- 45' Class C4
  - IN: 1- POLE 45' CLASS 4 WOOD FULL TREAT
  - IN: 1- XA SNGL FB 10" STEEL PINS N/BOND
  - IN: 2- INS POLY DE 16KV HOT SHOE #4 & 1/O ACSR
  - IN: 1- TR OH 75KVA 2.4KV 120/240 1P
  - SN:
  - IN: 212- CD 1/O STR AL BARE ACSR GREASED
  - IN: 1- SEC 3-WIRE (2B4 RACK)
  - IN: 1- GR OH #6 SOL WP SECONDARY W/ROD
  - IN: 2- MISC AMAN TRANS BUSHING COVER 3.25-4.25
  - IN: 1- SEC 2" PVC FOR UNDER ARM W/#2 TW
  - IN: 1- AG DOWN GUY 3/8" - 50' LESS THAN 22.5KV
  - IN: 1- AG DOWN GUY 9/32" - 50' MORE THAN 22.5KV
- RM 2094699E** (1)
- 40' Class C5
  - RM: 1- POLE 40' CLASS 5 WOOD FULL TREAT
  - IN: 1- SEC 3-WIRE (2B4 RACK)

DESIGN NO. 44 - SOUTH BAY	PROJ. MGR. ESPINOSA, RICK	PLANNER ESPINOSA, RICK
DESIGNER	PHONE 310-763-8454	PHONE 310-763-8454
DESIGN NO. 578371_0.01	DESIGN NO. 028-088C	LAC B24-A5
DATE 04/25/14	WOODS 33306	SAN PEDRO
STR W/S BANDINI ST. 175' S/O C/L FIFTH ST. S		
SHEET 1 OF 1		
578371_0.01		
