



MANHOLE 26722

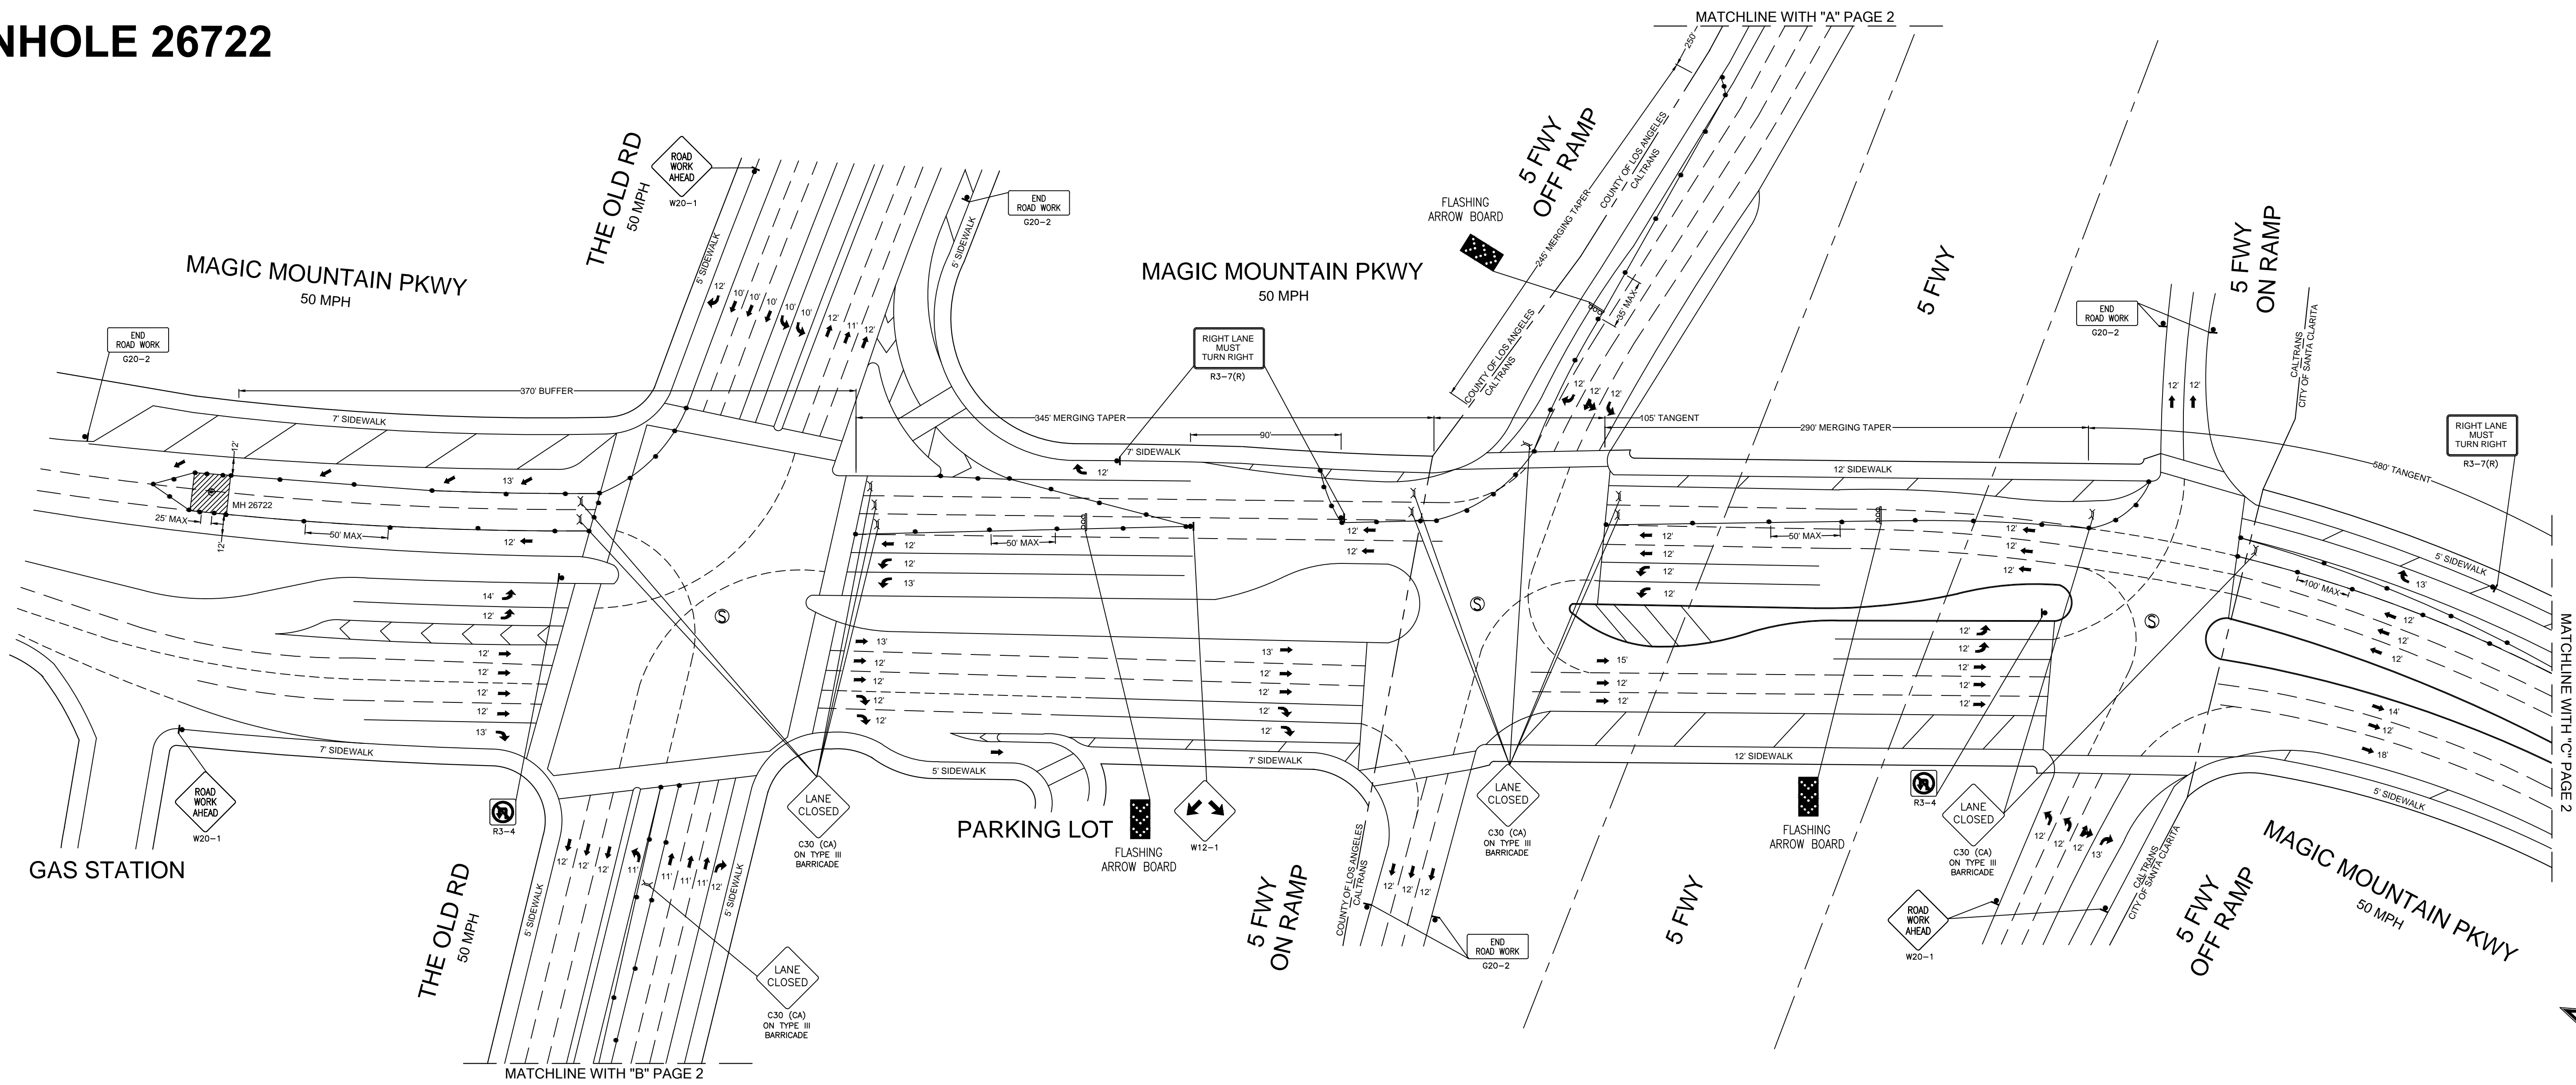

VICINITY MAP (N.T.S.)

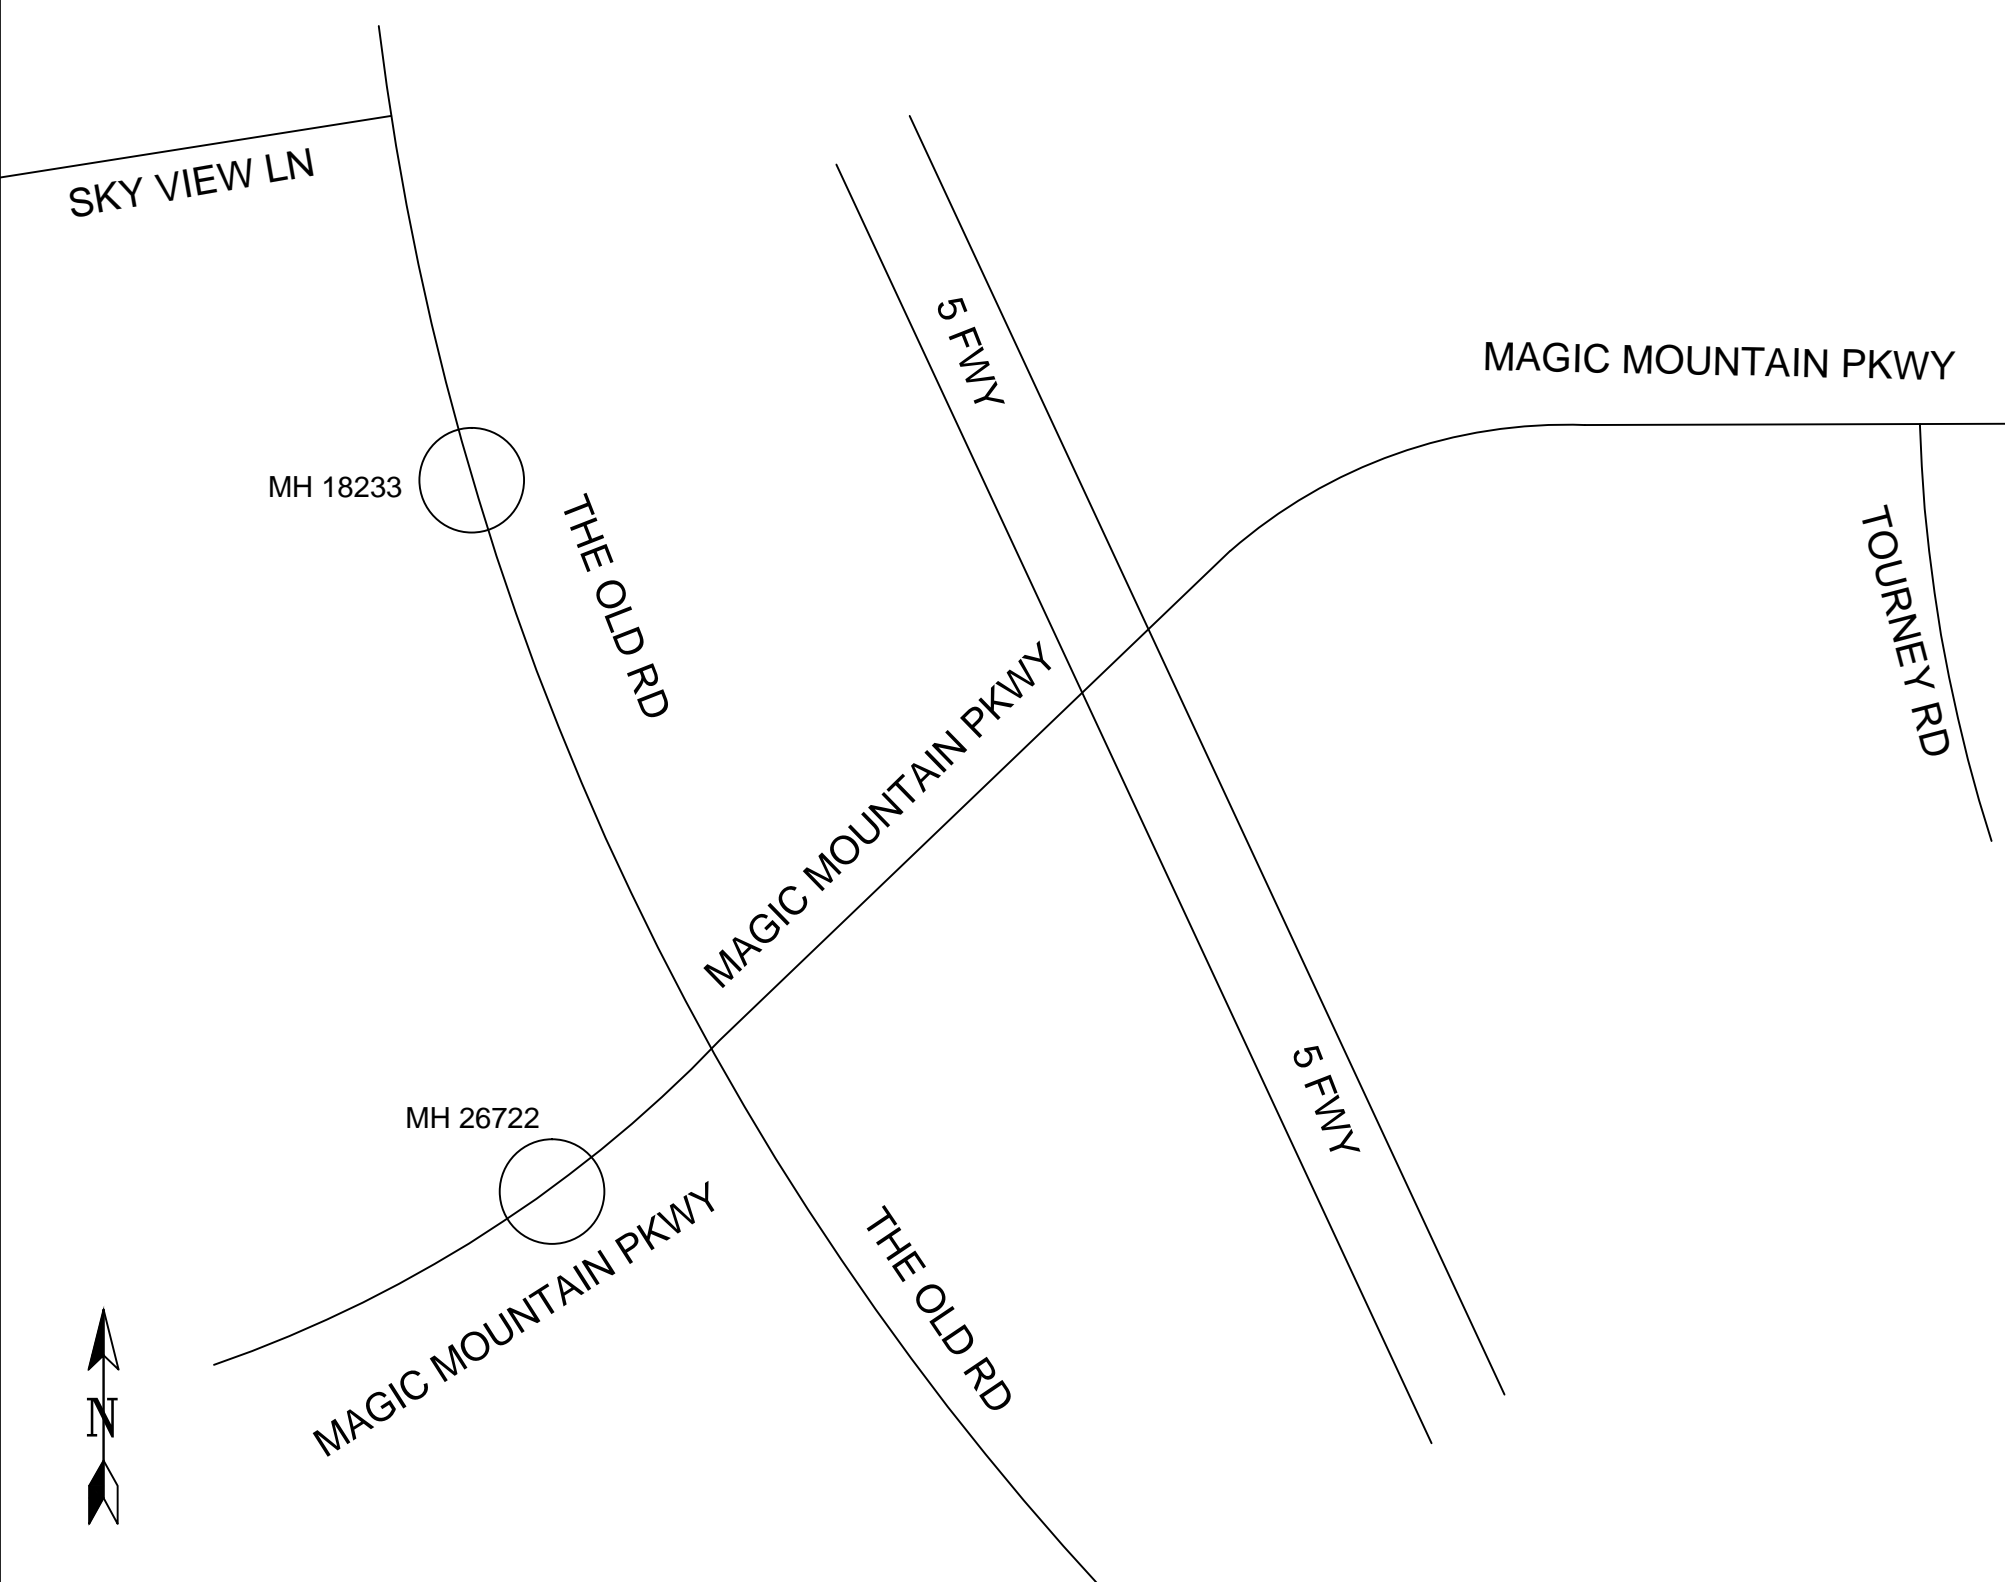

TRAFFIC CONTROL PLANS



GENERAL NOTES

1. ALL WORK AND MATERIALS DOES COMPLY WITH THE CALIFORNIA MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES (MUTCD) LATEST EDITION.
2. ALL STRIPING AND MARKINGS DOES CONFORM TO THE STATE OF CALIFORNIA, STANDARD PLANS AND SPECIFICATIONS, INCLUDING STANDARD PLAN A-20, DETAILS.
3. THE CONTRACTOR SHALL PROVIDE FOR ACCESS TO ALL ADJACENT PROPERTIES, AND DRIVEWAYS AT ALL TIMES.
4. FLASHING YELLOW BEACONS, TYPE "B", SHALL BE USED ON ALL W20-1 SIGNS AND ON ALL TYPE III BARRICADES GUARDING THE WORK AREA OVERNIGHT.
5. ALL SIGNS SHALL BE REFLECTORIZED AND STANDARD SIZE.
6. ALL TUBULAR DELINEATORS AND CONES SHALL BE 28" MINIMUM HEIGHT, REFLECTORIZED AND MAINTAINED ERECT IN THE INDICATED POSITION AT ALL TIMES, AND SHALL BE REPAIRED, REPLACED, OR CLEANED AS NECESSARY TO PRESERVE THEIR APPEARANCE AND CONTINUITY, AND SHALL INCLUDE A 12" HIGH-INTENSITY REFLECTORIZED SLEEVE, IF USED DURING NIGHT-TIME HOURS.
7. THE CONTRACTOR SHALL MAINTAIN, ON A CONTINUOUS BASIS, ALL SIGNS, DELINEATORS, BARRICADES, ETC., TO ENSURE PROPER FLOW AND SAFETY OF TRAFFIC DURING CONSTRUCTION.
8. THE CONTRACTOR SHALL HAVE ALL SIGNS, DELINEATORS, BARRICADES, ETC., PROPERLY INSTALLED PRIOR TO COMMENCING CONSTRUCTION.
9. CONSTRUCTION OPERATIONS SHALL BE CONDUCTED IN SUCH A MANNER AS TO CAUSE AS LITTLE INCONVENIENCE AS POSSIBLE TO ADJUTING PROPERTY OWNERS.
10. ADDITIONAL TRAFFIC CONTROLS, TRAFFIC SIGNS, OR BARRICADING MAY BE REQUIRED IN THE FIELD. THE CONTRACTOR SHALL BE RESPONSIBLE FOR THE PLACEMENT OF ANY ADDITIONAL DEVICES NECESSARY TO ASSURE SAFETY TO THE PUBLIC AT ALL TIMES DURING CONSTRUCTION.
11. EXACT LOCATION AND TYPE OF CONSTRUCTION SIGNS SHALL BE DIRECTED BY THE ENGINEER BASED UPON CONSTRUCTION CONDITIONS.
12. MOVE DELINEATORS AND/OR CONES TO SIDEWALK DURING NON-WORKING HOURS. REMOVE BARRICADES ETC. FROM TRAVEL LANE.
13. REMOVE OR TURN OFF SIGNS DURING NON-WORK HOURS.
14. ALL CONFLICTING LINES, EXISTING CURB PAINT, AND MARKINGS SHALL BE REMOVED BY WET SANDBLASTING OR OTHER APPROVED METHOD PRIOR TO INSTALLATION OF NEW/TEMPORARY STRIPING. ALL CONFLICTING RAISED PAVEMENT MARKERS SHALL BE REMOVED. PAVEMENT THAT IS DAMAGED DUE TO REMOVAL OF MARKERS SHALL BE REPAIRED TO THE SATISFACTION OF THE CITY ENGINEER AND/OR STATE INSPECTOR.


LEGEND:

	= WORK AREA		= EXISTING DRIVEWAY
	= TRAFFIC CONE		= TYPE II BARRICADE
	= HIGH LEVEL WARNING DEVICE		= EXISTING RED CURB
	= PORTABLE SIGN		= DOUBLE YELLOW LANE LINES
	= EXISTING SIGN		= EXISTING STRIPING
	= TYPE III BARRICADES		= SIGNALIZED INTERSECTION
	= TYPE III BARRICADES W/SIGN		= EXISTING LANE FLOW DIRECTION
	= FLASHING ARROW BOARD		= POST TEMPORARY TOW AWAY NO STOPPING SIGNS
	= FLAGMAN		= DIRECTION OF TRAFFIC FLOW

WORK HOURS: 9:00 A.M. TO 3:30 P.M.
MONDAY TO FRIDAY


 at&t 600 E GREEN ST RM 300 PASADENA, CA 91101-0020			DATE	AT&TID	LAYOUT ENGINEER
	DRAWN		10/07/2013	MBM	TELEPHONE NUMBER
	CHECKED				EMAIL ADDRESS
	APPROVED				FACILITY ENGINEER AMY ILLANGAKOON
	DATE		REVISIONS		TELEPHONE NUMBER 949-313-6094
CHC Consulting, LLC 1700 E. Garry Ave. , Suite 210 Santa Ana, CA 92705 (949) 250-0004 / FAX (949) 250-0006					GEOC
					KC-12
					CENTRAL OFFICE
					NEWHALL
					UNDERGROUND CONSTRUCTION ROUTINE ORDER ESTIMATE NUMBER
SCALE		1" = 50'		THOMAS GUIDE 4550-C2	9231306
FILE NAME:					DRAWING:
9231306 TCP					1/3

MANHOLE 26722 CONT.

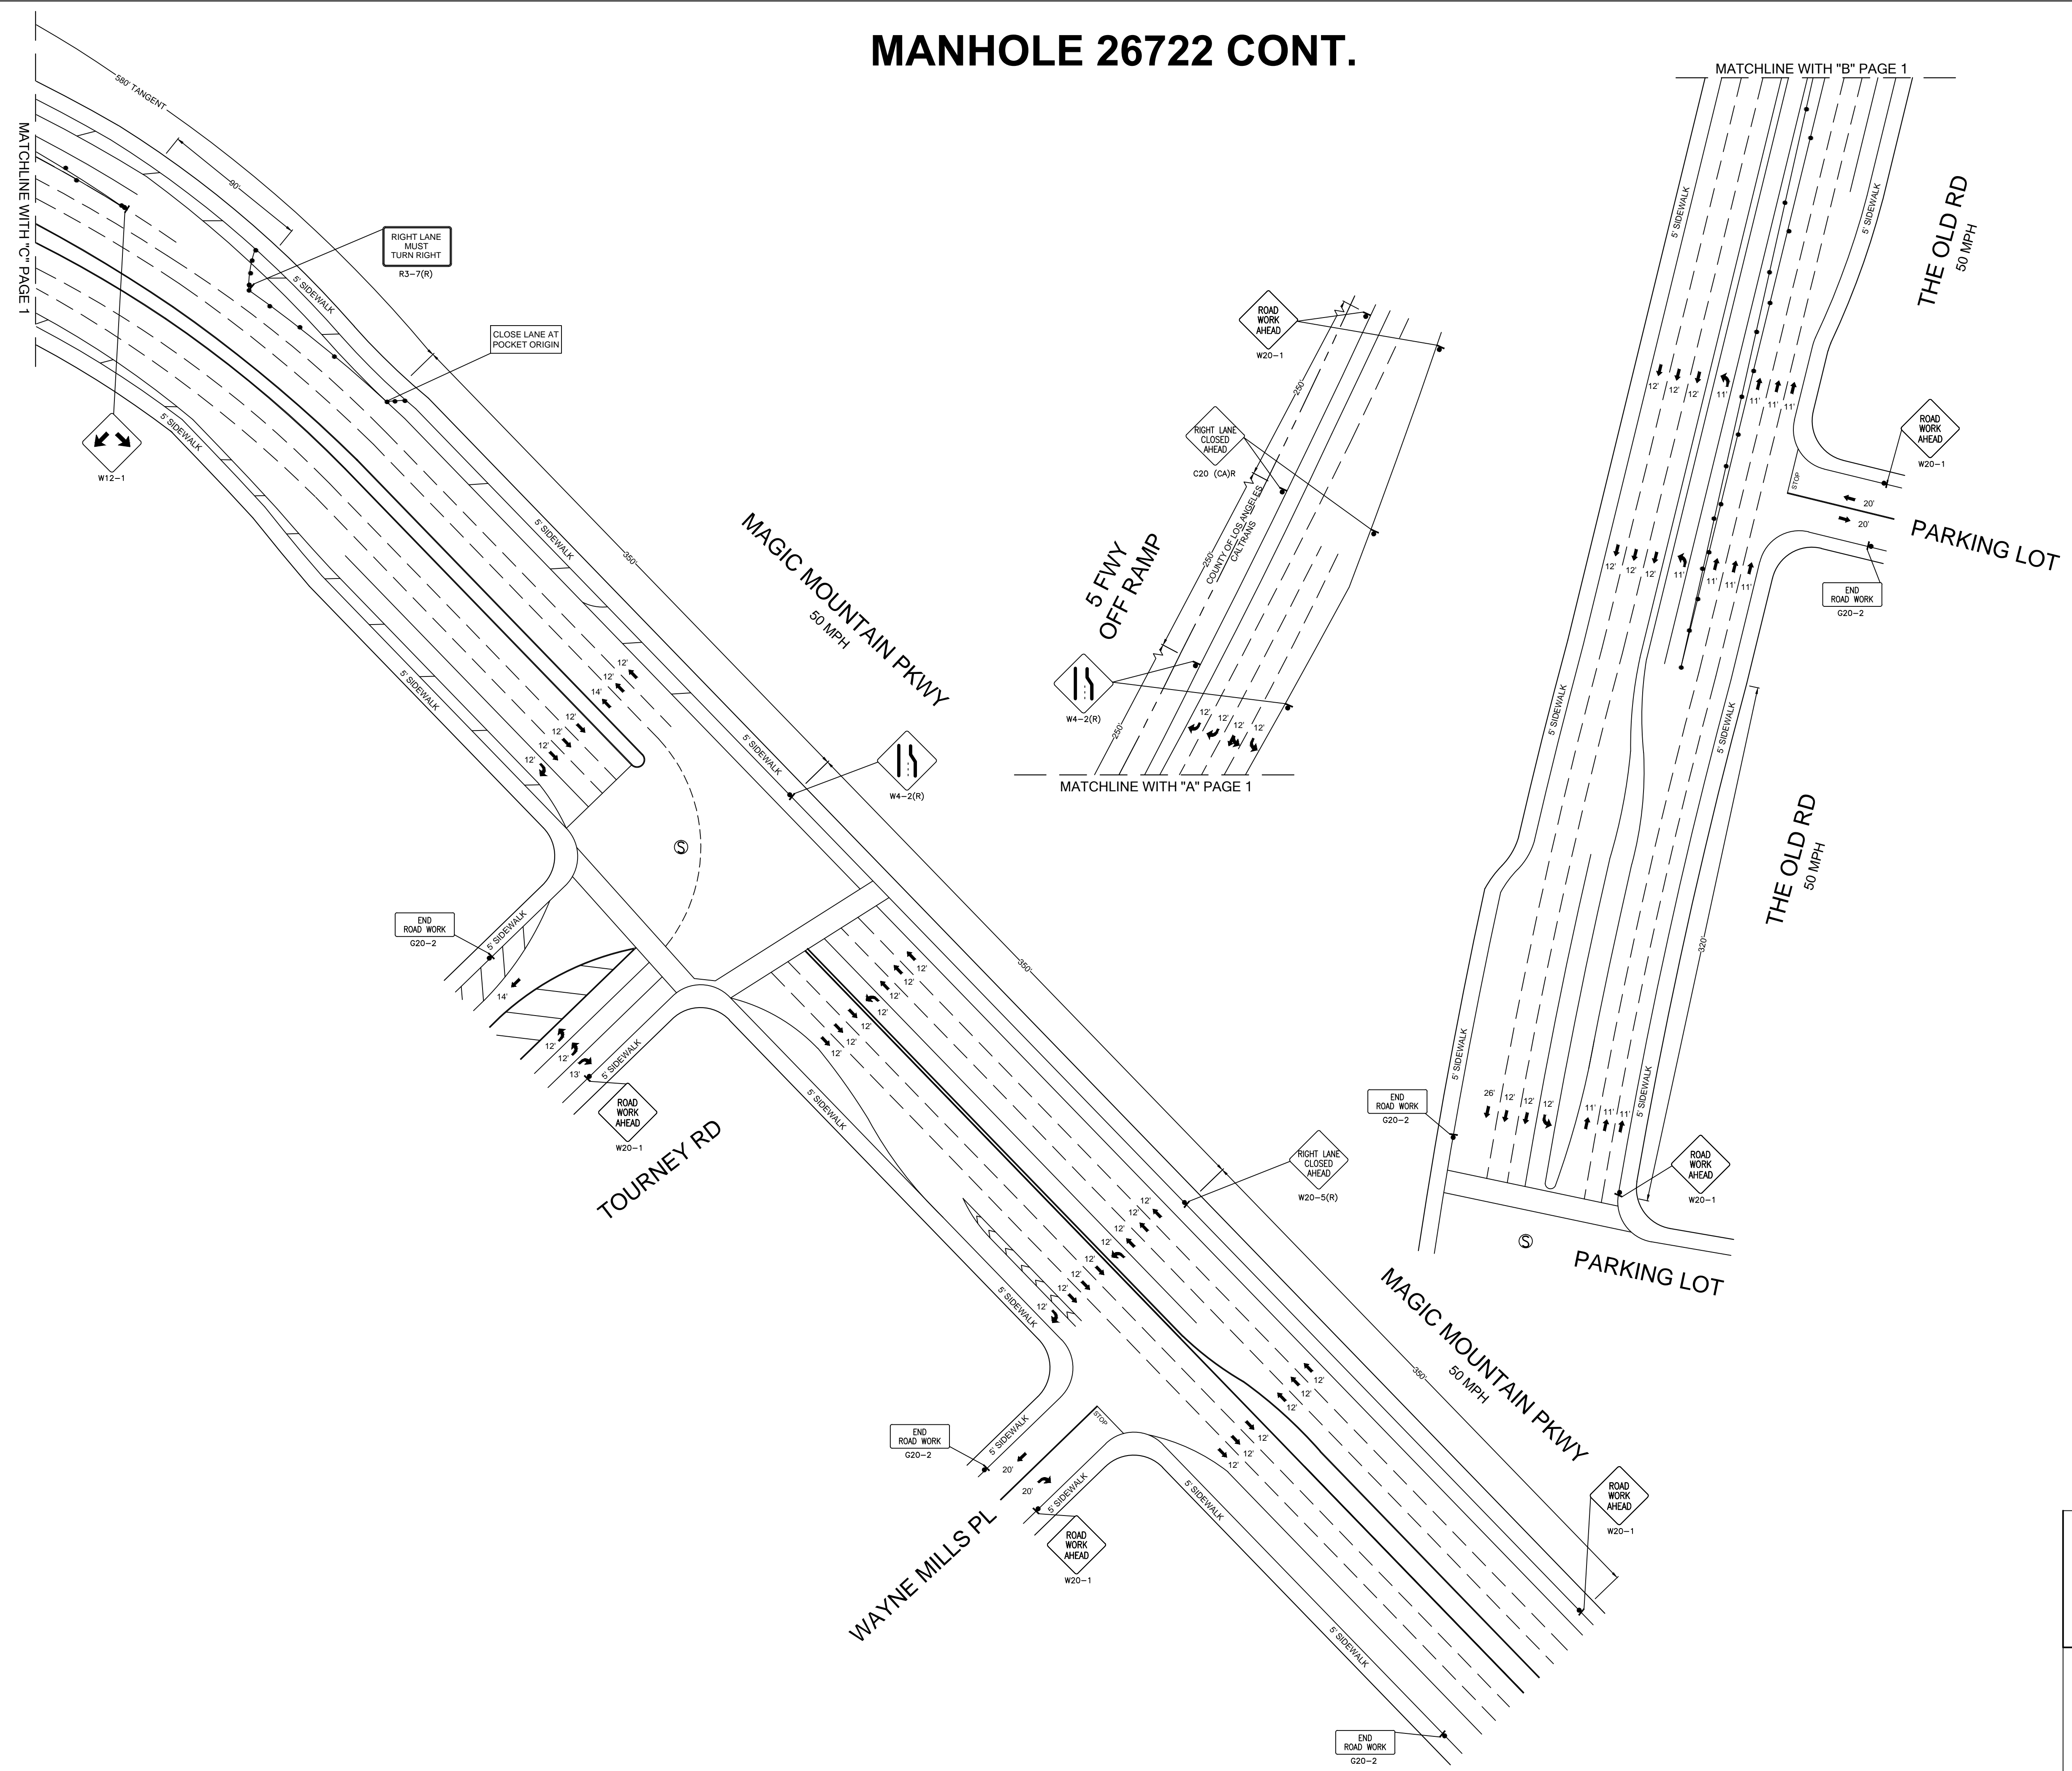



LEGEND:

	= WORK AREA		= EXISTING DRIVEWAY
	= TRAFFIC CONE		= TYPE II BARRICADE
	= HIGH LEVEL WARNING DEVICE		= EXISTING RED CURB
	= PORTABLE SIGN		= DOUBLE YELLOW LANE LINES
	= EXISTING SIGN		= EXISTING STRIPING
	= TYPE III BARRICADES		= SIGNALIZED INTERSECTION
	= TYPE III BARRICADES W/SIGN		= EXISTING LANE FLOW DIRECTION
	= FLASHING ARROW BOARD		= POST TEMPORARY TOW AWAY NO STOPPING SIGNS
	= FLAGMAN		= DIRECTION OF TRAFFIC FLOW

 at&t 600 E GREEN ST RM 300 PASADENA, CA 91101-2020		<div></div>		WORK HOURS: 9:00 A.M. TO 3:30 P.M. MONDAY TO FRIDAY							
CHC Consulting, LLC 1700 E. Garry Ave. , Suite 210 Santa Ana, CA 92705 (949) 250-0004 / FAX (949) 250-0006		<div></div>		DATE		AT&TID		LAYOUT ENGINEER			
		<div></div>		DRAWN		10/07/2013		MBM		TELEPHONE NUMBER	
		<div></div>		CHECKED						EMAIL ADDRESS	
		<div></div>		APPROVED						FACILITY ENGINEER	
		<div></div>		DATE		REVISIONS				AMY ILLANGAKOON	
		<div></div>								TELEPHONE NUMBER	
		<div></div>								949-313-6094	
		<div></div>								GEOLOGIST	
		<div></div>								KC-12	
		<div></div>								CENTRAL OFFICE	
<div></div>								NEWHALL			
<div></div>								UNDERGROUND CONSTRUCTION			
<div></div>								ROUTINE ORDER/ESTIMATE NUMBER			
<div></div>		SCALE		1" = 50'		THOMAS GUIDE		9231306			
<div></div>						4550-C2		DRAWING:			
<div></div>		FILE NAME:				9231306 TCP		2/3			

MANHOLE 18233

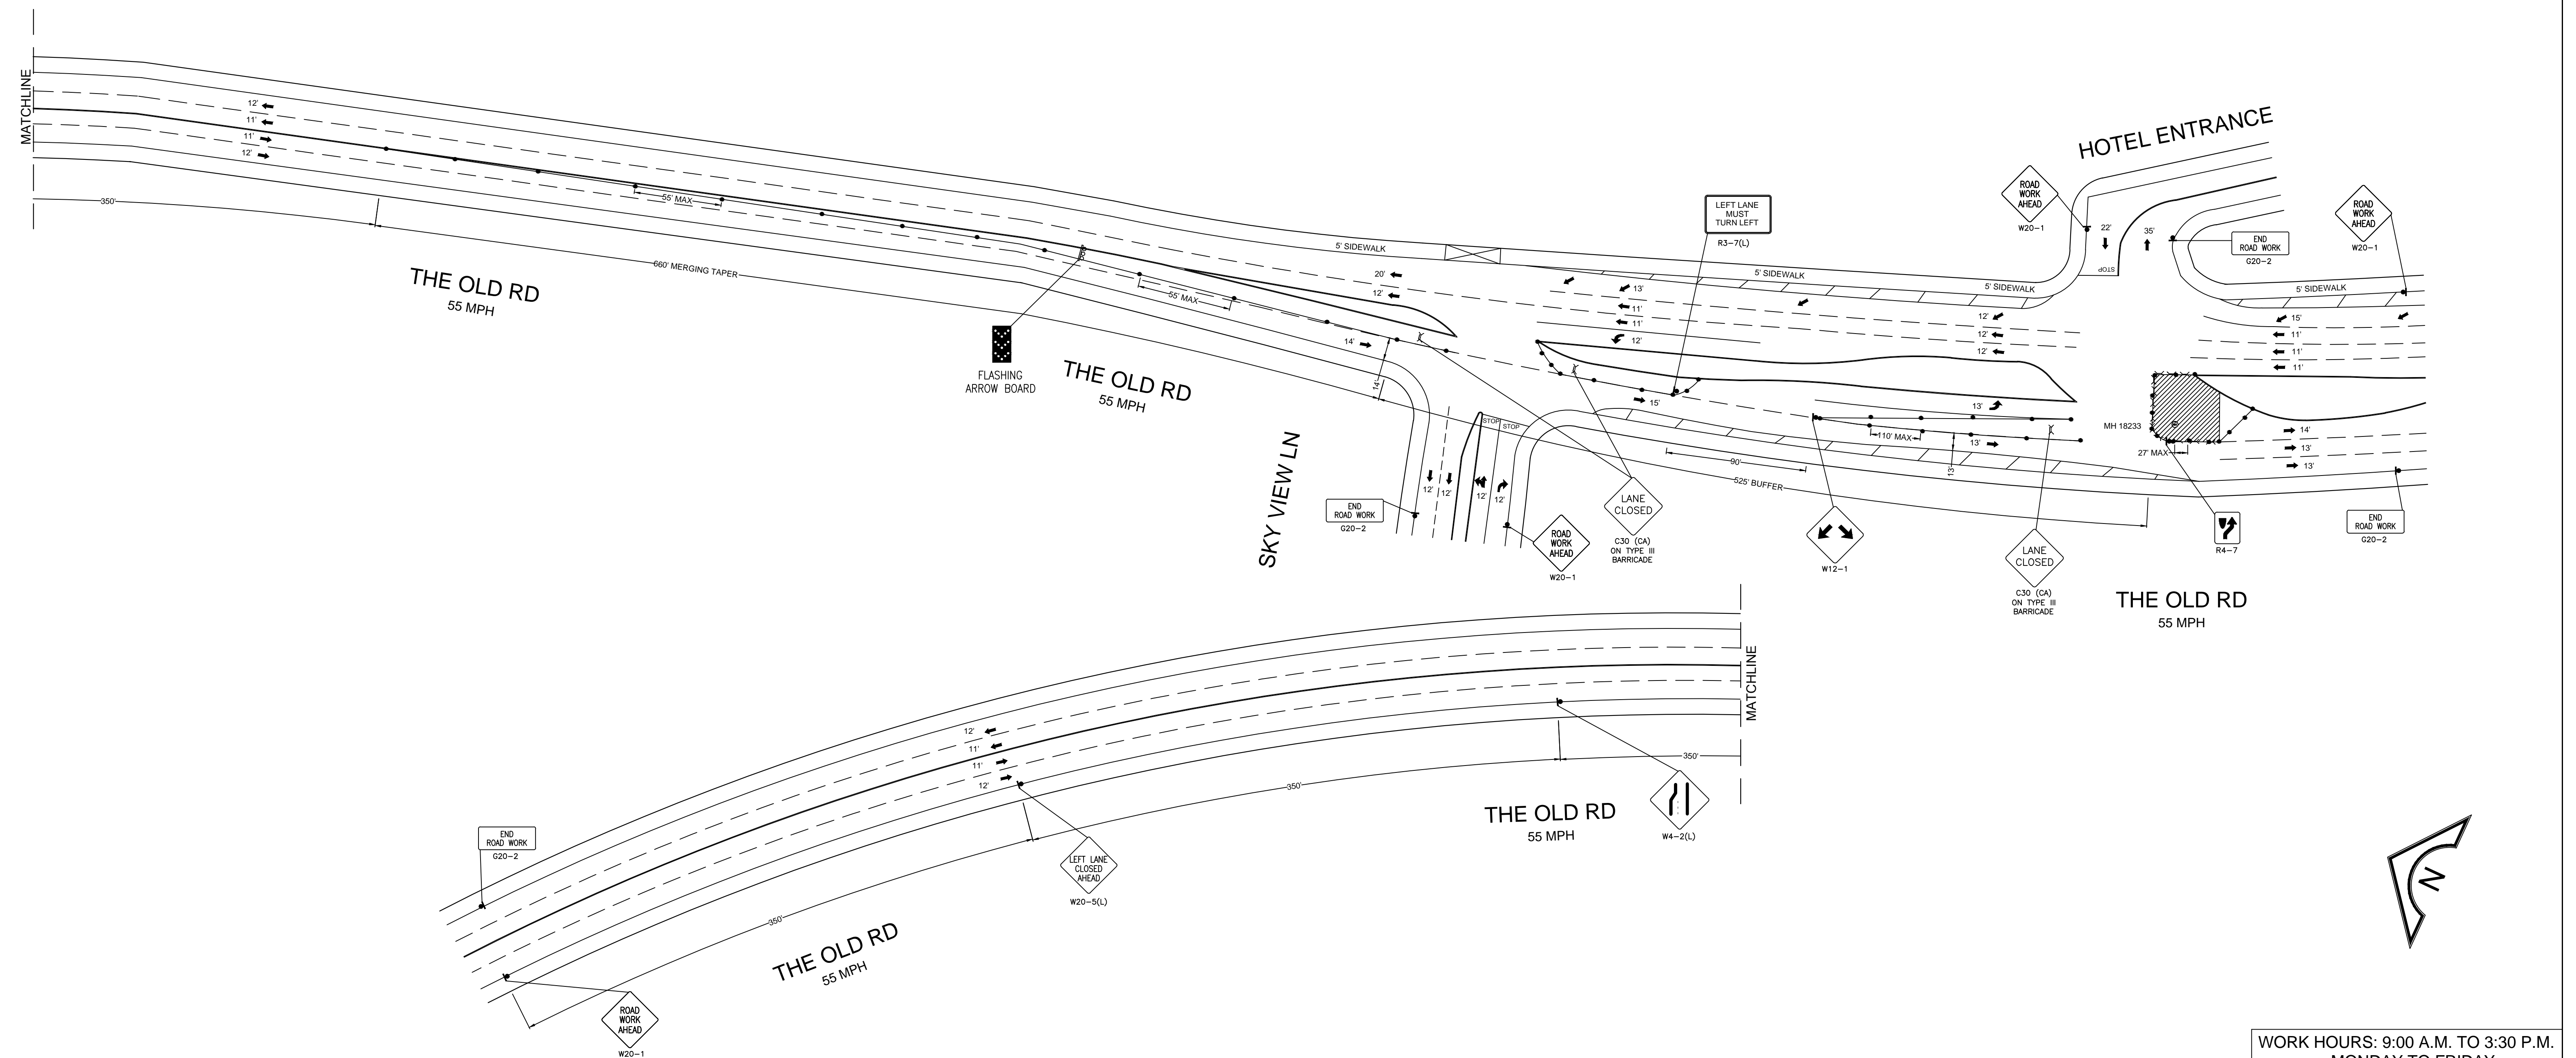

<div><div>600 E GREEN ST RM 300 PASADENA, CA 91101-2020</div></div>				WORK HOURS: 9:00 A.M. TO 3:30 P.M. MONDAY TO FRIDAY	
		<div><div></div><div>DRAWN</div><div>CHECKED</div><div>APPROVED</div><div>DATE</div></div>	<div><div></div><div>10/07/2013</div><div></div><div></div><div>REVISIONS</div></div>	<div><div>AT&TID</div><div>MBM</div><div></div><div></div><div>THOMAS GUIDE</div></div>	<div><div>LAYOUT ENGINEER</div><div>TELEPHONE NUMBER</div><div>EMAIL ADDRESS</div><div>FACILITY ENGINEER AMY ILLANGAKOON</div><div>TELEPHONE NUMBER 949-313-6094</div><div>OFFICE KC-12</div><div>CENTRAL OFFICE NEWHALL</div><div>UNDERGROUND CONSTRUCTION ROUTINE ORDER/ESTIMATE NUMBER</div></div>
<div><div>CHC Consulting, LLC</div><div>1700 E. Garry Ave. , Suite 210 Santa Ana, CA 92705 (949) 250-0004 / FAX (949) 250-0006</div></div>		<div><div>SCALE</div><div>1" = 50'</div></div>		<div><div>4550-C2</div><div>9231306</div></div>	
		<div><div>FILE NAME:</div><div>9231306 TCP</div></div>		<div><div>DRAWING:</div><div>3/3</div></div>	
