



Curb side concrete

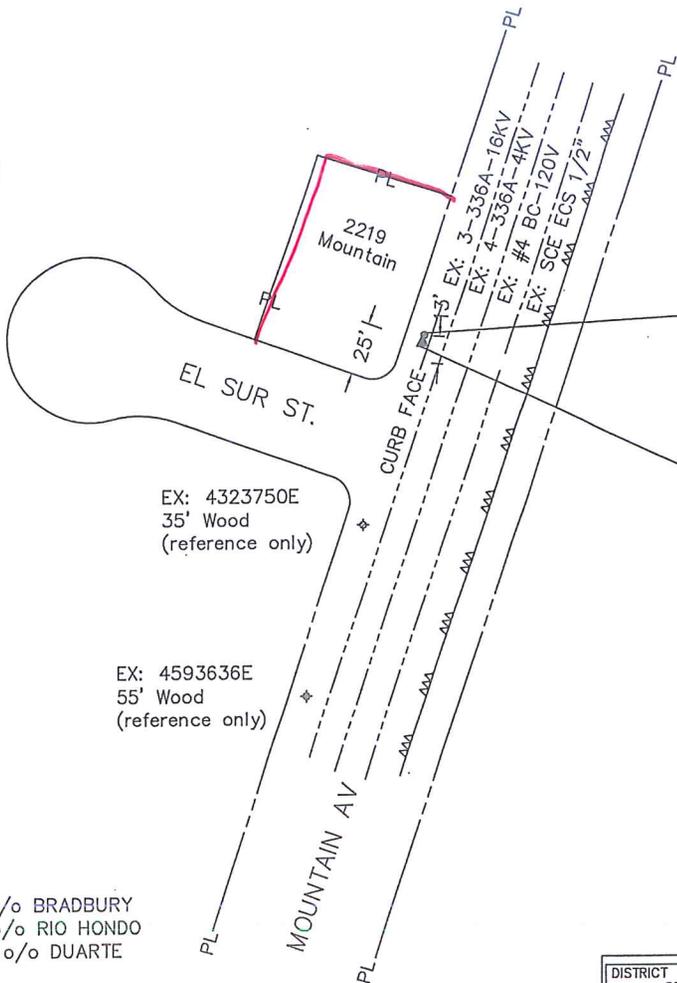

POLE	126872E	1
55'	Class H2	
IN: 16KV, 600A Omni Rupter SW-Inverted Type		
IN: 10' Crossarm V-Brace		
IN: 4-4KV Glass & Pin Insulators		
IN: 1-4KV Neutral Glass & Pin Insulator		
IN: Avian Covers at 4KV Level		
*Transfer Extg Secondaries & Service's		
*Transfer Extg Street Light		
RM	126872E	2
55'	Wood-1949	Class C3
RM: 16KV, 600A KPF SW & Crossarm		
RM: 10' Crossarm & 4KV Pin Insulators		



CIRCUIT & SUB: BATEMAN 16KV o/o BRADBURY
 SPILLWAY 16KV o/o RIO HONDO
 SANITARIUM 4KV o/o DUARTE

NOTE TO CREW:
 Replace Det. Pole, Set new pole at hard north, line truck access ok.
 Replace 16KV KPF switch with Omni-Rupter.
 Replace 4KV Crossarm & Insulators.
 Install Avian Triangle Guards.

Service Planner: Raul Valenzuela
 (626) 607-7100

*(P) 1-30-14
 RB*

DISTRICT 27 - MONROVIA	PROJ. MGR. TRAN, TOM PHONE 626-303-8420	PLANNER VALENZUELA, RAUL PHONE 626-303-8420	
FOREMAN	TRUCK NO. P/E	INVENTORY MAP NO. THOMAS GUIDE 072-085D LACO 567H7	GRID NO. DESIGN NO. 547658_0.01
CSD 140 Y ___ N ___	BY-PASS CODE	EXISTING CHANGE TO	TLM CHECKED ___ LOAD
PRODUCT/SAP NO. 780962-INFRA. REPLC - DET POLE REPLC	PRODUCT/SAP NO.	PRODUCT/SAP NO.	ASSOCIATED DESIGN NO.
			PROPOSED CONSTRUCTION (LOCATION) F/O 2219 MOUNTAIN AVE DUARTE, CA 91010
	11/18/13	Raul Valenzuela	SHEET 1 OF 1
TYPE APPROVED BY	DATE	CHECKED BY	DRAWN BY PAX #
Southern California Edison Company			JOB NO. 547658_0.01

Pole CS @ 2219 Mountain Ave

Duarte/CA County

PERMIT NEEDED

AUTHORIZATION FOR JOINT POLE TRANSACTION

J.P. FORM 2-1 Preliminary 1/95

Date Prepared 12/03/2013

This authorization is in accordance with Joint Pole Agreement and Routine. The undersigned have agreed on joint work as specified hereon.

Date Sent _____

Confirming Agreement _____

In Field _____

By Telephone _____

Est. Const. Start _____

No. of Pages 3

J.P. Auth.No. E6027-405779275

UTILITY	REPRESENTATIVE	DISTRICT-DIVISION-EXCHANGE	APPROVED	TAXING INSTRUCTIONS	ACCOUNTING DATA
E	RAUL VALENZUELA	MONROVIA	TOM TRAN	MONROVIA	TD 780962
VZ	DAVID ARMENTA	FOOTHILL			

POLE NO.	Pole Length Anchor Size	Year Set	Record				Proposed				Item No.	LOCATION AND NATURE OF WORK <small>If not in accordance with Joint Pole agreement and routine-state reasons.</small>		
			Pole Trt Class Anchor Direct.	16KV E			16KV E							
					VZ							E TO REPLACE SEC 7.11, 19.6	1	
126872E	55	1949	FT	48-24		23-5			C-24		PTD		MOUNTAIN AV W/S 8' N/O EL SUR ST	2
			3						1/2(1)			5C	TOPPING POLE	3
									1/2(1)			10C	CEMENT SAW CUT BREAK AND REPAIR	4
														5
														6
126872E	55	2014	FT						48-24		23-5		MOUNTAIN AV W/S 26' N/O EL SUR ST	7
			H2											8
														9
														10
														11
														12
														13

POLE LEGEND:
P = PULL
PB = PULL BUTT
T = TRANSPORT
S = SALVAGE
D = DISPOSE
TN = TENANT

ANCHOR LEGEND:
AR = ANCHOR/ARM REMOVED
AT = ANCHOR/ARM TRANSFERRED

Show Quantity of Items to be billed in the Column of Party to be Paid.

GEOGRAPHICAL LOCATION

MONROVIA

COMMUNITY

VP/J.P.-03

Rev. Jan 2010
