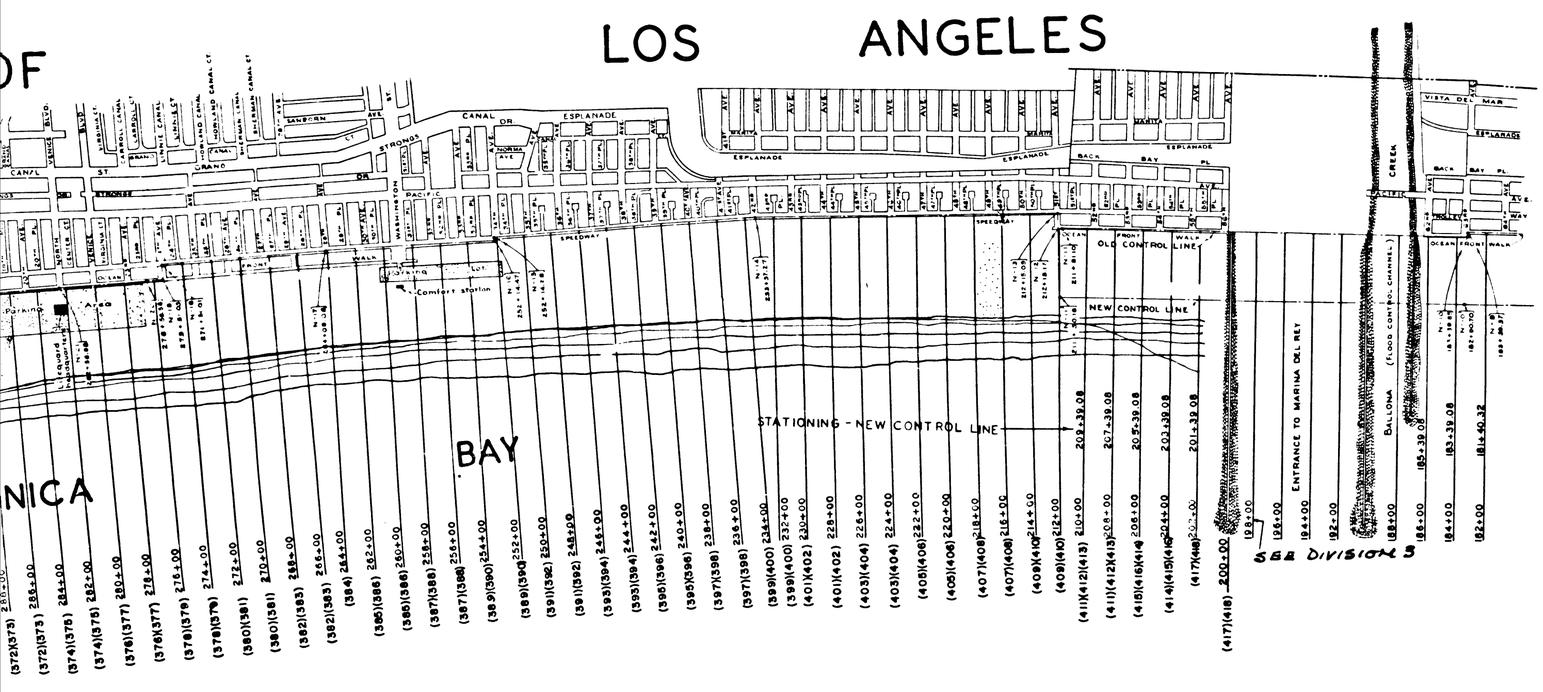

NUMBER STATION	ADJUSTED STATION	GRID COORDINATE NORTH	GRID COORDINATE EAST	FROM	TO	GRID BEARING	DISTANCE
N-13	212+15.09	4,100,965.80	4,149,209.11				
				N-13	N-14	N 31°57'34" W	2,122.27
N-14	233+37.27	4,102,766.38	4,148,085.75				
				N-14	N-15	N 35°35'35" W	1,877.10
N-15	252+14.28	4,104,292.78	4,146,993.23				
				N-15	N-16	S 55°20'10" W	12.23
N-16	252+14.47	4,104,285.83	4,146,983.17				
				N-16	N-17	N 34°42'23" W	1,194.67
N-17	264+09.08	4,105,267.94	4,146,302.96				
				N-17	N-18	N 36°00'38" W	1,141.96
N-18	275+51.01	4,106,191.70	4,145,631.56				
				N-18	N-19	S 53°59'49" W	112.77
N-19	275+51.03	4,106,125.41	4,145,540.32				
				N-19	N-20	N 36°00'18" W	105.56
N-20	276+56.58	4,106,210.81	4,145,478.26				
				N-20	N-21	N 36°00'18" W	602.45
N-21	282+56.98	4,106,696.55	4,145,125.28				
				N-21	N-22	N 36°00'18" W	523.25
N-22	287+80.17	4,107,119.84	4,144,817.69				
				N-22	N-23	N 36°00'18" W	483.89

BEACH AND OFFSHORE PROFILES

SANTA MONICA BAY

FROM

MALAGA COVE

TO

TOPANGA CANYON

FROM SURVEYS AND RECORDS OF THE COUNTY ENGNEER AND THE LOS ANGELES CITY ENGINEER

COUNTY SURVEYORS MAP NO. B-1726

DIVISION 4 OF 6 DIVISIONS

SHEET NO. 4 OF 47 SHEETS

SCALE: 1 INCH = 500 FEET

JOB NUMBERS: 7951, 8109, 8412, & 0300.02

JOHN A. LAMBIE - COUNTY ENGINEER

SURVEYED AS INDICATED

SURVEYED UNDER INSTRUCTIONS OF THE BOARD OF SUPERVISORS PER ORDERS DATED JULY 2 AND SEPT. 16, 1935 AND MARCH 6, 1945

F.B. REF'S. AS SHOWN

L.A. COUNTY F.B. 930 & F.B. 2100

FIELD WORK BY — M. A. VAN DEREN, F. H. BLANCHARD

& L.A. CITY BUREAU OF ENGINEERING

OFFICE WORK BY — J. S. HALE, C. W. HINZMAN

CHECKED BY — K. R. KVAMMEN, J. S. HALE, C. W. HINZMAN

DATUM: MEAN LOWER LOW WATER PER U.S.C. & G.S. TIDE GAUGE AT LOS ANGELES OUTER HARBOR. M.H.T. = 4.71

SEE INDEX SHEET NO. 1 OF 832 SHEETS

CSB-1726-10

A1 of A2

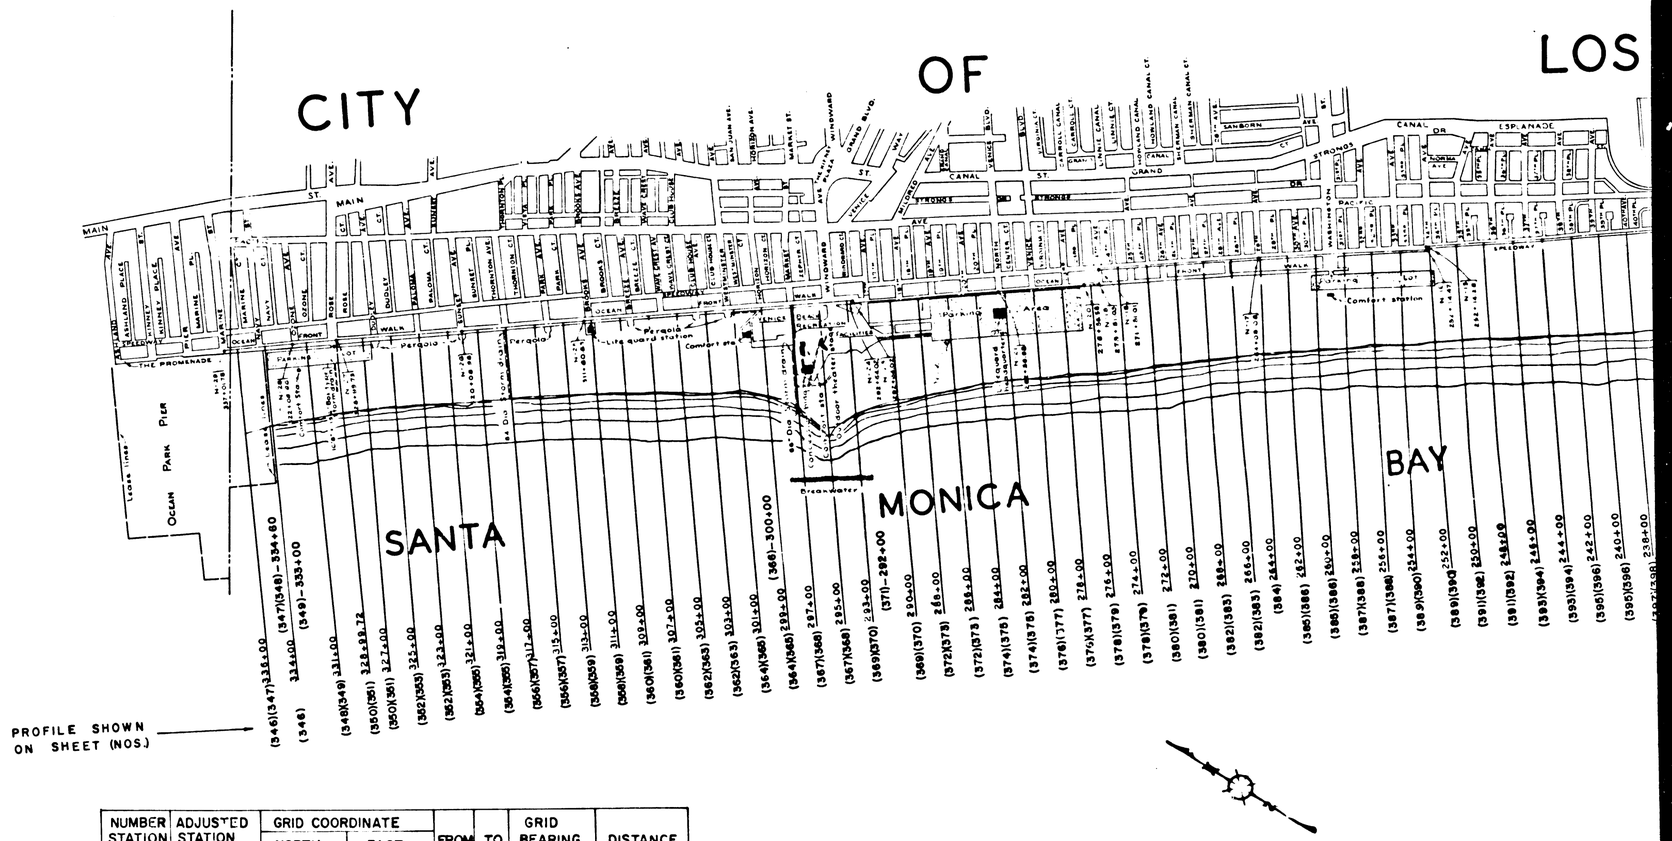

NUMBER STATION	ADJUSTED STATION	GRID COORDINATE NORTH	GRID COORDINATE EAST	FROM	TO	GRID BEARING	DISTANCE
N-22	287+80.17	4,107,119.84	4,144,817.69				
				N-22	N-23	N 36°00'18"W	483.89
N-23	292+64.02	4,107,511.29	4,144,533.23				
				N-23	N-24	N53°58'50"E	16.14
N-24	292+64.02	4,107,520.78	4,144,546.28				
				N-24	N-25	N 36°13'04"W	1,896.37
N-25	311+60.23	4,109,050.73	4,143,425.80				
				N-25	N-26	N 36°07'12"W	848.82
N-26	320+08.98	4,109,736.39	4,142,399.44				
				N-26	N-27	N 36°11'11"W	890.82
N-27	328+99.73	4,110,455.37	4,142,399.49				
				N-27	N-28	N 37°05'30"W	308.97
N-28	332+08.66	4,110,701.82	4,142,213.16				
				N-28	N-29	N 37°05'30"W	493.19
N-29	337+01.79	4,111,095.23	4,141,915.72				
				N-29	N-30	S 51°55'20"W	25.05

CSB-1726-10
A2 OF A2
