ASPLUNDH CONSTRUCTION CORP.

SOUTHERN CALIFORNIA EDISON
An EDISON INTERNATIONAL Company

DETERIORATED POLE REPLACEMENT

CIRCUIT (S):
EZRA 4KV o/o BRIDGE SUB

STA'S
11-12

ADDRESS:
LOCATION: LEMOLI AV E/S 11' S/O 152ND ST
CITY: HAWTHORNE
*** NOTES: E-ALL POLE**

11 — RM — 2083807E
40' — Class C5
RM: 1- POLE 40' CLASS 5 WOOD FULL TREAT
RM: 2- SEC ROLLER (166-CLEVIS & SPOOL)

SET 1' NORTH
POLE — 2083807E — 12
40' — Class C5
IN: 1- POLE 40' CLASS 5 WOOD FULL TREAT
IN: 1- SEC ROLLER (166-CLEVIS & SPOOL)

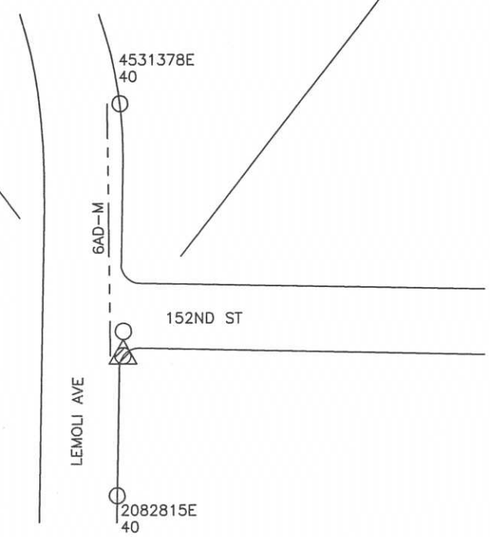

TRANSFER (S):
1-6AD-120V
1-100W ST LT

GPS: LAT: N 33° 53' 34.53"
LONG: W 118° 19' 49.81"

SPEED LIMIT 25

PEDESTRIAN TRAFFIC CONTROL REQUIRED
[X] YES [ ] NO

TLM DATA:

	SIZE	KVA	CUST.	% LOAD
EXIST				
PROP.				

VOLTAGE DROP ____ %
PRI. CIRC. _____

NOTES

JOINT POLE:	N
RENTER:	N
MITC FUME:	N
JOINT MEET:	N
TRUCK ACCESS:	Y
HAND SET:	N
CONTACT CATV:	N
ENVIRONMENTAL:	N
REAL PROP. REVIEW:	N
PAVEMENT REPAIR:	N
[ ] CONCRETE / [ ] ASPHALT	____X____

PERMIT REQ'D.

CALTRANS:	
ENCROACHMENT:	
RAILROAD:	
HELICOPTER:	
OTHER:	

NOT TO SCALE

DISTRICT 44 – SOUTH BAY	PROJ. MGR. RODRIGUEZ, JOHN.T. PHONE 909-469-0219	PLANNER HAUPT, KYLE PHONE 714-893-2405	
FOREMAN	TRUCK NO. / P/E / INVENTORY MAP NO. 44-66B	THOMAS GUIDE LA 733-F5 / GRID NO.	DESIGN NO. **551657_0.01**
CSD 140 Y____ N____ / BY-PASS CODE / EXISTING ____ CHANGE TO ____	TLM CHECKED ____ %LOAD	J.P.A. NO.	ASSOCIATED DESIGN NO.
PRODUCT/SAP NO. **TD787574**	PRODUCT/SAP NO.	PRODUCT/SAP NO.	

TYPE	APPROVED BY	DATE	CHECKED BY	DRAWN BY	PAX #
				V.B	

Southern California Edison Company

PROPOSED CONSTRUCTION (LOCATION)
DET POLE REPLACEMENT
XSTRT VARIOUS TORRANCE CA
TORRANCE

SHEET ____ OF ____

JOB NO. 551657_0.01
