ASPLUNDH CONSTRUCTION CORP.

SOUTHERN CALIFORNIA EDISON
An EDISON INTERNATIONAL Company

DETERIORATED POLE REPLACEMENT

CIRCUIT (S):
PAINER 12KV o/o SANTA FE SPRINGS SUB

STA'S
5-6

ADDRESS:
LOCATION: W/S GUNN AV S/O MULBERRY RD 10'
CITY: FULLERTON
*** NOTES:** E-ALL POLE
TRAFFIC CONTROL REQ'D

5 — RM — X15409E
40' Class C5
RM: 1- POLE 40' CLASS 5 WOOD FULL TREAT
RM: 1- SEC ROLLER (166-CLEVIS & SPOOL)

SET 1' SOUTH
POLE — 4843042E — 6
40' Class C5
IN: 1- POLE 40' CLASS 5 WOOD FULL TREAT
IN: 1- SEC ROLLER (166-CLEVIS & SPOOL)

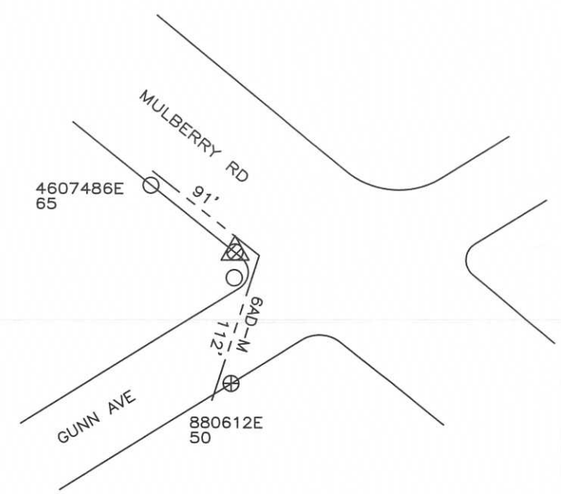

TRANSFER (S):
1-6AD-M

NOT TO SCALE

PERMIT REQ'D.

CALTRANS:	
ENCROACHMENT:	
RAILROAD:	
HELICOPTER:	
OTHER:	

SPEED LIMIT NA

PEDESTRIAN TRAFFIC CONTROL REQUIRED
[X] YES [ ] NO

GPS: LAT: N 33° 56' 43.8"
LONG: W 118° 01' 52.0"

TLM DATA:

	SIZE	KVA	CUST.	% LOAD
EXIST				
PROP.				

VOLTAGE DROP ____ %
PRI. CIRC. _____

NOTES

JOINT POLE:	
RENTER:	
MITC FUME:	
JOINT MEET:	
TRUCK ACCESS:	X
HAND SET:	
CONTACT CATV:	
ENVIRONMENTAL:	
REAL PROP. REVIEW:	
PAVEMENT REPAIR:	X
[X] CONCRETE / [ ] ASPHALT	4' X 4'

DISTRICT 47 – WHITTIER	PROJ. MGR. RODRIGUEZ, JOHN T PHONE 909-469-0219		PLANNER PETERSON, GRANT PHONE 714-893-2405		
FOREMAN	TRUCK NO.	P/E	INVENTORY MAP NO. 092-4278-1	THOMAS GUIDE CAL-707-D4	GRID NO.	DESIGN NO. 590536_0.01
CSD 140 Y ___ N ___	BY-PASS CODE	EXISTING ___ CHANGE TO ___	TLM CHECKED ___ %LOAD	J.P.A. NO.	ASSOCIATED DESIGN NO.
PRODUCT/SAP NO. 846323-INFRA REP - DET POLE RELACE	PRODUCT/SAP NO.		PRODUCT/SAP NO.		

TYPE	APPROVED BY	DATE	CHECKED BY	DRAWN BY	PAX #
				LW	

PROPOSED CONSTRUCTION (LOCATION)
DET POLE REPLACEMENT
XSTRT VARIOUS WHITTIER CA
WHITTIER

SHEET ___ OF ___

JOB NO. 590536_0.01

Southern California Edison Company
