P 4.7.14 T

PERMIT NOT NEEDED

WELLINGTON HEIGHTS / LA. CO

CAMY 4kV O/O BELVEDERE SUB

NOTES:

FIM IS WRONG 2279085E IS 90° FROM 7405E
6B SL LOOKS IDLE PLEASE VERIFY
REAR PROPERTY LINE POLE

LOC. 138' E/OF S. RECORD AVE
220' N/OF E. EAGLE ST
REAR OF ADD. 424 S. RECORD AVE.

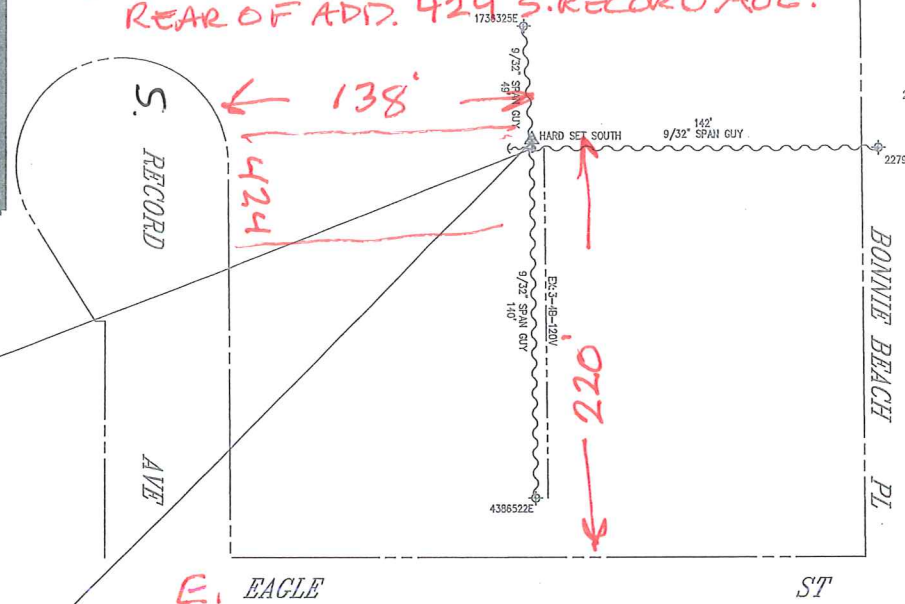



(14) POLE 7405E
40' Class C5
IN: 1- POLE 40' CLASS 5 WOOD FULL TREAT
IN: 1- XA SNGL FB 10' STEEL PINS SECONDARY
IN: 1- INS POLY DE 4KV RIG #6
IN: 5- SEC ROLLER (166-CLEVIS & SPOOL)
IN: 1- SEC 2" PVC FOR UNDER ARM W/#2 TW
IN: 2- SEC STEEL PIN & INS - PHASE
IN: 1- SEC STEEL PIN & INS - NEUTRAL
IN: 1- AG SPAN GUY 9/32" - 200'
IN: 1- AG DOWN GUY 3/8" - 50' LESS THAN 22.5KV

(13) RM 7405E
Pic. OK.
45' Class C4
RM: 1- POLE 45' CLASS 4 WOOD FULL TREAT
RM: 1- XA SNGL FB 10' STEEL PINS SECONDARY
RM: 1- XA DBLE FB 10' STEEL PINS SECONDARY
RM: 1- INS POLY DE 4KV RIG #6
RM: 4- SEC ROLLER (166-CLEVIS & SPOOL)
RM: 1- SEC 2" PVC FOR UNDER ARM W/#2 TW
RM: 2- SEC STEEL PIN & INS - PHASE
RM: 1- SEC STEEL PIN & INS - NEUTRAL
RM: 2- AG SPAN GUY 9/32" - 200'

TRANSFERS:
1- 6B SL
3- 4B 120V (S)
1- 9/32" S/G (S)
1- 9/32 S/G (E)
6- 4AT SVC

GPS
34°-01'-54.4"
118°-10'-52.0"

NOT TO SCALE

SOUTHERN CALIFORNIA EDISON
An EDISON INTERNATIONAL Company

SET IN SAME HOLE N OR SET ___ S HARD SET Y

ENVIRO REVIEW	N	HAND SET	Y	SPECIAL EQUIP NEEDED	N
JOINT MEET	N	PERMIT NEEDED	N	IF YES WHAT IS NEEDED?	
TRUCK ACCESS	N	NETCOMM SHEET	N		
PAVEMENT REPAIR	N	RIGHTS CHECK	N	EST. TIME TO REPLACE	
ASPHALT		PED TRAFFIC CONTROL	N	40 MH	
CONCRETE		OUTAGE	Y	CONTACT CATV	N
REPAIR SIZE		CSD-140	N	MITC POLE	N

DISTRICT 22 - MONTEBELLO	PROJ. MGR. RODRIGUEZ, JOHN T. PHONE 909-469-0219		PLANNER CARRILLO, CHRIS PHONE 909-322-5429		
FOREMAN	TRUCK NO.	P/E	INVENTORY MAP NO. 122-4230-1	THOMAS GUIDE 635 E6	GRID NO.
DESIGN NO. 490366_0.01					
CSD 140 Y___ N___	BY-PASS CODE	EXISTING ___ CHANGE TO ___	TLM CHECKED ___ %LOAD	J.P.A. NO. E 6022 000405842689	ASSOCIATED DESIGN NO.
PRODUCT/SAP NO. 698638 - DET POLE REPLACEMENT	PRODUCT/SAP NO.		PRODUCT/SAP NO.		

PROPOSED CONSTRUCTION (LOCATION)
424 RECORD AVE
EAST LOS ANGELES

TYPE	APPROVED BY	DATE	CHECKED BY	DRAWN BY	PAX #

SHEET ___ OF ___ JOB NO. 490366_0.01

Southern California Edison Company

PAGE NO. 3 J.P. AUTH. NO. E6022-000405842689

POLE NO.	Pole Length / Anchor Size	Year Set	Pole Trt / Class / Anchor Direct.	Record 120V E	Record HLA	Record	Record	Proposed 120K V E	Proposed HLA	Proposed	Proposed	Proposed	Item No.	LOCATION AND NATURE OF WORK If not in accordance with Joint Pole agreement and routine-state reasons.	
														E TO REPLACE PER SEC. 7.11, 7.4, 19.6, 14.3	1
85096H	40	1936	FT 5	.50	23'			C-5	LTD					EAGLE ST N/S 45' W/O MCBRIDE ST, LOS ANGELES	2
								1/2(1)					5C	TOP POLE	3
								1/2(1)				3X3	10C	CONCRETE REPAIR	4
															5
85096H	45		FT 2					39-10	23-5					EAGLE ST N/S 45' W/O MCBRIDE ST, EAST LOS ANGELES	6
									TN 23						7
								1/2(1)					19A		8
								1/2(1)					15B	VIS STRIPS	9
															10
				4KV				4KV						E TO REPLACE PER SEC. 7.11, 10.8, 19.4	11
7405E	45	1932	FT 5	34-8	20-1			PTD						RECORD AV P/L E, 235' N/O EAGLE ST, EAST LOS ANGELES	12
								1					78A	CATV	13
															14
7405E	40		FT 5					34-8	20-1					RECORD AV P/L E, 234' N/O EAGLE ST, EAST LOS ANGELES	15
														HARD SET SOUTH	16
								1/2(1)					13B	FENCE	17
															18
															19

POLE LEGEND:
P = PULL (Item 5A)
PB = PULL BUTT
T = TRANSPORT (Item 5B)
S = SALVAGE
D = DISPOSE (Item 5D)
TN = TENANT
L = LOWER TOP(Item 5E)
C(XX) = FOOTAGE CUT
SCZ = SAFETY CLEARANCE ZONE

ANCHOR/ARM LEGEND:
AR = ANCHOR/ARM REMOVED
AT = ANCHOR/ARM TRANSFERRED

Show Quantity of Items to be billed in the Column of Party to be Paid.

GEOGRAPHICAL LOCATION

EAST LA
COMMUNITY

Rev. Jul 2013
