P 4.7.14 T

PERMIT NEEDED

EAST LOS ANGELES / LA. CO.

GLEASON 16kV O/O REPETTO SUB
BURGER 4kV O/O BICKNELL SUB

AT CURB W/SIDE S. FORD BL.
18' N/OF S. HUMPHREYS. AV.
ACROSS FROM ADD 660 S. FORD BL.

(17) RM 83647E
55' Class C3
RM: 1- POLE 55' CLASS 3 WOOD FULL TREAT
RM: 1- XA SNGL VB 10' STEEL PINS N/BOND
RM: 1- XA SNGL VB 10' STEEL PINS
RM: 3- INS GLASS & PIN 4KV
RM: 1- INS NEUT GLASS & PIN 4KV
RM: 1- SEC ROLLER (166-CLEVIS & SPOOL)
RM: 3- INS POLY W/PIN 16(25)KV CLMP #4-336 ACSR

CONC.

(18) POLE 83647E
55' Class C2
IN: 1- POLE 55' CLASS 2 WOOD FULL TREAT
IN: 1- XA SNGL VB 10' STEEL PINS N/BOND
IN: 1- XA SNGL VB 10' STEEL PINS
IN: 4- INS POLY W/PIN 12KV CLMP #6-4/0 CU
IN: 1- SEC ROLLER (166-CLEVIS & SPOOL)
IN: 3- INS POLY W/PIN 16KV CLMP #6-4/0 CU

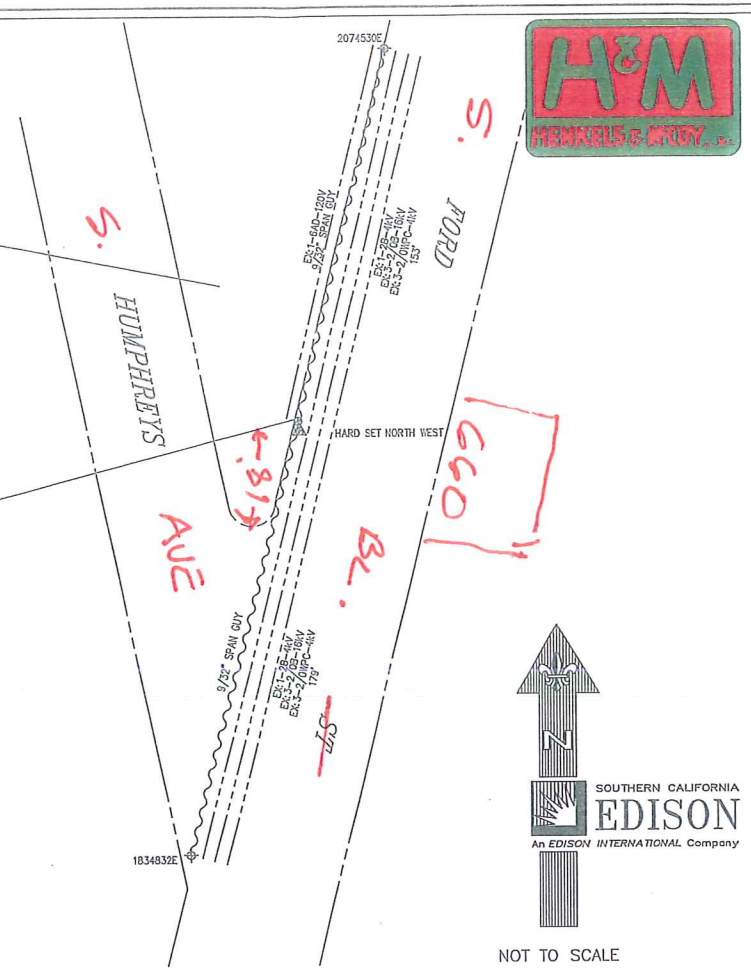

GPS
34°-01'-34.8"
118°-10'-09.9"

TRANSFERS:
3- 2/0B 16kV (N&S)
2- 2/0WPC 4kBV (N&S)
1- 2B 4kV (N&S)
1- 6AD ST/LT (N)
1- 6' MAST ARM ST/LT
1- 9/32" S/G (N)
1- 9/32 S/G (S)

SET IN SAME HOLE N OR SET ____' NW HARD SET Y

ENVIRO REVIEW	N	HAND SET	N	SPECIAL EQUIP NEEDED	N
JOINT MEET	Y	PERMIT NEEDED	Y	IF YES WHAT IS NEEDED?	
TRUCK ACCESS	Y	NETCOMM SHEET	N		
PAVEMENT REPAIR	Y	RIGHTS CHECK	N	EST. TIME TO REPLACE	
ASPHALT		PED TRAFFIC CONTROL	Y	40 MH	
CONCRETE	Y	OUTAGE	N	CONTACT CATV	Y
REPAIR SIZE	3x3	CSD-140	N	MITC POLE	N

DISTRICT 22 - MONTEBELLO	PROJ. MGR. RODRIGUEZ, JOHN T. PHONE 909-469-0219		PLANNER CARRILLO, CHRIS PHONE 909-322-5429		
FOREMAN	TRUCK NO.	P/E	INVENTORY MAP NO. 122-4236-1	THOMAS GUIDE 635-F7	GRID NO.
DESIGN NO. 490366_0.01					
CSD 140 Y___ N___	BY-PASS CODE	EXISTING ___ CHANGE TO ___	TLM CHECKED ___ %LOAD	J.P.A. NO. E 6022 000405842689	ASSOCIATED DESIGN NO.
PRODUCT/SAP NO. 698638 - DET POLE REPLACEMENT	PRODUCT/SAP NO.			PRODUCT/SAP NO.	

TYPE	APPROVED BY	DATE	CHECKED BY	DRAWN BY	PAX #

PROPOSED CONSTRUCTION (LOCATION)
660 S FORD BLVD
EAST LOS ANGELES

SHEET ___ OF ___

JOB NO. 490366_0.01

Southern California Edison Company

POLE NO.	Pole Length / Anchor Size	Year Set	Pole Trt / Class / Anchor Direct.	Record 4KV E	Record HLA	Record ATC NG	Record ATS	Proposed 4KV E	Proposed HLA	Proposed ATC	Proposed NG	Proposed ATS	Item No.	LOCATION AND NATURE OF WORK If not in accordance with Joint Pole agreement and routine-state reasons.	
														E TO REPLACE PER SEC. 7.11, 14.3, 19.6	1
83647E	55	1940	FT 3	48-17	21-3	23-1	25-1	C-15	PTD					FORD BL W/S 3' N/O HUMPHREYS AV, EAST LOS ANGELES	2
								1/5(1)						TOP POLE	3
															4
															5
83647E	55		FT 5					48-16	21-3	23-1	23-1	25-1		FORD BL W/S 4' N/O HUMPHREYS AV, EAST LOS ANGELES	6
								24-1						HARD SET NORTH WEST	7
								TN 24							8
								1/5(1)					15B	VIS STRIPS	9
								1/5(1)				3X3	10C	CONCRETE REPAIR	10
															11
															12
															13
															14
															15
															16
															17
															18
															19

POLE LEGEND:
P = PULL (Item 5A)
PB = PULL BUTT
T = TRANSPORT (Item 5B)
S = SALVAGE
D = DISPOSE (Item 5D)
TN = TENANT

L = LOWER TOP(Item 5E)
C(XX) = FOOTAGE CUT
SCZ = SAFETY CLEARANCE ZONE

ANCHOR/ARM LEGEND:
AR = ANCHOR/ARM REMOVED
AT = ANCHOR/ARM TRANSFERRED

Show Quantity of Items to be billed in the Column of Party to be Paid.

GEOGRAPHICAL LOCATION

EAST LA
COMMUNITY

Rev. Jul 2013
