(P) 4.7.14 (T)

PERMIT NEEDED

WELLINGTON HEIGHTS/LA.CO.

HICKS 4kV O/O BELVEDERE SUB

AT CURB W/SIDE NASSAU AVE
156' S/OF E. EAGLE ST
AT ADD 453 NASSAU AV.

(16) POLE 9407E
45' Class C2
IN: 1- POLE 45' CLASS 2 WOOD FULL TREAT
IN: 1- XA SNGL FB 10' STEEL PINS N/BOND
IN: 1- XA SNGL FB 10' STEEL PINS SECONDARY
IN: 2- INS GLASS & ANGLE PIN 12KV
IN: 2- SEC STEEL PIN & INS - PHASE
IN: 1- SEC STEEL PIN & INS - NEUTRAL
IN: 2- AG SPAN GUY 9/32" - 200'

(15) RM 9407E
40' Class C5
RM: 1- POLE 40' CLASS 5 WOOD FULL TREAT
RM: 1- XA DBLE FB 10' STEEL PINS N/BOND
RM: 2- INS GLASS & PIN 4KV
RM: 2- INS NEUT GLASS & PIN 4KV
RM: 1- SEC ROLLER (166-CLEVIS & SPOOL)
RM: 4- SEC STEEL PIN & INS - PHASE
RM: 2- SEC STEEL PIN & INS - NEUTRAL
RM: 2- AG SPAN GUY 9/32" - 200'

ASPHALT

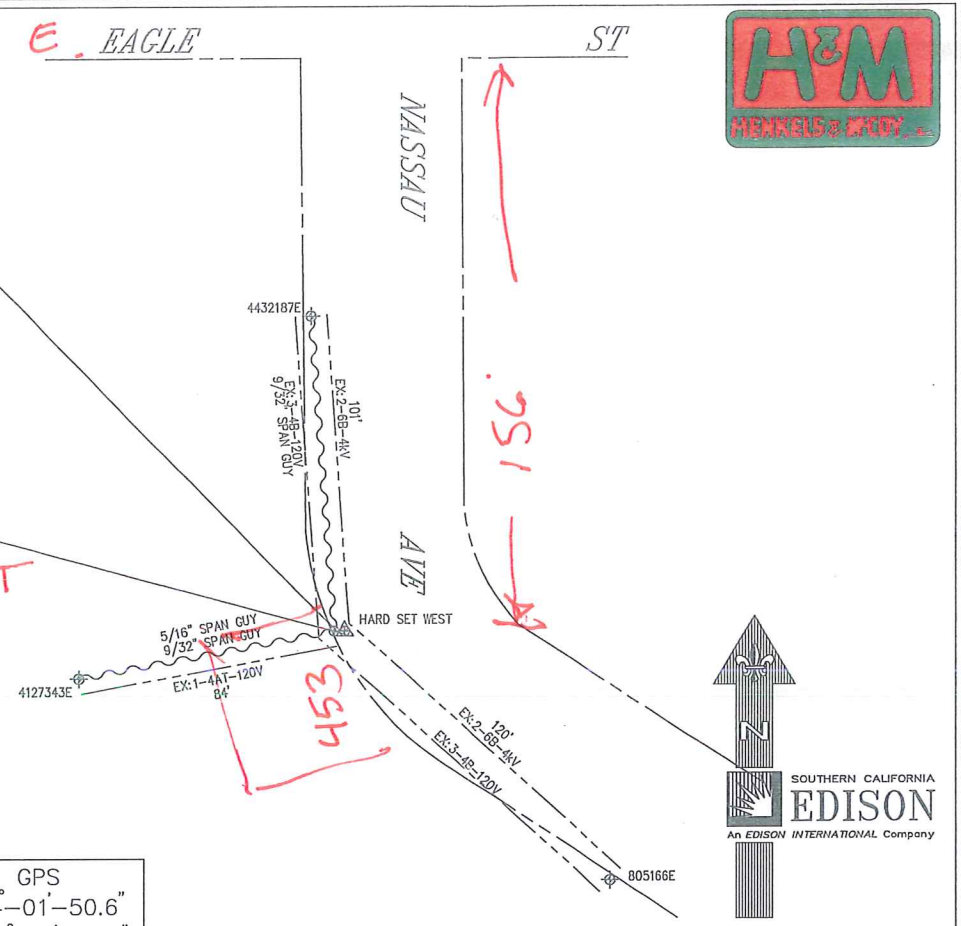

TRANSFERS:
2- 6B 4kV (N&S)
3- 4B 120V (N&S)
1- 4AT 120V (WO
2- 4AT SVC
1 6' MAST ARM ST/LT

SET IN SAME HOLE N OR SET ' W HARD SET Y

ENVIRO REVIEW	N	HAND SET	N	SPECIAL EQUIP NEEDED	N
JOINT MEET	N	PERMIT NEEDED	Y	IF YES WHAT IS NEEDED?	
TRUCK ACCESS	Y	NETCOMM SHEET	N		
PAVEMENT REPAIR	Y	RIGHTS CHECK	N	EST. TIME TO REPLACE	
ASPHALT	Y	PED TRAFFIC CONTROL	Y	40 MH	
CONCRETE		OUTAGE	Y	CONTACT CATV	Y
REPAIR SIZE	2x4	CSD-140	N	MITC POLE	N

GPS
34°-01'-50.6"
118°-11'-05.6"

DISTRICT 22 - MONTEBELLO	PROJ. MGR. RODRIGUEZ, JOHN T. PHONE 909-469-0219		PLANNER CARRILLO, CHRIS PHONE 909-322-5429		
FOREMAN	TRUCK NO.	P/E	INVENTORY MAP NO. 122-4230-1	THOMAS GUIDE 635-D6	GRID NO.
DESIGN NO. 490366_0.01					
CSD 140 Y___ N___	BY-PASS CODE	EXISTING CHANGE TO	TLM CHECKED	%LOAD	J.P.A. NO. E 6022 000405842689
ASSOCIATED DESIGN NO.					
PRODUCT/SAP NO. 698638 - DET POLE REPLACEMENT	PRODUCT/SAP NO.		PRODUCT/SAP NO.		

TYPE	APPROVED BY	DATE	CHECKED BY	DRAWN BY	PAX #

Southern California Edison Company

PROPOSED CONSTRUCTION (LOCATION)
453 NASSAU AVE
EAST LOS ANGELES

SHEET ___ OF ___

JOB NO. 490366_0.01

PAGE NO. 4 J.P. AUTH. NO. E6022-000405842689

POLE NO.	Pole Length / Anchor Size	Year Set	Pole Trt / Class / Anchor Direct.	Record 4KV E	Record HLA	Record	Record	Proposed 4KV E	Proposed HLA	Proposed	Proposed	Proposed	Item No.	LOCATION AND NATURE OF WORK If not in accordance with Joint Pole agreement and routine-state reasons.	
														E TO REPLACE PER SEC. 7.11, 19.6, 14.3	1
9407E	40	1933	FT 5	34-11	23-5			C-10	PTD					NASSAU ST W/S 150' S/O EAGLE ST, BELVEDERE	2
								1/2(1)					5C	TOP POLE	3
								1/2(1)				3X3	10C	CONCRTE REPAIR	4
															5
9407E	45		FT 2					39-9	23-5					NASSAU ST W/S 150' S/O EAGLE ST, EAST LOS ANGELES	6
								24-1						HARD SET WEST	7
								TN 24							8
								1/2(1)					15B	VIS STRIPS	9
															10
															11
															12
															13
															14
															15
															16
															17
															18
															19

POLE LEGEND:
P = PULL (Item 5A)
PB = PULL BUTT
T = TRANSPORT (Item 5B)
S = SALVAGE
D = DISPOSE (Item 5D)
TN = TENANT

L = LOWER TOP(Item 5E)
C(XX) = FOOTAGE CUT
SCZ = SAFETY CLEARANCE ZONE

ANCHOR/ARM LEGEND:
AR = ANCHOR/ARM REMOVED
AT = ANCHOR/ARM TRANSFERRED

Show Quantity of Items to be billed in the Column of Party to be Paid.

GEOGRAPHICAL LOCATION

EAST LA
COMMUNITY

Rev. Jul 2013
