04/11

E to PTD

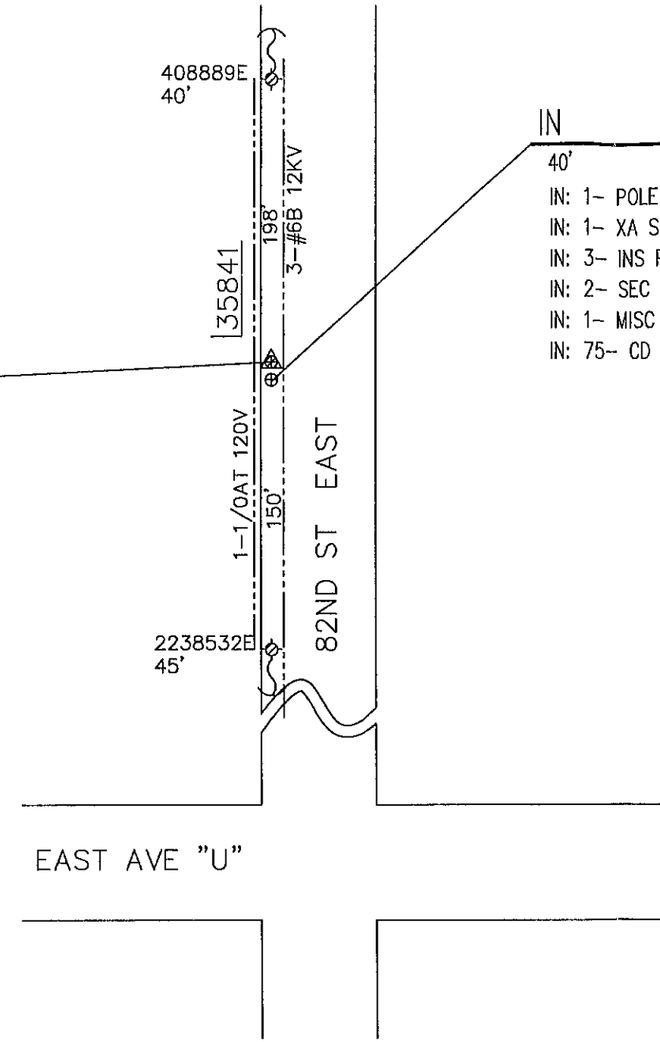

5 RM 408888E
40' Class C5
RM: 1- POLE 40' CLASS 5 WOOD FULL TREAT
RM: 1- XA SNGL FB 10' STEEL PINS
RM: 1- XA SNGL FB 10' STEEL PINS SECONDARY
RM: 3- INS GLASS/POLY 35KV & LESS
RM: 1- SEC ROLLER (166-CLEVIS & SPOOL)
RM: 1- SEC END ARM RACK WITH 3 SPOOL RACK
RM: 1- SEC 2" PVC FOR UNDER ARM W/#2 TW
RM: 75- CD ALL SIZES AL/CU 3/C
NOTE:

SET HARD SOUTH
E TO CUT 10'
TEL TO PTD

IN 408888E 6
40' Class C5
IN: 1- POLE 40' CLASS 5 WOOD FULL TREAT
IN: 1- XA SNGL FB 10' STEEL PINS
IN: 3- INS POLY W/PIN 12KV CLMP #6-4/0 CU
IN: 2- SEC ROLLER (166-CLEVIS & SPOOL)
IN: 1- MISC AVIAN HOOD FOR HENDRIX INSUL #4-653
IN: 75- CD #4 STR AL TRIPLEX W/ACSR NEUTRAL

NOTE TO CREW
TRANSFER:
3-#6B 12KV
1-1/0AT 120V

NOTES:
CIRCUIT: CALIBER 12KV
SUB: PALMDALE
CIRCUIT: N/A
SUB: N/A
REAR PROPERTY NO
TRUCK ACCESS YES
HAND DIG NO
TRAFFIC CONTROL NO
PTC NO
ROUTE # N/A
BULLETIN 322 NO
ENVIRONMENTAL NO
PERMIT REQ'D NO
TYPE N/A
TREE TRIMMING NO
CONCRETE REPAIR REQ'D NO
CRANE SET NO
GPS:
LAT: 34° 31' 58.3"
LON: 117° 59' 01.7"
ELEV: 2827'

SOUTHERN CALIFORNIA EDISON
An EDISON INTERNATIONAL Company

NOT TO SCALE

UNDERGROUND SERVICE ALERT
Dial 811
Call USA
For Underground Locating
2 Working Days Before You Dig

DISTRICT 36 - ANTELOPE VALLEY	PROJ. MGR. RODRIGUEZ, JOHN THEODORE PHONE 714-973-5678		PLANNER McDONALD, KEVIN / HWI PHONE 951-826-8800		
FOREMAN	TRUCK NO.	P/E	INVENTORY MAP NO. 121-86	THOMAS GUIDE LA 4287 H1	GRID NO.
DESIGN NO. 498887_0.01					
CSD 140 Y ___ N X	BY-PASS CODE	EXISTING ___ CHANGE TO ___	TLM CHECKED ___ %LOAD	J.P.A. NO. E6036-405569580	ASSOCIATED DESIGN NO.
PRODUCT/SAP NO. 710745-INFRASTRUCTURE REPLACEMENT - DET POLE REPLACEMENT			PRODUCT/SAP NO. SR# 1632188		PRODUCT/SAP NO. PROJ# 703433
TYPE	APPROVED BY	DATE	CHECKED BY	DRAWN BY HWI/MMF	PAX #
PROPOSED CONSTRUCTION (LOCATION) TD710745 35841 82ND ST EAST LITTLEROCK					
SHEET ___ OF ___				JOB NO. 498887_0.01	

Southern California Edison Company
