ASPLUNDH CONSTRUCTION CORP.

SOUTHERN CALIFORNIA EDISON
An EDISON INTERNATIONAL Company

DETERIORATED POLE REPLACEMENT

CIRCUIT (S):
WILDCAT 16KV o/o BULLIS SUB
RAYBORN 4KV o/o BULLIS SUB

STA'S 17-18

1

ADDRESS:
LOCATION: SAN LUIS ST N/S 15' W/O COOKACRE AV
CITY: COMPTON
*** NOTES:**

SET HARD EAST

(18) POLE 382604E
55' Class C2
IN: 1– POLE 55' CLASS 2 WOOD FULL TREAT
IN: 1– XA SNGL FB 10' STEEL PINS
IN: 2– XA SNGL FB 10' STEEL PINS SECONDARY
IN: 3– INS POLY W/PIN 16(25)KV CLMP #4–336 ACSR
IN: 6– INS POLY W/PIN 12KV CLMP #6–4/0 CU
IN: 3– INS POLY DE 4KV RIG #4
IN: 1– INS GLASS DE ROLLER #4 SOL
IN: 1– SEC ROLLER (166–CLEVIS & SPOOL)
IN: 1– AG BLOCK & POLE KEY

(17) RM 382604E
45' Class C4
RM: 1– POLE 45' CLASS 4 WOOD FULL TREAT
RM: 1– XA SNGL FB 10' STEEL PINS
RM: 2– XA SNGL FB 10' STEEL PINS N/BOND
RM: 3– INS POLY W/PIN 16(25)KV CLMP #4–336 ACSR
RM: 6– INS GLASS & PIN 4KV
RM: 2– INS NEUT GLASS & PIN 4KV
RM: 3– INS POLY DE 4KV RIG #4
RM: 1– INS GLASS DE ROLLER #4 SOL
RM: 1– SEC ROLLER (166–CLEVIS & SPOOL)
RM: 1– MISC POLE TOP EXTENSION STEEL W/O ARM

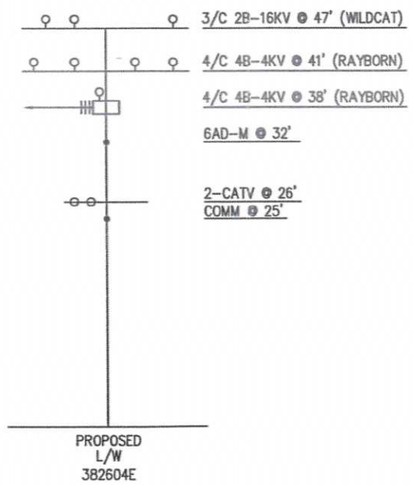

TRANSFER (S):
3/C 2B-16KV
4/C 4B-4KV
4/C 4B-4KV (S)
1-6AD-M (E)
1-2" RISER

EXISTING RISER DETAIL



PROPOSED RISER DETAIL



NOT TO SCALE

PERMIT REQ'D.

CALTRANS:	
ENCROACHMENT:	
RAILROAD:	
HELICOPTER:	
OTHER:	

SPEED LIMIT 25

PEDESTRIAN TRAFFIC CONTROL REQUIRED
[X] YES [ ] NO

GPS: LAT: N 33° 53' 49.6"
LONG: W 118° 11' 40.8"

TLM DATA:

	SIZE	KVA	CUST.	% LOAD
EXIST				
PROP.				

VOLTAGE DROP ____ %
PRI. CIRC. _____

NOTES

JOINT POLE:	Y
RENTER:	Y
MITC FUME:	N
JOINT MEET:	N
TRUCK ACCESS:	Y
HAND SET:	N
CONTACT CATV:	N
ENVIRONMENTAL:	N
REAL PROP. REVIEW:	N
PAVEMENT REPAIR:	N
[ ] CONCRETE / [ ] ASPHALT	____X____

DISTRICT 32 – COMPTON		PROJ. MGR. RODRIGUEZ, JOHN T PHONE 909–469–0219		PLANNER COTA, VANESSA PHONE 714–893–2405	
FOREMAN		TRUCK NO.	P/E	INVENTORY MAP NO. 74–4227–1	THOMAS GUIDE LA 735–C4
GRID NO.	DESIGN NO. 512264_0.01				
CSD 140 Y____ N____	BY–PASS CODE	EXISTING _____ CHANGE TO _____	TLM CHECKED _____ %LOAD	J.P.A. NO. E6032 40597990	ASSOCIATED DESIGN NO.
PRODUCT/SAP NO. TD729491		PRODUCT/SAP NO.		PRODUCT/SAP NO.	

TYPE	APPROVED BY	DATE	CHECKED BY	DRAWN BY	PAX #
				CB	

PROPOSED CONSTRUCTION (LOCATION)
DET POLE REPLACEMENT
VARIOUS LOCATIONS
COMPTON

SHEET ____ OF ____

JOB NO. 512264_0.01

Southern California Edison Company
