1993399E

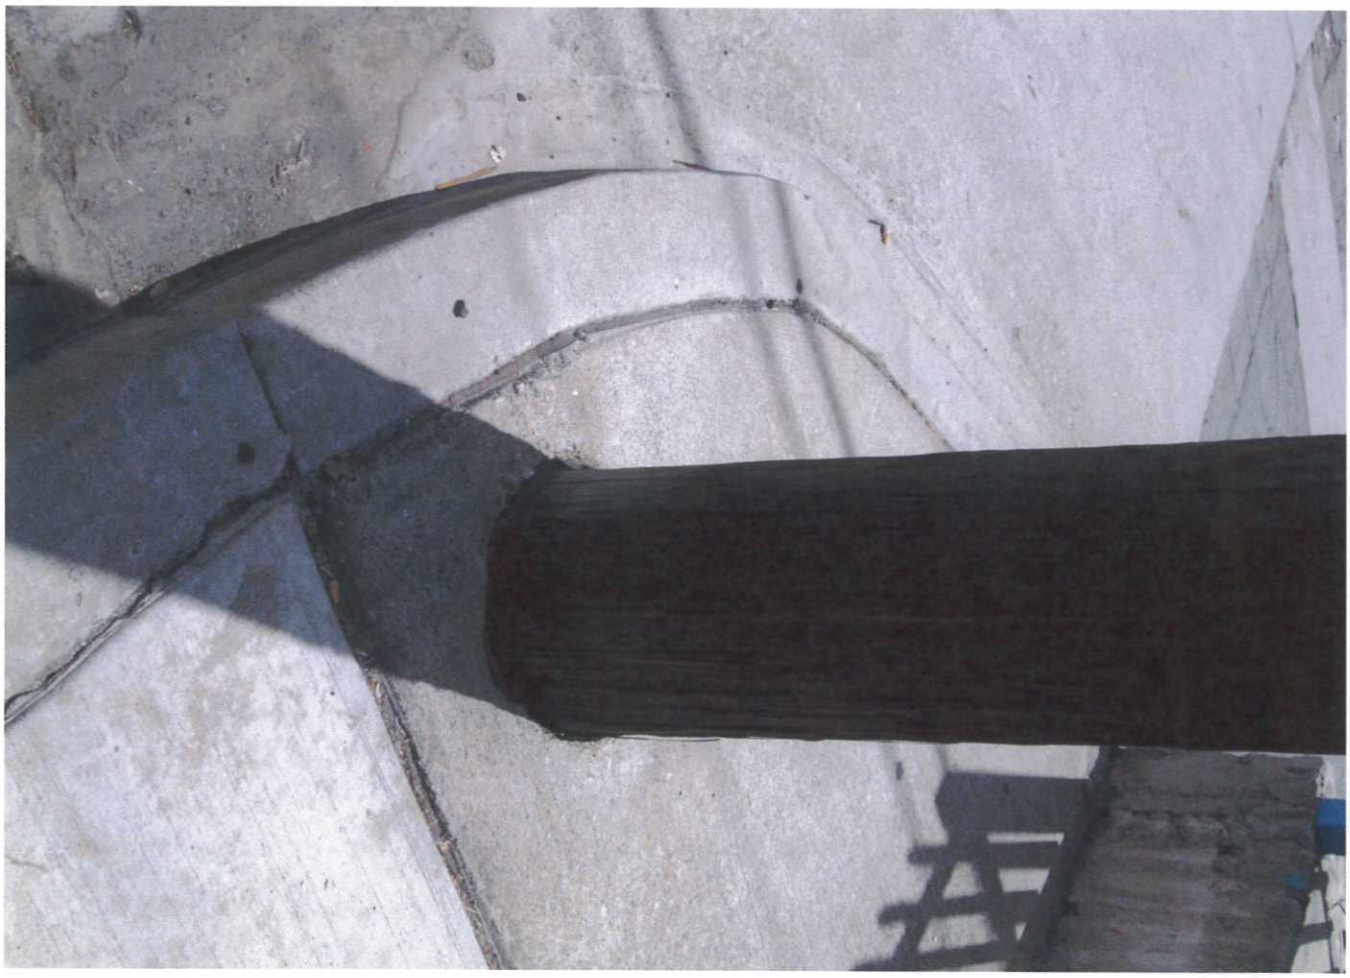

ASPLUNDH CONSTRUCTION CORP.

SOUTHERN CALIFORNIA EDISON
An EDISON INTERNATIONAL Company

DETERIORATED POLE REPLACEMENT

CIRCUIT (S):
TERRADELL 12KV o/o PASSONS SUB

STA'S
5-6

ADDRESS: 8706 NORWALK WHITTIER
LOCATION: WALNUT ST S/S 123' E/O NORWALK
CITY: LOS NIETOS
*** NOTES:** REPLACE 1 O/W SERVICE

5 — RM — 1993399E
45' Class C4
RM: 1– POLE 45' CLASS 4 WOOD FULL TREAT
RM: 62– CD ALL SIZES AL/CU 3/C
RM: 1– XA SNGL FB 10' STEEL PINS
RM: 2– XA SNGL FB 10' STEEL PINS SECONDARY
RM: 2– INS GLASS & PIN 12KV
RM: 3– SEC ROLLER (166–CLEVIS & SPOOL)
RM: 8– SEC STEEL PIN & INS – NEUTRAL
RM: 4– SEC STEEL PIN & INS – PHASE
RM: 1– AG SPAN GUY 9/32" – 200'

SET HARD NORTH WEST
POLE — 1993399E — 6
50' Class H1
IN: 1– POLE 50' CLASS H1 WOOD FULL TREAT
IN: 62– CD #4 STR AL TRIPLEX W/ACSR NEUTRAL
IN: 1– XA SNGL FB 10' STEEL PINS
IN: 2– XA SNGL FB 10' STEEL PINS SECONDARY
IN: 2– INS POLY W/PIN 12KV CLMP #6–4/0 CU
IN: 9– SEC ROLLER (166–CLEVIS & SPOOL)
IN: 8– SEC STEEL PIN & INS – NEUTRAL
IN: 4– SEC STEEL PIN & INS – PHASE
IN: 1– AG SPAN GUY 9/32" – 200'
IN: 1– AG BLOCK & POLE KEY

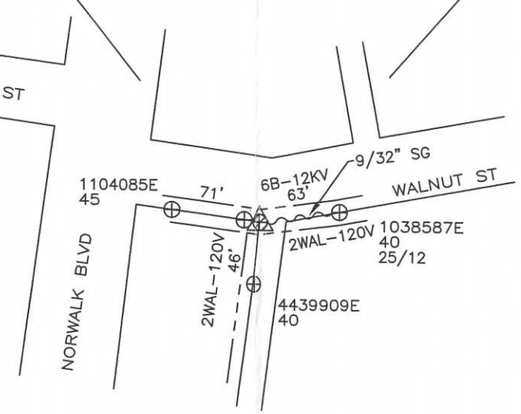

TRANSFER (S):
2/C 6B-12KV
3-2WAL-120V
3-2WAL-120V (NW)
6-2WAL-120V (SE)

NOT TO SCALE

PERMIT REQ'D.	
CALTRANS:	
ENCROACHMENT:	
RAILROAD:	
HELICOPTER:	
OTHER:	

SPEED LIMIT 25

PEDESTRIAN TRAFFIC CONTROL REQUIRED
[X] YES [ ] NO

GPS: LAT: N 33° 57' 43.22"
LONG: W 118° 4' 12.89"

TLM DATA:

	SIZE	KVA	CUST.	% LOAD
EXIST				
PROP.				

VOLTAGE DROP ____ %
PRI. CIRC. ____

NOTES	
JOINT POLE:	Y
RENTER:	N
MITC FUME:	N
JOINT MEET:	N
TRUCK ACCESS:	Y
HAND SET:	N
CONTACT CATV:	N
ENVIRONMENTAL:	N
REAL PROP. REVIEW:	N
PAVEMENT REPAIR:	Y
[X] CONCRETE [ ] ASPHALT	4' X 4'

DISTRICT 47 – WHITTIER		PROJ. MGR. RODRIGUEZ, JOHN T PHONE 909–469–0219		PLANNER HUA, TRINA PHONE 714–893–2405	
FOREMAN		TRUCK NO.	P/E	INVENTORY MAP NO. 098–4266–1	THOMAS GUIDE LA–706–J2
GRID NO.	DESIGN NO. 524081_0.01				
CSD 140 Y ___ N ___	BY–PASS CODE	EXISTING ___ CHANGE TO ___	TLM CHECKED ___ %LOAD	J.P.A. NO. 4400209244	ASSOCIATED DESIGN NO.
PRODUCT/SAP NO. 745354-INFRA REP - DET POLE RELACE		PRODUCT/SAP NO.		PRODUCT/SAP NO.	

TYPE	APPROVED BY	DATE	CHECKED BY	DRAWN BY	PAX #
				TH	

PROPOSED CONSTRUCTION (LOCATION)
DET POLE REPLACEMENT
XSTRT VARIOUS WHITTIER CA 99999
WHITTIER

SHEET ___ OF ___
JOB NO. 524081_0.01

Southern California Edison Company

SANTA FE SPRINGS LOS ANGELES CO. 098-4266-1
