1718

F.B. 1718

DATE	J.N.	DESCRIPTION	NOTES	PAGES
		Cont From F.B. 1709		
11-50	1390	MENDOCINO ST. Raymond Ave. to Santa Rosa Ave.	Topog	5-12
			X-sect	13-28
"	"	MARIPOSA ST. Fair Oaks Ave. to Santa Rosa Ave.	Topog	29-40
			X-sect	41-62
"	"	SCRIPPS LANE Mariposa St. to Foothill Blvd.	Topog	63-66
			X-sect	67-72
"	"	FOOTHILL BLVD.(S.Hwy) Faircoaks Ave. to West Line Lot 58 Tr 13471	Topog	73-76
			X-sect	77-82
"	"	MANOR ST. Fair Oaks Ave. to Mc Nally St.	Topog	83-86
			X-sect	87-92
"	"	Mc NALLY AVE. Manor St. to Terrace St.	Topog	93-94
			X-sect	95-98
"	"	TERRACE ST. Fair Oaks Ave. to Mc Nally Ave.	Topog	99-102
			X-sect	103-108
12-50	"	HARRIET ST. " "	Topog	109-112
			X-sect	113-118
"	"	" Raymond Ave. to Highview Ave.	Topog	119-122
			X-sect	123-128
"	"	EAST LA VENEZIA Fair Oaks Ave. to North La Venezia	Topog	129-132
			X-sect	133-138
"	"	NORTH LA VENEZIA 80' ± S .of East La Venezia to Calav eras	Topog	139-140
			X-sect	141-144
1-51	"	CALAVERAS ST. Fair Oaks Ave. to Raymond Ave. Profile 24' N. of		145-150

Not incorporated in P.W. file
Plotted and Checked 2-51

Notes Checked by
Map No.
Office Work
Checked
Date

Survey of
W.O. Tape No. Std.
Surveyed by
Notes
Indexed Date

F. B. PG.

OVER

INDEX TO F.B. 1718

DATE	J.N.	DESCRIPTION	NOTES	PAGES
10-51	1390	S'erly Line Lots 4to17 inc. Tr. 4523	Topog	151-156
			X-sect	157-160
"	"	ABANDONED R/W Between Calaveras St.& Mendocino St. Marengo Ave. to Raymond Ave.	Topog	161-168
			X-sect	169-176
"	"	CALAVERSA ST.(N.Side)(Curb Line to PL. Fair Oaks Ave. to Raymond Ave.	Topog	177-184
"	"	1st Lot Line S.of Mariposa St. Marengo Ave. to E'erly Line Tr.2147	Topog	185-186
			X-sect	187-188
"	"	PRIVATE PAVED RD. West of Marengo Ave. & North of Mariposa St.	Topog	189-190
"	"	1st Lot Line (out) S.of Foot Hill Blvd. East & West of Private Paved Rd.	Topog	191-194
		Private Paved Rd.& Lot Line East & West	X-sect	195-200
11-51	"	S'erly Lines Lots 70,71,72,73 Tr.6161 Highview Ave. to East	Topog	201-202
			X-sect	203-206
"	"	ABANDONED R/W IN BLK 22 M.R.16-45,46 Marengo Ave. to East	Topog	207-216
			X-sect	217-222
"	"	" " 15 " Santa Anita Ave. to East	Topog	223-226
			X-sect	231-236
"	"	R/W Between Lots 5&6 Blk 15 M.R. 16-45-46 Abandonded R/W to North	Topog	227-230
"	"	EASEMENT IN Blk 23 M.R.16-45-46 Marengo Ave. to East	Topog	237-242
			X-sect	243-246
"	"	EASEMENT IN McNALLY TR. Marengo Ave. to East	Topog	247-252
			X-sect	253-258

F. B. _____ PG. _____

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made and Name of Person Making Change. With Date and Name of Person in Red Ink Circled

Do not extend notes this side of this line.

Notes Ck'd by:	Survey of: Mendocino Ave	F. B. 778 Pg. 5
Map No.	W. O. 1390 Tape No.	St'd. °E
Office Work	Surveyed by: J. J. Lanigan	
Checked	Notes J. L. Date 11-1-50	
Date	Indexed C. C. Johnson	

FEB 20 '51

Location
of
IMPROVEMENTS
on
MENDOCINO ST.
from
RAYMOND AVE.
to
SANTA ROSA AVE.
C. I. 1390

J. J. Lanigan
C. W. Lewis
W. A. Raphael
E. W. Evans

Notes: Any Additions or Changes to This Sheet Must Be Made in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76F3088 847 10M 1-49

F. B. 1718 Pg. 6

cont. bot. pg. 7
(34) & (37)

St.

817

926

no plumbing
in basement

107.9

12.5

8.4

.05

59.8

817

1789.1

230

12" pp - with underground lead

MENDOCINO

230

10" guy pole 0+73.4

beg. of 25' conc. gutter at 0+31.0

21.4

beg. of curb at 1+19.8

31.1

0+27.0

120 S.W.H.H. office

5.3' curb

38.1

0+10.6

0+11.0

19.9

25' conc. gutter

123' conc. gutter

15" C.O.R.R.C.P.P. at E. edge @ curbs

RAYMOND

AVE.

57a 0+00 S.P.K.W.
per F.B. 1707-41

9' approx. cor. at 0+17

0+23.5

RETURN TO
LOS ANGELES COUNTY SURVEYOR
1.728 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes C'k'd by
Map No.
Office Work
Checked
Date

Survey of Highland Ave
W.O. 390 Tape No. Std. °F
Surveyed by J. J. Lonergan
Notes J. J. L. Date 11-19-51
Indexed C. Johnson

F. B. 1776 Pg. 7

Notes: Any Additions or Changes of This Sheet Must be Made by Check in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

7-52 OSB 247 10M 1-48

Highland Ave
Sta 3795.12
Sta 4+00
Sta 4+22.0
Sta 4+35.8
Sta 4+77.8
Sta 5+00.3
Sta 5+35.5
Sta 5+79.5
Sta 6+21.3
Sta 6+35.8
Sta 6+91.8
Sta 7+09.8
Sta 3+71.4
Sta 3+81.1
Sta 3+92.1
Sta 3+32.7
Sta 3+56.0
Sta 3+75.6
Sta 3+99.4
Sta 4+32.2
Sta 4+41.4
Sta 4+47.8
Sta 4+70.8
Sta 4+80.9
Sta 4+88.2
Sta 5+00.3
Sta 5+17.9
Sta 5+53.5
Sta 5+79.5
Sta 6+21.3
Sta 6+35.8
Sta 6+91.8
Sta 7+09.8
Sta 7+22.0
Sta 7+35.8
Sta 7+46.6
Sta 7+56.0
Sta 7+75.6
Sta 7+99.4
Sta 8+32.2
Sta 8+41.4
Sta 8+47.8
Sta 8+70.8
Sta 8+80.9
Sta 8+88.2
Sta 9+00.3
Sta 9+17.9
Sta 9+53.5
Sta 9+79.5
Sta 10+21.3
Sta 10+35.8
Sta 10+91.8
Sta 11+09.8
Sta 11+22.0
Sta 11+35.8
Sta 11+46.6
Sta 11+56.0
Sta 11+75.6
Sta 11+99.4
Sta 12+32.2
Sta 12+41.4
Sta 12+47.8
Sta 12+70.8
Sta 12+80.9
Sta 12+88.2
Sta 13+00.3
Sta 13+17.9
Sta 13+53.5
Sta 13+79.5
Sta 14+21.3
Sta 14+35.8
Sta 14+91.8
Sta 15+09.8
Sta 15+22.0
Sta 15+35.8
Sta 15+46.6
Sta 15+56.0
Sta 15+75.6
Sta 15+99.4
Sta 16+32.2
Sta 16+41.4
Sta 16+47.8
Sta 16+70.8
Sta 16+80.9
Sta 16+88.2
Sta 17+00.3
Sta 17+17.9
Sta 17+53.5
Sta 17+79.5
Sta 18+21.3
Sta 18+35.8
Sta 18+91.8
Sta 19+09.8
Sta 19+22.0
Sta 19+35.8
Sta 19+46.6
Sta 19+56.0
Sta 19+75.6
Sta 19+99.4
Sta 20+32.2
Sta 20+41.4
Sta 20+47.8
Sta 20+70.8
Sta 20+80.9
Sta 20+88.2
Sta 21+00.3
Sta 21+17.9
Sta 21+53.5
Sta 21+79.5
Sta 22+21.3
Sta 22+35.8
Sta 22+91.8
Sta 23+09.8
Sta 23+22.0
Sta 23+35.8
Sta 23+46.6
Sta 23+56.0
Sta 23+75.6
Sta 23+99.4
Sta 24+32.2
Sta 24+41.4
Sta 24+47.8
Sta 24+70.8
Sta 24+80.9
Sta 24+88.2
Sta 25+00.3
Sta 25+17.9
Sta 25+53.5
Sta 25+79.5
Sta 26+21.3
Sta 26+35.8
Sta 26+91.8
Sta 27+09.8
Sta 27+22.0
Sta 27+35.8
Sta 27+46.6
Sta 27+56.0
Sta 27+75.6
Sta 27+99.4
Sta 28+32.2
Sta 28+41.4
Sta 28+47.8
Sta 28+70.8
Sta 28+80.9
Sta 28+88.2
Sta 29+00.3
Sta 29+17.9
Sta 29+53.5
Sta 29+79.5
Sta 30+21.3
Sta 30+35.8
Sta 30+91.8
Sta 31+09.8
Sta 31+22.0
Sta 31+35.8
Sta 31+46.6
Sta 31+56.0
Sta 31+75.6
Sta 31+99.4
Sta 32+32.2
Sta 32+41.4
Sta 32+47.8
Sta 32+70.8
Sta 32+80.9
Sta 32+88.2
Sta 33+00.3
Sta 33+17.9
Sta 33+53.5
Sta 33+79.5
Sta 34+21.3
Sta 34+35.8
Sta 34+91.8
Sta 35+09.8
Sta 35+22.0
Sta 35+35.8
Sta 35+46.6
Sta 35+56.0
Sta 35+75.6
Sta 35+99.4
Sta 36+32.2
Sta 36+41.4
Sta 36+47.8
Sta 36+70.8
Sta 36+80.9
Sta 36+88.2
Sta 37+00.3
Sta 37+17.9
Sta 37+53.5
Sta 37+79.5
Sta 38+21.3
Sta 38+35.8
Sta 38+91.8
Sta 39+09.8
Sta 39+22.0
Sta 39+35.8
Sta 39+46.6
Sta 39+56.0
Sta 39+75.6
Sta 39+99.4
Sta 40+32.2
Sta 40+41.4
Sta 40+47.8
Sta 40+70.8
Sta 40+80.9
Sta 40+88.2
Sta 41+00.3
Sta 41+17.9
Sta 41+53.5
Sta 41+79.5
Sta 42+21.3
Sta 42+35.8
Sta 42+91.8
Sta 43+09.8
Sta 43+22.0
Sta 43+35.8
Sta 43+46.6
Sta 43+56.0
Sta 43+75.6
Sta 43+99.4
Sta 44+32.2
Sta 44+41.4
Sta 44+47.8
Sta 44+70.8
Sta 44+80.9
Sta 44+88.2
Sta 45+00.3
Sta 45+17.9
Sta 45+53.5
Sta 45+79.5
Sta 46+21.3
Sta 46+35.8
Sta 46+91.8
Sta 47+09.8
Sta 47+22.0
Sta 47+35.8
Sta 47+46.6
Sta 47+56.0
Sta 47+75.6
Sta 47+99.4
Sta 48+32.2
Sta 48+41.4
Sta 48+47.8
Sta 48+70.8
Sta 48+80.9
Sta 48+88.2
Sta 49+00.3
Sta 49+17.9
Sta 49+53.5
Sta 49+79.5
Sta 50+21.3
Sta 50+35.8
Sta 50+91.8
Sta 51+09.8
Sta 51+22.0
Sta 51+35.8
Sta 51+46.6
Sta 51+56.0
Sta 51+75.6
Sta 51+99.4
Sta 52+32.2
Sta 52+41.4
Sta 52+47.8
Sta 52+70.8
Sta 52+80.9
Sta 52+88.2
Sta 53+00.3
Sta 53+17.9
Sta 53+53.5
Sta 53+79.5
Sta 54+21.3
Sta 54+35.8
Sta 54+91.8
Sta 55+09.8
Sta 55+22.0
Sta 55+35.8
Sta 55+46.6
Sta 55+56.0
Sta 55+75.6
Sta 55+99.4
Sta 56+32.2
Sta 56+41.4
Sta 56+47.8
Sta 56+70.8
Sta 56+80.9
Sta 56+88.2
Sta 57+00.3
Sta 57+17.9
Sta 57+53.5
Sta 57+79.5
Sta 58+21.3
Sta 58+35.8
Sta 58+91.8
Sta 59+09.8
Sta 59+22.0
Sta 59+35.8
Sta 59+46.6
Sta 59+56.0
Sta 59+75.6
Sta 59+99.4
Sta 60+32.2
Sta 60+41.4
Sta 60+47.8
Sta 60+70.8
Sta 60+80.9
Sta 60+88.2
Sta 61+00.3
Sta 61+17.9
Sta 61+53.5
Sta 61+79.5
Sta 62+21.3
Sta 62+35.8
Sta 62+91.8
Sta 63+09.8
Sta 63+22.0
Sta 63+35.8
Sta 63+46.6
Sta 63+56.0
Sta 63+75.6
Sta 63+99.4
Sta 64+32.2
Sta 64+41.4
Sta 64+47.8
Sta 64+70.8
Sta 64+80.9
Sta 64+88.2
Sta 65+00.3
Sta 65+17.9
Sta 65+53.5
Sta 65+79.5
Sta 66+21.3
Sta 66+35.8
Sta 66+91.8
Sta 67+09.8
Sta 67+22.0
Sta 67+35.8
Sta 67+46.6
Sta 67+56.0
Sta 67+75.6
Sta 67+99.4
Sta 68+32.2
Sta 68+41.4
Sta 68+47.8
Sta 68+70.8
Sta 68+80.9
Sta 68+88.2
Sta 69+00.3
Sta 69+17.9
Sta 69+53.5
Sta 69+79.5
Sta 70+21.3
Sta 70+35.8
Sta 70+91.8
Sta 71+09.8
Sta 71+22.0
Sta 71+35.8
Sta 71+46.6
Sta 71+56.0
Sta 71+75.6
Sta 71+99.4
Sta 72+32.2
Sta 72+41.4
Sta 72+47.8
Sta 72+70.8
Sta 72+80.9
Sta 72+88.2
Sta 73+00.3
Sta 73+17.9
Sta 73+53.5
Sta 73+79.5
Sta 74+21.3
Sta 74+35.8
Sta 74+91.8
Sta 75+09.8
Sta 75+22.0
Sta 75+35.8
Sta 75+46.6
Sta 75+56.0
Sta 75+75.6
Sta 75+99.4
Sta 76+32.2
Sta 76+41.4
Sta 76+47.8
Sta 76+70.8
Sta 76+80.9
Sta 76+88.2
Sta 77+00.3
Sta 77+17.9
Sta 77+53.5
Sta 77+79.5
Sta 78+21.3
Sta 78+35.8
Sta 78+91.8
Sta 79+09.8
Sta 79+22.0
Sta 79+35.8
Sta 79+46.6
Sta 79+56.0
Sta 79+75.6
Sta 79+99.4
Sta 80+32.2
Sta 80+41.4
Sta 80+47.8
Sta 80+70.8
Sta 80+80.9
Sta 80+88.2
Sta 81+00.3
Sta 81+17.9
Sta 81+53.5
Sta 81+79.5
Sta 82+21.3
Sta 82+35.8
Sta 82+91.8
Sta 83+09.8
Sta 83+22.0
Sta 83+35.8
Sta 83+46.6
Sta 83+56.0
Sta 83+75.6
Sta 83+99.4
Sta 84+32.2
Sta 84+41.4
Sta 84+47.8
Sta 84+70.8
Sta 84+80.9
Sta 84+88.2
Sta 85+00.3
Sta 85+17.9
Sta 85+53.5
Sta 85+79.5
Sta 86+21.3
Sta 86+35.8
Sta 86+91.8
Sta 87+09.8
Sta 87+22.0
Sta 87+35.8
Sta 87+46.6
Sta 87+56.0
Sta 87+75.6
Sta 87+99.4
Sta 88+32.2
Sta 88+41.4
Sta 88+47.8
Sta 88+70.8
Sta 88+80.9
Sta 88+88.2
Sta 89+00.3
Sta 89+17.9
Sta 89+53.5
Sta 89+79.5
Sta 90+21.3
Sta 90+35.8
Sta 90+91.8
Sta 91+09.8
Sta 91+22.0
Sta 91+35.8
Sta 91+46.6
Sta 91+56.0
Sta 91+75.6
Sta 91+99.4
Sta 92+32.2
Sta 92+41.4
Sta 92+47.8
Sta 92+70.8
Sta 92+80.9
Sta 92+88.2
Sta 93+00.3
Sta 93+17.9
Sta 93+53.5
Sta 93+79.5
Sta 94+21.3
Sta 94+35.8
Sta 94+91.8
Sta 95+09.8
Sta 95+22.0
Sta 95+35.8
Sta 95+46.6
Sta 95+56.0
Sta 95+75.6
Sta 95+99.4
Sta 96+32.2
Sta 96+41.4
Sta 96+47.8
Sta 96+70.8
Sta 96+80.9
Sta 96+88.2
Sta 97+00.3
Sta 97+17.9
Sta 97+53.5
Sta 97+79.5
Sta 98+21.3
Sta 98+35.8
Sta 98+91.8
Sta 99+09.8
Sta 99+22.0
Sta 99+35.8
Sta 99+46.6
Sta 99+56.0
Sta 99+75.6
Sta 99+99.4
Sta 100+32.2
Sta 100+41.4
Sta 100+47.8
Sta 100+70.8
Sta 100+80.9
Sta 100+88.2
Sta 101+00.3
Sta 101+17.9
Sta 101+53.5
Sta 101+79.5
Sta 102+21.3
Sta 102+35.8
Sta 102+91.8
Sta 103+09.8
Sta 103+22.0
Sta 103+35.8
Sta 103+46.6
Sta 103+56.0
Sta 103+75.6
Sta 103+99.4
Sta 104+32.2
Sta 104+41.4
Sta 104+47.8
Sta 104+70.8
Sta 104+80.9
Sta 104+88.2
Sta 105+00.3
Sta 105+17.9
Sta 105+53.5
Sta 105+79.5
Sta 106+21.3
Sta 106+35.8
Sta 106+91.8
Sta 107+09.8
Sta 107+22.0
Sta 107+35.8
Sta 107+46.6
Sta 107+56.0
Sta 107+75.6
Sta 107+99.4
Sta 108+32.2
Sta 108+41.4
Sta 108+47.8
Sta 108+70.8
Sta 108+80.9
Sta 108+88.2
Sta 109+00.3
Sta 109+17.9
Sta 109+53.5
Sta 109+79.5
Sta 110+21.3
Sta 110+35.8
Sta 110+91.8
Sta 111+09.8
Sta 111+22.0
Sta 111+35.8
Sta 111+46.6
Sta 111+56.0
Sta 111+75.6
Sta 111+99.4
Sta 112+32.2
Sta 112+41.4
Sta 112+47.8
Sta 112+70.8
Sta 112+80.9
Sta 112+88.2
Sta 113+00.3
Sta 113+17.9
Sta 113+53.5
Sta 113+79.5
Sta 114+21.3
Sta 114+35.8
Sta 114+91.8
Sta 115+09.8
Sta 115+22.0
Sta 115+35.8
Sta 115+46.6
Sta 115+56.0
Sta 115+75.6
Sta 115+99.4
Sta 116+32.2
Sta 116+41.4
Sta 116+47.8
Sta 116+70.8
Sta 116+80.9
Sta 116+88.2
Sta 117+00.3
Sta 117+17.9
Sta 117+53.5
Sta 117+79.5
Sta 118+21.3
Sta 118+35.8
Sta 118+91.8
Sta 119+09.8
Sta 119+22.0
Sta 119+35.8
Sta 119+46.6
Sta 119+56.0
Sta 119+75.6
Sta 119+99.4
Sta 120+32.2
Sta 120+41.4
Sta 120+47.8
Sta 120+70.8
Sta 120+80.9
Sta 120+88.2
Sta 121+00.3
Sta 121+17.9
Sta 121+53.5
Sta 121+79.5
Sta 122+21.3
Sta 122+35.8
Sta 122+91.8
Sta 123+09.8
Sta 123+22.0
Sta 123+35.8
Sta 123+46.6
Sta 123+56.0
Sta 123+75.6
Sta 123+99.4
Sta 124+32.2
Sta 124+41.4
Sta 124+47.8
Sta 124+70.8
Sta 124+80.9
Sta 124+88.2
Sta 125+00.3
Sta 125+17.9
Sta 125+53.5
Sta 125+79.5
Sta 126+21.3
Sta 126+35.8
Sta 126+91.8
Sta 127+09.8
Sta 127+22.0
Sta 127+35.8
Sta 127+46.6
Sta 127+56.0
Sta 127+75.6
Sta 127+99.4
Sta 128+32.2
Sta 128+41.4
Sta 128+47.8
Sta 128+70.8
Sta 128+80.9
Sta 128+88.2
Sta 129+00.3
Sta 129+17.9
Sta 129+53.5
Sta 129+79.5
Sta 130+21.3
Sta 130+35.8
Sta 130+91.8
Sta 131+09.8
Sta 131+22.0
Sta 131+35.8
Sta 131+46.6
Sta 131+56.0
Sta 131+75.6
Sta 131+99.4
Sta 132+32.2
Sta 132+41.4
Sta 132+47.8
Sta 132+70.8
Sta 132+80.9
Sta 132+88.2
Sta 133+00.3
Sta 133+17.9
Sta 133+53.5
Sta 133+79.5
Sta 134+21.3
Sta 134+35.8
Sta 134+91.8
Sta 135+09.8
Sta 135+22.0
Sta 135+35.8
Sta 135+46.6
Sta 135+56.0
Sta 135+75.6
Sta 135+99.4
Sta 136+32.2
Sta 136+41.4
Sta 136+47.8
Sta 136+70.8
Sta 136+80.9
Sta 136+88.2
Sta 137+00.3
Sta 137+17.9
Sta 137+53.5
Sta 137+79.5
Sta 138+21.3
Sta 138+35.8
Sta 138+91.8
Sta 139+09.8
Sta 139+22.0
Sta 139+35.8
Sta 139+46.6
Sta 139+56.0
Sta 139+75.6
Sta 139+99.4
Sta 140+32.2
Sta 140+41.4
Sta 140+47.8
Sta 140+70.8
Sta 140+80.9
Sta 140+88.2
Sta 141+00.3
Sta 141+17.9
Sta 141+53.5
Sta 141+79.5
Sta 142+21.3
Sta 142+35.8
Sta 142+91.8
Sta 143+09.8
Sta 143+22.0
Sta 143+35.8
Sta 143+46.6
Sta 143+56.0
Sta 143+75.6
Sta 143+99.4
Sta 144+32.2
Sta 144+41.4
Sta 144+47.8
Sta 144+70.8
Sta 144+80.9
Sta 144+88.2
Sta 145+00.3
Sta 145+17.9
Sta 145+53.5
Sta 145+79.5
Sta 146+21.3
Sta 146+35.8
Sta 146+91.8
Sta 147+09.8
Sta 147+22.0
Sta 147+35.8
Sta 147+46.6
Sta 147+56.0
Sta 147+75.6
Sta 147+99.4
Sta 148+32.2
Sta 148+41.4
Sta 148+47.8
Sta 148+70.8
Sta 148+80.9
Sta 148+88.2
Sta 149+00.3
Sta 149+17.9
Sta 149+53.5
Sta 149+79.5
Sta 150+21.3
Sta 150+35.8
Sta 150+91.8
Sta 151+09.8
Sta 151+22.0
Sta 151+35.8
Sta 151+46.6
Sta 151+56.0
Sta 151+75.6
Sta 151+99.4
Sta 152+32.2
Sta 152+41.4
Sta 152+47.8
Sta 152+70.8
Sta 152+80.9
Sta 152+88.2
Sta 153+00.3
Sta 153+17.9
Sta 153+53.5
Sta 153+79.5
Sta 154+21.3
Sta 154+35.8
Sta 154+91.8
Sta 155+09.8
Sta 155+22.0
Sta 155+35.8
Sta 155+46.6
Sta 155+56.0
Sta 155+75.6
Sta 155+99.4
Sta 156+32.2
Sta 156+41.4
Sta 156+47.8
Sta 156+70.8
Sta 156+80.9
Sta 156+88.2
Sta 157+00.3
Sta 157+17.9
Sta 157+53.5
Sta 157+79.5
Sta 158+21.3
Sta 158+35.8
Sta 158+91.8
Sta 159+09.8
Sta 159+22.0
Sta 159+35.8
Sta 159+46.6
Sta 159+56.0
Sta 159+75.6
Sta 159+99.4
Sta 160+32.2
Sta 160+41.4
Sta 160+47.8
Sta 160+70.8
Sta 160+80.9
Sta 160+88.2
Sta 161+00.3
Sta 161+17.9
Sta 161+53.5
Sta 161+79.5
Sta 162+21.3
Sta 162+35.8
Sta 162+91.8
Sta 163+09.8
Sta 163+22.0
Sta 163+35.8
Sta 163+46.6
Sta 163+56.0
Sta 163+75.6
Sta 163+99.4
Sta 164+32.2
Sta 164+41.4
Sta 164+47.8
Sta 164+70.8
Sta 164+80.9
Sta 164+88.2
Sta 165+00.3
Sta 165+17.9
Sta 165+53.5
Sta 165+79.5
Sta 166+21.3
Sta 166+35.8
Sta 166+91.8
Sta 167+09.8
Sta 167+22.0
Sta 167+35.8
Sta 167+46.6
Sta 167+56.0
Sta 167+75.6
Sta 167+99.4
Sta 168+32.2
Sta 168+41.4
Sta 168+47.8
Sta 168+70.8
Sta 168+80.9
Sta 168+88.2
Sta 169+00.3
Sta 169+17.9
Sta 169+53.5
Sta 169+79.5
Sta 170+21.3
Sta 170+35.8
Sta 170+91.8
Sta 171+09.8
Sta 171+22.0
Sta 171+35.8
Sta 171+46.6
Sta 171+56.0
Sta 171+75.6
Sta 171+99.4
Sta 172+32.2
Sta 172+41.4
Sta 172+47.8
Sta 172+70.8
Sta 172+80.9
Sta 172+88.2
Sta 173+00.3
Sta 173+17.9
Sta 173+53.5
Sta 173+79.5
Sta 174+21.3
Sta 174+35.8
Sta 174+91.8
Sta 175+09.8
Sta 175+22.0
Sta 175+35.8
Sta 175+46.6
Sta 175+56.0
Sta 175+75.6
Sta 175+99.4
Sta 176+32.2
Sta 176+41.4
Sta 176+47.8
Sta 176+70.8
Sta 176+80.9
Sta 176+88.2
Sta 177+00.3
Sta 177+17.9
Sta 177+53.5
Sta 177+79.5
Sta 178+21.3
Sta 178+35.8
Sta 178+91.8
Sta 179+09.8
Sta 179+22.0
Sta 179+35.8
Sta 179+46.6
Sta 179+56.0
Sta 179+75.6
Sta 179+99.4
Sta 180+32.2
Sta 180+41.4
Sta 180+47.8
Sta 180+70.8
Sta 180+80.9
Sta 180+88.2
Sta 181+00.3
Sta 181+17.9
Sta 181+53.5
Sta 181+79.5
Sta 182+21.3
Sta 182+35.8
Sta 182+91.8
Sta 183+09.8
Sta 183+22.0
Sta 183+35.8
Sta 183+46.6
Sta 183+56.0
Sta 183+75.6
Sta 183+99.4
Sta 184+32.2
Sta 184+41.4
Sta 184+47.8
Sta 184+70.8
Sta 184+80.9
Sta 184+88.2
Sta 185+00.3
Sta 185+17.9
Sta 185+53.5
Sta 185+79.5
Sta 186+21.3
Sta 186+35.8
Sta 186+91.8
Sta 187+09.8
Sta 187+22.0
Sta 187+35.8
Sta 187+46.6
Sta 187+56.0
Sta 187+75.6
Sta 187+99.4
Sta 188+32.2
Sta 188+41.4
Sta 188+47.8
Sta 188+70.8
Sta 188+80.9
Sta 188+88.2
Sta 189+00.3
Sta 189+17.9
Sta 189+53.5
Sta 189+79.5
Sta 190+21.3
Sta 190+35.8
Sta 190+91.8
Sta 191+09.8
Sta 191+22.0
Sta 191+35.8
Sta 191+46.6
Sta 191+56.0
Sta 191+75.6
Sta 191+99.4
Sta 192+32.2
Sta 192+41.4
Sta 192+47.8
Sta 192+70.8
Sta 192+80.9
Sta 192+88.2
Sta 193+00.3
Sta 193+17.9
Sta 193+53.5
Sta 193+79.5
Sta 194+21.3
Sta 194+35.8
Sta 194+91.8
Sta 195+09.8
Sta 195+22.0
Sta 195+35.8
Sta 195+46.6
Sta 195+56.0
Sta 195+75.6
Sta 195+99.4
Sta 196+32.2
Sta 196+41.4
Sta 196+47.8
Sta 196+70.8
Sta 196+80.9
Sta 196+88.2
Sta 197+00.3
Sta 197+17.9
Sta 197+53.5
Sta 197+79.5
Sta 198+21.3
Sta 198+35.8
Sta 198+91.8
Sta 199+09.8
Sta 199+22.0
Sta 199+35.8
Sta 199+46.6
Sta 199+56.0
Sta 199+75.6
Sta 199+99.4
Sta 200+32.2
Sta 200+41.4
Sta 200+47.8
Sta 200+70.8
Sta 200+80.9
Sta 200+88.2
Sta 201+00.3
Sta 201+17.9
Sta 201+53.5
Sta 201+79.5
Sta 202+21.3
Sta 202+35.8
Sta 202+91.8
Sta 203+09.8
Sta 203+22.0
Sta 203+35.8
Sta 203+46.6
Sta 203+56.0
Sta 203+75.6
Sta 203+99.4
Sta 204+32.2
Sta 204+41.4
Sta 204+47.8
Sta 204+70.8
Sta 204+80.9
Sta 204+88.2
Sta 205+00.3
Sta 205+17.9
Sta 205+53.5
Sta 205+79.5
Sta 206+21.3
Sta 206+35.8
Sta 206+91.8
Sta 207+09.8
Sta 207+22.0
Sta 207+35.8
Sta 207+46.6
Sta 207+56.0
Sta 207+75.6
Sta 207+99.4
Sta 208+32.2
Sta 208+41.4
Sta 208+47.8
Sta 208+70.8
Sta 208+80.9
Sta 208+88.2
Sta 209+00.3
Sta 209+17.9
Sta 209+53.5
Sta 209+79.5
Sta 210+21.3
Sta 210+35.8
Sta 210+91.8
Sta 211+09.8
Sta 211+22.0
Sta 211+35.8
Sta 211+46.6
Sta 211+56.0
Sta 211+75.6
Sta 211+99.4
Sta 212+32.2
Sta 212+41.4
Sta 212+47.8
Sta 212+70.8
Sta 212+80.9
Sta 212+88.2
Sta 213+00.3
Sta 213+17.9
Sta 213+53.5
Sta 213+79.5
Sta 214+21.3
Sta 214+35.8
Sta 214+91.8
Sta 215+09.8
Sta 215+22.0
Sta 215+35.8
Sta 215+46.6
Sta 215+56.0
Sta 215+75.6
Sta 215+99.4
Sta 216+32.2
Sta 216+41.4
Sta 216+47.8
Sta 216+70.8
Sta 216+80.9
Sta 216+88.2
Sta 217+00.3
Sta 217+17.9
Sta 217+53.5
Sta 217+79.5
Sta 218+21.3
Sta 218+35.8
Sta 218+91.8
Sta 219+09.8
Sta 219+22.0
Sta 219+35.8
Sta 219+46.6
Sta 219+56.0
Sta 219+75.6
Sta 219+99.4
Sta 220+32.2
Sta 220+41.4
Sta 220+47.8
Sta 220+70.8
Sta 220+80.9
Sta 220+88.2
Sta 221+00.3
Sta 221+17.9
Sta 221+53.5
Sta 221+79.5
Sta 222+21.3
Sta 222+35.8
Sta 222+91.8
Sta 223+09.8
Sta 223+22.0
Sta 223+35.8
Sta 223+46.6
Sta 223+56.0
Sta 223+75.6
Sta 223+99.4
Sta 224+32.2
Sta 224+41.4
Sta 224+47.8
Sta 224+70.8
Sta 224+80.9
Sta 224+88.2
Sta 225+00.3
Sta 225+17.9
Sta 225+53.5
Sta 225+79.5
Sta 226+21.3
Sta 226+35.8
Sta 226+91.8
Sta 227+09.8
Sta 227+22.0
Sta 227+35.8
Sta 227+46.6
Sta 227+56.0
Sta 227+75.6
Sta 227+99.4
Sta 228+32.2
Sta 228+41.4
Sta 228+47.8
Sta 228+70.8
Sta 228+80.9
Sta 228+88.2
Sta 229+00.3
Sta 229+17.9
Sta 229+53.5
Sta 229+79.5
Sta 230+21.3
Sta 230+35.8
Sta 230+91.8
Sta 231+09.8
Sta 231+22.0
Sta 231+35.8
Sta 231+46.6
Sta 231+56.0
Sta 231+75.6
Sta 231+99.4
Sta 232+32.2
Sta 232+41.4
Sta 232+47.8
Sta 232+70.8
Sta 232+80.9
Sta 232+88.2
Sta 233+00.3
Sta 233+17.9
Sta 233+53.5
Sta 233+79.5
Sta 234+21.3
Sta 234+35.8
Sta 234+91.8
Sta 235+09.8
Sta 235+22.0
Sta 235+35.8
Sta 235+46.6
Sta 235+56.0
Sta 235+75.6
Sta 235+99.4
Sta 236+32.2
Sta 236+41.4
Sta 236+47.8
Sta 236+70.8
Sta 236+80.9
Sta 236+88.2
Sta 237+00.3
Sta 237+17.9
Sta 237+53.5
Sta 237+79.5
Sta 238+21.3
Sta 238+35.8
Sta 238+91.8
Sta 239+09.8
Sta 239+22.0
Sta 239+35.8
Sta 239+46.6
Sta 239+56.0
Sta 239+75.6
Sta 239+99.4
Sta 240+32.2
Sta 240+41.4
Sta 240+47.8
Sta 240+70.8
Sta 240+80.9
Sta 240+88.2
Sta 241+00.3
Sta 241+17.9
Sta 241+53.5
Sta 241+79.5
Sta 242+21.3
Sta 242+35.8
Sta 242+91.8
Sta 243+09.8
Sta 243+22.0
Sta 243+35.8
Sta 243+46.6
Sta 243+56.0
Sta 243+75.6
Sta 243+99.4
Sta 244+32.2
Sta 244+41.4
Sta 244+47.8
Sta 244+70.8
Sta 244+80.9
Sta 244+88.2
Sta 245+00.3
Sta 245+17.9
Sta 245+53.5
Sta 245+79.5
Sta 246+21.3
Sta 246+35.8
Sta 246+91.8
Sta 247+09.8
Sta 247+22.0
Sta 247+35.8
Sta 247+46.6
Sta 247+56.0
Sta 247+75.6
Sta 247+99.4
Sta 248+32.2
Sta 248+41.4
Sta 248+47.8
Sta 248+70.8
Sta 248+80.9
Sta 248+88.2
Sta 249+00.3
Sta 249+17.9
Sta 249+53.5
Sta 249+79.5
Sta 250+21.3
Sta 250+35.8
Sta 250+91.8
Sta 251+09.8
Sta 251+22.0
Sta 251+35.8
Sta 251+46.6
Sta 251+56.0
Sta 251+75.6
Sta 251+99.4
Sta 252+32.2
Sta 252+41.4
Sta 252+47.8
Sta 252+70.8
Sta 252+80.9
Sta 252+88.2
Sta 253+00.3
Sta 253+17.9
Sta 253+53.5
Sta 253+79.5
Sta 254+21.3
Sta 254+35.8
Sta 254+91.8
Sta 255+09.8
Sta 255+22.0
Sta 255+35.8
Sta 255+46.6
Sta 255+56.0
Sta 255+75.6
Sta 255+99.4
Sta 256+32.2
Sta 256+41.4
Sta 256+47.8
Sta 256+70.8
Sta 256+80.9
Sta 256+88.2
Sta 257+00.3
Sta 257+17.9
Sta 257+53.5
Sta 257+79.5
Sta 258+21.3
Sta 258+35.8
Sta 258+91.8
Sta 259+09.8
Sta 259+22.0
Sta 259+35.8
Sta 259+46.6
Sta 259+56.0
Sta 259+75.6
Sta 259+99.4
Sta 260+32.2
Sta 260+41.4
Sta 260+47.8
Sta 260+70.8
Sta 260+80.9
Sta 260+88.2
Sta 261+00.3
Sta 261+17.9
Sta 261+53.5
Sta 261+79.5
Sta 262+21.3
Sta 262+35.8
Sta 262+91.8
Sta 263+09.8
Sta 263+22.0
Sta 263+35.8
Sta 263+46.6
Sta 263+56.0
Sta 263+75.6
Sta 263+99.4
Sta 264+32.2
Sta 264+41.4
Sta 264+47.8
Sta 264+70.8
Sta 264+80.9
Sta 264+88.2
Sta 265+00.3
Sta 265+17.9
Sta 265+53.5
Sta 265+79.5
Sta 266+21.3
Sta 266+35.8
Sta 266+91.8
Sta 267+09.8
Sta 267+22.0
Sta 267+35.8
Sta 267+46.6
Sta 267+56.0
Sta 267+75.6
Sta 267+99.4
Sta 268+32.2
Sta 268+41.4
Sta 268+47.8
Sta 268+70.8
Sta 268+80.9
Sta 268+88.2
Sta 269+00.3
Sta 269+17.9
Sta 269+53.5
Sta 269+79.5
Sta 270+21.3
Sta 270+35.8
Sta 270+91.8
Sta 271+09.8
Sta 271+22.0
Sta 271+35.8
Sta 271+46.6
Sta 271+56.0
Sta 271+75.6
Sta 271+99.4
Sta 272+32.2
Sta 272+41.4
Sta 272+47.8
Sta 272+70.8
Sta 272+80.9
Sta 272+88.2
Sta 273+00.3
Sta 273+17.9
Sta 273+53.5
Sta 273+79.5
Sta 274+21.3
Sta 274+35.8
Sta 274+91.8
Sta 275+09.8
Sta 275+22.0
Sta 275+35.8
Sta 275+46.6
Sta 275+56.0
Sta 275+75.6
Sta 275+99.4
Sta 276+32.2
Sta 276+41.4
Sta 276+47.8
Sta 276+70.8
Sta 276+80.9
Sta 276+88.2
Sta 277+00.3
Sta 277+17.9
Sta 277+53.5
Sta 277+79.5
Sta 278+21.3
Sta 278+35.8
Sta 278+91.8
Sta 279+09.8
Sta 279+22.0
Sta 279+35.8
Sta 279+46.6
Sta 279+56.0
Sta 279+75.6
Sta 279+99.4
Sta 280+32.2
Sta 280+41.4
Sta 280+47.8
Sta 280+70.8
Sta 280+80.9
Sta 280+88.2
Sta 281+00.3
Sta 281+17.9
Sta 281+53.5
Sta 281+79.5
Sta 282+21.3
Sta 282+35.8
Sta 282+91.8
Sta 283+09.8
Sta 283+22.0
Sta 283+35.8
Sta 283+46.6
Sta 283+56.0
Sta 283+75.6
Sta 283+99.4
Sta 284+32.2
Sta 284+41.4
Sta 284+47.8
Sta 284+70.8
Sta 284+80.9
Sta 284+88.2
Sta 285+00.3
Sta 285+17.9
Sta 285+53.5
Sta 285+79.5
Sta 286+21.3
Sta 286+35.8
Sta 286+91.8
Sta 287+09.8
Sta 287+22.0
Sta 287+35.8
Sta 287+46.6
Sta 287+56.0
Sta 287+75.6
Sta 287+99.4
Sta 288+32.2
Sta 288+41.4
Sta 288+47.8
Sta 288+70.8
Sta 288+80.9
Sta 288+88.2
Sta 289+00.3
Sta 289+17.9
Sta 289+53.5
Sta 289+79.5
Sta 290+21.3
Sta 290+35.8
Sta 290+91.8
Sta 291+09.8
Sta 291+22.0
Sta 291+35.8
Sta 291+46.6
Sta 291+56.0
Sta 291+75.6
Sta 291+99.4
Sta 292+32.2
Sta 292+41.4
Sta 292+47.8
Sta 292+70.8
Sta 292+80.9
Sta 292+88.2
Sta 293+00.3
Sta 293+17.9
Sta 293+53.5
Sta 293+79.5
Sta 294+21.3
Sta 294+35.8
Sta 294+91.8
Sta 295+09.8
Sta 295+22.0
Sta 295+35.8
Sta 295+46.6
Sta 295+56.0
Sta 295+75.6
Sta 295+99.4
Sta 296+32.2
Sta 296+41.4
Sta 296+47.8
Sta 296+70.8
Sta 296+80.9
Sta 296+88.2
Sta 297+00.3
Sta 297+17.9
Sta 297+53.5
Sta 297+79.5
Sta 298+21.3
Sta 298+35.8
Sta 298+91.8
Sta 299+09.8
Sta 299+22.0
Sta 299+35.8
Sta 299+46.6
Sta 299+56.0
Sta 299+75.6
Sta 299+99.4
Sta 300+32.2
Sta 300+41.4
Sta 300+47.8
Sta 300+70.8
Sta 300+80.9
Sta 300+88.2
Sta 301+00.3
Sta 301+17.9
Sta 301+53.5
Sta 301+79.5
Sta 302+21.3
Sta 302+35.8
Sta 302+91.8
Sta 303+09.8
Sta 303+22.0
Sta 303+35.8
Sta 303+46.6
Sta 303+56.0
Sta 303+75.6
Sta 303+99.4
Sta 304+32.2
Sta 304+41.4
Sta 304+47.8
Sta 304+70.8
Sta 304+80.9
Sta 304+88.2
Sta 305+00.3
Sta 305+17.9
Sta 305+53.5
Sta 305+79.5
Sta 306+21.3
Sta 306+35.8
Sta 306+91.8
Sta 307+09.8
Sta 307+22.0
Sta 307+35.8
Sta 307+46.6
Sta 307+56.0
Sta 307+75.6
Sta 307+99.4
Sta 308+32.2
Sta 308+41.4
Sta 308+47.8
Sta 308+70.8
Sta 308+80.9
Sta 308+88.2
Sta 309+00.3
Sta 309+17.9
Sta 309+53.5
Sta 309+79.5
Sta 310+21.3
Sta 310+35.8
Sta 310+91.8
Sta 311+09.8
Sta 311+22.0
Sta 311+35.8
Sta 311+46.6
Sta 311+56.0
Sta 311+75.6
Sta 311+99.4
Sta 312+32.2
Sta 312+41.4
Sta 312+47.8
Sta 312+70.8
Sta 312+80.9
Sta 312+88.2
Sta 313+00.3
Sta 313+17.9
Sta 313+53.5
Sta 313+79.5
Sta 314+21.3
Sta 314+35.8
Sta 314+91.8
Sta 315+09.8
S

F. B. 1718 Pg. 8

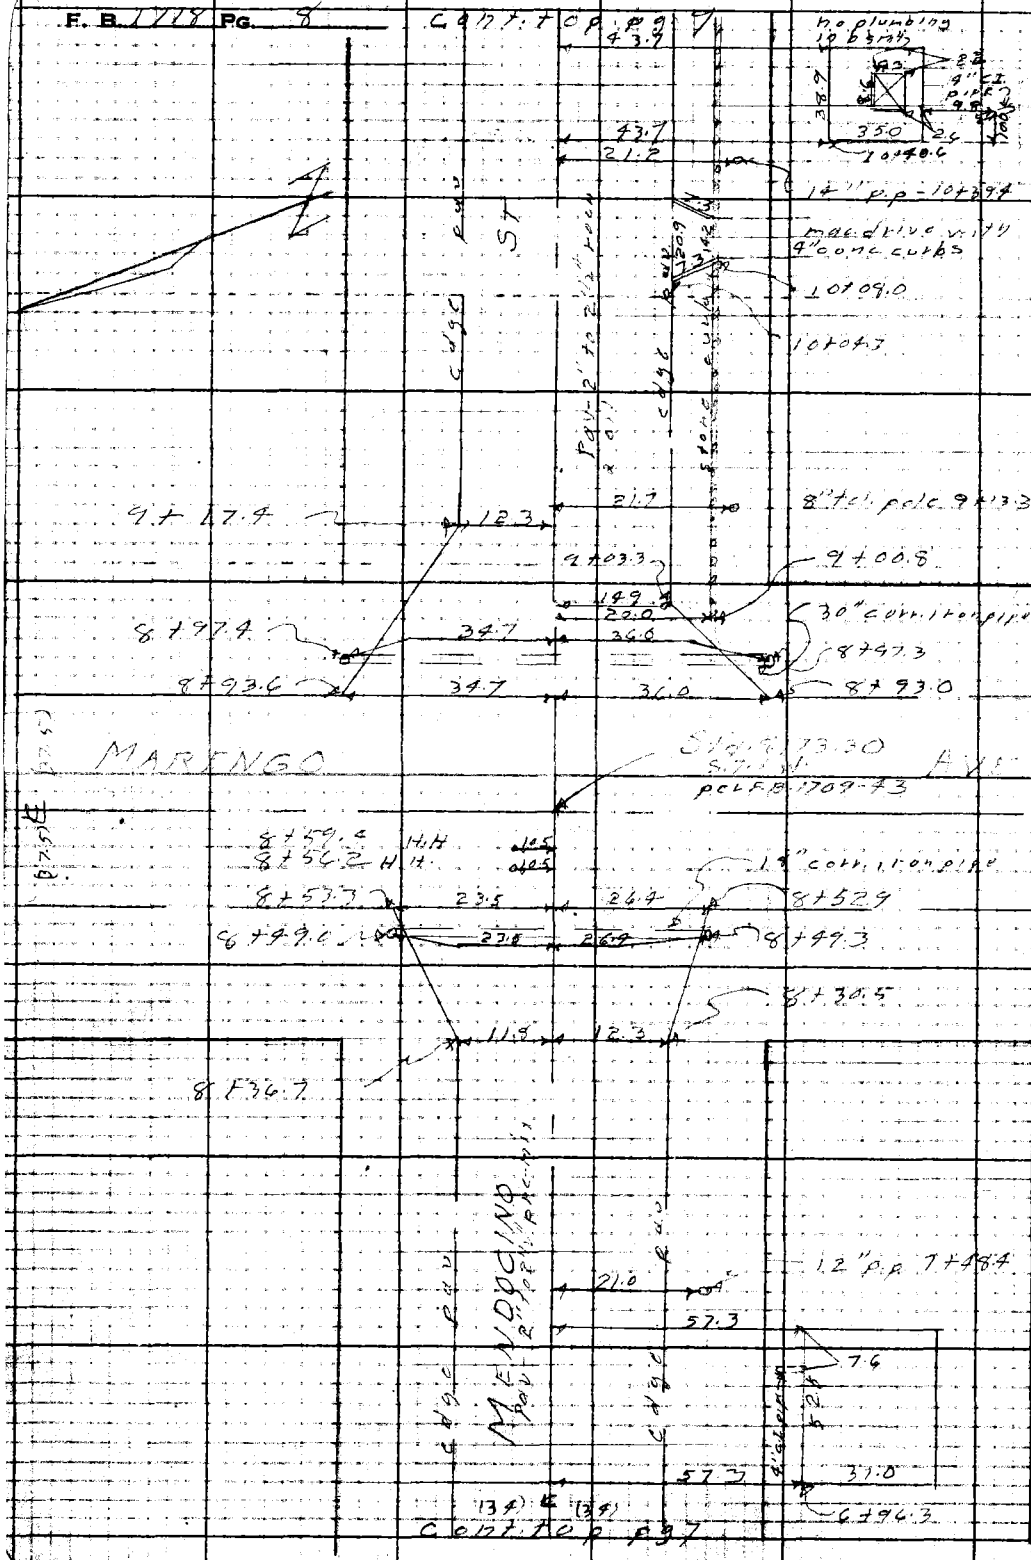

7.3
(2.1)
(1.4)

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Checked in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by	Survey of Mar. 1939 Av.
Map No.	W. O. 1707 Tape No. St'd. °F
Office Work	Surveyed by W. V. Lapiqas
Checked	Notes J. C. Date 11-14-39
Date	Indexed E. C. Johnson

F. B. 1778 Pg. 9

Notes: Any Additions or Changes of This Sheet Must be Made or Checked in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

7873085 247 10M 1-49

MENDOCINO ST.

Sta. 14+10.3

15+81.8

102.3

53.8

R0.6

78.3

21.1

19.5

32.8

19.3

16.7

18.0

15.0

15.1

14.1

21.6

12+92.0

12+79.2

12+73.4

12+72.8

12+69.0

12+49.2

12+37.9

Cont. top pg 8

(37)

(38)

306

105

5.0

11.0

14.2

26.8

42.0

43.0

garage apart

37.8

14+89.3

7.6

4" V.C. pipe

(1.0)

12" p.p. 13+87.8

26.4

9" C.I. pipe

6.8

6.6

6.6 below flow

13+38.6

18" p.p. 13+38.6

5.5

Inac. drive with conc. curbs

13+06.6

12+93.3

12+72.6

12+70.2

12+69.0

Note - This Artemis plan catches to stone curb at this length at curb - but is wacky around corner E. of ditch

12" 11+30.7

Inac. drive with 9" conc. curbs

19+37.9

12" p.p. 12+32.2

15+87.5

Toilet in

15+89.5

Continue left on plan newly laid with top cover (0.5)

92.3

172.42

Artemis pav. ends

Sta. 12+92.2

Sta. 12+72.6

Sta. 12+70.2

Sta. 12+69.0

18" corrug. pipe 12+19.10" acad.

1' head wall

Sta. 12+49.2

Sta. 12+37.9

Sta. 12+32.2

Sta. 11+30.7

Sta. 13+06.6

Sta. 13+38.6

Sta. 15+87.5

Sta. 15+89.5

Sta. 19+37.9

Sta. 14+89.3

Sta. 15+81.8

Sta. 14+10.3

Sta. 12+92.0

Sta. 12+79.2

Sta. 12+73.4

Sta. 12+72.8

F. B. 1718 Pg. 10

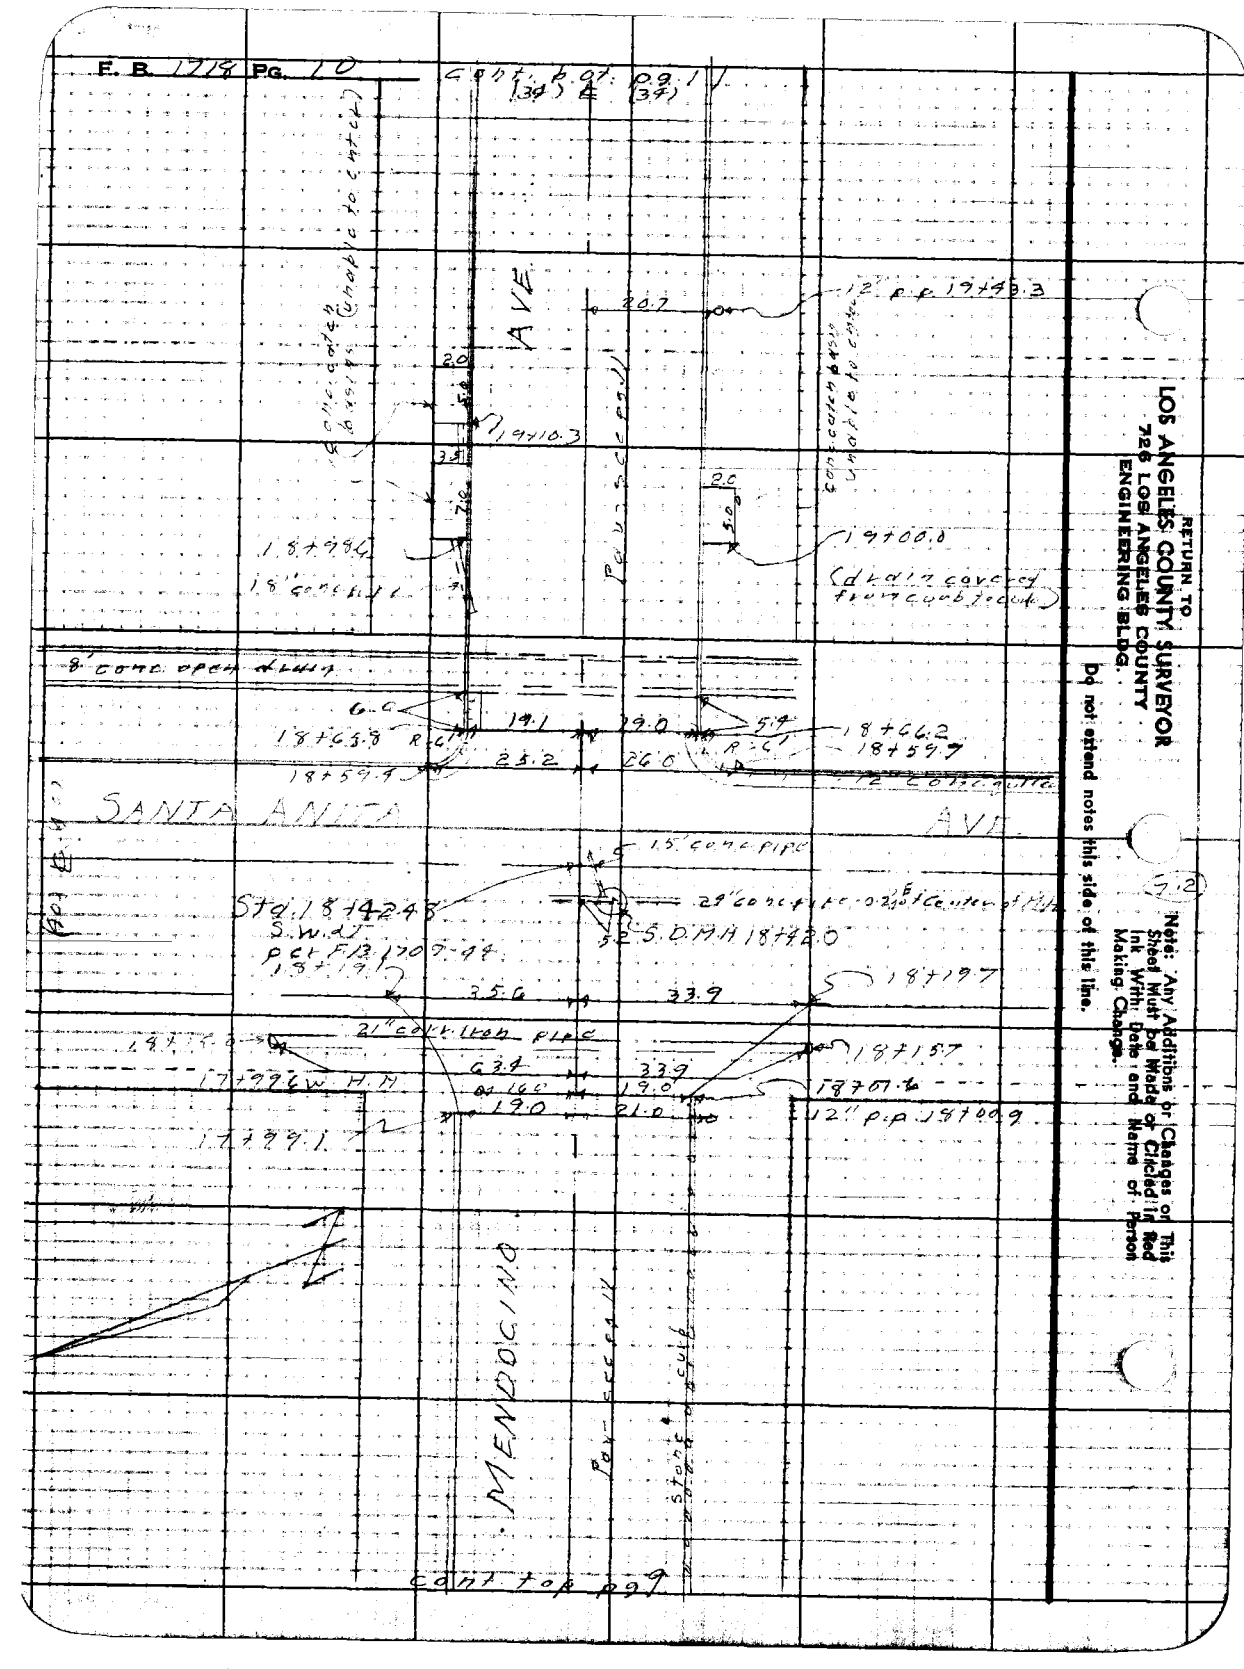

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Marengo Ave
W. O. 2390 Tape No. SF'd °F.
Surveyed by J. J. Longyear
Notes J. J. L. Date 7/12-30
Indexed A. C. Johnson

F. B. 1118 Pg. 11

Notes: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
720 LOS ANGELES COUNTY
ENGINEERING BLDG.

7ER3095 247 10M 1-48

MENDOCINO

Pavt from E 70 ft to 2 ft N of ℄ Mendocino

77.0
58.5
Edge right
12" W.P.
12" W.P. 22+81.6
77.0
20.5
12" R.C.P.
21+27.4
19.4
25.3
R=6'
21+18.6
21+12.4
Mac. dri-ine
20+85.3
22.7
18.7
R=9'
20+81.4
106.0
1060
22+81.0
24.7.6
House
20.4.
24.7.6
21.3
39.3
39.6
21+20.6
20+70.0
Swimming pool
81.0
45.7
Basement under entire house has 7 skylights & 5 windows

COST. Top. p. 18

F. B. 1774 Pg. 12

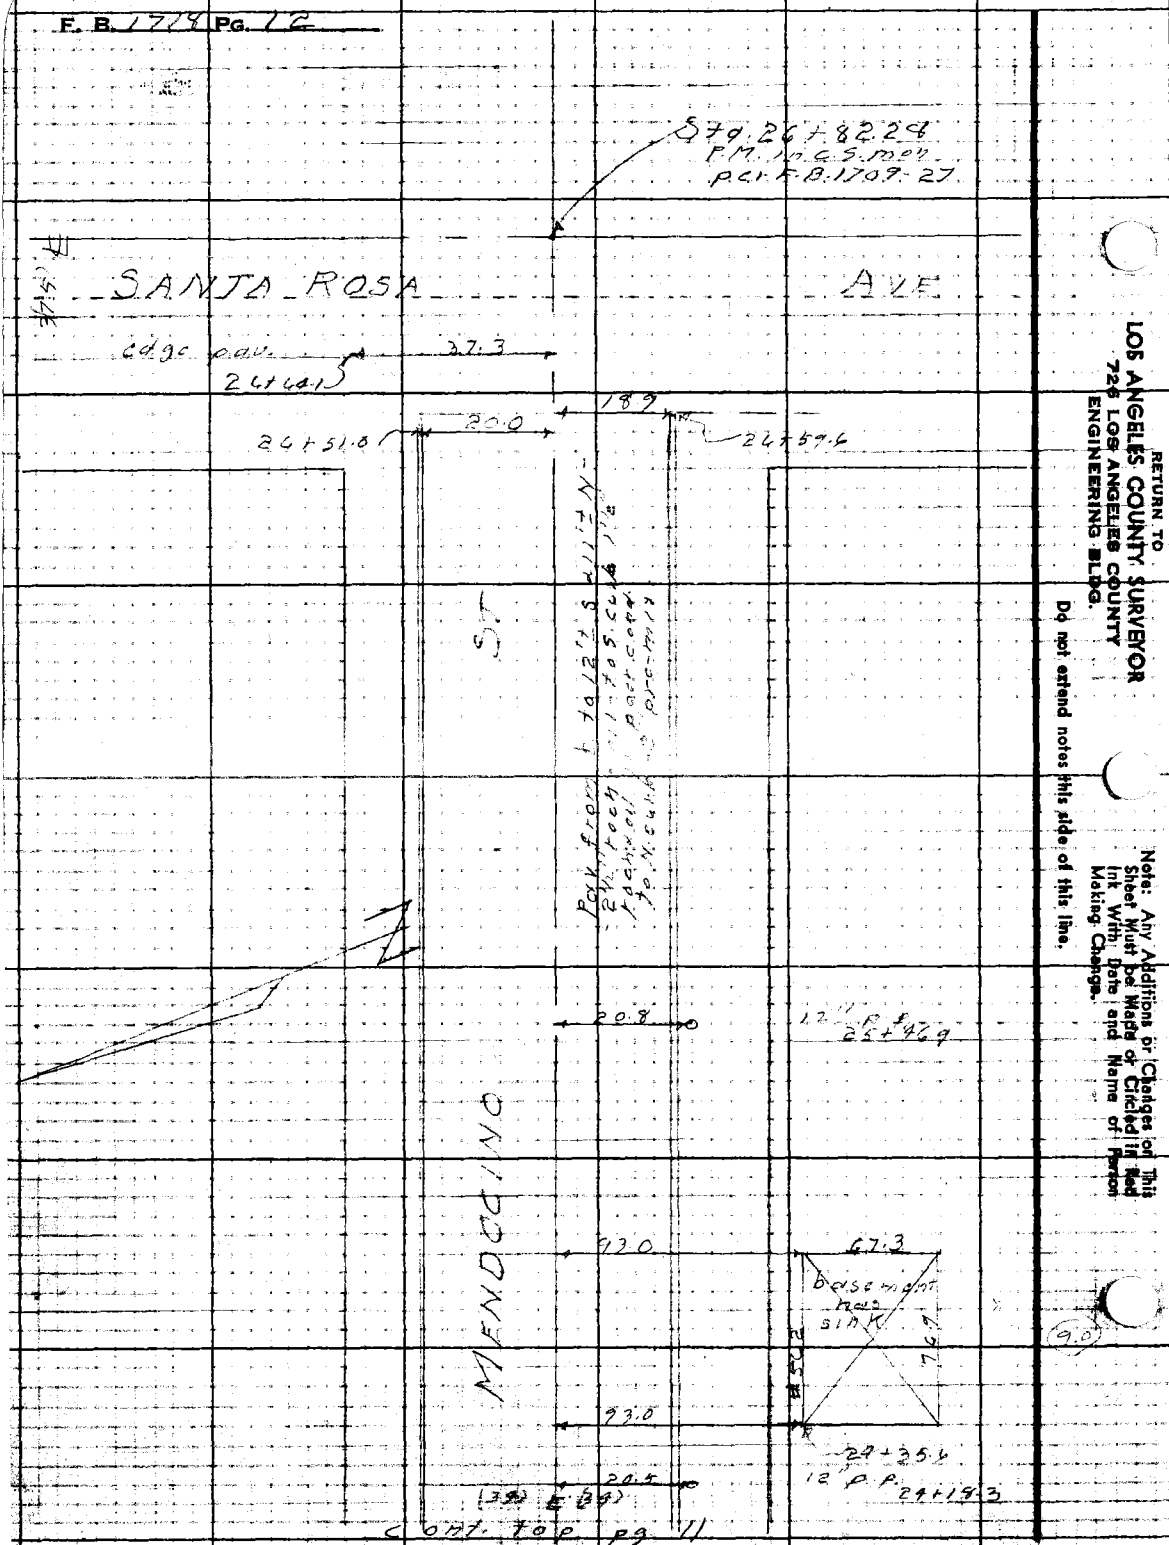

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Changes.

Profile Notes Red. Plotted Job No. 1390 Division No. V F.B. 1778 Pg. 13

Date Date

X-Sec. Notes Chkd. LCM Checked Survey by J.V. Lanigan Notes by C.H. Lewis Date 1-28-50

Date Date

PROFILE

and

CROSS-SECTIONS

of

MENDOCINO STREET

from

RAYMOND AVENUE

to

SANTA ROSA AVENUE

C.I. 1390

J.V. Lanigan
C.H. Lewis
H.H. Raphael
E.W. Evans

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

76L298 307 5-49

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ X-Sec. No. ____

Plotted ____ Date ____ Checked ____ Date ____

Notes Red. ____ Date ____ Notes Chkd. ____ Date ____

Job No. 390 Division No. V

Survey of Manchester Ave.

Survey by Lee Gen. Notes Lewis

Indexed L. C. Johnson Date ____

STATION	B. S.	H. I.	F. S.	ELEV.		
BMAE476	2.79	1254.62		1251.83	BM AE 476 Elev. 1251.829	FB 1568-111
					Raymond Ave. & Manchester Blvd. NE Cor	
					Bt spk in curb 12' N of S. end	
0+00			4.80	1250.82		
			10.20	1244.42	℄ of Raymond Ave 100' S'ly of Manchester Blvd	
			10.90	1243.72	E. gut " " " " "	
			10.12	1244.49	E cb " " " " "	
			0.32	1254.30	℄ " " 75' N'ly "	
			0.96	1253.66	E gut " " " " "	
			6.04	1254.58	E cL " " " " "	
			4.00	1250.62	gut N.E. cor. of cb 5.	
			3.42	1251.20	cb. " " " " 4	
0+10.6			8.55	1245.07		38' R gut
"			7.64	1245.98		" cL
			5.7	1248.9	S.E ppty cor.	
			1.0	1253.6	NE ppty cor	
0+51			3.84	1250.78		21' R gut
"			2.98	1251.64		" cb
1+00			6.35	1254.27	℄	
"			1.51	1253.11		21' R gut
"			0.70	1253.92		" cL

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. Notes Red Plotted Job No. 5310 Division No.
X-Sec. No. Notes Date Date Survey of Mattison Avenue F.B. 718 PG. 13
Notes Chkd. Checked Survey by Lewis Date 11-15-50
Date Date Map No. Notes Date

STATION	B. S.	H. I.	F. S.	ELEV.	Mendocino Street
1+00		1254 62	0 46	1254 16	20' L gut
"			⊕ 0 24	1254 86	" cb
T. P.	7 47	1261 73	0 36	1254 26	
1+89.1			5 2	1256 76	81'R Floor to Hse # 204 E Mendocino
2+51			13 3	1248 4	118'R basement " " "
1+89.1			8 8	1257 8	124'R. ground elev. S.W. cor Hse
2+10			4 68	1257 05	℄
"			5 81	1255 94	21' R gut
"			5 17	1256 58	" cb.
"			4 94	1256 79	20' L gut
"			4 29	1257 44	" cb.
3+80			3 30	1258 43	℄
"			4 69	1257 04	21' R gut
"			4 03	1257 70	" cb
"			3 90	1257 83	20' L gut
"			3 27	1258 46	" cb
TP DM AE 482	5 50	1264 03	3 20	1258 53	T.P. BM 482 Elev. 1258.520
3+95.12			4 88	1259 15	℄ Int. Mendocino & Vissalia Pl.
			5 40	1258 63	gut W and NW cb Int
			4 78	1259 25	cb " " " "
			4 92	1259 11	gut N " " " "

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 PG. 16 | Job No. 1390 Division No. V | Notes Red. | Plotted | Profile No.
Survey of Montebello Avenue | Date | Date | X-Sec. No.
Survey by Lewis | Notes | Notes Chkd. | Checked
Indexed E. C. Johnson | Date | Date | Date

STATION	B. S.	H. I.	F. S.	ELEV.		
		1264 03	4 29	1259 74	cb N end NW cb 1-ft	
			4 2	1259 8	NW ppty cor	
			226	1261 77	E Visscher 60' N'ly of Mendocino	
			320	1261 83	E gut " " "	"
			257	1261 46	E cb " " "	"
			293	1261 10	W gut " " "	"
			228	1261 75	" " " " "	"
			484	1259 19	gut N end NE cb 1-ft	
			425	1259 78	cb " " " " "	
			535	1258 68	gut E " " " "	
			476	1259 27	cb " " " " "	
			2 6	1261 4	NE ppty cor	
4+00			486	1259 17		
"			617	1257 86		21' R gut
"			552	1258 51		cb
4+24			15 5	1248 5	124' R - ct+ basement to H-S-E # 234 E. Mendocino	
"			10 4	1253 6	136' R ground at SE cor " " "	
4+52			17 5	1246 5	232' R Floor elev garage apt. " "	
"			22 5	1241 5	270' R ground at SE cor " " " "	
5+00			508	1253 95		
			621	1257 82		21' R

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ Notes Red. ____ Plotted ____ Job No. 1223 Division No. ____ F.B. 1378 PG. 17
X-Sec. No. ____ Notes Chkd. ____ Checked ____ Survey by Lewis Notes Lewis Date 11-15-50
Date ____ Date ____ Date ____ Map No. ____ Checked by: ____ Date ____

Survey of Alameda Avenue

STATION	B. S.	H. I.	F. S.	ELEV.	Mendocino	Street
5+00		126403	553	125850		21'R. cb
"			572	125831	20'L gut	
			507	125896	" " cb	
T.P.	4 42	1263 38	507	125896	T.P.	
5+09.3			23 5	1239 9	218'R bot. of swimm pool	
5+36			6 0	1257 4	91.5'R Floor elev. Hse #256 E. Mendocino	
"			14 2	1249 2	106'R basement elev. " "	"
5+53.5			10 8	1252 6	138'R ground at S.E. cor "	"
6+00			483	1258 55		℄
"			578	1257 60		21'R gut
"			518	1258 20		" cb
"			552	1257 86	20'L gut	
"			488	1258 50	" cb	
6+04			7 0	1256 4	84'R Floor elev. Hse #266 E. Mendocino	
"			11 1	1252 3	128'R ground S.W. cor " "	"
6+21.3			548	1257 90	20'L gut at cb. end	
"			492	1258 46	" cb at end	
6+85.2			646	1256 92		21'R gut at cb.
"			582	1257 56		" cb " "
7+00			533	1258 05		℄
"			575	1257 63		12'R edge of pavmt

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 Pg. 18 | Job No. 1390 Division No. V | Profile No. | Notes Red. | Plotted | Date | X-Sec. No. | Notes Chkd. | Checked | Date

Survey of Matenga Avenue.

Survey by Lanigan Notes Lewis

Indexed A. C. Johnson Date

STATION	B. S.	H. I.	F. S.	ELEV.	Mendocino	Street
7+00		1263 38	69	1256 5		20' R. gut
"			6 4	1259 0		23' " brk
"			7 1	1255 3		34' R P.L
"			5 38	1262 00	12'L edge pvmt	
"			5 6	1258 8	20'L gut	
"			3 5	1261 2	34'L P.L.	
7+41			11 4	1252 0	57'R. 4" V.C.P. outlet of Hse # 280 E Mendo.	
T.P.	2 93	1260 99	5 32	1255 06	T.P.	
8+00			4 42	1255 57		
"			4 90	1256 09		12' R edge pvmt.
"			6 2	1254 8		19' R ditch
"			5 4	1255 6		21' R S. bank
"			6 3	1254 7		34' R P.L
"			4 33	1256 66	12'L edge pvmt	
"			4 5	1256 5	18'L ditch	
"			3 5	1257 5	34'L P.L	
8+49			8 8	1254 2	27'R. Flo line 18" cast iron pipe outlet	
"			6 0	1256 3	24'L " " "	" " inlet
			3 2	1257 8	NW ppty cor.	
			7 1	1254 9	SW. " "	
8+73 30			5 22	1256 77	℄ int. Mendocino &	Matenga

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. Date
X-Sec. No. Date
Notes Chkd. Date
Checked Date
Notes Red. Date
Plotted Date
Job No. 2[illegible] Division No. V
Survey of Malonga Avenue
Survey by Eastlake Notes Lewis Date 11-15-55
Map No. Checked Date
F.B. 1[illegible] PG. 19

STATION	B. S.	H. I.	F. S.	ELEV.	Mendocino Street.
		126099	11 17	124982	℄ Malonga 100' S'l'y of Mendocino
			0 01	126098	" " 85' N'l'y " "
8+97			6 3/5	1254 7	35' L Floline 30" conc. iron pipe inlet
"			11 0	12500	36' R " " " " " " outlet
			8 1	1252 9	S.E. ppty cor
			3 5	1257 5	NE " "
10+00			690	125409	℄
"			7 46	125353	11' R edge curb
"			9 2	1251 8	20' R Gutter
"			8 5	1252 5	20' R. Top of wall
"			9 5	1251 5	34' R. P. L.
"			6 67	125432	11' L edge pavmt.
"		✓	4 8	1256 2	34' L P.L.
T. P.	331	1257.41	689	125410	T. P.
10+50			8 5	12489	44' R Floor elev. Hse # 338
10+50			12 1	12453	89' R 4" C.I. pipe at rear
10+71			15 8	12416	71' R basement Hse # 338
11+10			394	125347	℄
"			4 71	125270	11' R. edge pavmt
"			6 4/5	1251 0	21' R. gut
"			5 5	1251 9	22' R wall

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 Pg. 20 | Job No. 1390 Division No. K | Notes Red. | Plotted | No.
Survey of Mahaiwe Avenue | Date | Date | X-Sec.
Survey by Lavigne | Notes Keuls | Notes Chkd. | Checked | No.
Indexed E. C. Johnson | Date | Date | Date

STATION	B. S.	H. I.	F. S.	ELEV.	Mendocino	Street
11+00		1257 41	6 6	1250 8		34' R. P.L
"			3 98	1253 43	11' L edge of pvmt.	
"			2 1	1255 3	34 L. P.L	
12+00			4 32	1253 09		℄
"			4 85	1252 56		11 R edge pvmt
"			6 6	1250 8		21' R. gut
"			5 6	1251 8		" wall
"			7 4	1250 0		34' R P.L.
"			4 29	1253 12	11' L edge pvmt.	
"			2 12	1255 2	34' L P.L.	
T.P.	5 11	1257 42	5 10	1252 31	bt spk in bvmt	
12+73			8 3	1249 1		15' R. Flowline 18" culvert
			6 5	1250 9	15' L Flowline 18" culvert.	inlet
13+00			4 58	1252 84		℄
13+06			5 02	1252 40		15' R bvmt
"			6 40	1251 02		21' R gut
"			5 6	1251 8		" wall
"			7 2	1250 4		34' P/
"			4 60	1252 82	13' L edge of pvmt	
"			5 0	1252 4	14' L bvmt	
"			3 2	1254 1	34' L P.L	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ Notes Red. ____ Plotted ____ Job No. ____ Division No. ____
X-Sec. No. ____ Date ____ Date ____ Survey of Mattenson Avenue
Notes Chkd. ____ Checked ____ Survey by Lewis Notes Lewis Date 11-17-50
Date ____ Date ____ Map No. ____ Indexed Date ____

F.B. 171 PG. 21

STATION	B. S.	H. I.	F. S.	ELEV.	Mendocino Street
14+00		1257 42	4 36	1253 06	℄
"			4 96	1252 46	15'R brk
"			6 33	1251 09	21'R gut
"			5 5	1251 9	21'R [illegible]
"			6 8	1250 6	34'R P.L.
"			4 35	1253 07	13'L. edge pvmt
"			4 6	1252 8	16'L brk
"			3 0	1254 4	34'L P.L.
14+43			15 5	1241 9	Elev. of 4" C.I. pipe 105'R. at rear of Hse # 396
"			14 3	12431	" basement floor Hse # 396 95'R
14+97			12 4	12450	" 4" V.C. pipe 97'Rt rear of garage, apt
15+00			3 95	125347	℄
"			5 00	1252 42	15'R brk
"			5 95	1251 47	21'R gut
"			5 4	12520	" top wall
"			6 2	1251 2	34'R P.L.
"			4 11	1253 31	13'L edge pvmt.
"			4 2	12532	13'L brk
"			2 9	1254 5	34'L P.L.
T.P.	4 99	1258 47	3 94	1253 48	T.P.
15+77			17 2	1241 3	136'R ℄ tr basement # Hse # 416

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ X-Sec. No. ____
Plotted ____ Date ____ Checked ____ Date ____
Notes Red. ____ Date ____ Notes Chkd. ____ Date ____
Job No. 1390 Division No. V
Survey of Alameda Avenue
Survey by Los Angeles
Notes Levels
Indexed C. Johnson Date
F.B. 1715 Pg. 22

STATION	B. S.	H. I.	F. S.	ELEV.	Menadocino	Street
15+87.5		1258.47	14.9	1243.6	145' Rt. ground at SW cor. hse.	
15+97			15.8	1242.7	196' " Floor elev. garage opt.	
"			17.7	1240.8	214 " ground at SW cor. garage opt.	
16+10			4.46	1254.01		℄
"			5.42	1253.05		15' R. b-k
"			6.82	1251.65		21' " gut
"			6.3	1252.2		" " top curb
"			6.8	1251.7		34' " P.L.
"			5.15	1253.32	19'L gut at beginning	
"			4.51	1253.96	" cb " "	
"			3.0	1255.47	34'L P.L.	
T.P.	8.27	1263.07	3.67	1254.80	T.P.	
16+90			8.45	125-.62		℄
"			9.34	1253.73		15' R. b-k
"			10.24	1252.39		21' R gut
"			10.9	1253.1		" top wall
"			10.3	1252.8		34' R P.L.
"			8.70	1254.37	19'L gut	
"			8.10	1254.97	" cb	
17+99			6.24	1257.83		℄
			7.24	1255.81		15' R b-k

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red No. Date Plotted Job No. 1326 Division No. V
X-Sec. Notes Chkd. No. Date Checked Survey of Manchenco Avenue
Survey by Lantz & Lewis Notes Lewis Date 11-17-50
Map No. Indexed Johnson Date F.B. 1778 PG. 23

STATION	B. S.	H. I.	F. S.	ELEV.	Mendocino	Street
17+99		1263.07	8 4	1254 7		20' R gut
"			7 8	1255 3		21' R. top wall
"			8 8	1254 3		SW. ppty cor.
"			6 48	1256 59	19'L gut.	
"			5 97	1257 10	" " cb. at end	
"			4 2	1258 9	NW. ppty co	
18+15			4 3	1258 8	63 4 L Flo line of 21" corr. iron pipe inlet	
18+15			10 4	1252 2	33 9 R " " " " " " outlet	
18+42			13 3	1249 8	5.2 R " " 24" conc. storm drain at in	
18+42.48			5 63	1257 44	℄ int. Mendocino & Santa Anita	
			10 71	1252 36	℄ Santa Anita 80' S'ly	
			12 07	1251 00	E. gut. " " "	
			11 27	1251 80	E. cb " " "	
			0 08	1262 99	℄ " " N'ly	
			1 41	1261 66	E. gut " " "	
			0 75	1262 32	E. cb " " "	
			8 32	1254 75	gut S. and SE cb. at ℄	
			7 57	1255 50	cb " " " " "	
			7 20	1255 87	gut E " " " "	
			7 02	1256 05	cb " " " " "	
			4 92	1258 15	gut " " NE "	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1778 PG. 24 | Job No. 1390 Division No. V | Notes Red. | Plotted | No. | Profile
Survey of Mahewood Avenue | Date | Date | No. | X-Sec.
Survey by Lanigan Notes Lewis | Notes Chkd. | Checked
Indexed A. C. Johnson Date | Date | Date

STATION	B. S.	H. I.	F. S.	ELEV.	Mendocino	Street
		1263.07	4.78	1258.29	cb at E end N.E. cb not.	
			5.09	1257.98	gut N " " " "	
			4.43	1258.62	cb " " " "	
18+76			7.2	1255.9	20' L Floline of conc. culvert inlet	
18+75			9.9	1253.2	20 R " " " " "	
			7.7	1255.4		SE pptg cor
			3.6	1259.5	NE pptg cor.	
19+00			4.98	1258.09	℄	
"			7.12	1255.95		19' R gut
"			6.49	1256.58		" cb
"			5.57	1257.50	19' L gut	
"			4.91	1258.16	" cb	
20+00			4.12	1258.95	℄	
"			5.08	1257.99		14' R bck
"			5.94	1257.13		19' R gut
"			5.13	1257.94		" cb
"			4.43	1258.64	19 L gut	
		1	3.80	1259.27	" cb.	
T. P.	5.95	1264.92	4.10	1258.97	T. P.	
T. P.		1	9.35	1255.57	T. P.	
	2.18	1257.75				

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. Notes Red. Plotted Job No. 1390 Division No. U
X-Sec. No. Notes Chkd. Checked Survey of Mantanga Avenue
Date Date Date Survey by Lanigan Notes Lewis Date 11-17-58
Date Map No. Indexed Tabulated Date

F.B. 1418 PG. 25

STATION	B. S.	H. I.	F. S.	ELEV.	Mendocino	Street
20+53		1257 75	10 9	1246 9	129' R. ctr. basement to Hse # 508	
21+30			18 3	1239 5	209' R. drain of swimming pool	" "
21+50			14 9	1242 9	267' R Floor elev. to rear house	" "
"			16 6	1241 2	288' R ground at SW Cor rear house	
T.P	816	1265 56	0 35	1257 40	T.P.	
21+00			5 94	1259 62		℄
"			6 77	1258 79		14' R brk
"			7 42	1258 14		19' " gut
"			6 72	1258 84		" cb
"			6 10	1259 46	19' L gut	
"			5 33	1260 23	" cb	
22+00			5 26	1260 30		℄
"			5 95	1259 61		14' R brk
"			6 80	1258 76		19' R gut
"			6 01	1259 55		" cb
"			5 57	1259 99	19' L gut	
"			4 62	1260 94	" cb.	
22+90			4 64	1260 92		℄
"			5 55	1260 01		14' R. brk
"			6 50	1259 06		19' " gut
"			5 65	1259 91		" " cb

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 PG. 26 | Job No. 1390 Division No. 11 | Survey of Mar-Lenigo Avenue | Survey by Lemigan Notes Lewis Date | Indexed A. C. Johnson

Profile No. ____ Plotted ____ Date ____ Notes Red. ____ Date ____ Notes Chkd. ____ Date ____ Checked ____ Date ____ X-Sec. No. ____

STATION	B. S.	H. I.	F. S.	ELEV.	Mendocino	Street
22+90		1265 56	4 82	1260 74	19' L gut	
"			4 12	1260 44	" cb	
23 + 40			14 8	1250 8	106' R basement floor elev.	Hse # 536
23 + 10			12 3	1253 3	135' R ground at SW cor.	" "
24+00			4 67	1260 89		
"			5 73	1259 83		14' R. b-k
"			6 83	1258 73		19' R gut
"			6 24	1259 32		" cb
"			4 67	1260 89	19' L gut	
"			3 96	1260 60	" cb	
T. P	4 74	1265 64	4 66	1260 90	T. P.	
24+35			16 2	1249 2	160' R ground at SW cor.	Hse # 562
24 +73			18 6	1247 6	176' R ctr. basement floor	" "
25+00			4 21	1260 33		
"			5 82	1259 82		14' R b-k
"			7 15	1258 49		19' R gut
"			6 37	1259 27		" cb
"			4 95	1260 69	19' L gut	
"			4 35	1261 29	" cb	
26+00			4 85	1260 79		
"			5 80	1259 84		14' R. b-k

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Mendocino	Street
26+00		1265 64	7 13	1258 51		19' R gut
"			6 45	1259 19		" cb
"			5 12	1260 52	19' L gut	
"			4 57	1261 07	" cb	
T. P.	6 09	1266 88	4 85	1260 79	T. P.	
26+51			6 42	1260 46	19' L gut	
			5 92	1260 96	" cb at end	
26+59			7 00	1259 88		15' R brk
"			8 33	1258 55		19 " gut
"			7 64	1259 24		" "
			8 9/10	1258 0/1		SW. ppty cor
			3 3/10	1263 6/10	NW ppty cor	
26+82.28			5 61	1261 27	& int. Mendocino & Santa Rosa	
			12 13	1254 75	& Santa Rosa 90' S'l'y	
			0 27	1266 61	75' N'l'y	
27+82			7 87	1259 01		
BMAE149			7 66	1259 22	BMAE 149 Elev 1259.202 FB 1449 P. 15 Santa Rosa Ave & Mendocino St. S.W. cor. Bt. spk. in curb 6' W of E. end.	

Profile
Notes Red. ____ Plotted ____ Job No. 1390 Division No. V
No. ____ Date ____ Date ____ Survey of Mayenga Ave
X-Sec. ____ Notes Chkd. ____ Checked ____ Survey by Langdon Notes Kept Date 11-17-50
No. ____ Date ____ Date ____ Map No. ____ Index ____ Date ____

F.B. 1718 PG. 27

F.B. 1719 PG. 28 | Job No. 1390 | Division No. V. | Notes Red. | Plotted | Profile

Survey of Malenge Ave | Date | Date | No.

Survey by Lanigan | Notes Lewis | Notes Chkd. | Checked | X-Sec.

Indexed | Date | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	

76L298 307 5-49

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR

726 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend notes this side of this line.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK. WITH DATE AND NAME OF PERSON MAKING CHANGE.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Mariposa Ave
W. O. 1390 Tape No. Std. by
Surveyed by J. J. Lonigro
Notes D.D.L. Date 11-28-50
Indexed: H. C. Peterson

F. B. 1716 PG. 29

FB 2051

Note: Any Additions or Changes of This Sheet Must be Made in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
of
IMPROVEMENTS
on
MARIPOSA ST
from
FAIR OAKS AVE
to
SANTA ROSA AVE
C.I. 1390

J. J. Lonigro
C. H. Lewis
W. H. Rabbet
E. W. Evans

7-47 3053 10M

F. B. 1718 PG. 30

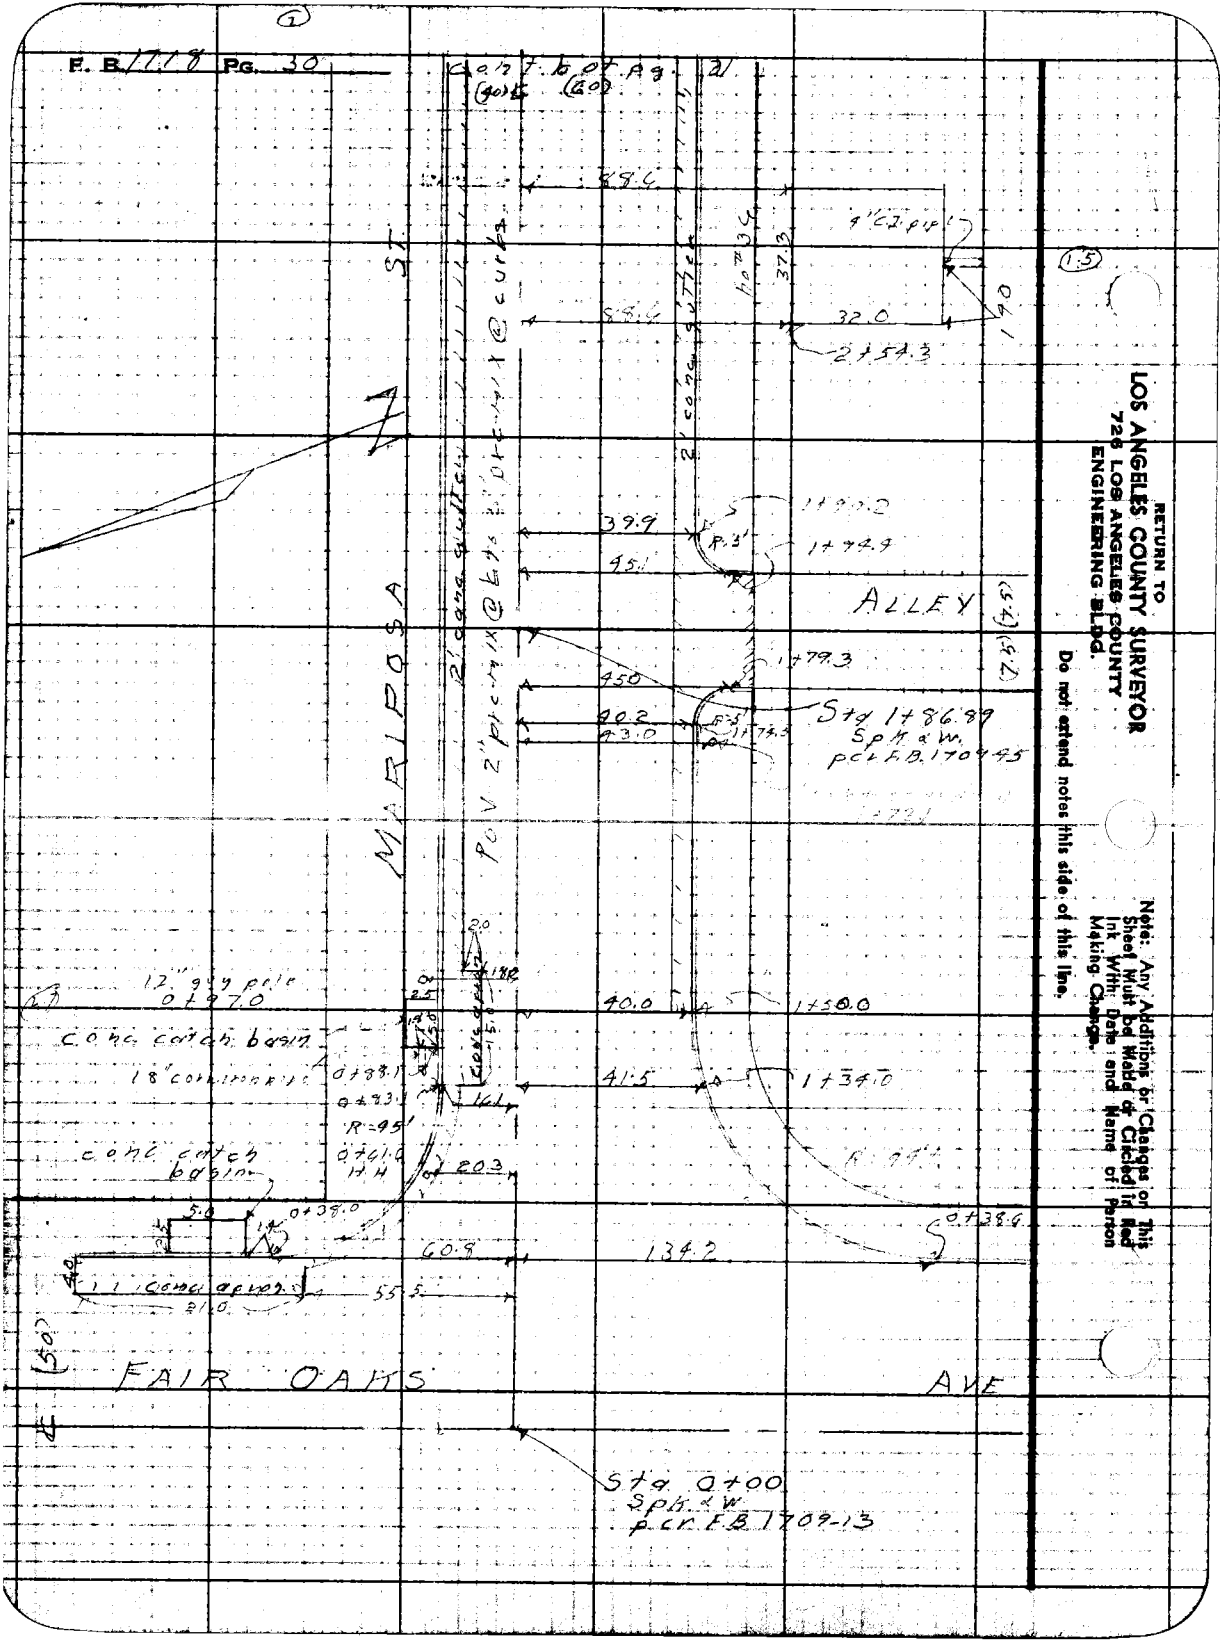

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made & Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Marengo Ave
W. O. 3900 Tape No. Std'd
Surveyed by J. J. Lanigan
Noted J.J.L. Date N-2030
Indexed C. Johnson

F. B. 1719 PG. 31

Notes: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
720 LOS ANGELES COUNTY
ENGINEERING BLDG.

76-2000 247 10M 1-69

94.8
94.8
94.9
94.9
94.8
92.8
90.0
51.0
52.2
40.0
32.1
32.3
18.0
9.5
17.6
119.57
P=12K
Δ=72°24'
R=12
Δ=72°24'
5+08.7
4+72
4+82
4+09.7
4+05.5
3+54.8
3+44.6
M^c NALLY
AVE.
MARIPOSA
Sta 3+74.37
Spk w.s.t
per E.A. 1709-96
Top 2" Monument
Edge of Gutter
Edge of Gutter
Edge of Gutter
Top P&P

F. B. 1718 PG. 32

Cont. to pg. 33

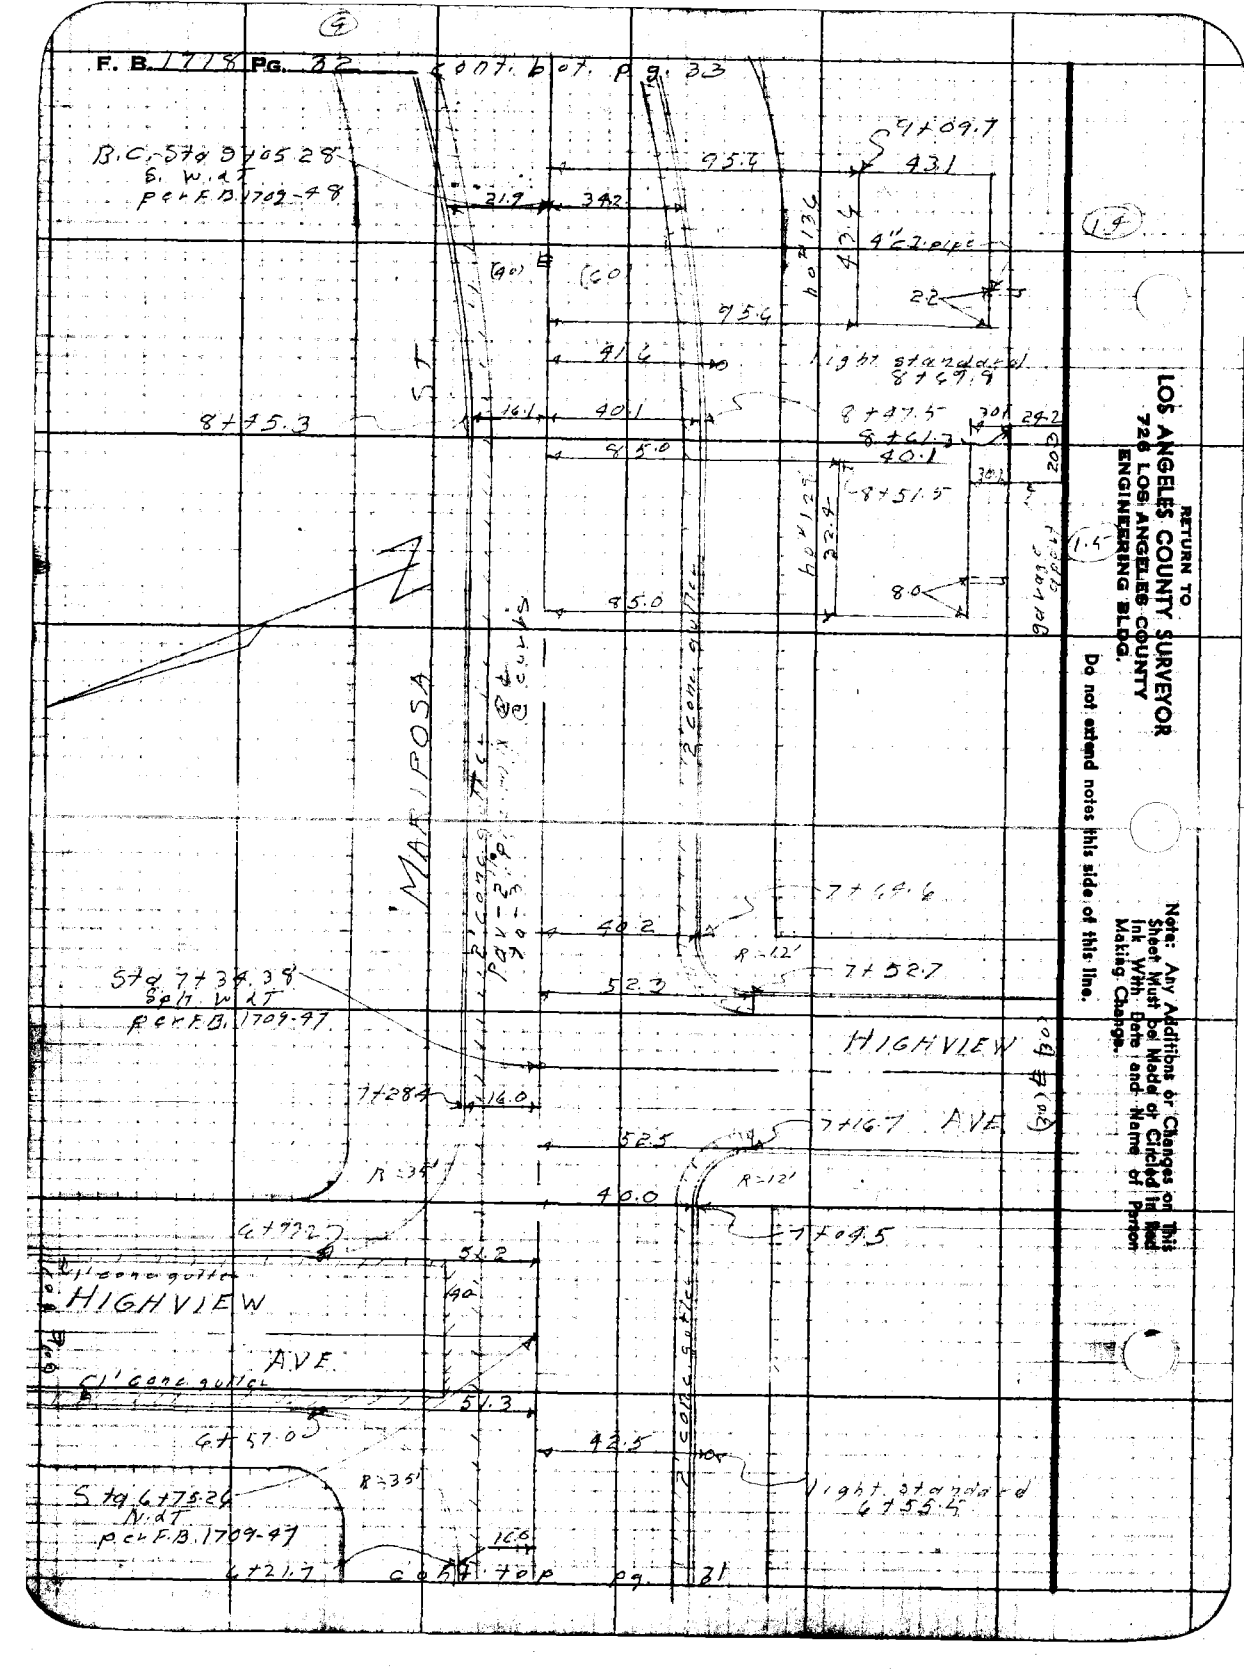

RETURN TO
LOS ANGELES COUNTY SURVEYOR
720 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by	Survey of Maienge Ave
Map No.	W.O. 7300 Tape No. Std.
Office Work	Surveyed by: V.J. Lanigan
Checked	Noted V.J.L. Date 11-20-58
Date	Indexed: A. C. Johnson

F. B. 1718 PG. 33

Notes: Any Additions or Changes of This Sheet Must be Made or Checked in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Capitol Ave. 99'

2' Concrete

RAYMOND AVE

(82.4') ℄ 27.5'

E.C. Sta. 11+00.45
S.W.L.T.
P.C.V.F.B. 1709.99

70+57.3

R=20'

526

10+50.1

Light Standard 10+98.8

172

178

11+00.3

7.8' Corrugated Pipe

10+80.3

P.O.B. Sta 10+02.87
L.L.T.
P.C.V.F.B. 1749.98

10+84.2

Conc. catch basin
3.5 x 7.0

Sta 10+00

MAR VISTA

Tank

12" Conc. Pipe @ 0.3% Flow

12" Conc. outlet

(100')

Cont. to pg 34

Conc. R.P.S.M.H.

97+63.5

97+53.0

85.7

14.8

3.81

85.7

8.7

9" C.I. pipe

(12)

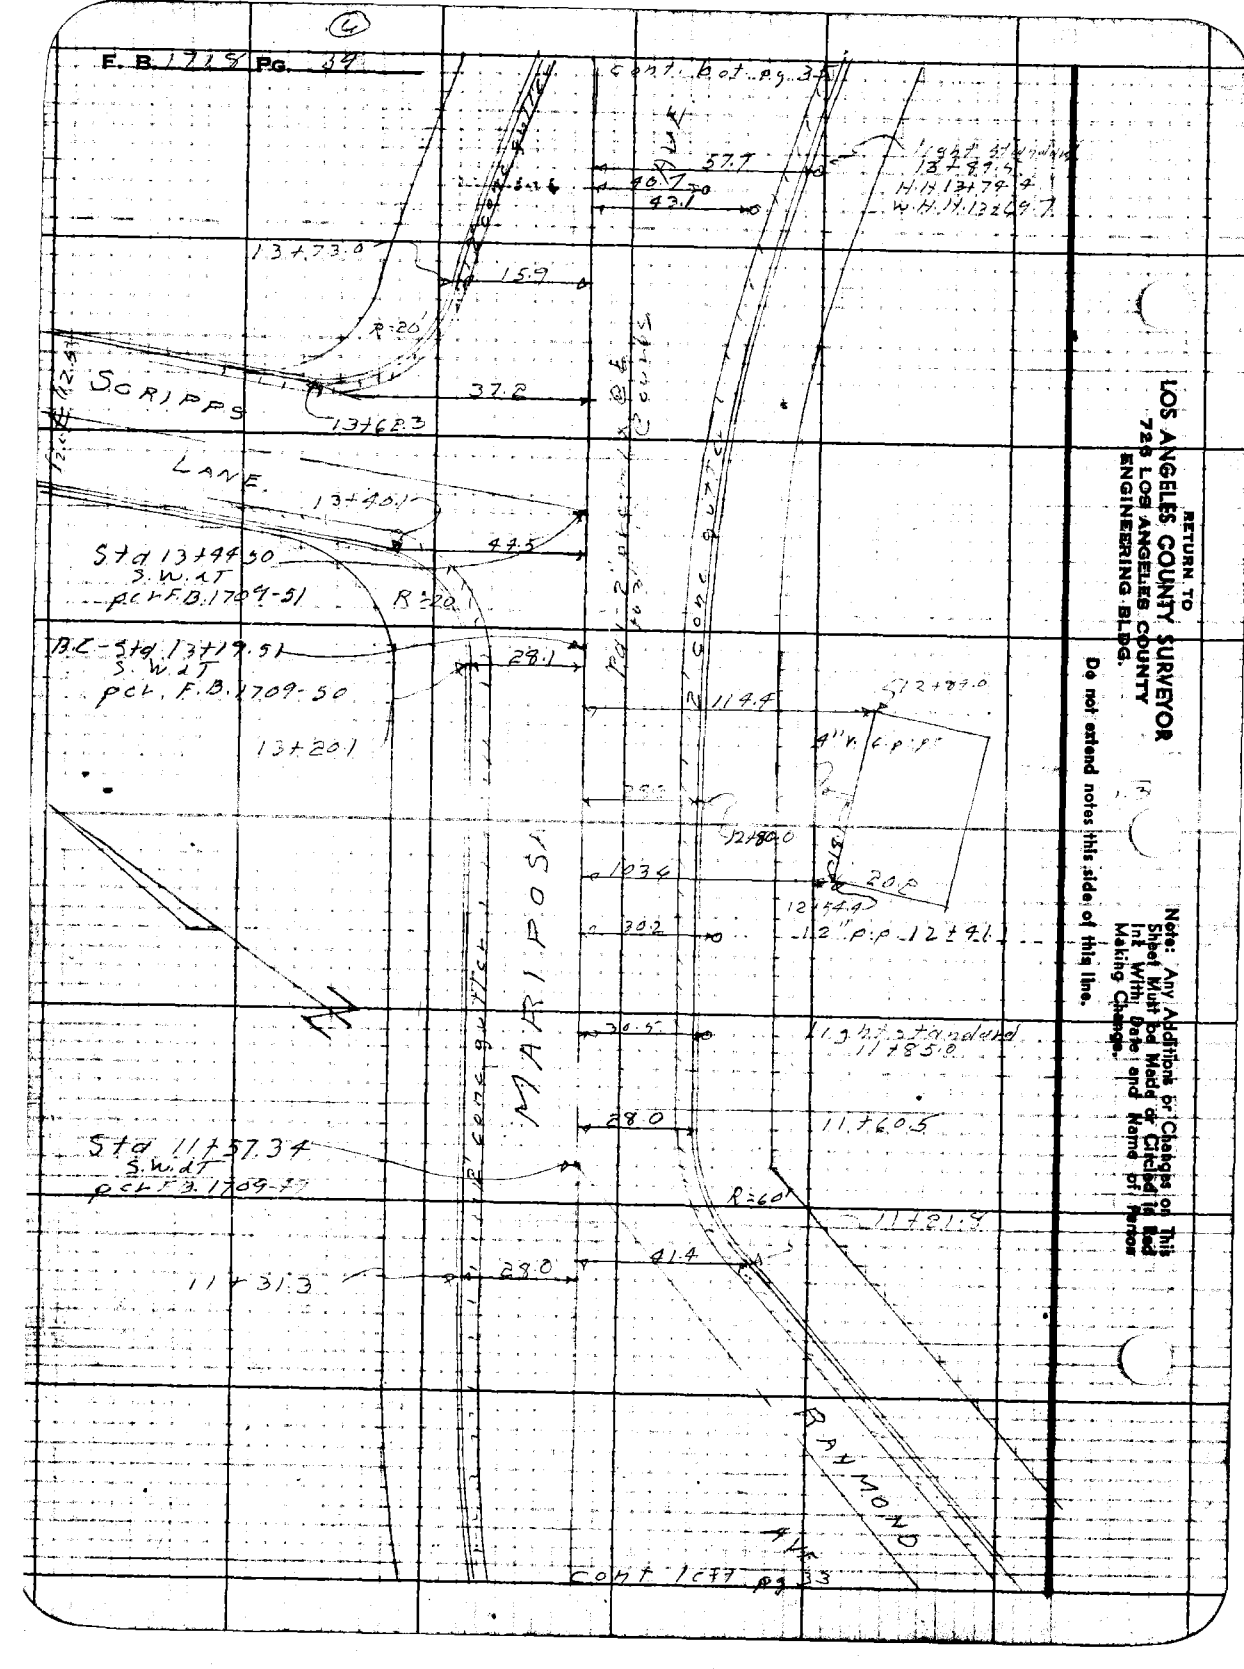

RETURN TO
LOS ANGELES COUNTY SURVEYOR
720 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by	Survey of Marengo Ave.
Map No.	W.O. 3795 Page No. Std.
Office Work	Surveyed by W.J.L. & Assistant
Checked	Notes W.J.L. Date 11-6-57
Date	Indexed: R. C. Jan. 2008

F. B. 1719 PG. 35

Note: Any Additions or Changes of This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
7128 LOS ANGELES COUNTY
ENGINEERING BLDG.

75-F2005 2-67 10M 1-68

15+72.4

75.8

28.2

28.1

15+23.6

51.8

39.5

H.W. 2.5

9"V.C.P.

9.0

27

7.5.8

15+20.4

S74°13'12.52"E
S.W. 2.7
P.C. F.B. 1709-51

5.60

81.15'

ccsp. pool in front unable to locate outlet

H.W. 2.0

81.9'

29.1

14+99.0

PROPOSED 2" WATER MAIN

Pav. 2" Pressure Pc. Unit

P.I. - S74°14'13.99"E
2.7 L.F.
P.C. F.B. 1709-51

14+22.2

62.8

14+26.4

14+05.6

Exhibit Map pg. 34

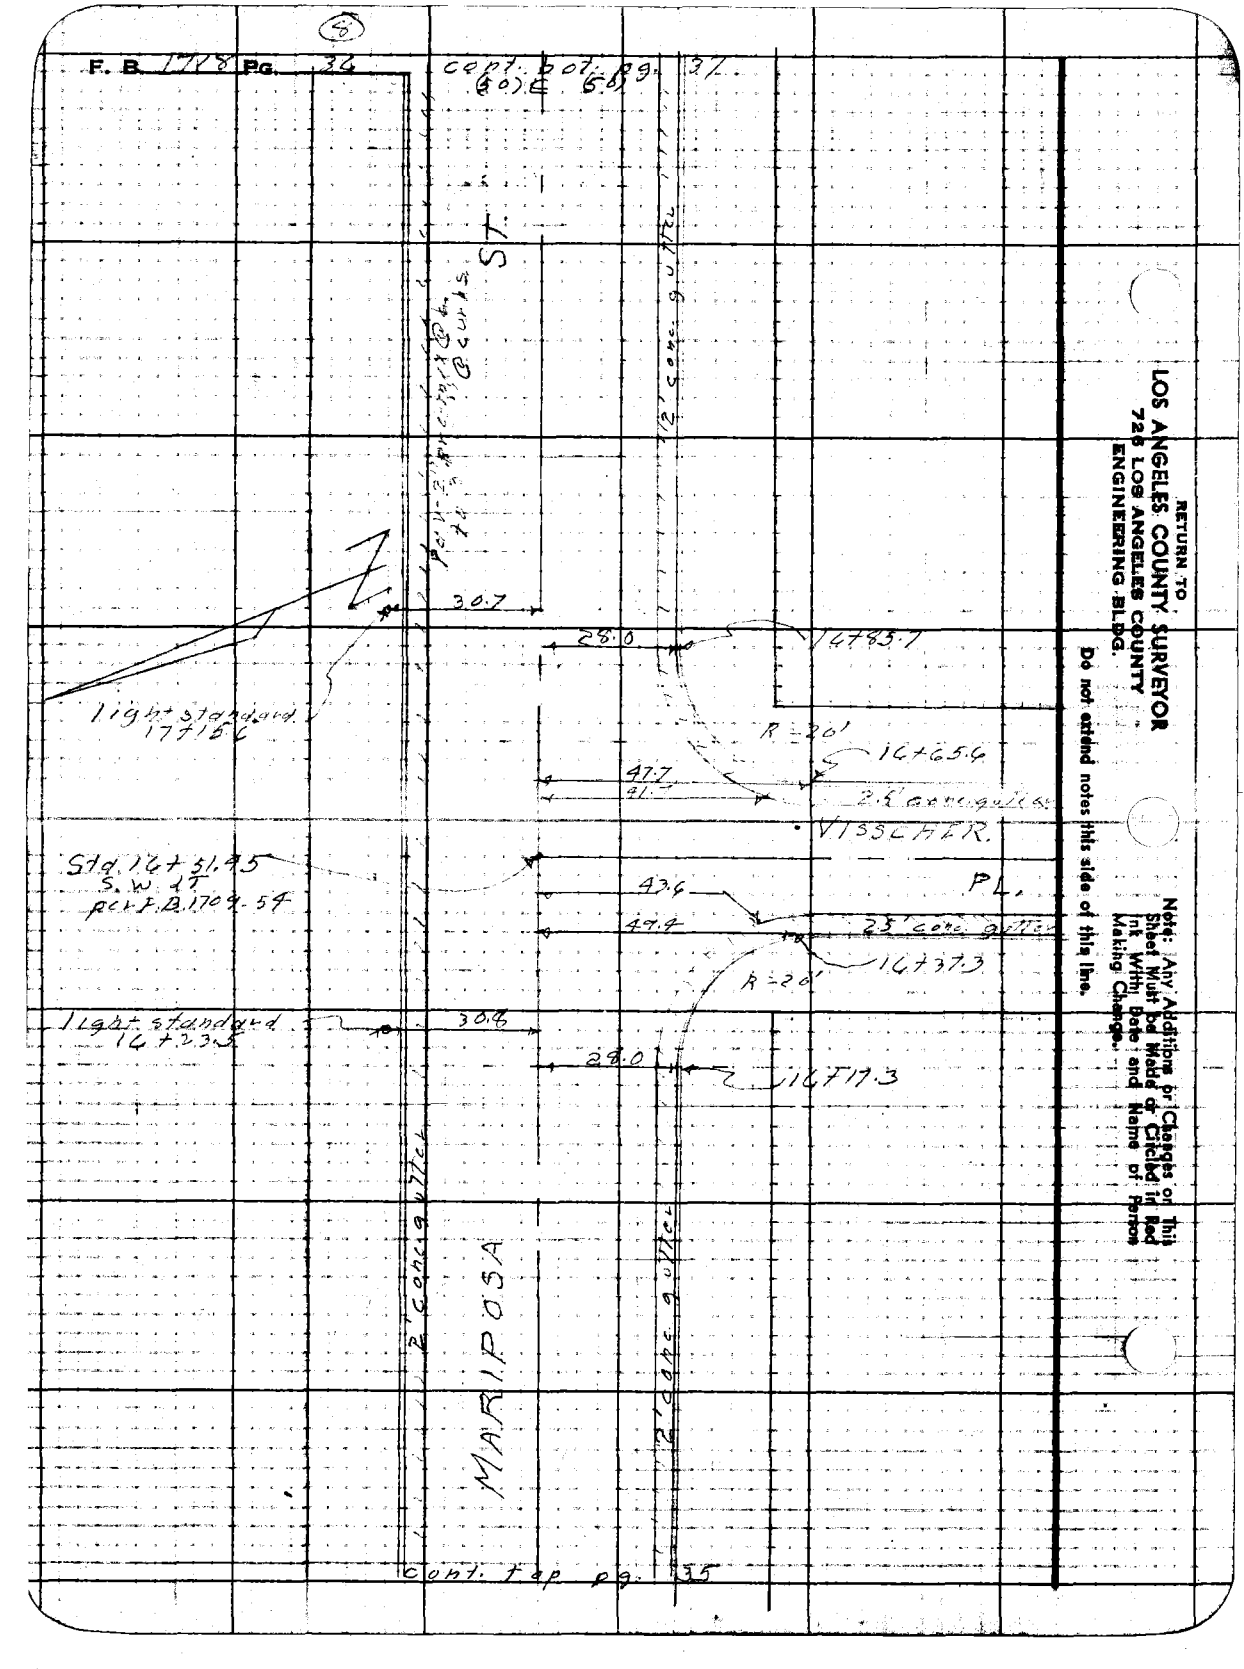

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

F. B. 1778 Pg. 37

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Mortgage Sur.
W. O. 3794 Tape No. Std. Ft.
Surveyed by J. J. Lanigan
Noted J.J.L. Date 11-24-54
Indexed E. C. Johnson

Notes: Any Additions or Changes of This Sheet Must Be Made or Checked in Red Ink With Date and Name of Person Making Change.

Do not attach notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
720 LOS ANGELES COUNTY
ENGINEERING BLDG.

12" RCP 21+44.3

38.7

ST

(4.7) conc. catch basin 2 21+73.4

12" RCP 21+67.8

18" conc. RCP

21+73.4

21+73.8

21+73.5

28.0

37.9

12" A.C.P. 21+70.9

29.0

37.1

conc. catch basin

18" conc. RCP

R=20'

21+59.4

59.2

48.2

48.1

21+53.6

MARENGO

21+27.51 S.W.27 AVE

P.C.V. F.B. 1709-33

21+45.4

21+45.5

21+05.5

48.1

47.2

53.3

21+93.5

10' guy pole 20+91.3

R=20

R=20

38.1

28.0

28.0

conc. catch basin

18" conc. RCP

20+85.5

20+80.3

conc. catch basin

18" conc. RCP

20+93.4

H.H. 20+76.9

27.9

38.1

18" guy pole 20+55.7

19+90.9 light standard

30.6

70.3

47.5

septic tank in easement unable to locate outlet

48.0

70.2

19+42.7

67.7

34.3

70+30

A.C.I. pipe

8.0

91.0

69.7

18+96.2

MARIPOSA

(60) E (50)

CONST. TOP P.J. 34

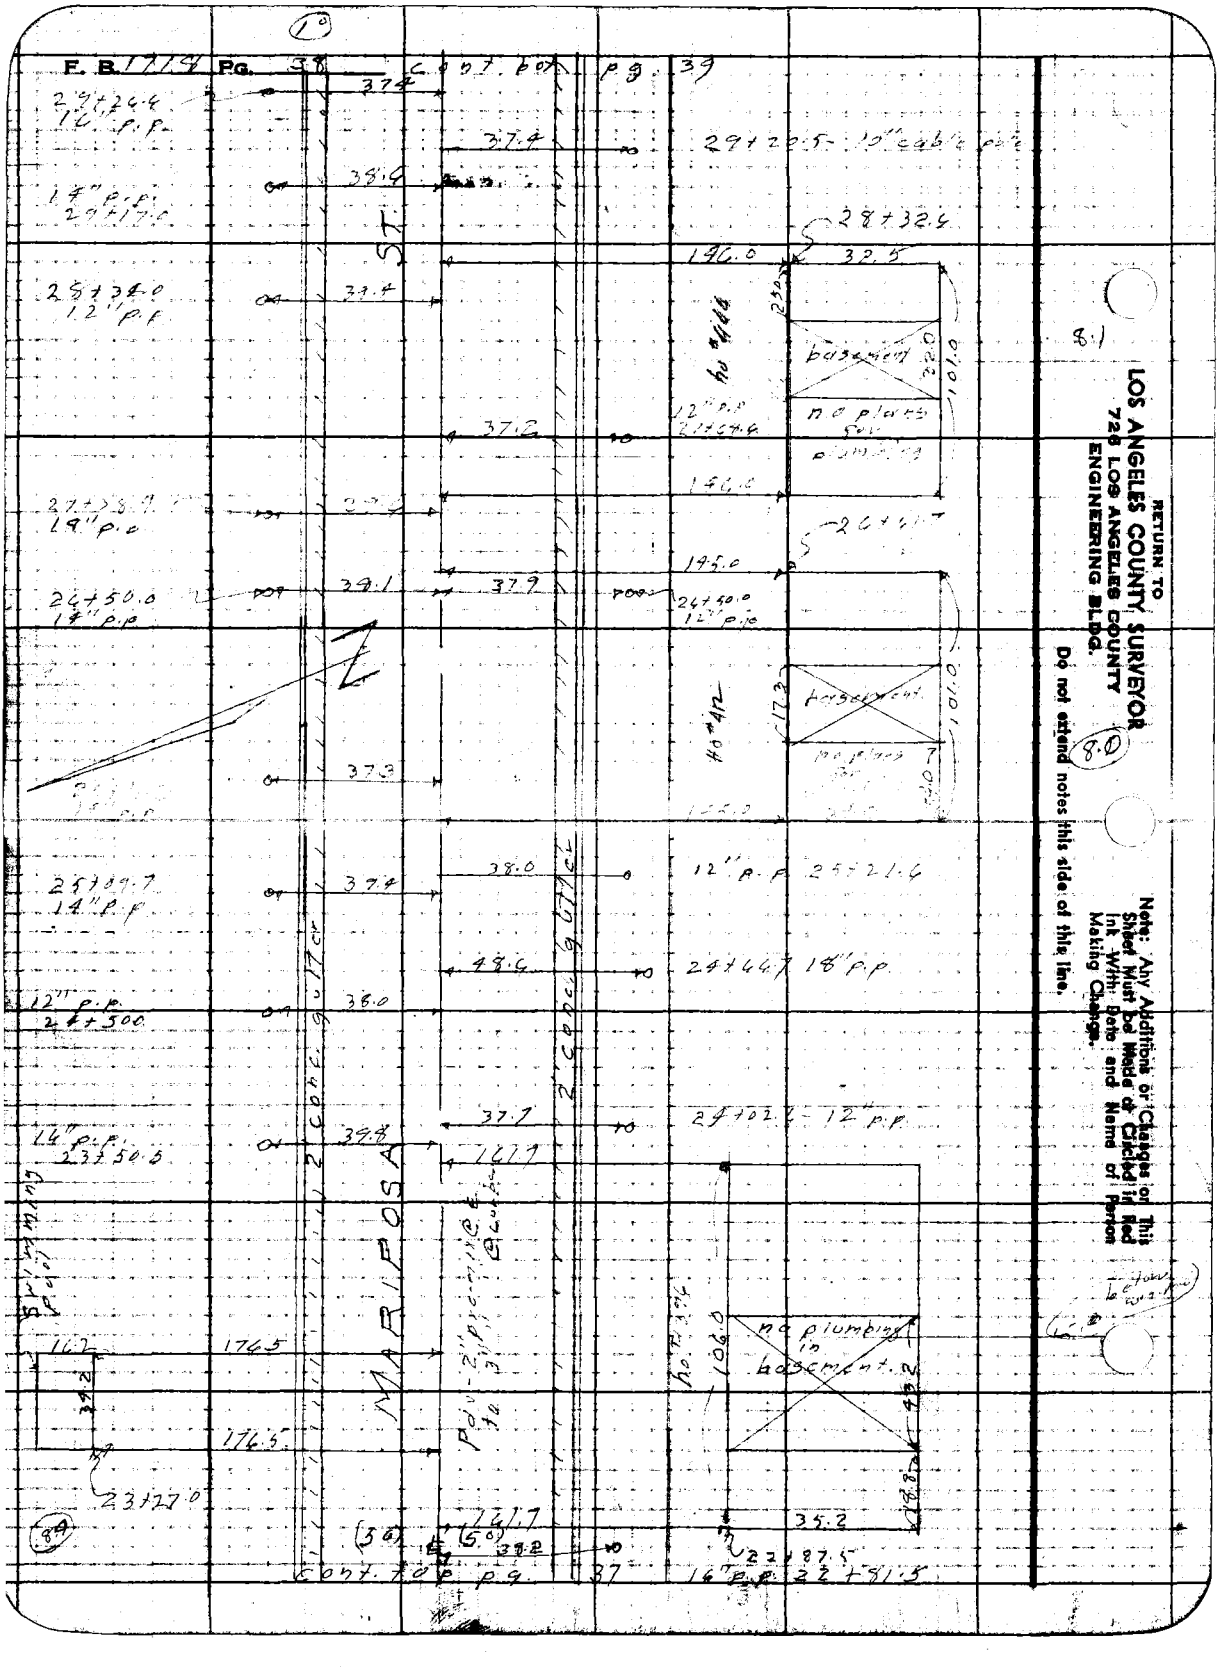
F. B. 1114 Pg. 38
Cont. for pg. 39
pg. 39
MARIPOSA ST.
2 CODES SOUTH
Pol. 2" pipe in Ec
Cont. for pg. 37
RETURN TO
LOS ANGELES COUNTY SURVEYOR
720 LOS ANGELES COUNTY
ENGINEERING BLDG.
Do not extend notes this side of this line.
Note: Any Additions or Changes or This Sheet Must be Made & Circled in Red Ink With Date and Name of Person Making Change.
basement
no plumbing in basement
8.1
8.0

(17)

Notes Ck'd by	Survey of Melrose Ave
Map No.	W.O. [illegible] Comp No. Std
Office Work	Surveyed by J.J. Longo
Checked	Noted J.J.L Date 11/12/48
Date	Indexed [illegible]

F. B. 1275 PG. 39

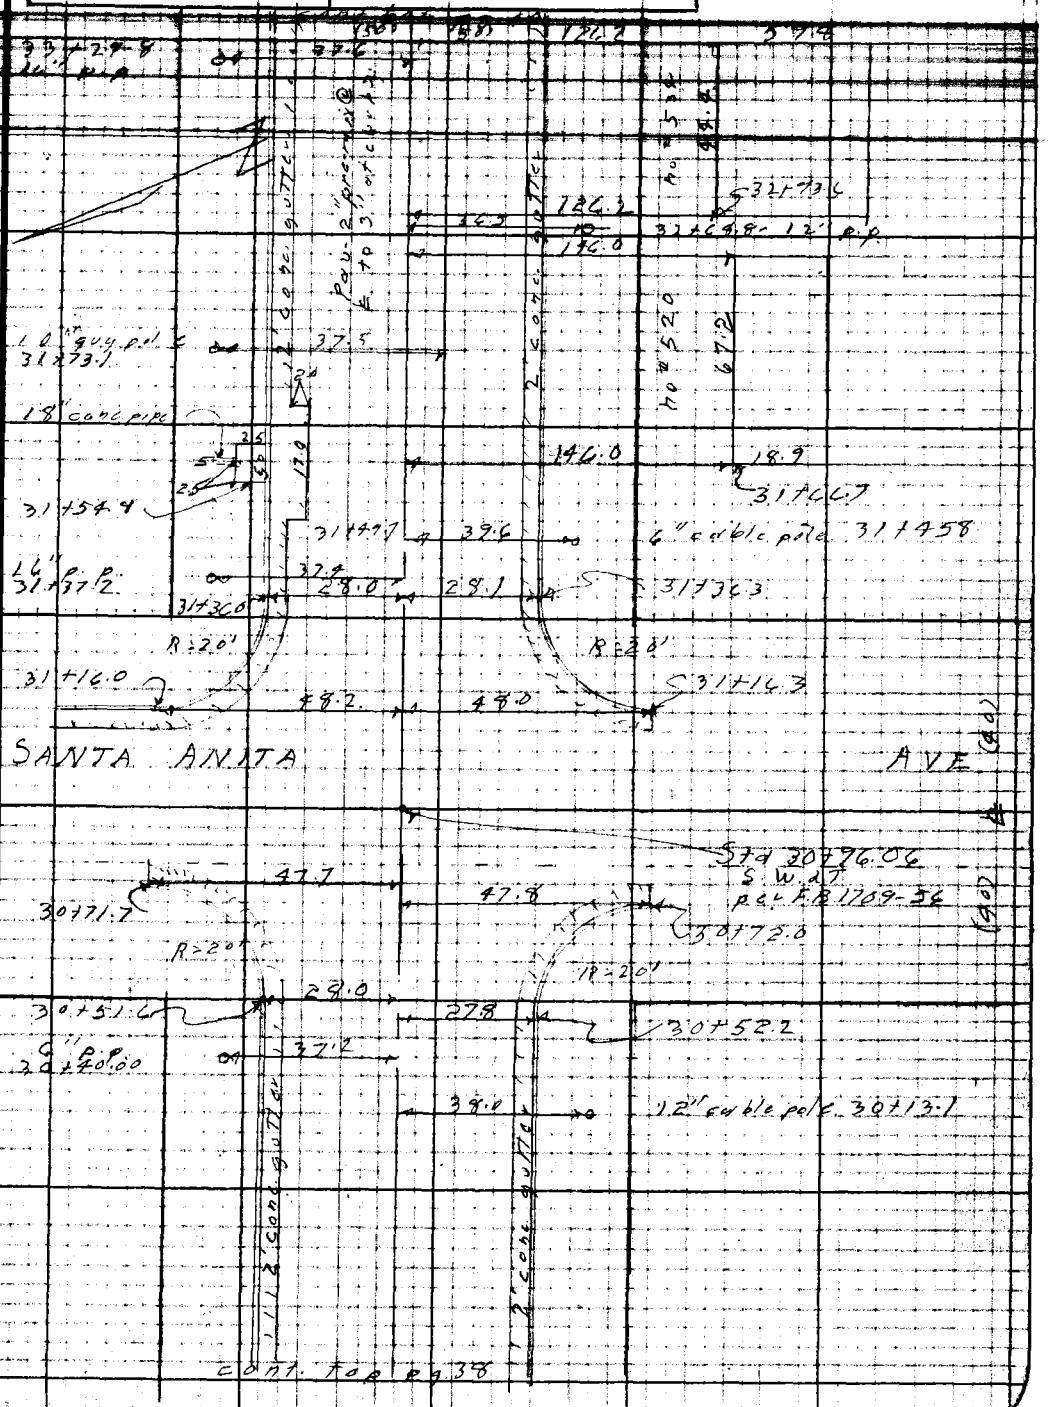

Notes: Any Additions or Changes on This Sheet Must Be Made or Checked in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
720 LOS ANGELES COUNTY
ENGINEERING BLDG.

76F3095 247 10M 1-49

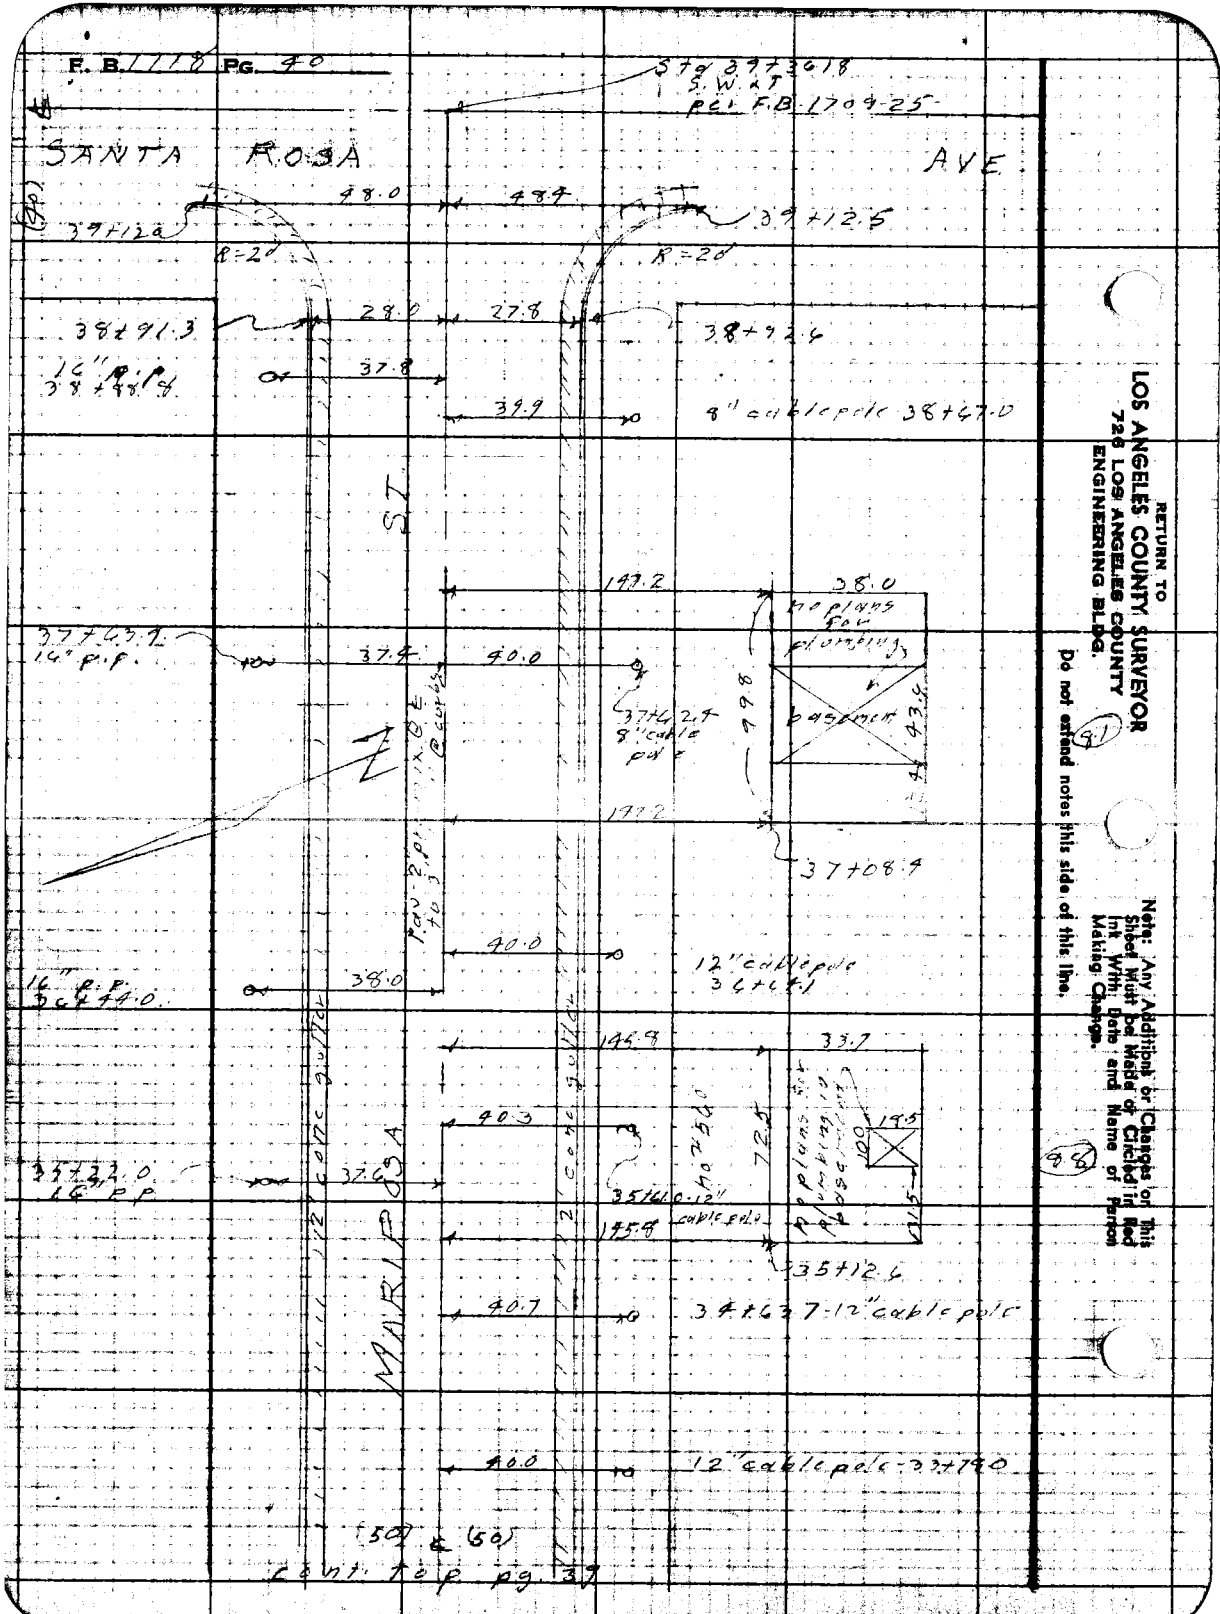
F. B. 1118 PG. 40
S79°39'30"E
S. W. cor
PCI F.B. 1709-25
SANTA ROSA AVE
98.0
48.9
39+12.5
39+12.8
R=20'
R=20'
38+91.3
16" P.P.
38+48.4
28.0
27.8
37.8
39.9
38+92.6
8" cable pole 38+47.0
ST
147.2
38.0
no plans for plumbing
37+63.7
16" P.P.
37.4
40.0
37+62.7
8" cable pole
basement
43.6
99.8
147.2
37+08.7
40.0
12" cable pole
36+64.1
16" P.P.
36+44.0
38.0
Fav. 2.01 to 3.01
IX. CO. Curves
145.9
33.7
40.3
19.5
10.0
7.25
4.0
4.5
35+73.0
16" P.P.
37.6
12" cable pole
35+60.0
14.58
35+12.6
40.7
34+63.7-12" cable pole
MARIPOSA
40.0
12" cable pole-33+78.0
[50] & [50]
Cont. to pg. 39
RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.
Do not extend notes this side of this line.
Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.
9-1
9-8

Profile No. | Notes Red. [illegible] Date [illegible] | Plotted [illegible] Date [illegible] | Job No. 1390 | Division No. V | Survey of M[illegible]

X-Sec. No. | Notes Chkd. JJM Date 12/28/50 | Checked [illegible] Date [illegible] | Survey by Lanigan, Notes Lewis Date 11-24-50 | Map No. [illegible]

F.B. 1718 PG. 41

PROFILE
and
CROSS-SECTIONS
of
MARIPOSA STREET
from
FAIR OAKS AVENUE
to
SANTA ROSA AVENUE
C.I. 1390

J.J. Lanigan
C.H. Lewis
H.H. Raphael
E.W. Evans

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

761-298 307 5-49

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 7118 Pg. 42 | Job No. 1390 Division No. L | Profile No. | X-Sec. No.
Survey of Marengo Ave.
Survey by Lantigua Notes Lewis Notes Chkd. Checked
Indexed A. C. Tennson Date Date Plotted Date Notes Red. Date

STATION	B. S.	H. I.	F. S.	ELEV.	Mariposa Street
BM AE 264	8.68	1278.07		1269.39	BM AE 264 Elev. 1269.388 FB 1447-244 Fair Oaks Avenue & Mariposa St. N.W. Cor. L-N in cb. 4' W of W. end C.R.
0+00			3.17	1274.90	℄ int. Mariposa St & Fair Oaks Ave
0-23			4.03	1274.04	Wedge of Fair Oaks pvmt.
			10.86	1267.21	℄ of Fair Oaks 134' S'ly
			12.71	1265.36	gut S end SE cb. Het
			11.99	1266.08	cb " " " " "
T.P.		✓	2.01	1276.06	T.P.
	6.48	1282.54			
			5.34	1277.20	gut N end NE cb Het
			4.68	1277.86	cb " " " " "
			7.20	1275.34	gut E " " " "
			6.53	1276.01	cb " " " " "
			9 2/3	1273 3/3	Flo line of pipe in catch basin
			4 3/3	1278 2/3	NE poly conc.
			9.22	1273.32	gut End SE cb Het
			8.63	1273.91	cb " " " "
			8 5/6	1273 9/6	P.L. " " " "
1+50			6.74	1275.80	℄
"			6.95	1275.79	16'L gut

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. Notes Red Date Plotted Date Job No 1300 Division No. V
X-Sec. No. Notes Chkd. Date Checked Date Survey of Mariposa Ave
Survey by Lewis Notes Lewis Date 11-24-50
Map No. Date Date
F.B. 1716 Pg. 43

STATION	B. S.	H. I.	F. S.	ELEV.	Mariposa Street
1+50		1282 54	6 33	1276 21	16'L cb
			8 94	1273 60	gut W end SW cor ret- at alley
			8 46	1274 08	cb " " " " " " "
			8 40	1274 14	gut S " " " " " "
			8 24	1274 30	cb " " " " " " "
			8 08	1274 46	gut S " " SE " " "
			7 95	1274 59	cb
			8 53	1274 01	gut E
			7 29	1274 65	cb
2+00			6 65	1275 89	℄
			8 70	1273 84	R cross gut
			8 45	1274 09	60'R bldg
			11 97	1270 57	℄ of Alley 92' S'ly
2+68			14 7	1267 8	120'R elev of 4" CI Pipe near edge of road
"			16 2	1266 5	back lot line " " "
3+00			6 22	1276 32	℄
"			8 17	1274 37	40 R gut
"			7 49	1275 05	" " cb
"			6 56	1275 98	16'L gut
			5 91	1276 63	" cb
1+86.89	?		6 12	1276 42	℄ int Mariposa & McNally Ave

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ Plotted ____ Date ____ X-Sec. No. ____ Notes Red. ____ Date ____ Notes Chkd. ____ Date ____ Checked ____ Date ____

Job No. 1370 Division No. V Notes Mariposa Avenue

Survey of Mariposa Avenue

Survey by Lenigan Notes Kelly's

Indexed L. C. Johnson Date

PG. 44

STATION	B. S.	H. I.	F. S.	ELEV.	Mariposa	Street
		1282 54 ✓	7 7	127- 8	S.W. ppty cor.	
			801	127- 53	gut W end SW	eb Ext
			735	127- 19	cb " " "	" "
			876	127- 78	gut S " "	" "
			810	127- 44	cb " " "	" "
			857	127- 77	gut " " SE	" "
			790	127- 64	cb " " "	" "
			792	127- 62	gut E " "	" "
			730	127- 24	cb " " "	" "
			859	127- 95	℄ of 22nd Way	65' S'ly brk
			1182	127- 72	" " "	100' "
			1120	127- 94	W gut. "	90' "
			1044	127- 10	W cb. "	" "
			1123	127- 31	E gut "	" "
			1054	127- 00	E. cb. "	" "
			7 8	1274 7	S.E. ppty cor.	
1+86.89			635	1276 19	16' L gut	
"			572	1276 82	" cb	
T.P.			612 ✓	127- 42 ✓	T.P.	
	5 25	1281 67 ✓				
4+77			12 8	1268 9	129' R elev. 4" CI pipe at garage	Hse #72

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. 1222 Division No. K
No. Date Date Survey of Mariposa Avenue
X-Sec. Notes Chkd. Checked Survey by Lewis Notes Lewis Date 11-24-50
No. Date Date Map No. Checked Date

F.B. 1718 PG. 45

STATION	B. S.	H. I.	F. S.	ELEV.	Mariposa Street
4+85		1281 67	12 3	1269 4	127' R 4" CI pipe at rear of Hse # 72
4+90			15 0	1266 7	180' back lot line
5+00			495	1276 72	℄
"			674	1274 89	40' R gut
"			607	1275 60	" cb.
"			513	1276 54	16' L gut
"			454	1277 13	" cb
5+14			12 8	1268 9	128' R elev of 4" CI pipe rear of Hse # 88
5+40			14 0	1267 7	180' ±R back lot line
6+00			460	1277 07	℄
"			657	1275 10	40' R gut
"			576	1275 91	" " cb
"			490	1276 77	16' L gut
"			425	1277 42	" cb
T. P.		1	419	1277 48	BM AE 479 Elev. 1277.468
	3 51	1280 99			
			416	1276 83	gut W and NW cb-et
			350	1277 49	cb " " " " "
			293	1278 06	gut N " " " "
			231	1278 68	cb " " " " "
6+75.26			371	1277 28	℄ int Mariposa & Highview

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 PG. 46 | Job No. 1392 Division No. | Profile No. | Notes Red. | Plotted | Date | X-Sec. No. | Notes Chkd. | Checked | Date

Survey of Mariposa Street

Survey by Lewis Notes Lewis

Indexed J. C. Johnson Date

STATION	B. S.	H. I.	F. S.	ELEV.	Mariposa	Street
		1280 99	392	1277 07	16'L. cross gut	
			020	127[illegible] 79	& Highview 100' N'l'y	
			061	127[illegible] 38	w. gut " "	"
			000	127[illegible] 99	" cb " "	"
			085	1278[illegible] 14	E gut " "	"
			015	1280 84	" cb " "	"
			297	1278 02	gut, N end NE cb ret	
			230	1278[illegible] 69	cb " " "	" "
			383	127[illegible] 16	gut E " "	" "
			320	1277 79	cb " " "	" "
7+34 38			359	1277 40	Rint Mariposa & Highview (to South)	
			553	1278 46	gut W end SW. cb ret.	
			489	1276 10	cb " " "	" "
			596	1275 03	gut S " "	" "
			535	1275 64	cb " " "	" "
			625	1274 74	gut " " SE.	" "
			562	1278 37	cb " " "	" "
			552	1278 47	gut E " "	" "
			483	1276 16	cb " " "	" "
			5 1	1275 9	SW. ppty cor.	
			5 2	1275 8	SE " "	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted. Job No. 120-. Division No.
No. Date Survey of Marengo Avenue
X-Sec. Notes Chkd. Checked Survey by Lanigan Notes Lewis Date 11-24-50
No. Date Date Map No. Indexed Johnson Date F.B. 1178 PG. 47

STATION	B. S.	H. I.	F. S.	ELEV.	Marengo Ave.	Street
		1280.99	829	1272.70	Top Highview 100' S'ly	
			866	1272.33	W gut " "	"
			800	1272.99	" ch " "	"
			891	1272.08	E gut " "	"
			824	1272.75	" ch " "	"
8+00			343	1277.56	℄	
"			511	1275.88		40' R gut
"			478	1276.51		" ch
"			365	1277.34	16' L gut	
"			300	1277.99	" ch	
T.P.		1	341	1277.58	T.P.	
	4.24	1281.82				
8+26			12 1	1269.7	126' R elev. on outlet pipe rear of Hse #128	
8+60			12 6	1269.2	170' R Floor level garage apt	
8+40			13 6	1268.2	180' R back lot line & SW. cor " "	
8+68			12 5	1269.3	138' R elev. on 4" CI pipe rear of Hse #126	
"			13 8	1268.0	180' R back lot line	
9+00			384	1277.98	℄	
"			500	1276.82		35' R gut
"			431	1277.51		" " ch
"			401	1277.81	22' L gut	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 Pg. 48

Job No. 1390 Division No. V Profile No. X-Sec. No.

Survey of Mariposa Ave. Notes Red. Plotted

Survey by Lanigan Notes Lewis Date Date

Indexed A. C. Johnson Notes Chkd. Checked

Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	Mariposa	Street
		128182	330	1277 52	22' L. cb.	
T. P.		1	379	1278 03	T. P.	
	890	128693				
			17 7	1269 2		
			21 2	1246 7		
10+00			780	1279 13	on back Tangent.	
"			806	1278 87	"	2.5 R gut
"			741	1279 52	"	" cb
"			613	1280 80	70.5' L. "	gut
"			548	1281 45	" " "	cb
			654	1280 39	gut W and S.W. cb Lot	
			587	1281 06	cb " " " "	"
			7 2	1279 9	SW. ppty cor.	
			958	1279 35	gut S and S.W. cb Lot	
			894	1277 99	cb " " " "	"
10+87 5			10 0	1279 9	18" corr. iron pipe outlet in catch basin	
10+93			9 9	1277 0	" " " " inlet " " "	
11+57 34			102	1281 91	℄ int. Mariposa & Raymond.	
			785	1279 58	℄ Raymond 100'	5' Y
			1085	1279 58	" " 140'	"
			1227	1279 46	W gut " "	"

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. Notes Red. Plotted Job No. 1390 Division No. V
X-Sec. No. Notes Chkd. Checked Survey of Manhattan Ave.
Date Date Date Survey by Harrison Notes Lewis Date 11-24-50
Date Map No. Checked Johnson Date

F.B. 1715 PG. 49

STATION	B. S.	H. I.	F. S.	ELEV.	Manhattan	Street
		1286 93	11 58	1275 35	W. cb of Raymond 140' S'ly	
			10 98	1275 95	Edge pvmt "	" "
			11 44	1275 49	E gut "	" "
			10 58	1276 35	E cb "	" "
			4 93	1282 00	gut S end SE cb ret	
			4 26	1282 67	cb " " "	" "
			2 03	1284 90	gut E " "	" "
			1 35	1285 58	cb " " "	" "
T. P.			0 69	1286 24	T. P.	
	1089	1297 13				
12+00			8 85	1288 28		℄
"			10 19	1286 94		28' R gut
"			9 57	1287 56		" cb
"			9 04	1288 09	28' L gut	
"			8 40	1288 73	" cb	
12+65±			7 9/2	1289 2/2	105' R 4" V.C pipe at Hse # 232	
12+41			9 5/2	1287 6/2	180'± back lot line	
13+00			2 64	1294 49		℄
"			4 16	1292 97		29' R gut
"			3 45	1293 68		" cb
			2 79	1294 34	28' L gut	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 PG. 30
Job No. 1390 Division No. V Notes Red. Plotted Profile No.
Survey of Mateuszo Avenue Date Date X-Sec. No.
Survey by Kanagan Notes Lewis Notes Chkd. Checked
Indexed E. C. Johnson Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	Mariposa Street
13+00		1297 13	213	1295 00	28'L cb
			164	1295 49	gut W end NW cb Int at Scripps Lane
			096	1296 17	cb " " " " " "
BM AE 474			1 28	1295 85	BM AE 474 Elev. 1295.838
	7 39	1303 23			
			591	1297 32	gut N end NW cb Int
			544	1297 79	cb " " " "
			487	1298 36	gut " NE " "
			436	1298 87	cb " " " "
			519	1298 24	gut E end " " "
			452	1298 91	cb " " " " "
			601	1297 22	℄ int Mariposa & Scripps Lane
			604	1297 19	25'L cross gutter & Scripps Lane
			369	1299 54	℄ Scripps Lane 75'N'ly
			402	1299 21	W gut " " " "
			354	1299 69	" cL " " " "
			322	1300 01	E gut " " " "
			272	1300 51	" cb " " " "
14+00			364	1299 59	℄ (tan.)
			391	1299 32	3'L gut
			322	1300 01	" cb

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ Date ____ X-Sec. No. ____ Date ____ Notes Chkd. ____ Date ____ Plotted ____ Date ____ Checked ____ Date ____ Job No. 1290 Division No. ____ Survey of Marengo Avenue Survey by Hamilton Notes Louis Date 11-24-50 Map No. ____ Date ____ F.B. 1 PG. 51

STATION	B. S.	H. I.	F. S.	ELEV.	Marengo	Street
14+00		1303 23	4 24	1298 99		65'±R gut
"			3 61	1299 62		" cb
14+49			6 0 2	1297 2	111' R S.W. cor (ground) Hse #250	
"			3 7	1299 5	82' R Floor elev. of "	"
"			9 -	1294 -	180'±R back lot line?	"
T.P.			226	130097	T.P.	
	8 24	1309 21				
15+29			14 2	1295 0	127' R elev. on 4" WC. pipe at Hse #250	
			13 5	1295 7	180' R back of line	
15+43			582	1303 39		℄
"			753	1301 68		28' R gut
"			687	1302 34		" cb
"			588	1303 33	28' L gut	
"			524	1303 97	" cb	
16+17			529	1303 92		℄
T.P.			533	1303 88	T.P.	
	5 20	1309 08				
			678	1302 30	gut W end S.W. cl lot	
			617	1302 91	cb " " " "	
			858	1300 50	gut S " " " "	
			793	1301 15	cb " " " "	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 PG. 52
Survey of Mayengo Avenue
Survey by Lanigan Notes Lewis
Indexed L. C. Johnson Date 1-11-50
Job No. 1390 Division No. 4
Profile No. X-Sec. No.
Plotted Date
Notes Red. Date
Notes Chkd. Date
Checked Date

STATION	B. S.	H. I.	F. S.	ELEV.	Mariposa	Street
		130908	7 0	1302 1	SW. opp'g cor.	
			8 20	1300 88	gut S end S.E cb 1-et	
			7 87	130 50	cb " " " "	"
			6 92	130 16	gut E end " " "	"
			6 29	130 79	cb " " " "	"
			5 21	1303 87	℄ int. Mariposa + Visscher Place	
			10 51	1298 57	℄ Visscher Pl. 100' S 1'y	
			11 20	1297 88	w gut. " " "	"
			10 59	1298 49	" cb " " "	"
			11 03	1299 05	E gut " " "	"
			10 40	1299 68	" cb " " "	"
			515	130 73	N gut Mariposa at ℄ prod. of Visscher Pl	
			454	1304 54	" cb " " "	"
17+00			535	1303 73	℄	
"			696	1302 12		28' R gut
"			632	1303 76		" cb
"			529	130 79	28' L gut	
"			466	1304 42	" cb	
"			2 2	1306 9	50' L P L.	
"			0 0	1309 1	90' L	
18+00			563	1303 45	℄	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. Division No. V F.B. PG. 5-2
No. Date Date Survey of Mariposa Avenue
X-Sec. Notes Chkd. Checked Survey by Sanborn Notes Lewis Date 11-27-50
No. Date Date Map No. Andrew Johnson Date

STATION	B. S.	H. I.	F. S.	ELEV.	Mariposa	Street
18+00		1309 08	7 29	1301 79		28' R. gut
"			4 63	1302 45		" cb
"			5 59	1303 49	28' L gut	
"			4 96	1304 12	" cb	
T. P.			5 63	1303 45	T. P.	
	5 28	1308 73				
18+94			14 9	1293 8	111' R. elev. on 4" GI. pipe at rear of Hse # 310	
"			18 9	1289 8	180' " back lot line	" "
19+00			5 56	1303 17	℄	
"			7 21	1301 52		28' R gut
"			6 58	1302 15		cb
"			5 56	1303 17	28' L gut	
"			4 94	1303 79	" cb	
19+42			11 9	1297 7	70' R Floor elev. Hse # 320	
"			14 8	1294 5	120' R. ground at SW cor. Hse # 320	
"			19 0	1289 7	180' R " at back lot line " "	
20+00			5 92	1302 81	℄	
"			7 58	1301 15		28' ? gut
"			6 98	1301 75		" cl
"			5 84	1302 89	28' L gut	
"			5 18	1303 55	" cb	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ X-Sec. No. ____

Plotted ____ Date ____ Checked ____ Date ____

Notes Red. ____ Date ____ Notes Chkd. ____ Date ____

Job No. 1390 Division No. K

Survey of Mateo 90 Avenue

Survey by Lawson Notes Louis

Indexed K. C. Johnson Date ____

F.B. 1718 PG. 54

STATION	B. S.	H. I.	F. S.	ELEV.	Mariposa Street
BMAE473		1308 73	7 24	1301 49	BM #AE473 Elev 1301.477
	7 51	1308 99			
20 + 78			10 9	1299 0	28' L Flo-line 18" conc iron pipe outlet in catch basin
20 + 99			11 9	129? 1	53 R " " " " inlet to " "
			8 45	1300 54	gut at W end SW cb. net
			7 82	1301 17	cb " " " " " "
			10 20	129? 79	gut " S " " " "
			9 58	129? 11	cb " " " " " "
			8 9	130 6	S.W. ppty cor.
			6 22	130? 77	gut at W. end N.W. cb net
			5 59	130? 40	cb " " " " " "
			5 21	130? 78	gut " N " " " "
			4 55	130? 44	cb " " " " " "
			3 1	130? 3	NW ppty cor.
21 + 02			8 9	1301 0	52' L Flo-line of 18" conc iron pipe outlet in catch basin
			6 53	1308 46	℄ int. Mariposa St + Marengo Ave.
			12 20	129? 79	℄ of Marengo Ave 90' S'ly
			0 40	130? 59	℄ Marengo Ave 100' N'ly
			10 33	1298 66	gut. S. end S.E. cb net
			9 65	1299 14	cb " " " "
			8 27	1300 72	gut E " " " "

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Mariposa	5 Feet
		1308.99	7.62	1301.37	cb E end S.E. cb Ret. Mariposa & Marengo	
21+60			12.2	1296.8	59' R. Floline 18" conc. SD inlet to catch basin	
			5.19	1303.80	gut N end NE cb Ret	
			4.54	1304.45	cb " " " " "	
			6.05	1302.94	gut E " " " " "	
			5.36	1303.63	cb " " " " "	
21+55			8.0	1301.0	52' L Floline 18" conc. SD outlet at catch b	
21+81			10.0	1299.0	28' L " " " " inlet " "	
			3.5	1305.5	N.E. ppty corner	
			8.2	1300.8	S.E. " "	
22+00			5.99	1303.00		℄
"			7.78	1301.21		28' R gut
"			7.15	1301.84		" cb
"			5.94	1303.05	28' L gut.	
"			5.28	1303.71	" cb	
23+00			5.28	1303.71		℄
"			6.90	1302.09		28' R gut
"			6.29	1302.70		" cb
"			5.20	1303.79	28' L gut.	
"			4.56	1304.43	" cb	
T. P.			5.28	1303.71	T.P.	

Profile
No. ____ Notes Red. ____ Plotted ____ Job No. 1208 Division No. 4
X-Sec. ____ Date ____ Date ____ Survey of Mariposa Avenue
No. ____ Notes Chkd. ____ Checked ____ Survey by Bartlett Notes Jenkins Date 11-27-50
Date ____ Date ____ Map No. ____ Indexed Johnson Date ____

F.B. 1718 PG. 55

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 PG. 56
Job No. 1390 Division No. K
Survey of Mariposa Avenue
Survey by Lanigan Notes Kaiser
Indexed E. C. Johnson Date
Profile No. X-Sec. No.
Plotted Date Checked Date
Notes Red Date Notes Chkd. Date

STATION	B. S.	H. I.	F. S.	ELEV.	Mariposa Street
T.P.	4 98	130869		1308 21	T.P.
23+28			14 6	129[illegible] 1	199' R Floor elev. to House # 376
"			25 1	128[illegible] 6	" basement " " " "
			17 1	1291 6	" ground at S.E. cor. " "
23+60			(F)3 2	131[illegible] 7	184' L elev. of swimming pool drain
24+00			4 17	1304 52	℄
"			5 29	130[illegible] 30	28' R gut
"			5 16	130[illegible] 3	" cb
"			4 14	1304 55	28' L gut
"			3 51	1305 18	" cb
25+00			3 41	1305 28	℄
"			5 04	1303 5	28' R gut
"			4 41	1304 28	" cb
"			3 34	1305 35	28' L gut
"			2 66	1306 03	" cb
26+00			2 57	1306 12	℄
"			4 23	1304 46	28' R gut
"			3 63	1306 06	" cb
"			2 55	1306 14	22' L gut
"			1 92	1306 17	" cb
T.P.			2 56	1306 13	T.P.

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red_____ Plotted_____ Job No. 1227 Division No. V
No._____ Date_____ Date_____ Survey of Marengo Avenue
X-Sec. Notes Chkd._____ Checked_____ Survey by Lanyon & Notes Keuris Date 11-27-50
No._____ Date_____ Date_____ Map No._____ Inked Johnson Date_____

F.B. 1316 PG. 57

STATION	B. S.	H. I.	F. S.	ELEV.	Marengo	Street
T. P	3 49	1309 62		1306 13	T. P	
26+11			10 4	1299 2	16.2' R	Floor elev. of Hse # 412
"			18 4	1291 2	" basement	" " " "
			17 4	1292 2	18.9' R ground elev. S.W. cor.	" "
27+00			2 68	1306 94		℄
"			4 40	1305 22		28' R. gut
"			3 69	1305 93		" cb
			2 66	1306 96	28' L gut	
			2 00	1307 62	" cb	
T. P.			2 69	1306 93	T. P.	
	4 56	1311 49				
27+91			13 8	1297 7	16.2' R. Floor elev. Hse # 444	
"			21 9	1289 6	basement " "	
			18 0	1293 5	17.8' R ground elev. rear of house	44
> See page 58 for 28+00						℄
29+00			3 00	1308 49		
"			4 73	1306 76		28' R gut.
"			4 08	1307 41		" cb
"			2 94	1308 55	28' L gut.	
"			2 29	1309 20	" cb.	
30+00			2 24	1309 25		℄
"			3 83	1307 66		28' R gut

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ X-Sec. No. ____

Notes Red. ____ Date ____ Plotted ____ Date ____

Notes Chkd. ____ Date ____ Checked ____ Date ____

Job No. 1390 Division No. V

Survey of Maywood Avenue

Survey by Langan Notes Lewis

Indexed R. C. Johnson

F.B. 1718 PG. 58

STATION	B. S.	H. I.	F. S.	ELEV.	Matilda	Street
29+00		1311 49	3 20	1308 29		28' R cb
"			2 13	1309 36	28' L gut	
"			1 47	1310 02	" cb	
T.P.			2 23	1308 26	T.P.	
	4 69	1313 95				
28+00 OK	out of line		6 22	1307 73		
"			7 91	1306 04		28' R gut.
"			7.28	1306 67		" cb
"			6 23	1307 72	28' L gut.	
"			5 57	1308 38	" cb.	
30+21			6 25	1307 70		28' R gut at grade b+k.
"			5 58	1308 37		cb " " "
30+52.2			6 67	1307 28		28' R gut at ret. (no cb - driveway)
			8 95	1305 00	gut. S and SW cb	ret
			8 21	1305 74	cb " " " "	"
			4 02	1309 93	gut W and N.W. cb	ret
			3 35	1310 60	cb " " " "	"
			2 18	1311 77	gut N. " " "	"
			1 59	1312 36	cb " " " "	"
			1 8	1312 3	NW Poly cut	
			8 5	1305 5	SW " "	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Mariposa Street
30+96.06		1313 95	4 05	1309 90	℄ int. Mariposa & Santa Anita Ave
			11 25	1302 70	100' S'l'y
			040	1313 45	60' N'l'y
			835	1305 60	gut Sand SE cb ret.
			772	1306 23	cb " " " " "
			606	1307 89	gut E " " " "
			542	1308 53	cb " " " " "
			6 9/10	1307 1/10	SE ppty cor
			0 4/10	1313 6/10	NE " "
			175	1312 20	gut, N and NE cb ret.
			109	1312 86	cb " " " " "
			310	1310 85	gut E " " " "
			243	1311 52	cb " " " " "
31+56.9			29.0	1311 05	31' L. Floline 18" conc. pipe in catch basin
T.P.			3.65	1310 50	BM AE 466 elev. 1310.487
	4.02	1314 52			
31+62			12 0/10	1302 5/10	146' R. Floor elev. Nse # 520
"			14 7/10	1299 8/10	165' R ground at SW cor " "
32+00			4.22	1310 30	℄
"			5.81	1308 71	28' R. gut
"			5.16	1309 36	" cb

Profile
No. ____ Date ____
X-Sec.
No. ____ Date ____
Notes Red. ____ Date ____
Notes Chkd. ____ Date ____
Plotted ____ Date ____
Checked ____ Date ____
Job No. 1393 Division No. ____
Survey of Masonite Avenue
Survey by Lewis Notes Lewis Date 11-27-58
Map No. ____ Date ____
F.B. 1718 PG. 5-9

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 PG. 60
Job No. 1390 Division No. V
Survey of Manchester Avenue
Survey by Lovigan Notes C. Johnson Date: [illegible]
Indexed
Profile No. Platted Date Checked Date
X-Sec. No. Notes Red. Date Notes Chkd. Date

STATION	B. S.	H. I.	F. S.	ELEV.	Manchester Avenue	
32+00		1314 52	417	1310 35	28' L gut	
"			350	1311 02	" cb	
32+93.6			11 [illegible]	130[illegible] [illegible]	126' R. Floor elev. Hse #534	
"			15 8	129[illegible] [illegible]	186' " ground at SW. Cor. Hse. #534	
33+00			388	1313 64		℄
"			551	1309 01		28' R gut
"			485	1309 [illegible]7		" cb
"			377	1310 75	28' L gut	
"			314	1311 38	" cb	
T.P.			388	1310 64	T.P.	
	4 62	1315 26				
34+00			425	1311 01		℄
"			587	1309 39		28' R gut
"			523	1310 [illegible]3		" cb
"			426	1311 00	28' L gut	
"			358	1311 [illegible]8	" cb	
35+00			390	1311 [illegible]6		℄
"			557	1309 [illegible]9		28' R gut
"			492	1310 34		" cb
"			393	1311 33	28' L gut	
"			326	1312 00	" cb	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ Notes Red. ____ Plotted ____ Job No. 1393 Division No. V F.B. 1778 PG. 61
X-Sec. No. ____ Notes Chkd. ____ Checked ____ Survey of Alterations Notes Kewitt Date 11-27-50
Date ____ Date ____ Date ____ Survey by Bauman Map No. ____ Date ____

STATION	B. S.	H. I.	F. S.	ELEV.	Mariposa Street
35+00		1315 26	10 8	1326 1	190' L ground
35+12 6			11 8	1303 5	146' R Floor level Hse # 560
"			17 0	1298 3	" ground at SW cor. " "
35+49			19 9	1295 4	170' R elev. elr. basement " "
36+00			3 65	1311 61	℄
"			5 22	1310 04	28' R gut
"			4 61	1310 65	" cb
"			3 60	1311 66	28' L gut.
"			2 96	1312 30	" cb.
37+00			3 26	1312 00	℄
"			4 88	1310 38	28' R gut
"			4 24	1311 02	" cb
"			3 28	1311 98	28' L gut
"			2 64	1312 62	" cb
T. P.			3 26	1312 00	T. P.
	4 67	1316 67			
37+42			11 4	1305 3	146' R Floor elev. Hse # 560
"			19 5	1297 2	152' R ctr basement " "
"			17 2	1299 5	185' R ground at rear " "
38+00			4 36	1312 31	℄
			6 00	1310 67	28' R gut

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ___ X-Sec. No. ___
Plotted ___ Date ___ Checked ___ Date ___
Notes Red. ___ Date ___ Notes Chkd. ___ Date ___
Division No. ___
Job No. 1390 Notes Aerial
Survey of Watering 90 Avenue
Survey by Monigan
Indexed J. C. Johnson
F.B. 1718 PG. 62

STATION	B. S.	H. I.	F. S.	ELEV.	Mariposa	Street
38+00		1316 67	534	1313 33		28' R cb
"			436	1312 31	28' L gut	
"			373	1312 94	" cb	
38+71			594	1310 73	28' R. gut at end of curb on Mariposa	
			526	1311 41	" " " "	
			661	1310 06	gut W end SW cb not (in driveway)	
			897	1309 70	gut S " " " "	
			835	1309 32	cb " " " " "	
			374	1313 13	gut W " NW " "	
			310	1313 77	cb " " " " "	
			208	1314 59	gut N " " " "	
			142	1313 25	cb " " " " "	
			09	1313 8	NW ppty cor	
			7 5	1313 8	SW " "	
				1312 31	℄ int. Mariposa St & Santa Rosa Ave.	
			1126	1309 11	℄ Santa Rosa 100' S'l'y	
			014	1316 93	" " 60 N'l'y	
			504	1311 53	℄ Mariposa St 100' E'l'y	
			374	1312 93	BM AE 147 Elev. 1312.938 FB 1447 P. 56 Santa Rosa Ave + Mariposa St. NE cor. Bt spk in cb. 1' E of E end C.R.	

BM AE 147

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Marengo Ave
W.O. 1390 Tape No. Std. 1-ft
Surveyed by J. J. Lanigan
Noted J.J.L. Date 11-22-50
Indexed Co. Engineer

F. B. 1718 PG. 63

Feb 20 '51

Notes: Any Additions or Changes on This Sheet Must be Noted or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
720 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION of IMPROVEMENTS on SCRIPPS LANE from MARIPOSA ST. to FOOTHILL BLVD.

C.I. 1390

J. J. Lanigan
C. H. Lewis
H. H. Raphael
E. W. Evans

7st 2098 247 10M 1-49

F. B. 1719 PG. 64

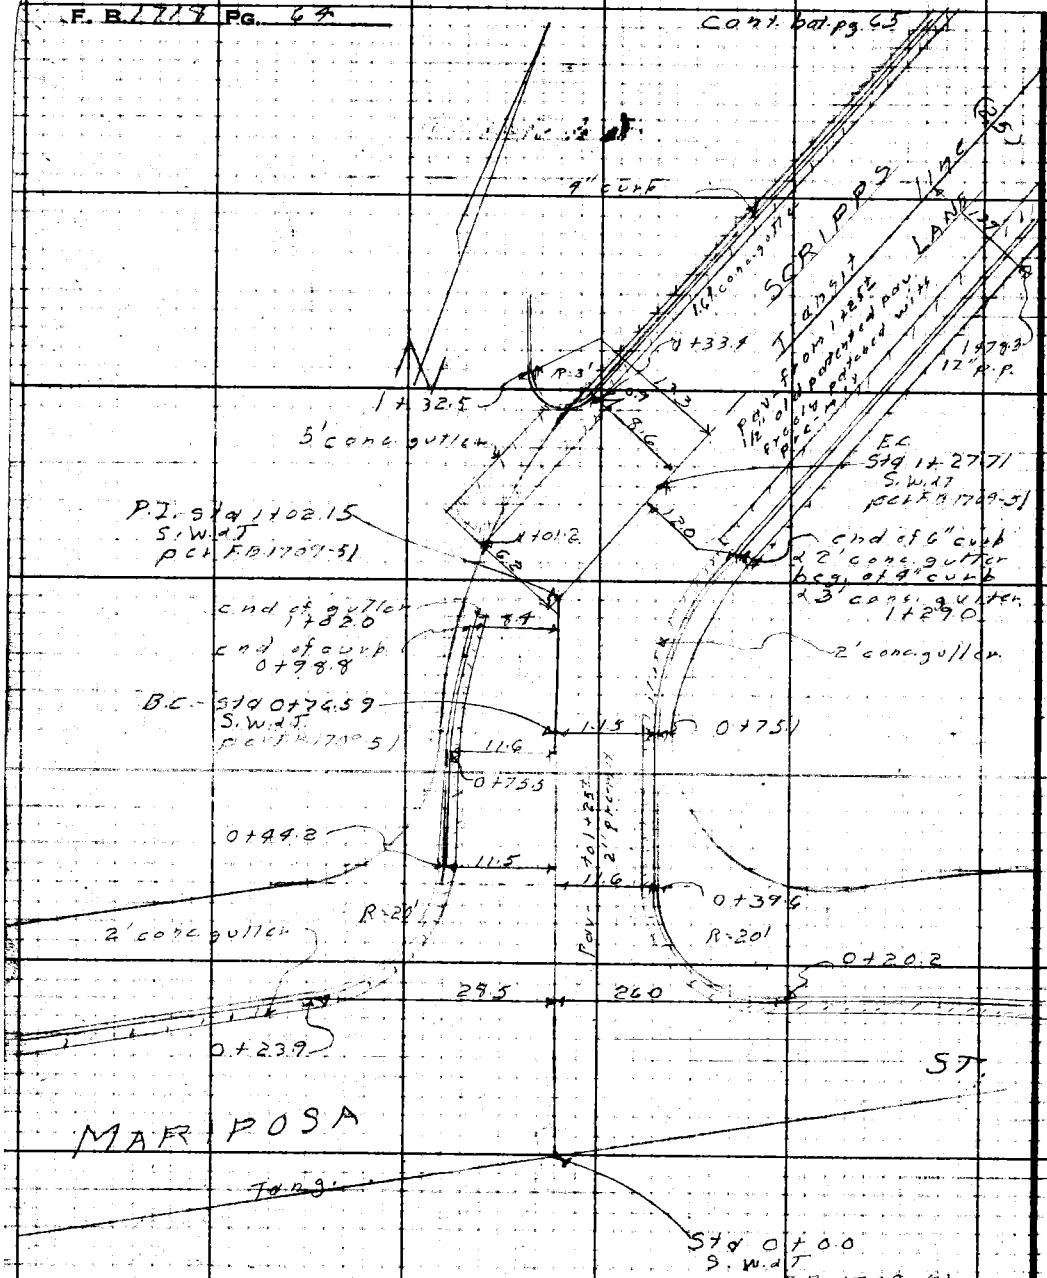

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made & Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Materge Ave.
W.O. 32[illegible] Tape No. Std. by
Surveyed by J.J. Lamigan
Noted J.J.L. Date 11-4-50
Indexed G. Johnson

F. B. 1778 Pg. 65

Notes: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los ANGELES COUNTY
ENGINEERING BLDG.

FOOTHILL BLVD.

Sta 6+88.15
spl. d w
Acme 21702-19

6+92.4
25.1
30.4
6+33.9
edge pvmt
11.4
18.0
edge pvmt
R 10+7
end of curb & gutter
6+27.9
7.8
12.3
end of curb & gutter
6+29.5
6+20.5
6+44.4
2' conc. arch culvert
approx. line
5+95.5
13.7
15.3
1.9 P.P. 5+91.9
5+81.3
166.5
42.0
39.4
5+78.2
no #210 Foothill Blvd.
54.0
LANE
16.5.5
house has basement - unable to enter
unable to locate outlet
12" corr. metal pipe culvert
93.1
24.3
house
27.0
93.7
5+06.0
same
12" corr. metal pipe culvert
172.5
basement has plumbing
51.0
101.0
3+69.8
21.0
2 bathrooms
1 laundry unit
in basement
8.5
TRIPPS
83.0
63.0
156.5
3+27.0
68.8
3+00.0
2+81.0
3' conc. gutter
(25)
2+78.0
6' open stone gutter
cont. top pg 69

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

F. B. 1773 Pg. 66

Profile No. | Notes Red. [illegible] | Plotted | Job No. 1393 | Division No. V | F.B. 1718 | Pg. 67
Date 11-28-50 | Date | Survey of Montenegro Ave.
X-Sec. No. | Notes Chkd. LCM | Checked | Survey by Lanigan | Notes Lewis | Date 11-28-50
Date 12/29/50 | Date | Map No. [illegible] Johnson | Date Feb 20 '51

PROFILE
and
CROSS-SECTIONS
of
SCRIPPS LANE
from
MARIPOSA STREET
to
FOOTHILL BLVD
C.I. 1390

J.V. Lanigan
C.H. Lewis
H.H. Raphael
E.W. Evans

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

76L298 307 5-49

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 PG. 68 | Job No. 1390 Division No. V | Profile No. | Plotted Date | X-Sec. No. | Notes Red. Date | Notes Chkd. Date | Checked Date

Survey of Mariposa Ave.

Survey by Lenigan Notes Lewis Date

Indexed L.C. Johnson Date

STATION	B. S.	H. I.	F. S.	ELEV.	Scripps	Lane
BM AE 474	10 62	1306 46		1295 84	BM-AE 474 Elev. 1295.838 F.B. 1568 P 110	
					Mariposa St & Scripps Lane NW. cor	
					Bt spk in curb 5' W of W. end c.R.	
0+00			9 25	1296 81	℄ int. Scripps lane & Mariposa St (Tangent)	
0-36			10 95	1295 51	gut on ℄ prod of Scripps lane	
"			10 26	1296 20	cb " " " " " "	" "
0+24			9 33	1296 13	cross-gutter on ℄	" "
			8 41	1296 05	gut E end NE cb. ret.	
			7 77	1296 -9	cb " " " " "	
			8 12	1295 34	gut N " " " "	
			7 57	1295 89	cb " " " " "	
			11 00	1295 46	gut W " NW " "	
			10 32	1295 14	cb " " " " "	
			9 15	1295 31	gut N " " " "	
			8 69	1295 77	cb " " " " "	
0+98 ±			6 33	1300 13	84'L gut at end of curb	
"			583	1300 63	" cb " " " "	"
1+33 ±			4 29	1301 17		℄
"			4 81	1301 65		12° R. gut
"			4 28	1301 18		" cb
"			500	1301 46	8.6' L gut.	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Scripps	Lane
1+33 4		1306 46	4 56	1301 90	8.6 L cb	
2+00			0 23	1306 23		℄
"			0 69	1305 77		12' R gut
"			0 19	1306 27		" cb
"			0 72	1305 74	8' L gut	
"			0 22	1306 24	" cb	
T. P.			0 22	1306 24	T. P.	
	10 39	1316 63				
3+00			4 26	1312 37		℄
"			4 80	131 183		12' R gut
"			4 34	1312 29		" cb
"			4 72	1311 91	8' L gut	
"			4 29	1312 34	" cb	
"			4 3	1312 3	14' L top brk	
"			5 7	1310 9	16' L bot brk	
"			11 2	1305 4	71' L Flo-line of ditch	
"			8 0	1308 6	68' L Top of ditch bank	
3+20			3 8	1312 8	220' L ground at low corner (S.W.) of HS	
3+53			8 3	1308 3	188' L ctr basement with plug	

Profile
No. ____ Notes Red. ____ Plotted ____ Job No. 1390 Division No. V
X-Sec. Date ____ Date ____ Survey of Marengo Avenue
No. ____ Notes Chkd. ____ Checked ____ Survey by Kanigan Notes Lewis Date 11-28-50
Date ____ Date ____ Map No. ____ Checked by Lane Date ____

F.B. 1718 PG. 69

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK. WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 Pg. 70 | Job No. 1390 Division No. | Profile No. | X-Sec. No.
Survey of Marengo Avenue | Plotted | Notes Red | Date | Checked | Notes Chkd. | Date | Date
Survey by Lantgy Notes Lewis
Indexed K. C. Johnson Date

STATION	B. S.	H. I.	F. S.	ELEV.	Sewers	Lane
3+44 -		1316 63		1301 9	127'R ctr basement of Hse. with bldg.	
T.P.			026	1316 37	T.P.	
	6 24	1322 61				
4+00			442	1318 19		℄
"			446	1318 15		12'R gut
"			395	1318 66		" cb
"			460	1318 01	8'L gut	
"			412	1318 49	" cb	
T.P.			136	1321 25	T.P.	
	7 49	1328 74				
5+00			450	1324 24		℄
			481	1323 93		12'R gut
			440	1324 34		" cb
			491	1323 83	8'L gut	
			438	1324 36	" cb	
			4 5/8	1324 3	13'L blk. top	
			6 1/8	1323 2	17'L " bot	
			9 1/8	1319 2	45'L E bank of ditch	
			14 3/8	1314 2	52'L Flowline " "	
			11 3/8	1317 2	93'L ground at SE cor Hse.	
5+06			10 4/8	1318 2	" Floor elev. "	" "
"						

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Setting	Lane
T. P.		1328 74	0 06	1328 68	T. P.	
	298	1331 66				
5+47			+1 2	1333 4	165' R. Floor elev. of	
			0 2	1331 5	ground at SW cor. show cor.	
6+00			1 67	1329 99		
"			2 05	1329 61		12' R. gut
"			1 62	1330 04		" eb.
"			2 21	1329 45	8' L gut	
"			1 78	1329 88	" eb.	
5+78 2			8 6	1323 1	39.4 L. Top E bank of ditch	
"			13 1	1318 6	43' L Flowline of ditch	
5+95 5			7 2	1324 5	13.7 L. " of conc. arch culvert	
T. P.		1	1 66	1330 00	T. P.	
	8 95	1338 95				
			8 07	1330 88	gut S end SE eb ret.	
			7 64	1331 31	eb " " " " "	
			7 49	1331 46	gut at end of eb	
			6 99	1331 96	eb " "	
			8 45	1330 50	gut S " " SW eb ret.	
			8 02	1330 93	eb " " " "	
			7 46	1331 49	gut at end of eb.	

Profile No. ____ Notes Red. ____ Plotted ____ Job No. 13 [illegible] Division No. 11
X-Sec. No. ____ Notes Chkd. ____ Checked ____ Survey by Lentzen Notes Lewis Date 1/28-5
Date ____ Date ____ Date ____ Survey of Manzanita Avenue
Date ____ Date ____ Date ____ Map No. [illegible] Date ____

F.B. 1778 PG. 71

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK. WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 PG. 72
Job No. 1390 Division No. V Notes Red. Plotted Profile No.
Survey of Maywood Acres Date Date X-Sec.
Survey by Louis Notes Chkd. Checked
Notes Lewis
J. C. Johnson Date Date
Indexed Date

STATION	B. S.	H. I.	F. S.	ELEV.	Scripps	Lane
		1338.95	7.02	133[illegible].93	cb at end	
			4.70	133[illegible].25	℄ int. Scripps Lane & Foothill Blvd	
			3.75	133[illegible].20	10.2' E'l'y on ℄ of	" "
			4.27	133[illegible].68	" W'l'y " " "	" "
BMAE258			5.26	1333.69	BMAE 258 Elev. 1333.714 FB 1447-237	
					Foothill Blvd. & Scripps Lane. [illegible]	
					12" spt in cb 1.5' E of W end.	

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Marengo Ave.
W. O. 1781 Tape No. Std. °F
Surveyed By J. J. Lonigan
Notes J. J. L. Date 7-23-52
Indexed C. Johnson

F. B. 1718 PG. 73

LOCATION
of
IMPROVEMENTS
on
FOOTHILL BLVD.
(SOUTH ROADWAY)
from
FAIR OAKS AVE.
to
WESTERLY LINE LOT "58" - TRACT "13971
C.J. 1390

J. J. Lonigan
C. H. Lewis
H. H. Raphael
E. W. Evans

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County
ENGINEERING BLDG.

76F3098 247 10M 1-49

F. B. 1718 Pg. 14 cont. bet. sta. 7.5

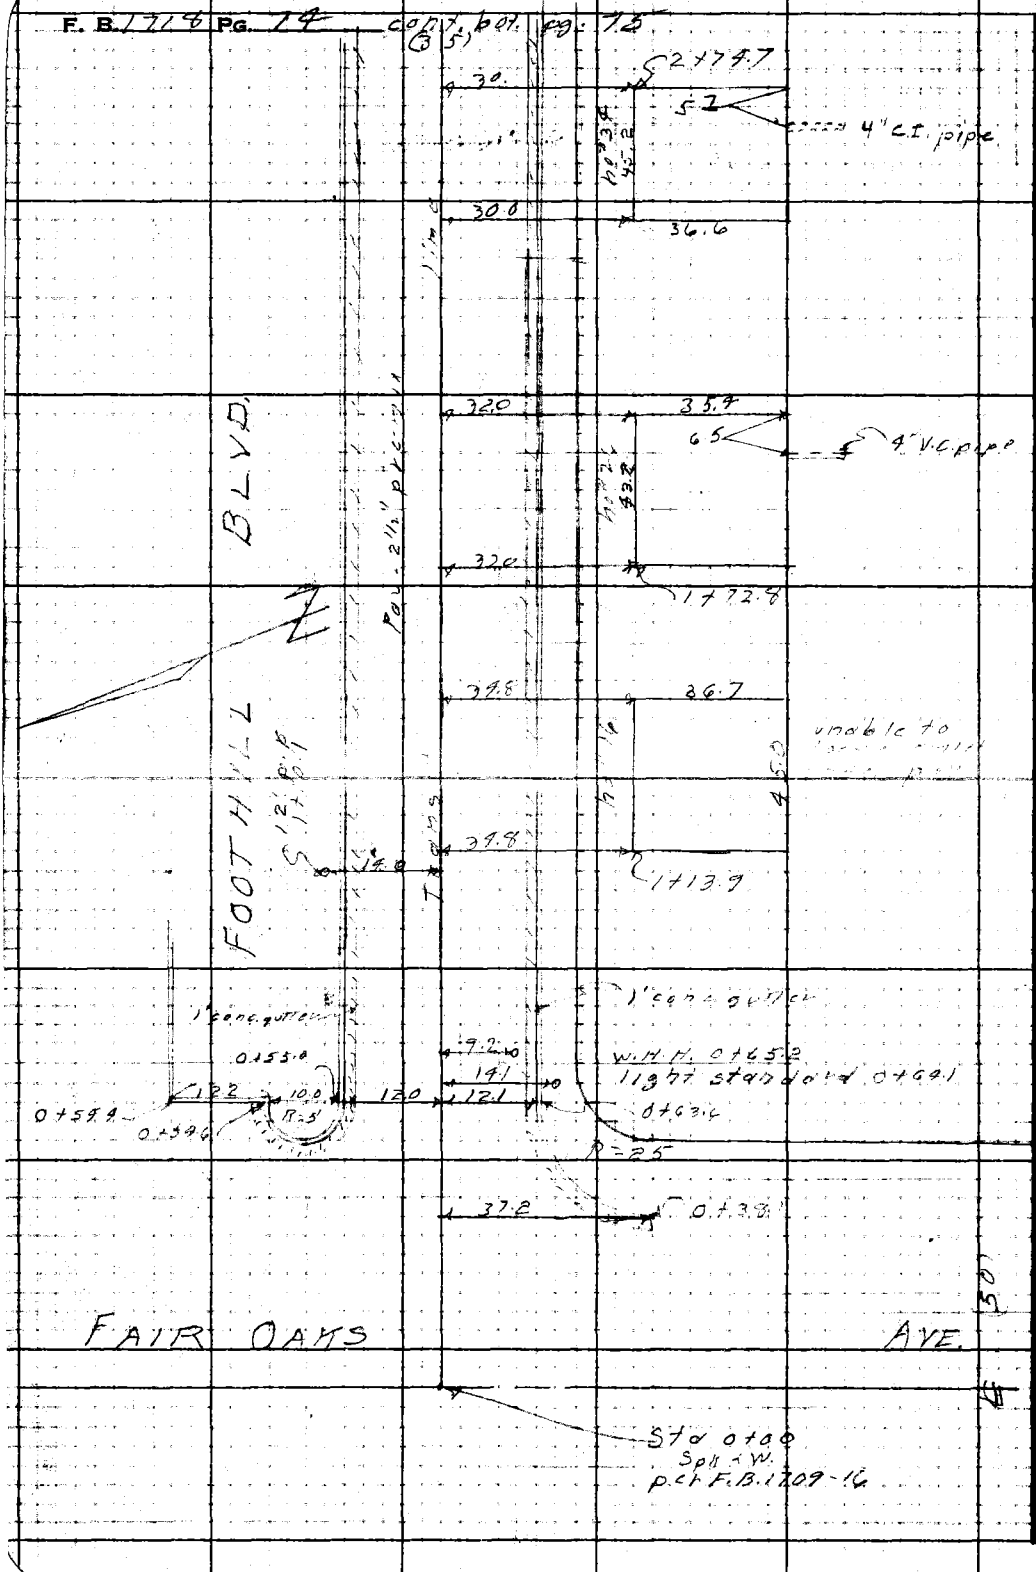

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

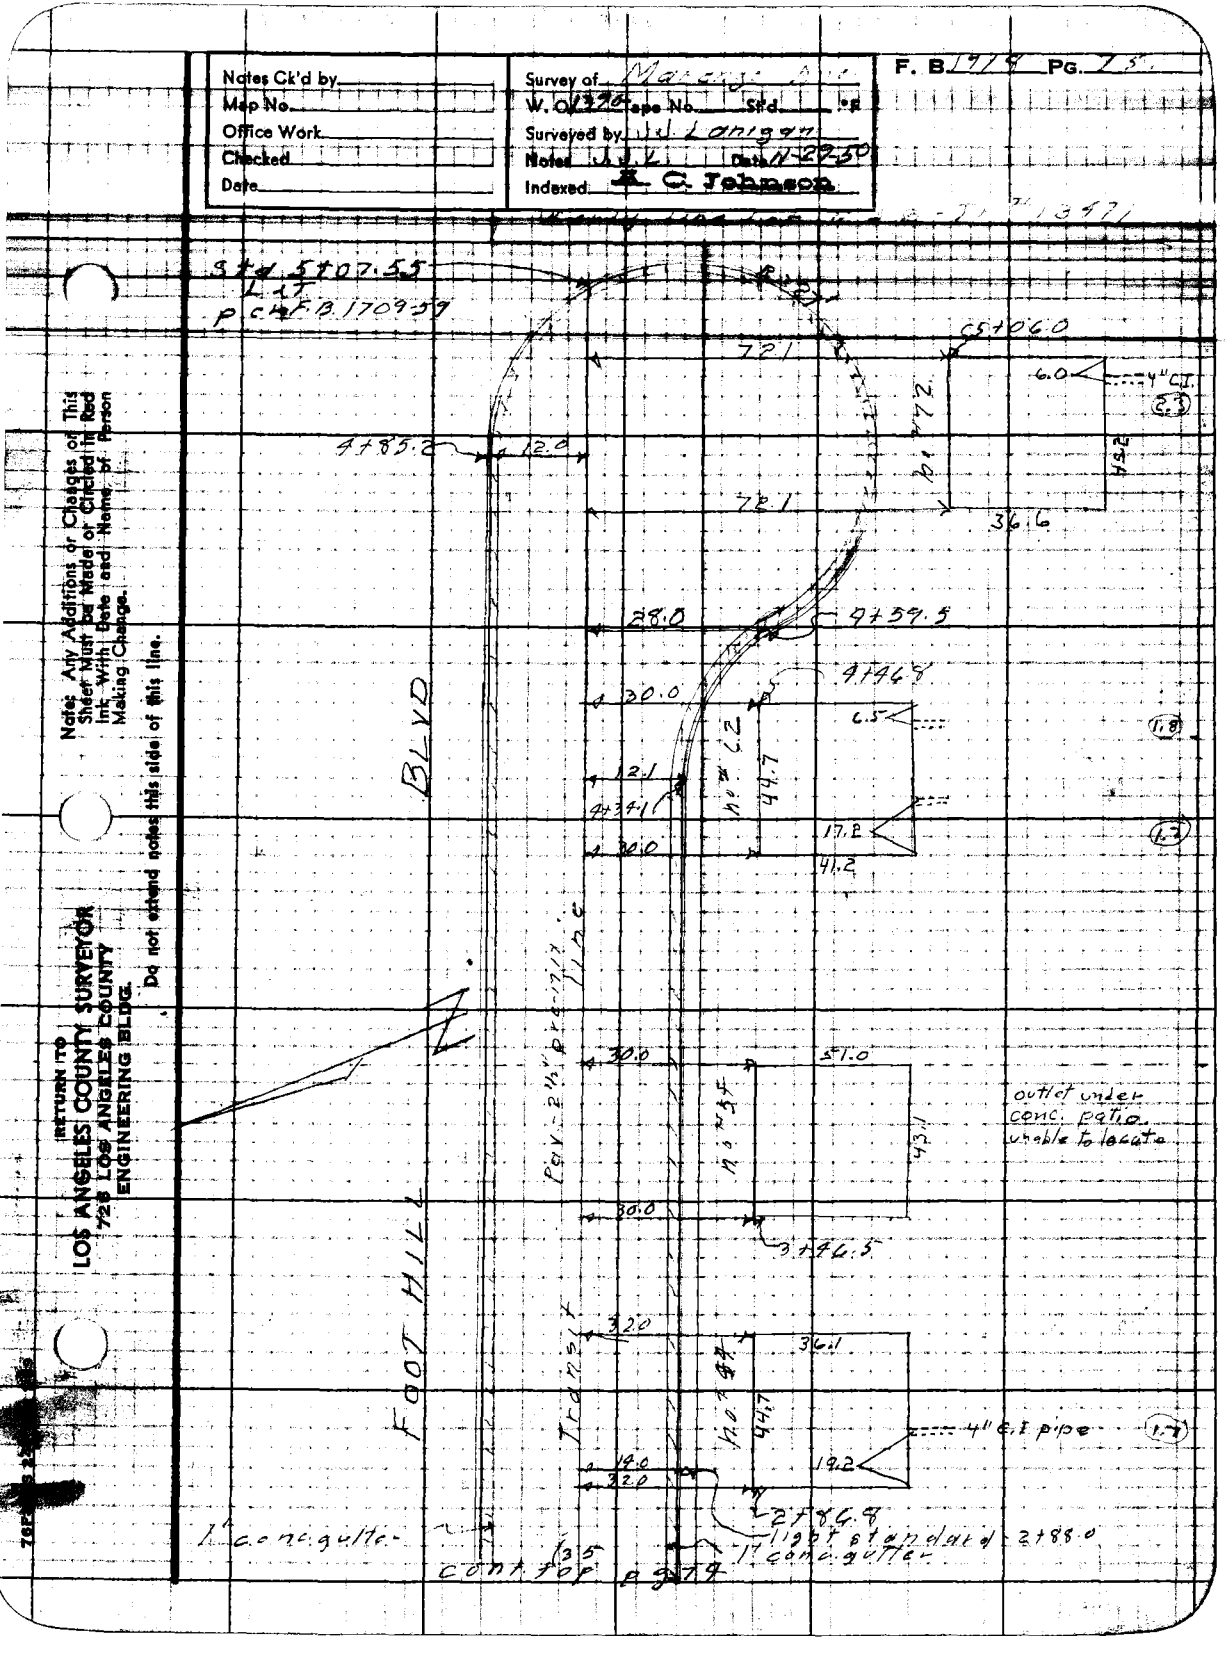
Notes Ck'd by
Map No.
Office Work
Checked
Date
Survey of
W. O.
Tape No.
Std.
Surveyed by
Noted
Date
Indexed
F. B.
PG.
Note: Any Additions or Changes of This Sheet Must be Made or Checked in Red Ink With Date and Name of Person Making Change.
Do not extend notes this side of this line.
RETURN TO
LOS ANGELES COUNTY SURVEYOR
728 LOS ANGELES COUNTY
ENGINEERING BLDG.
BLVD
FOOT HILL
Transit
Pav. 2½" A.C. on 6" C.R.B.
outlet under conc. patio. unable to locate
4" C.I. pipe
conc. gutter
conc. gutter
cont. on p.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

F. B. 1717 Pg. 24

Profile No. | Notes Red. | Plotted | Job No. 1390 | Division No. V | F.B. 1718 PG. 77
Date | Date | Survey of Makenzo Avenue
X-Sec. No. | Notes Chkd. LCM | Checked | Survey by Lanigan | Notes Lewis | Date 11-29-50
Date 12/29/50 | Date | Map No. | Indexed | Date FEB 20 '51

PROFILE
and
CROSS-SECTIONS
of
FOOTHILL BLVD. (SOUTH RDWY.)
from
FAIR OAKS AVENUE
to
WESTERLY LINE OF LOT # 58 · TRACT # 13471
C.I. 1390

J.J. Lanigan
C.H. Lewis
H.H. Raphael
E.W. Evans

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

761.298 307 5-49

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 Pg. 78 | Job No. 1390 Division No. V | Profile | No. | Plotted | Date | X-Sec. | No. | Date

Survey of Foothill Blvd. | Notes Red. | Date | Checked | Date

Survey by Lewis & Notes Lewis | Notes Chkd. | Date

Indexed R. C. Johnson Date

STATION	B. S.	H. I.	F. S.	ELEV.	Foothill	Blvd.
BM AE 255	3 76	1330 99		1327 23	BM AE 255 Elev. 1327.232 F.B. 1447 P. 236	
					Foothill Blvd. + Fair Oaks Ave. at ℄ Int.	
					Los Angeles County Survey Control System Traverse Station	
					Altadena Bl. in hand hole, 2 mon. 12"	
0 + 00			6 01	1324 98	℄ Int	
			11 93	1319 06	℄ Fair Oaks 90° S'ly	
			9 27	1322 72	gut S. end SE CB Int	
			8 63	1322 36	" " " " " "	
			8 32	1322 67	gut E " " " "	
			7 63	1323 36	cb " " " " "	
			8 1	1323 3	ppty line at " " "	
			6 88	1324 11	gut E end NE " "	
			5 97	1325 02	CB " " " " "	
			6 23	1324 76	gut N " " " "	
			5 48	1325 51	cb " " " " "	
0 + 90			7 04	1323 95		℄
"			8 15	1322 84		12' R gut
"			7 52	1323 47		" cb
"			6 82	1324 17	12' L gut	
"			5 83	1325 16	" cb	
			13 [illegible]	1317 [illegible]	Sur on Lot # 2	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. 1332 Division No. V
No. Date Date Survey of Maclay Ave. Assessment
X-Sec. Notes Chkd. Checked Survey by Lewis Notes Lewis Date 11-29-55
No. Date Date Map No. Checked Date

F.B. 1718 PG. 79

STATION	B. S.	H. I.	F. S.	ELEV.	Foothill Blvd	South Roadway
1+13		1330 99	11 2	1319 8	72' R. ground at Low cor. (S.W.) Hse #16	
			8 3	1322 8	35' " Floor elev.	" "
T.P.			642	1324 57	T.P.	
	735	1331 92				
			14 9	1317 0	S.W. cor Lot #3	
2+00			736	1324 56		
"			845	1323 47		12' R gut
"			781	1324 11		" cb
"			701	1324 91	12' L gut	
"			602	1325 90	" cb	
2+16			13 0	1318 9	68' R. ground at Low cor (St.) Hse #26	
2+10			14 8	1317 1	" elev. of 4" C.O. pipe at outlet	
			9 0	1322 9	Floor elev. Hse #26	
T.P.			735	1324 57	T.P.	
	780	1332 37				
			15 5	1316 9	S.W. cor. Lot #4	
2+29			12 9	1319 5	67' R gr. Low cor. (S.W.) Hse #34	
"			9 1	1323 3	" Floor elev.	" "
2+34 ? (2469)			12 2	1320 2	" Elev. on 4" CI. pipe	" "
T.P.			717	1325 20	T.P.	
	835	1330 55				

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 Pg. 80 | Job No. 1390 | Division No. 4 | Profile No. | X-Sec. No.
Survey of Altadena
Survey by Lewis & Johnson Date
Indexed K.C. Johnson Date
Notes Red. Date
Notes Chkd. Date
Checked Date

STATION	B. S.	H. I.	F. S.	ELEV.	Foothill Blvd.	(South roadway)
		1330 55 ✓	13 9	1316 7	SW cor Lot # 5	
2+86			10 7	1319 9	68'R ground at low corner (S.W.) Hse. # 44	
			6 9	1323 7	" Floor elevation	" "
3+06			12 5	1318 1	" Elev. 4" C.I. pipe outlet	" "
3+00			536	1323 19		
"			652	1324 33		12'R gut
"			587	1324 68		" cb
"			495	1325 60	12'L gut	
"			402	1326 53	" cb	
T.P.		✓	578	1324 77 ✓	T.P.	
	6 11	1330 88				
			13 6	1317 3	SW cor lot # 6	
3+46 5			10 9	1320 2	81'R ground at low corner Hse # 54 (S.W. cor.)	
"			6 8	1322 1	" Floor elevation	" "
4+00			508	1325 80		
"			628	1324 60		12'R gut
"			564	1325 24		" cb
"			471	1326 17	12'L gut	
"			368	1327 20	" cb	
T.P.		✓	508	1325 80 ✓	T.P.	
	5 56	1331 36				

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. Notes Red. Date Plotted Job No. 1260 Division No. V
X-Sec. No. Notes Chkd. Date Checked Survey of Marquise Ave
Survey by Lewis Notes Lewis Date 11-29-56
Map No. Indexed Tab Jacobs Date F.B. 1716 PG. 81

STATION	B. S.	H. I.	F. S.	ELEV.	Foothill Blvd.	South Roadway
		1331 36	13 2	1318 2		S.W. cor. Lot # 7
			5 8	1325 6	36' R	Floor elev. Hse # 62
4+02			10 4	1321 0	73' R	ground at house cor. " " (S.W. cor.)
4+19			11 9	1319 5	"	elev. on Westerly 4" C.I. flow. Hse # 62
4+40			11 8	1319 6	"	" " " Easterly " " " "
			16 7	1314 7		S.W. cor. Lot # 8
4+61			10 8	1320 6	109' R	ground at S. willow corner Hse # 72
5+00			13 1	1318 3	"	elev. 4" C.I. inlet & outlet "
			14 7	1316 7		SE cor. Lot # 8
5+00			7 5	1323 9	73' R	Floor elev. Hse # 72.
4+32±			5 29	1326 07		℄
"			6 49	1324 87		12' R gut
"			5 86	1325 50		" cb
4+85 ±			4 60	1326 76		℄
"			4 50	1326 86		12' L gut
"			3 51	1327 85		" cb
5+07			4 80	1326 56		gut at ℄ prod
"			3 91	1327 45		cb " "
BMAE256			800	1323 36	BMAE 256 Elev-1323.341 FB 1447 P 237	
					Foothill Blvd (S. rdwy) & Fair Oaks Ave. SE cor.	
					Bt. spk in comb. 1' E of E and C.R.	

1715 Pg. 82 | Job No. 1390 | Division No. V | Notes Red. | Plotted | Profile

Survey of Malezzo Ave. | Date | Date | No.

Survey by Lonigan | Notes Lewis | Notes Chkd. | Checked | X-Sec.

Indexed | Date | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

76L298 307 5-49

Notes Ck'd by	Survey of Maricopa Ave.
Map No.	W.O. 1378 Tape No. Std.
Office Work	Surveyed by J.J. Lanigan
Checked	Noted J.J.L. Date 11-27-40
Date	Indexed E. C. Johnson

F. B. 1718 PG. 83

FEB 20 01

Notes: Any Additions or Changes of This Sheet Must be Made in Red Ink, With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
of
IMPROVEMENTS
on
MANOR ST
from
FAIR OAKS AVE
to
McNALLY ~~STA~~
C.I. 1390

J. J. Lanigan
C. H. Lewis
H. H. Raphael
E. W. Evans

7-F-2088 847 10M 1-40

F. B. 1719 Pg. 87

Cont. bet. pgs. 85

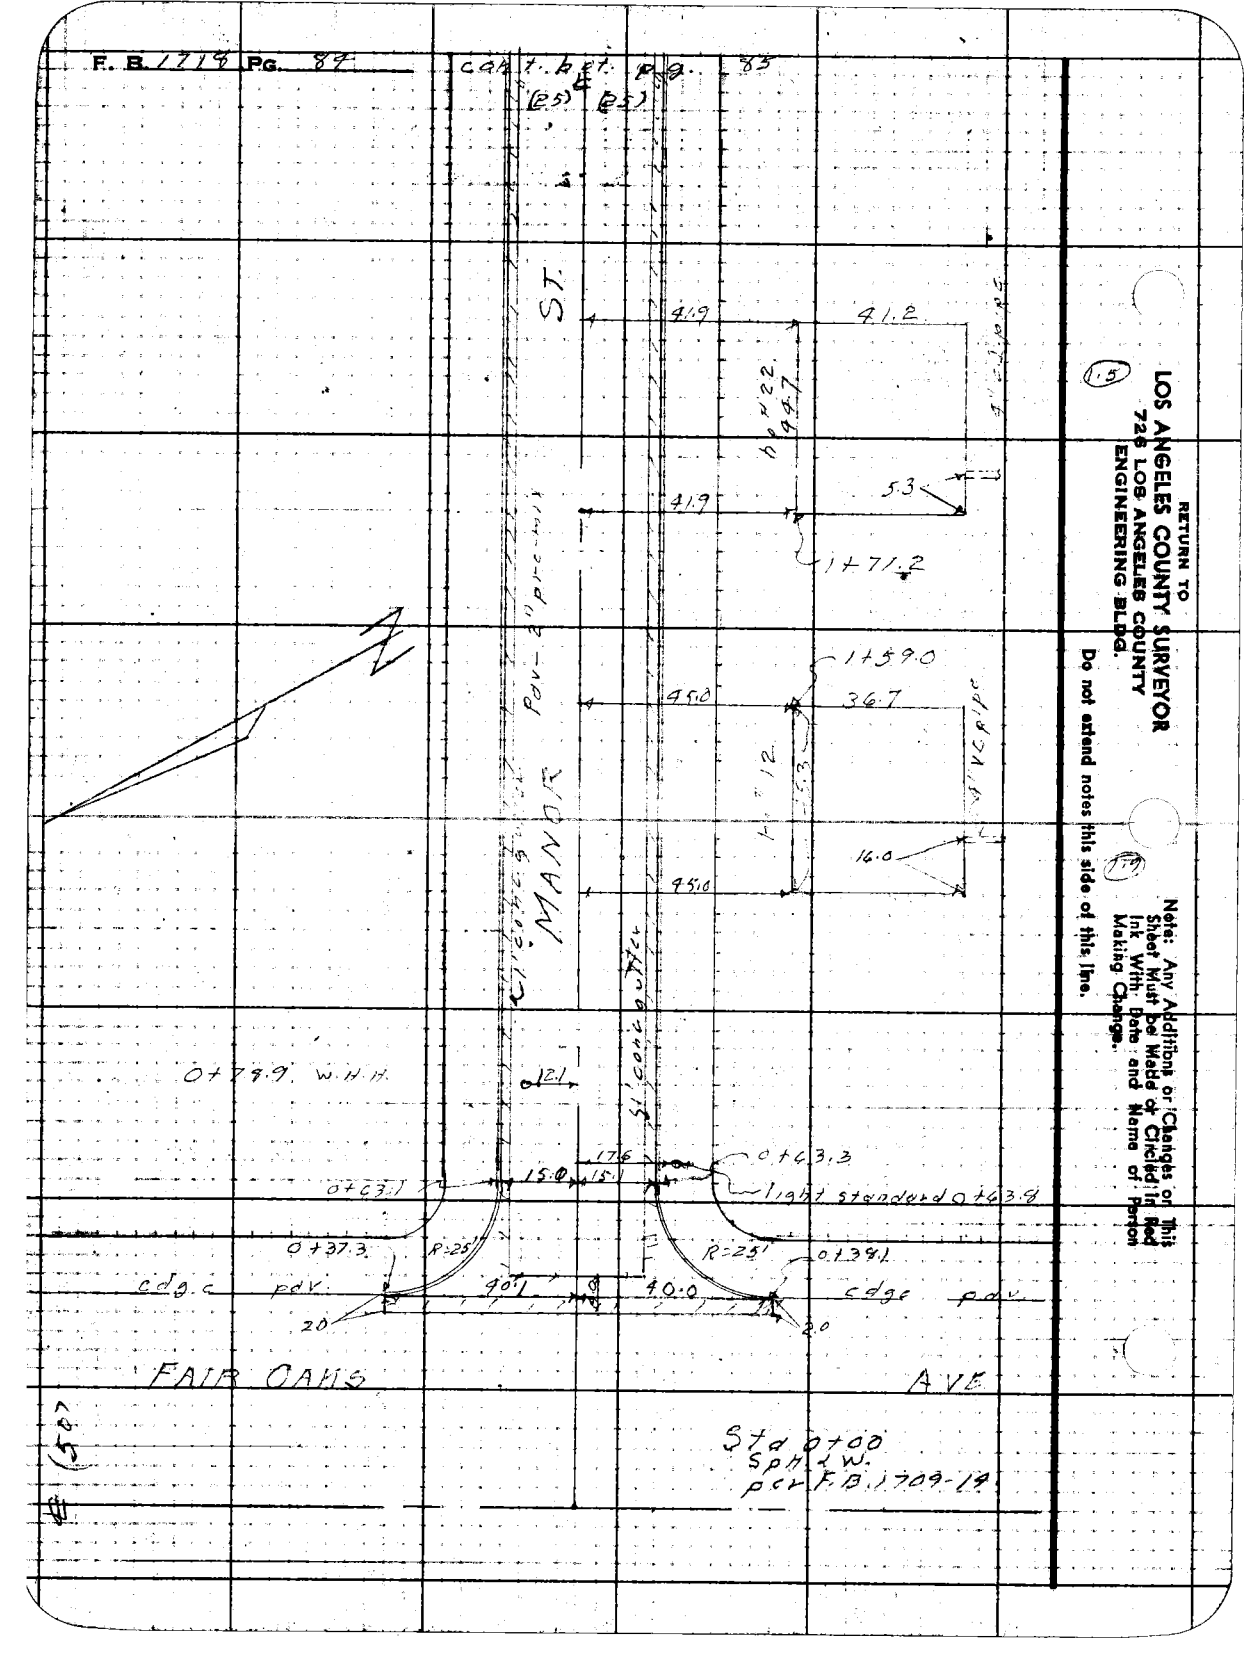

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by	Survey of Marengo Ave.
Map No.	W.O. [illegible] Tape No. Std.
Office Work	Surveyed by J. J. Kanigan
Checked	Noted J.J.K. Date 11-21-49
Date	Indexed A. G. Johnson

F. B. 1779 PG. 85

Notes: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

MENALLY AVE.

MANCHESTER ST.

Sta 3+70.05 SPH. per F.B. 1709-58

unable to locate outlet capped 10" reinforced outlet more than 3' deep

9" C.I. pipe

4" C.I. pipe (located inside wall)

Sta 2+30.9

Sta 2+94.5

Sta 3+89.7

Sta 3+99.7

Sta 3+54.8

Sta 3+21.0

Sta 3+42

Sta 3+18

Sta 3+99

Sta 2+44.6

Sta 2+32

Sta 2+17.6

Sta 2+19.50

Sta 2+39.9

Sta 2+36.7

Sta 2+42.1

Sta 2+35.9

Sta 2+43.6

Sta 2+42.6

Sta 2+39.9

68.8

35.0

98.8

40.0

26.4

42.1

15.0

17.6

39.9

36.7

5.6

4.7

5.0

2.9

R=25

R=40

Sta 2+64.8

Sta 2+64.8

Sta 2+64.8

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

F. B. 7778 PG. 88

Profile No. | Notes Red. | Plotted | Job No. 1390 | Division No.
Date | Date | Survey of Malengo Avenue
X-Sec. No. | Notes Chkd. LCM | Checked | Survey by | Notes | Date 11-30-50
Date 12/29/50 | Date | Map No. | Date FEB 20 '51

F.B. 818 PG. 87

PROFILE
and
CROSS-SECTIONS
of
MANOR STREET
from
FAIR OAKS AVENUE
to
McNALLY AVENUE
CI. 1390

J.V. Lanigan
C.H. Lewis
H.H. Raphael
E.W. Evans

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

76L298 307 5-49

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 Pg. 88. Job No. 4390 Division No. V Notes Red. Plotted Profile
Survey of Highway Surveys Date No.
Survey by Lawson Notes Lewis Notes Chkd. Checked X-Sec.
Indexed A. C. Johnson Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.		
BMAE263	7 36	1296 37		1289 01	BMAE263 Elev. 1289.013 FB1447-244	
					Fair Oaks Ave + Manor St. NW Cor.	
					BT spk in curb 2' N of N end C.P.	
0+00			5 25	1291 12	℄ int Manor & Fair Oaks.	
			10 69	1285 68	℄ Fair Oaks 100' S'ly	
			0 43	1295 94	" " " 80 N'ly	
			8 36	1288 01	gut S and SE cb + at	
			7 69	1288 68	cb " " " " "	
			6 62	1289 75	gut E " " " "	
			5 98	1295 39	cb " " " " "	
0+38			6 14	1290 23	Flo-line ℄ cross-gutter	
			3 91	1292 46	gut N and NE cb + at	
			3 19	1293 18	cb " " " " "	
			5 17	1291 20	gut E " " " "	
			4 50	1291 87	cb " " " " "	
			3 8/5	1292 5	NE pot 30'	
			6 4/5	1290 2	SE " "	
1+00			4 96	1291 41	℄	
"			6 05	1290 32		15' R gut
"			5 41	1290 96		" cb
"			4 98	1291 39	15' L gut	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red _____ Plotted _____ Job No. 1392 Division No. V F.B. 1718 PG. 89
No. _____ Date _____ Date _____ Survey of Manor Engineers
X-Sec. Notes Chkd. _____ Checked _____ Survey by Lewis Notes Lewis Date 11-30-56
No. _____ Date _____ Date _____ Map No. _____ Checked Date _____

STATION	B. S.	H. I.	F. S.	ELEV.	Manor	Street
1+00		1296 37	4 29	1292 08	15'L cb	
T.P.			4 95	1291 42		
	5 65	1297 07				
			12 5	1284 6	S.W. cor Lot # 25	
1+14			9 5	1287 6	ground at low corner Hse # 12	82 ?
"			6 2	1290 9	Floor level	" "
1+30			11 6	1285 5	elev. of 4" C.I. pipe	" " 82'
			11 5	1285 5	SW cor Lot # 24	
1+71 2			8 6	1288 5	ground at low corner Hse # 22	(S.W.
1+76 5			10 1	1287 0	elev. 4" C.I. pipe	" 84'
			6 0	1291 1	Floor elevation	" "
2+00			4 94	1292 13		
			6 04	1291 03		15'R gut
			5.38	1291 69		" cb
			4 99	1292 08	15'L gut	
			4 32	1292 75	" cb	
			11 0	1286 1	S.W. cor. Lot # 23	
T.P.			4 93	1292 14	T.P.	
	5 79	1297 93				
2+71			10 4	1287 5	77'R elev. 4" C.I. pipe	
			6 0	1291 9	Floor elev. Hse # 32	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 PG. 98 · Job No. 4390 Division No. V Notes Red. Plotted Profile No.
Survey of Alley Date Date X-Sec. No.
Survey by Lamb & Gay Notes Lots 1 & 2 Notes Chkd. Checked
Indexed E. C. Johnson Date Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	Marmot	Street
2+31		1297 93	8 7	129 8	77'R ground at Low corner (S.W.) Hse # 32	
			11 1	129 8	S.W. cor Lot # 22	
2+94			8 5	129 4	76'R ground at Low corner (SW) Hse # 42	
			4 7	129 2	Floor elev.	"
2+99			9 7	129 3	76'R elev. on 4" C.I. pipe	"
3+00			5 14	129 79	℄	
"			6 24	129 69		15'R gut
"			5 55	129 38		" cb
"			5 09	129 74	15'L gut.	
"			4.43	1293 50	" cb.	
T. P.			5 14	1292 79	T. P. spk at 3+00 ℄	
	7 66	1300 45				
			14 5	1285 9	S.W. corner of Lot # 21	
3+50			12 3	1288 2	114'R ground at Low corner (S.W.) Hse # 50	
			8 1	1292 4	Floor elevation of	" "
			13 2	1286 2	S.E. corner of Lot # 21	
3+21			7 37	1293 8	℄	
"			8 55	1291 0		15'R gut
"			7 90	1293 3		" cb
			7 04	1291 1	gut W and N.W. cb + ct	
			6 37	1291 4	cb " " "	" "

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Manor	Street
3 + 70		1300 45	5	1294 7	25' L. P.L	
			504	1295 41	gut N and NW cb ret	
			432	1296 12	cb	
3 + 70 05			583	1294 62	℄ int. Manor & McNally	
"			743	1293 02	40' R gut	
"			677	1293 68	" cb	
			604	1294 41	gut on ℄ prod of Manor	
3 + 84 9			417	1296 28	gut 48.8 L	
"			347	1296 98	cb "	
BM AE 486			5.61	1294 84	BM AE 486 Elev. 1294.857 F.B. 1528 - 12	
					McNally Ave. (E. side) at Manor St.	
					Bt spk in cb 12' N & prod Manor St.	

Profile Notes Red Plotted Job No. 1202 Division No. K F.B. 1718 PG. 91
No. Date Date Survey of Alterations & Additions
X-Sec. Notes Chkd. Checked Survey by Lewis Notes Lewis Date 12-1-50
No. Date Date Map No. Checked Johnson Date

Pg. 1718 92 Job No. 1390 Division No. V Notes Red. _____ Plotted _____ Profile

Survey of Marengo Ave Date _____ Date _____ No. _____

Survey by Lanigan Notes Lewis Notes Chkd. _____ Checked _____ X-Sec.

Indexed _____ Date _____ Date _____ Date _____ No. _____

STATION	B. S.	H. I.	F. S.	ELEV.

76L298 307 5-49

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR

726 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Notes Ck'd by	Survey of Alcondo Ave.
Map No.	W. O. 332 Tape No. Std.
Office Work	Surveyed by J. J. Lonigan
Checked	Notes J.J.L. Date Nov 29-50
Date	Indexed A. C. Johnson

F. B. 1714 Pg. 93

FEB 20 51

Notes: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION of IMPROVEMENTS on McNALLY AVE from MANOR ST to TERRACE ST C.I. 1390

J. J. Lonigan
C. H. Lewis
H. W. Raphael
E. W. Evans

76P3098 R47 10M 1-49

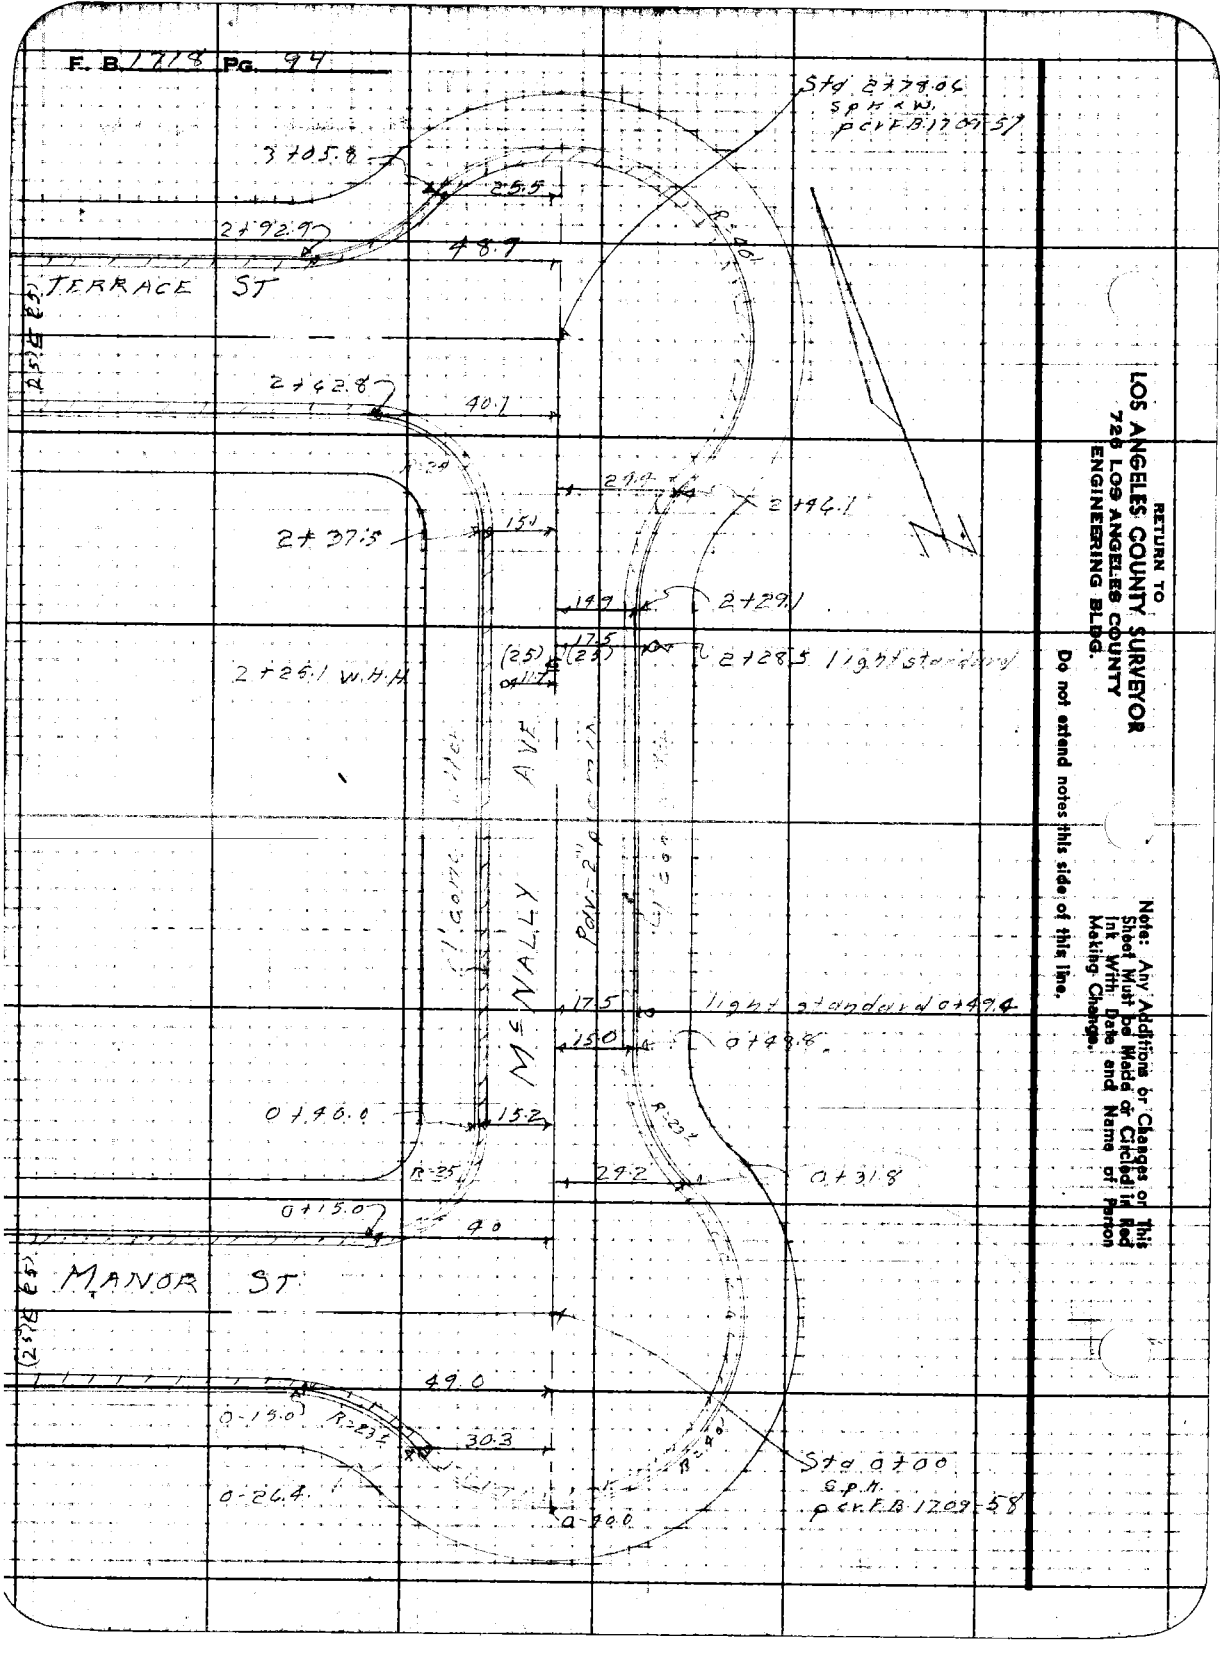

RETURN TO
LOS ANGELES COUNTY SURVEYOR
720 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

Profile No. | Notes Red. | Plotted | Job No. 1390 | Division No. | F.B. 1718 | PG. 95
Date | Date | Survey of McNALLY AVENUE
X-Sec. No. | Notes Chkd. LCM | Checked | Survey by Lanigan | Notes Lewis | Date 12-1-50
Date 12/29/50 | Date | Map No. | Indexed Johnson | Date Jr. 20 '51

PROFILE
and
CROSS-SECTIONS
of
McNALLY AVENUE
from
MANOR STREET
to
TERRACE STREET
C.I. 1390

V.J. Lanigan
C.H. Lewis
M.H. Raphael
E.W. Evans

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

76L298 307 5-49

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ X-Sec. No. ____

Job No. 1290 Division No. V Notes Red. ____ Plotted ____ Date ____

Survey of Marengo Avenue Notes Chkd. ____ Checked ____ Date ____

Survey by Lanigan Notes Lewis Date ____

Indexed E. C. Johnson Date ____

F.B. 771 & PG. 96

STATION	B. S.	H. I.	F. S.	ELEV.	McNally	Avenue
BM AE 486	5.21	1300.47		1295.26	BM AE 486 Elev. 1294.857 F.B. 660-28	
					McNally Ave. @ side of Manor St.	
					St. sta. is 12.5 ± E prod. of Manor St	
0+00			5.85	1294.62	@ int. McNally & Manor St	
0-40			7.45	1297.02	gut at E, prod	
			6.79	1292.68	"	
0+00			6.06	1294.41		40' R. gut
			7.04	1293.43	gut W and NW " "	
			6.37	1294.08	" " "	
			5.06	1294.41	gut N " "	
			4.35	1294.12	" " " "	
0+40			4.02	1294.45	25' L P.L.	
0+48.8			4.19	1296.28		40' R P
			3.49	1294.78	" "	
1+00			1.12	1294.85		
"			1.42	1294.85		15' R gut
"			0.76	1294.71		" "
"			1.80	1294.67	15' L gut	
"			1.13	1294.84	" "	
T. P.			1.10	1294.87	T. P.	
	11.88	1301.25				

/6L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. No. Date Plotted Date Job No. 1220 Division No. V
X-Sec. Notes Chkd. No. Date Checked Date Survey of Metenga Avenue
Survey by Lewis Notes Lewis Date 12-15-52
Map No. Date

F.B. 7178 Pg. 97

STATION	B. S.	H. I.	F. S.	ELEV.	McNally Avenue ℄
2+00		1311.25	6.56	1304.69	
"			6.79	1304.46	15' R gut
"			6.11	1305.14	" cb
"			—	—	
"			7.16	1304.09	15' L gut
"			6.50	1304.75	" cb
"			5.8	1305.5	145' L. back lot line
2+29			5.26	1305.99	15' R gut
"			4.59	1306.66	" cb
2+37.5			5.12	1306.13	gut s end SW cb ret
"			4.48	1306.77	cb " " " " "
"			4.1	1307.2	25' L PL
			3.39	1307.86	gut W end SW cb ret
			2.76	1308.49	cb " " " " "
2+78.06			2.42	1308.83	℄ int McNally & Terrace St
"			3.00	1308.25	40' R gut
3+18			3.28	1308.97	gut on ℄ prod
"			2.56	1309.69	cb " " "
2+92.9			2.39	1308.86	48' L gut
			1.71	1309.54	" cb
			2.62	1308.63	℄ Terrace 100' W'ly

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 Pg. 98
Job No. 1390 Division No. 4 Profile No. X-Sec. No.
Survey of McNally Avenue
Survey by Lawrence & Davis Notes Plotted Date
Indexed R. C. Johnson Date Notes Red. Date Notes Chkd. Date Checked Date

STATION	B. S.	H. I.	F. S.	ELEV.	McNally	Avenue
		1311 25	2 70	1305 55	N gut of Terrace St	100' w'ly
			2 03	1309 22	" cL "	" "
			3 61	1307 64	S gut "	" "
			3 00	1308 25	" cb "	" "
BM AE 487			201	[illegible]	BM AE 487 Elev. 1309.244 FB 1568 P 126	
					100' N'ly Ave. (E. side) at Terrace St.	
					Et. spk in cb 12' N of & prod of Terrace St.	

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Malenge Ave.
W.O. 1330 Tape No. Std. 66
Surveyed by J.J. Lanigan
Noted J.J.L. Date 11-20-50
Indexed C. Johnson

F. B. 1718 PG. 99

LOCATION of IMPROVEMENTS on TERRACE ST. from FAIR OAKS AVE. to McNALLY AVE C.I. 1390

J.J. Lanigan
C.H. Lewis
H.H. Raphael
E.W. Evans

Notes: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not attend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

76F3098 247 10M 1-49

F. B. 1718 Pg. 100

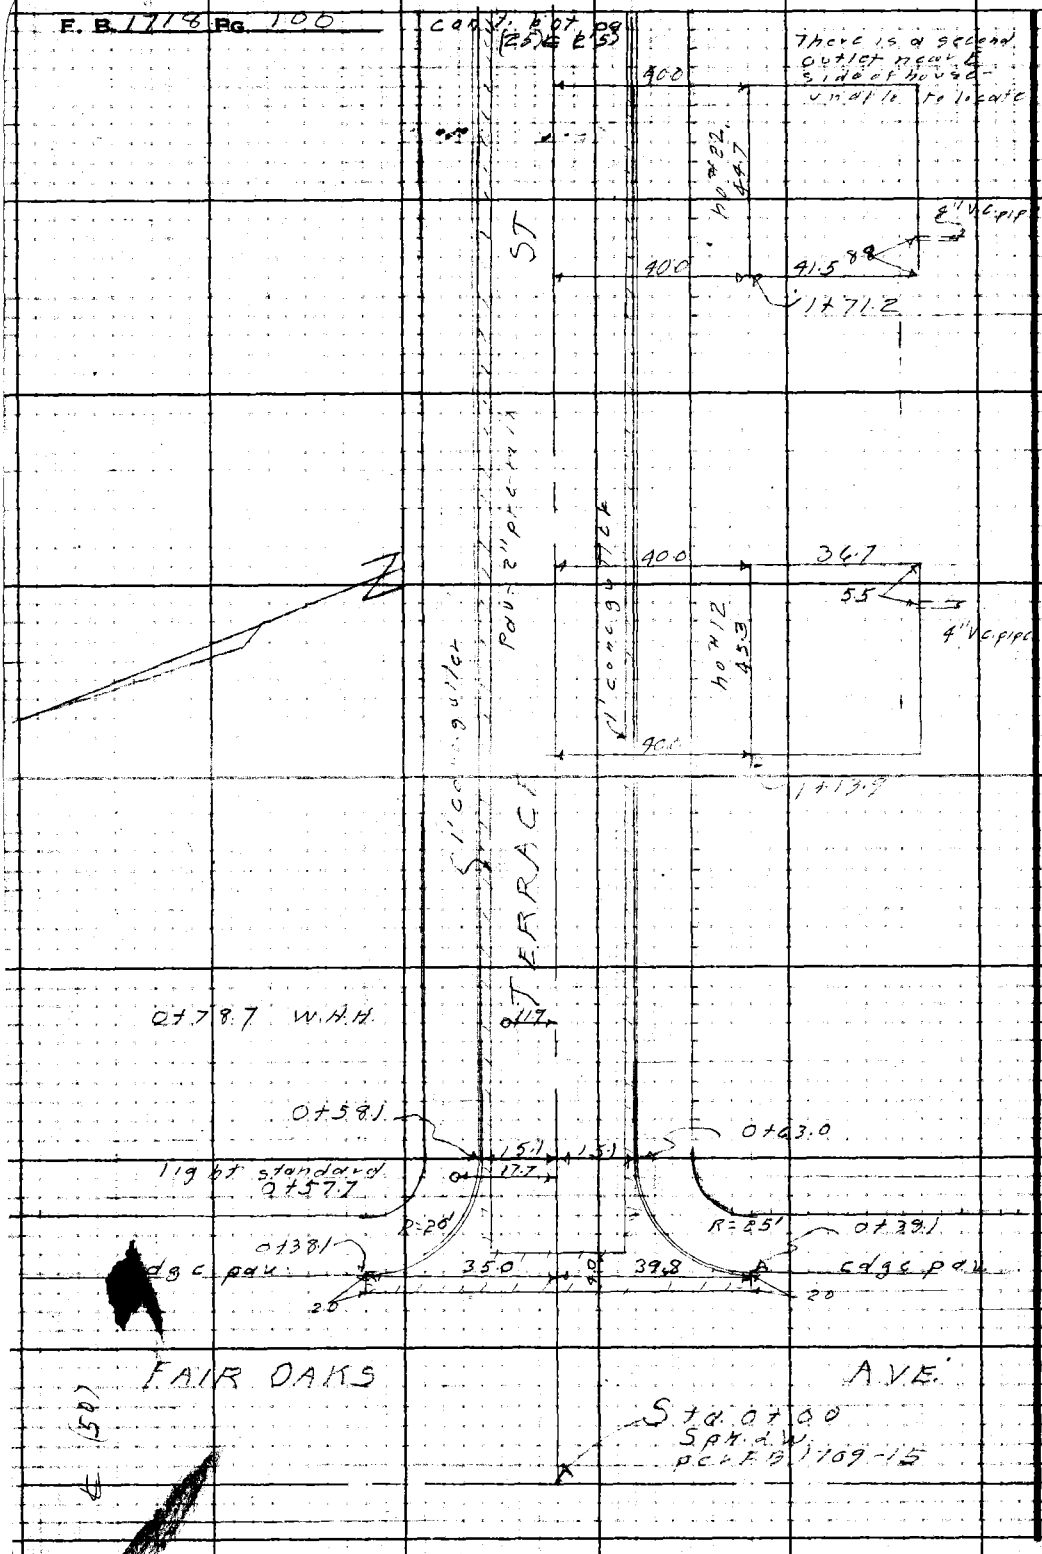

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by	Survey of Mc Nally Ave
Map No.	W.O. 2244 Tape No. Std.
Office Work	Surveyed by J. J. Lanigan
Checked	Noted J.J.L. Date 11-20-57
Date	Indexed A. C. Johnson

F. B. 1709 Pg. 101

Notes: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date Initialed Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

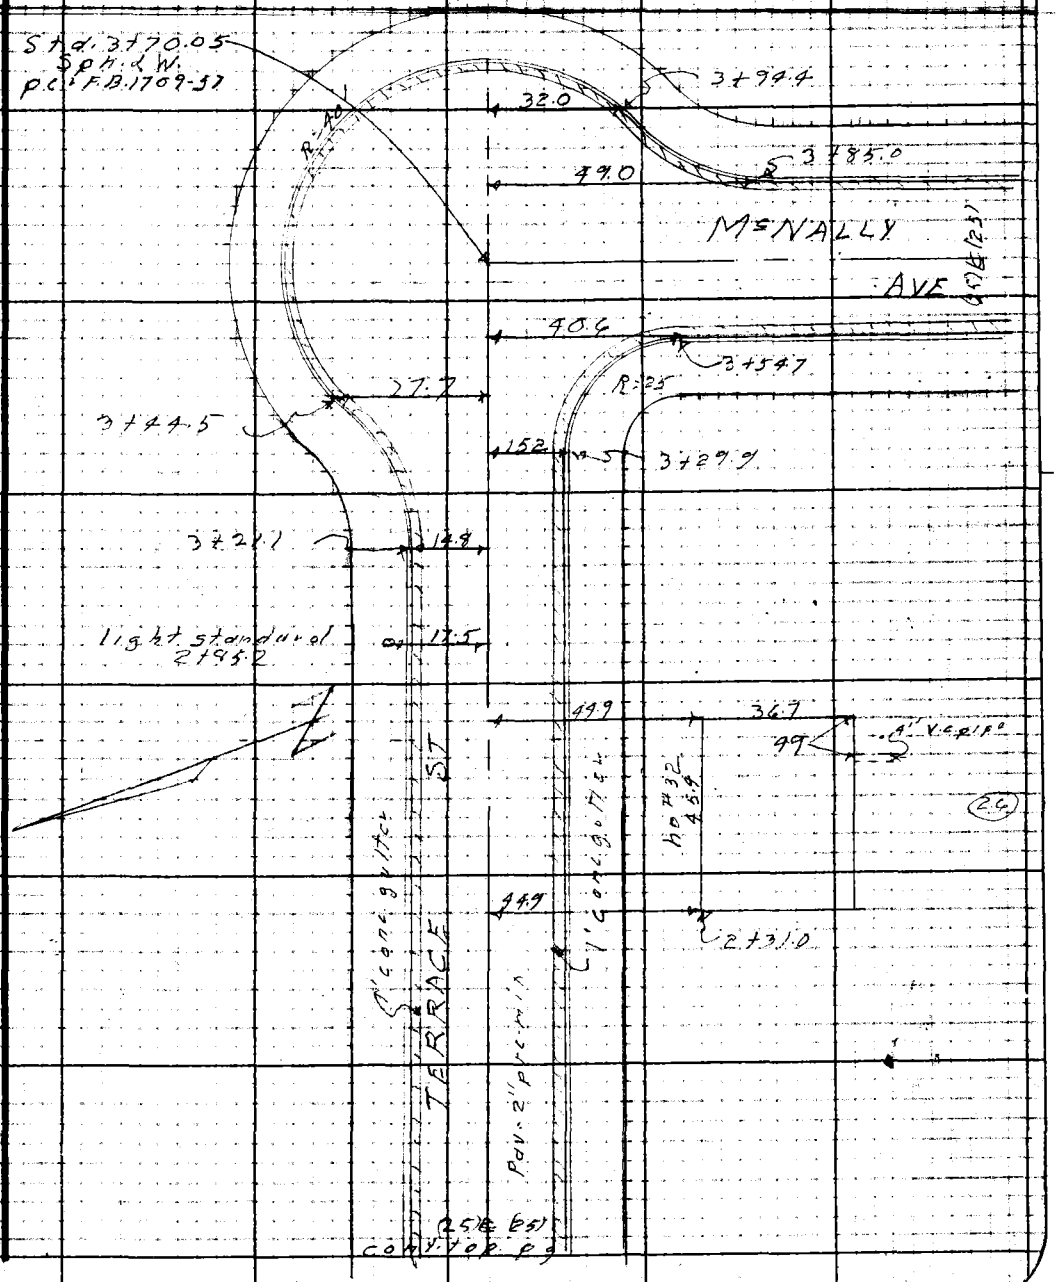

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

F. B. 1778 Pg. 102

Profile No. | Notes Red. | Plotted | Job No. 1390 | Division No. V | F.B. 1718 | Pg. 103
Date | Date | Survey of Marengo Avenue
X-Sec. No. | Notes Chkd. LCM | Checked | Survey by Lanigan | Notes Lewis | Date 12-1-50
Date 12/29/50 | Date | Map No. | Checked Johnson | Date

PROFILE
and
CROSS-SECTIONS
of
TERRACE STREET
from
FAIR OAKS AVENUE
to
McNALLY AVENUE
C.I. 1390

J.J. Lanigan
C.H. Lewis
H.H. Raphael
E.W. Evans

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK. WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

76L298 307 5-49

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 PG. 104
Job No. 1390 Division No. V Notes Red. Plotted Profile No.
Survey of Mckenzie 40 Acres Date Date X-Sec. No.
Survey by Lanigan Notes Lewis Notes Chkd. Checked
Indexed A. C. Johnson Date Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	Terrace	Street
BM AE 262	5 56	1311 30		1305.74	BM AE 262 Elev. 1305.74	FB 1447 - 244
					Fair Oaks Avenue & Terrace St SW. cor.	
					St spk in cl 6' W of W. end C.R.	
0 + 00			3 67	1307 63	& int. Terrace St & Fair Oaks Ave.	
			9 43	1301 87	E of Fair Oaks 100' S'ly	
			0 42	1310 88	" " " " 50' N'ly	
			6 63	1304 67	gut Sorm SE cb not	
			5 97	1305 33	cb " " " "	
			4 90	1306 40	gut E " " " "	
			4 26	1307 04	" " " " "	
0 + 63			4 R	1307		25' R RL.
			2 00	1307 30	gut N end NE cb. not.	
			1 81	1307 49	cb " " " "	
			2 33	1307 77	gut E " " " "	
			2 60	1307 50	cb " " " "	
0 + 58			2 L	13098	25' L. P.L.	
0 + 38			4 20	1307 08	[illegible] St.	
1 + 00			3 39	1307 91		
"			4 41	1306 89		15' R gut
"			3 81	1307 49		" cb
"			3 36	1307 94	15' L gut.	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Terrace	Street
1+00		1311 35	2 71	130859	15' L out	
T.P.			3 38	130792	T.P.	
	5 44	1313 36				
			12 5/8	13009	S.W cor Lot # 36 Th. 13471	
1+13.9			10 9/8	13034	71'R ground at low corner (S.W) Hse # 12	
1+51			12 3/8	13012	" elevation on 4" C.I. pipe "	
			5 8/8	13076	Floor elevation Hse #12	
			12 5/8	13009	SE cor Lot # 36	
1+71.3			9 9/8	13035	82' R ground at SW cor Hse # 32	
1+80			11 8/8	13016	" elevation on 4" C.I. pipe at Hse # 32	
			5 5/8	13079	Floor elevation " "	
2+00			4 97	130839		
"			5 99	130737		15' R gut
"			5 37	130799		" CL
"			5 02	130834	15' L gut	
"			4 37	130899	" CL	
T P			4 97	130839	T.P.	
	6 42	1314 81				
			14 0/8	13058	S.W. cor Lot # 38	
			6 5/8	13083	Floor elevation Hse # 32	
2+31.9			10 7/8	13041	82' R ground at S.W. cor Hse # 32	

Profile Notes Red. ____ Plotted ____ Job No. 1300 Division No. V F.B. 1518 PG. 105-
No. ____ Date ____ Date ____ Survey of Mission Hills
X-Sec. Notes Chkd. ____ Checked ____ Survey by Lewis Notes Lewis Date 12-1-57
No. ____ Date ____ Date ____ Map No. ____ Checked Johnson Date ____

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 PG. 106
Job No. 1390 Division No. 2 Profile No. X-Sec. No.
Survey of Alameda Avenue Platted Date
Survey by Lewis Notes Lewis Notes Chkd. Checked
Indexed C. Johnson Date 11 Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	Terrace	Street
2+71		1314 81	12 9	1301 9	82'R elec on 4"C I Pipe	
			12 8	1302 0	S.E. corner of dot # 38	
3+00			6 05	1308 76	℄	
			7 08	1307 73		15'R gut
			6 44	1307 37		" eb
			6 07	1307 74	15'L gut	
			5 41	1308 40	" eb	
3+21			5 93	1308 88	15'L gut	
"			5 84	1307 57	" eb	
3+30			6 95	1307 80		15'R gut
"			6 32	1307 49		" eb
"			6 4	1307		25'R P.L.
			8 69	1306 12	gut S and SW. at Hat	
			8 04	1306 77	eb " " " " "	
3+70 OS			5 98	1307 83	℄ int. terrace & R/W Nelly	
"			9 69	1305 12	℄ McNally 70' S'ly	
			10 26	1304 55	w gut " "	
			9 61	1305 20	w eb " "	
			9 94	1304 87	E gut "	
			9 27	1305 54	E eb "	
"			5 83	1308 98	40'L gut	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Terrace	Street
3+00		131481	510	130971	40' L cb	
3+42			882	130599		49' R gut
"			815	130666		" cb
4+10			655	130826	gut & prod	

F.B. 1718 PG. 108 Job No. 1390 Division No. V Notes Red. _____ Plotted _____ Profile

Survey of Marengo Avenue Date _____ Date _____ No. _____

Survey by Lanigan Notes Lewis Notes Chkd. _____ Checked _____ X-Sec.

Indexed _____ Date _____ Date _____ Date _____ No. _____

STATION	B. S.	H. I.	F. S.	ELEV.

76L298 307 5-49

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR

726 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend notes this side of this line.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Notes Ck'd by	Survey of Marengo Ave.
Map No.	W. of 710 Tape No. Std.
Office Work	Surveyed by J.J. Lanigan
Checked	Noted J.J.L. Date 12-7-50
Date	Indexed E. C. Johnson

F. B. 1778 PG. 109

PROJECT

Notes: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not attend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
728 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION of IMPROVEMENTS on HARRIET ST. from FAIR OAKS AVE. to McNALLY AVE. C.I. 1390

J.J. Lanigan
C.H. Lewis
N.H. Raphael
E.W. Evans

7673085 247 10M 1-49

F. B. 1718 Pg. 110

cont. plot Pg. 111

Sta 1+86.91
Spk & W
Pct F.B. 1709-35
10" P.P. 1+97.0

1+99.7
17.2
22.5
30.5
1+91.5
18.2
99.3
40.1
unable to locate out let
22.2
tub. to be set
527975
2972
ALLEY
edge pav.
edge pav
34.1
1+91.7
16.3
1+73.5
ST
pav
edge
HARRIET
edge
edge
19" P.P. 0+96.1
20.7
11.4
H.H. 0+59.6
0+53.6
18.1
R=15
19.9
0+47.1
0+38.0
33.1
R=15
12" conc gutter
23
3.5
0+32.0
2' conc gutter
2.3
0+29.3
Grds H.H.
16.2
FAIR OAKS
Sta 0+00
Pct F.B. 1709-11
AVE

RETURN TO
LOS ANGELES COUNTY SURVEYOR
728 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by		Survey of	Monroe Ave.
Map No.		W.O. 230	Spc. No.	Std.
Office Work		Surveyed by	J.J. Lonigan
Checked		Noted	J.J.L.	Date 2-17-59
Date		Indexed	C. Johnson

F. B. 1718 PG. 111

Notes: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

75F3098 847 10M 1-59

Sta 3+77.92
Sph. on
P.C. of F.B. 1708-35

47°08'57" 15.8

49

25.3

3+92.9

3+92.5

9.6

80'

M^c NALLY

60'

AVE

29.7

3+56.9

17.2

3+42.6

12" R.P.

3+32.3

20.1

65.5

47.1

pav'd

ST

33.2

m.o. #42

65.5

2+85.7

5.9

5.9

5.9

m.o. #28

32.5

5.9

2+43.0

HARRIET

11.0

5.7

2+91.0

(80 & 60)

cont. fdp pg. 110

F. B. 1119 Pg. 112

RETURN TO
LOS ANGELES COUNTY SURVEYOR
720 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

Profile No. | Notes Red. | Plotted | Job No. 1390 | Division No. V | F.B. 1718 | PG. 113
Date | Date | Survey of Malenga Avenue
X-Sec. No. | Notes Chkd. LCM | Checked | Survey by Lanigan | Notes Lewis | Date 12-1-50
Date 12/29/50 | Date | Map No. | Indexed K. Johnson | Date FEB 20 '51

PROFILE
and
CROSS-SECTIONS
on
HARRIET ST.
from
FAIR OAKS AVE.
to
McNALLY ST.
C.I. 1390

J.J. Lanigan
C.H. Lewis
H.H. Raphael
E.W. Evans

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

761.298 307 5-49

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ Plotted ____ Date ____ X-Sec. No. ____ Checked ____ Date ____

Job No. 1350 Division No. V. Notes Red ____ Date ____
Survey of Monterey Ave. Notes Chkd. ____ Date ____
Survey by Langley Notes Lewis Date ____
Indexed E. C. Johnson

F.B. 1718 PG. 14

STATION	B. S.	H. I.	F. S.	ELEV.	Harriet	Street
BM AE 266	4 16	1239 30		1235 14	BM AE 266 Elev. 1235.140 F.B. 1447-245	
					Fair Oaks Ave. & Harriet St. NW cor.	
					L+N in cb. 10' N of N end C.R.	
0+00			662	1232 38	℄ int. Harriet & Fair Oaks.	
			1185	1233 75	℄ of Fair Oaks 100' S'ly	
			1209	1233 21	E gut " " 90 "	
			1131	1233 99	" cb " " " "	
			932	1233 98	gut S end SE cb "	
			851	1234 17	cb S " " " "	
			813	1233 17	gut E " " " "	
			775	1233 55	cb "	
0+33			750	1233 80		℄ cross gut
			607	1233 23	gut E end NE cb. "	
			523	1233 07	cb " " " " "	
			561	1233 69	gut N " " " "	
			481	1234 49	cb " " " " "	
			054	1235 76	℄ Fair Oaks 110' N'ly	
			150	1235 80	E gut " " " "	
			066	1235 74	" cb " " " "	
			4 5	1235	NE ppty cor	
			8 0	1235	SE " "	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Hauviet	Stewart
0 + 85		123930	499	123431		℄
"			599	123336		20' R edge pvmt
"			7	12320		30' R P.L.
"			493	123437	18' L edge pvmt	
"			38	12355	30' L P.L.	
T.P.			474	123452	T.P.	
	611	124067				
1 + 869			547	123520	Alley & int.	
"			552	123515	17' L. cross gut.	
			148	123919	℄ of Alley 70' N'ly.	
1 + 78			92	12315	ground at SW cor Hse #20 (also back lot)	
"			70	12337	Floor elevation	"
2 + 00			534	123532		℄ 20' R edge pvmt
"			55	12352		22' R Top bank
"			67	12340		30' R P.L.
"			551	123516	17' L edge pvmt	
"			45	12362	20' L Top bank.	
"			37	12370	30' L P.L.	
T.P.			545	123522		
	547	124069				
2 + 13			92	12310	90' R Floor elevation of garage	

Profile
Notes Red. ____ Plotted ____ Job No. 1390 Division No. K
No. ____ Date ____ Date ____ Survey of Mateno to Avenue
X-Sec. Notes Chkd. ____ Checked ____ Survey by Williams Notes Lewis Date 12-1-50
No. ____ Date ____ Date ____ Map No. [redacted] Checked [redacted] Date ____
F.B. 1178 PG. 115

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 7119 PG. 114 — Job No. 1390 Division No. V — Profile No. — Notes Red. — Plotted — Date — X-Sec. No. — Date — Survey of Alameda Ave. — Notes Chkd. — Checked — Date — Survey by L. A. Eng. Dept. Notes L. Lewis — Date — Indexed C. Johnson

STATION	B. S.	H. I.	F. S.	ELEV.		
2+76		1240.69	11 2	1229.5	ground at low corner of (SE) Hse #1128	
"			6 1	1234.6	Floor elevation	" "
2+80			13 3	1227.4	15'0' R back of lot line?	
2+85			12 1	1228.6	ground at low corner (SW) Hse #1142	
"			8 2	1233.5	Floor elevation	" "
3+00			464	1236.35	℄	
"			495	1234.79		9'R edge pvmt
"			4 7	1232.3		12'R top bank
"			8 7	1231.3		30'R ℄ L.
"			490	1233.79	12'L edge pvmt	
"			3 2	1235.5	30'L P.L.	
3+74.42			443	1236.24	℄ int. McNally Ave & Harriet St.	
"			470	1232.79		9'R edge pvmt.
"			4 5	1234.1		12'R Top Bank
"			8 4	1232.2		30'R P.L
3+99.4			3 1	1233.3	NW ppty cor	
3+50.4			422	1232.7	30'L gut	
"			373	1230.6	30'L (end)	
3+73.4			412	1230.7	30'L gut	
"			371	1230.8	30'L end curb	
			2 2	1229.1	NE ppty cor	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	
3+74 42		124069	469	123600	cross gutter
			143	123922	& McNally 80' N'ly
			189	123880	W gut " "
			124	123945	W cb " "
			213	123856	E gut " "
			135	123939	" cb " "
4+75			472	123597	℄
BMAE484			320	123749	B.MAE484 - Elev-1237.491 - pcl.A.B.15 68-12 McNally Ave., & HARRIET ST. N.W. cor., 18" sp.in curb 10' N. of S.c.l.

Profile
No. X.Sec.
Notes Red Plotted Job No. 13911 Division No. V.
Notes Chkd. Date Date Survey of McNally Ave.
Date Checked Survey by J.J.L. Notes Cut Date 12-1-50
Date Map No. Indexed Job Book Date
F.B. 1178 PG. 117

F.B. 1718 PG. 119 Job No. 1390 Division No. V. Notes Red. Plotted Profile

Survey of Marengo Ave. Date Date No.

Survey by Lanigan Notes Lewis Notes Chkd. Checked X-Sec.

Indexed Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend notes this side of this line.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK. WITH DATE AND NAME OF PERSON MAKING CHANGE.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Marengo AVC.
W. O. 1390 Tape No. Std. °F
Surveyed by J. J. Lanigan
Noted J. J. L Date 12-1-50
Indexed A. C. Johnson

F. B. 1718 Pg. 119

SEP 20 '51

Notes: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
of
IMPROVEMENTS
on
HARRIET ST
from
RAYMOND AVE
to
HIGHVIEW AVE
C. I. 1390

J. J. Lanigan
C. H. Lewis
H. H. Raphael
E. W. Evans

76F3098 247 10M 5-49

F. B. 1719 PG. 12D

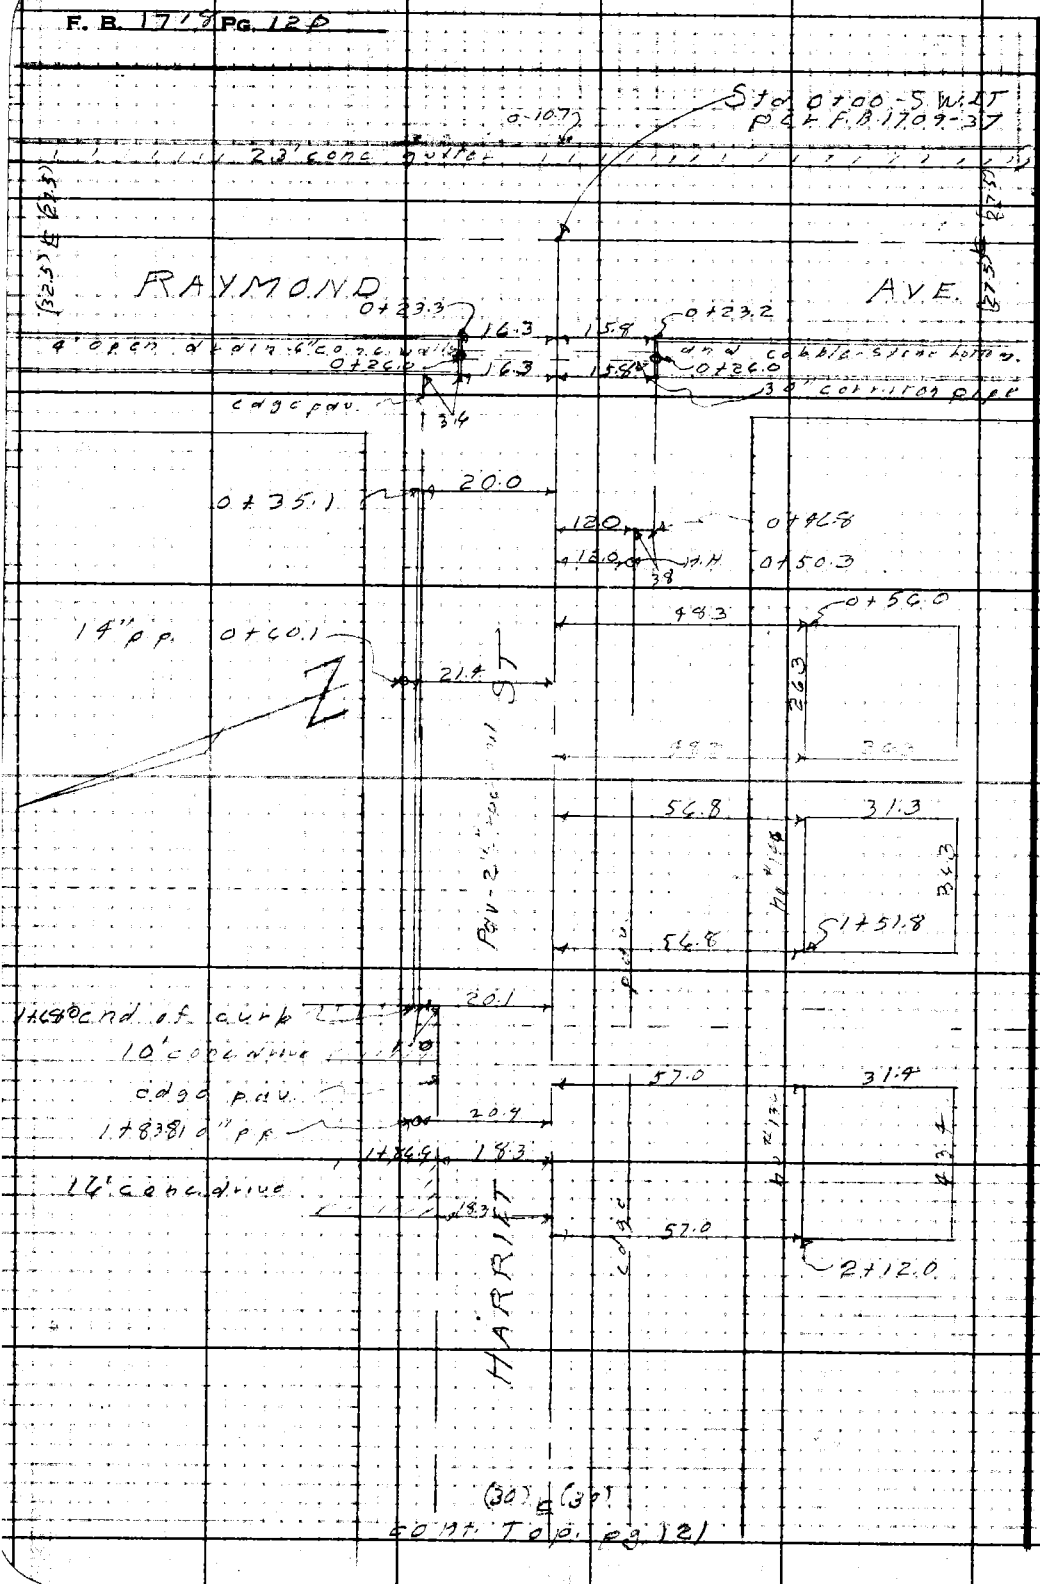

RETURN TO
LOS ANGELES COUNTY SURVEYOR
720 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

Notes Ck'd by	Survey of Alhambra Ave
Map No	W.O. 1590 Tape No. Std.
Office Work	Surveyed by J.J. Lonigan
Checked	Noted J.J.L. Date 12-7-50
Date	Indexed E. C. Johnson

F. B. 1715 PG. 12

Notes: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not attend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

cont' bot pg 720

21+28.0

63.1

55

17.9

23.9

34.2

Ho 4.29

Tubs. in basement

33.4

4.3

14" p.c.p.
21+58.3

21.35

63.7

edge pav

Pav. 2½ + rock roll

HARRIET

edge pav

63.9

21+93.0

17.5

55

Ho 4.14

23.5

34.2

32.3

4.5

Tubs. in basement

37+38.9

17.1

64.0

21+45.0

37+44.5

30.1

Ho 4.12

35.3

NIGHVIEW

11.0

64.0

38.3

AVE.

30.1

37+80.5

Std. 37+62.52
SPH & W.
P.C.I. F.P. 1709-36

37+90.1

17.3

edge pav

3.00 ± Bot

78F3pp 247 10M 1-49

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled In Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

F. B. 1774 Pg. 122

Profile No. ____ Notes Red. ____ Plotted ____ Job No. 1390 Division No. V F.B. 1118 PG. 123
Date 12-4-50 Date ____ Survey of Marengo Avenue
X-Sec. No. ____ Notes Chkd. LCM Checked ____ Survey by Lanigan Notes Lewis Date 12-4-50
Date 12/29/50 Date ____ Map No. ____ Indexed C. Johnson Date ____

PROFILE
and
CROSS-SECTIONS
of
HARRIET STREET
from
RAYMOND AVENUE
to
HIGHVIEW AVENUE

CI. 1390

V. V. Lanigan
C. H. Lewis
H. H. Raphael
E. W. Evans

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

76L298 307 5-49

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 PG. 124 | Job No. 4202 Division No. K Notes Red. Date Notes Chkd. Date | Profile No. Plotted Date Checked Date | X-Sec. No. Date

Survey of Maywood Ave. Notes Lewis

Survey by Kennedy & A. C. Johnson

Indexed

STATION	B. S.	H. I.	F. S.	ELEV.	Harriet Street
BMAE 477	4.70	1234.14		1229.44	BMAE 477 Elev. 1229.441 FB 1568 P. 112
					Raymond Ave. (E. side) at Harriet St.
					Bt. sph in sb 5' N of ℄ prod of Harriet St.
0+00			5.17	1229.97	℄ Int Harriet & Raymond
			1.00	1230.14	℄ Raymond 75' N
			1.64	1230.70	E gut. " " "
			0.88	1233.26	" eb " " "
			9.95	1229.19	℄ " " 5' N
			10.69	1227.45	E gut. " " "
			9.91	1229.23	" eb " " "
0+26			9.5	1229.5	16" R Flo-line 30" corr. iron pipe, inlet
"			11.0	1228.1	15° L " " " " " " outlet
0+28			6.16	1230.38	4-side break ℄
"			5.43	1231.11	12' R
"			6.81	1229.73	12' L
0+35 L			6.13	1229.31	20' R gut at eb beginning
"			5.31	1230.13	" eb
			5.8	1231.1	NW poly. corn.
			9.9	1227.1	SW. " "
T.P.			3.91	1230.23	T.P.
	6.50	1236.73			

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.		
0+56		1236 73	9 8	1226 9	50'L Floor elev. of House	
"			12 4	1224 3	75'L ground at low corner of House	
1+00			6 51	1230 22	℄	
"			6 86	1229 87		20'R gut
"			6 23	1230 50		" cb
"			6 84	1229 89	12'L edge pumt	
"			6 4	1230 3	17'L brk	
1+15			7 8	1228 7	30'L P.L	
"			7 7	1229 9	57'L Floor elev. Hse # 146	
"			11 6	1225 1	89'L ground at low corner Hse # 146	
1+50			15 0	1221 2	200'Lt back lot line	
1+68			7 5	1229 2	57'L Floor elevation of Hse # 136	
"			10 5	1226 2	89'L ground at SE (low corner) Hse # 136	
"			4 97	1231 76	20'R gut at end of curb	
"			4 60	1232 13	" cb " " " "	
2+00			4 10	1232 63	℄	
"			4 62	1232 11		18' Radge pumt
"			3 0	1233 7		30' R. P.L
"			4 27	1232 46	12'L edge pumt	
"			4 0	1232 7	16'L brk.	
"			6 4	1230 3	30'L P.L.	

Profile
No. X-Sec.
Notes Red. Plotted Job No. 1302 Division No. 1
Date Date Survey of Marengo Avenue
Notes Chkd. Checked Survey by Lewis Notes Lewis Date 12-11-50
Date Date Map No. Checked Date
F.B. 1718 PG. 125

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ X-Sec. No. ____

Job No. 1390 Division No. 2 Notes Red. ____ Plotted ____
Survey of Manzanar Avenues Date ____ Date ____
Survey by Lansing & Lewis Notes ____ Notes Chkd. ____ Checked ____
Indexed E. C. Johnson Date ____ Date ____ Date ____

F.B. 1516 PG. 126

STATION	B. S.	H. I.	F. S.	ELEV.	Harriet	Street
2+28		1236.72	6.5	123[illegible] 2	64' L Floor elevation	Hse # 128
"			10.3	12[illegible] 4	97' L ground at S.E. cor.	" "
2+46			13.2	12[illegible] 8	85' L basement floor	" "
2+75			15.6	122[illegible] 1	200' L± back lot line	
T.P.			2.96	123[illegible] 77		
	6.49	1240.26				
3+00			6.50	123[illegible] 76		℄
"			6.82	123[illegible] 44		18' R edge pavmt
"			5.7	123[illegible] 6		20' R. b+k
"			3.9	1236 4		30' R P.L.
"			6.77	123[illegible] 49	12' L edge pavmt.	
"			6.5	123[illegible] 7	18' L b+k	
"			9.2	123[illegible] 1	30' L P.L.	
3+10			11.0	1224 3	81' L Floor elevation	Hse # 118
"			18.5	122[illegible] 8	" basement floor	" "
"			14.2	1226 1	96' L ground at back	" "
3+45			12.3	1225 9	64' L Floor elevation	Hse # 112
"			16.8	1223 5	103' L ground at S.E. cor.	" "
			4.8	1235 2		NE ppty cor
3+445			5.95	1234 21		30' R out
"			5.20	1235 96		℄
3+62.52			5.86	1234 90	℄ Int Harriet & Highview	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Harriet	Street
3+62 52		1240 26	6 27	1233 99		18' R. cross-cut
"			220	1238 06	& Highview 100' N'l'y	
"			266	1237 60	E. cut " "	"
"			186	1238 40	" cb " "	"
"			256	1237 70	W cut " "	"
"			177	1238 49	" cb " "	"
3+62 52			6 09	1234 17	12' L edge pvmt	
"			5 8	1234 5	15' L	
"			8 5	1231 8	30' L PL	
3+80.5			590	1234 36		30' R. cut
"			519	1235 07		" " cb at end
			4 9	1235 4		NW ppty corner
4+62			5 23	1235 03		℄ 100' W
BM AE 483			4 86	1235 40	BM AE 483 Elev. 1235.402 FB 15-68 P 12	
					Highview Ave. & Harriet St. NE. Cor.	
					Bt. spk in curb 6' N of S. end.	

Profile
No. X-Sec.
Notes Red. Plotted Job No. 2200 Division No.
Notes Chkd. Checked Survey of Morenzo Avenue
Date Date Date
Survey by Lawson Notes Lawson Date 12-27-68
Map No. Unrecorded Date
F.B. 1715 PG. 27

F.B. 1718 PG. 128 Job No. 1370 Division No. V Notes Red. _____ Plotted _____ Profile

Survey of Marengo Avenue Date _____ Date _____ No. _____

Survey by Lanigan Notes Lewis Notes Chkd. _____ Checked _____ X-Sec.

Indexed _____ Date _____ Date _____ Date _____ No. _____

STATION	B. S.	H. I.	F. S.	ELEV.

76L298 307 5-49

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR

726 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend notes this side of this line.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK. WITH DATE AND NAME OF PERSON MAKING CHANGE.

Notes Ck'd by	Survey of Morengo Ave
Map No.	W. O. 134 Tape No. Std.
Office Work	Surveyed by J. J. Lonigan
Checked	Notes J. J. L. Date 12-4-50
Date	Indexed R. C. Tolman

F. B. 1718 PG. 129

FEB 20 51

Notes: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
728 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
of
IMPROVEMENTS
on
EAST LA VENEZIA
from
FAIR OAKS AVE.
to
NORTH LA VENEZIA
C.I 1390

J. J. Lonigan
C. H. Lewis
H. H. Raphael
E. W. Evans

76F3098 2-47 10M 1-49

F. B. 1719 PG. 120

cont. bot pg (120)

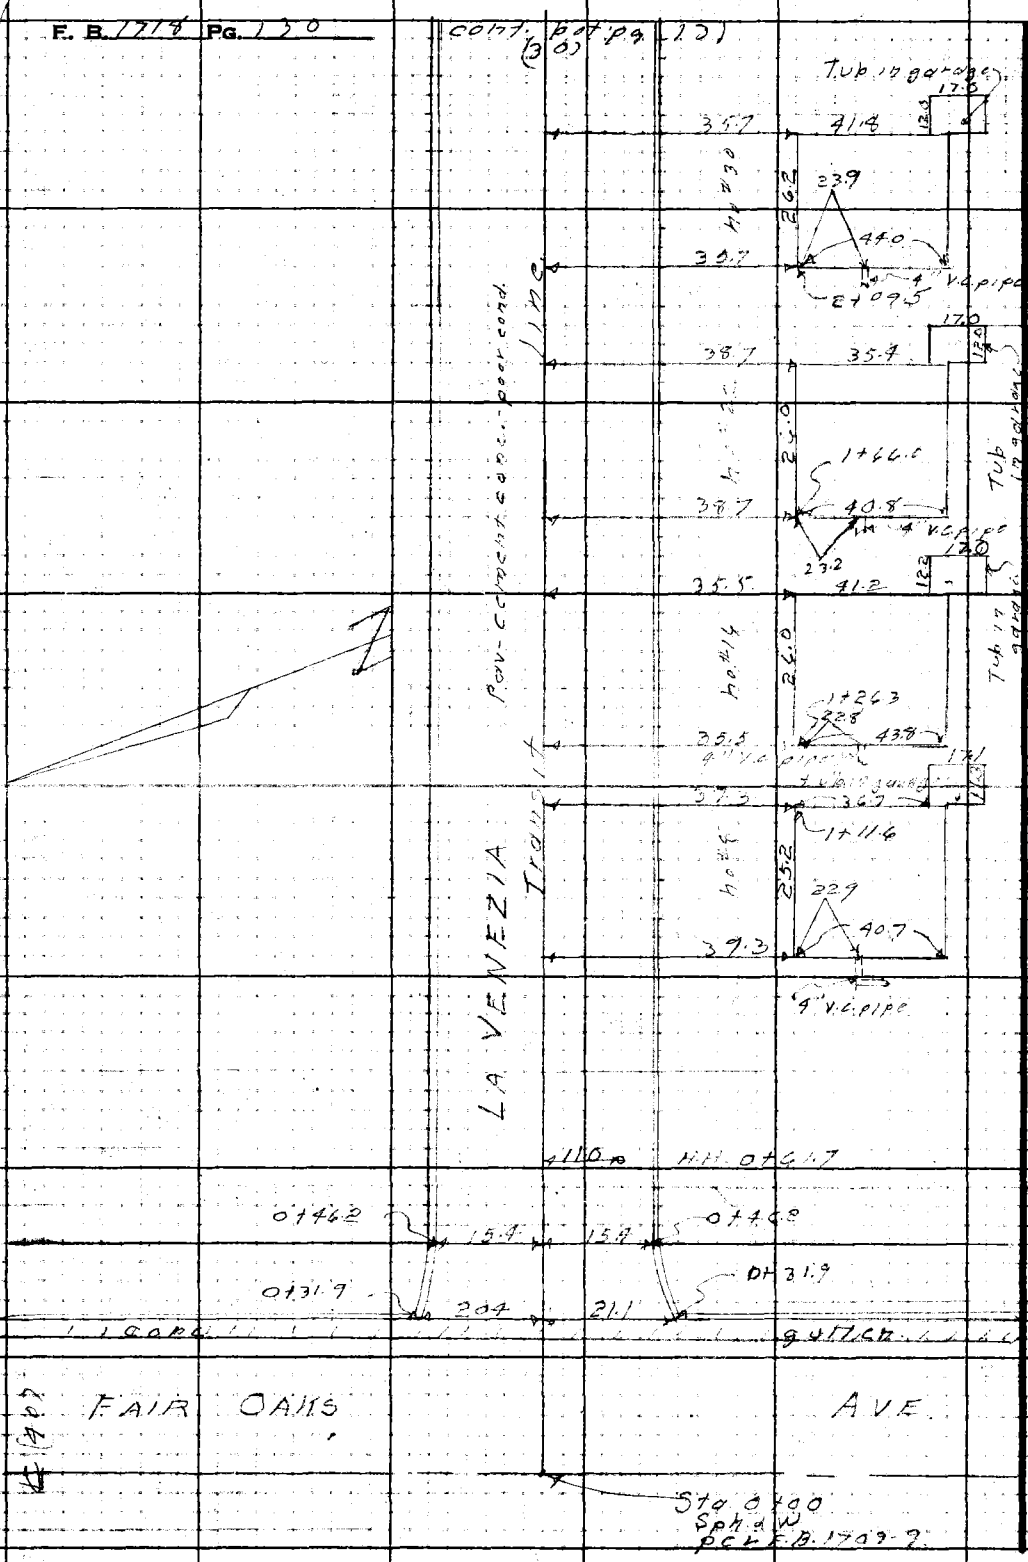
Tub in garage
17.3
12.3
35.7
41.4
44.30
26.2
23.9
44.0
30.7
4" V.C. pipe
E 7+09.5
17.0
12.0
38.7
35.7
1+66.0
40.8
4" V.C. pipe
23.2
35.5
41.2
12.2
Tub in garage
Pav. Contract Grade - poor cond.
1.1%
26.0
1+26.3
32.8
43.8
35.5
4" V.C. pipe
17.1
17.1
37.2
36.7
1+11.6
25.2
22.9
40.7
39.3
4" V.C. pipe
LA VENEZIA
Transit
House
House
House

Notes Ck'd by	Survey of Marengo Ave.
Map No.	W. O. 1330 Tape No. Std.
Office Work	Surveyed by V. V. Lamgan
Checked	Notes V.V.L. Date 12-2-59
Date	Indexed

F. B. 1778 Pg. 131

Notes: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

7875086 247 10M 1-49

LA VENEZIA

Transit

Line

(30')

9+37.73
S.A.T.d.W.
P.C. F.B. 1709-37

23.1 26.0

9+29.8 R=10'

9+19.0

9+11.7

R=10'

15.5 15.5

4+07.9

37.7 35.1

17.0

12.0

Tube in garage

(1.7)

24.0

37.7

22.7 41.3

9" V.C.P.I.P.

3+32.6

36.0 32.8

17.0

12.0

Tube in garage

(1.9)

24.6 46.8

9" V.C.P.I.P.

2+92.8

36.0

35.9 42.0

17.0

12.0

Tube in garage

(1.0)

24.4 44.2

9" V.C.P.I.P.

2+52.9

35.9

Point of Tangency
LA VENEZIA

(30')

Cont'd top pg 1730

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

F. B. 1716 Pg. 137

Profile No.
Notes Red. Plotted Job No. 1390 Division No.
Date Date Survey of Marengo Avenue
X-Sec. No.
Notes Chkd. LCH Checked Survey by Lanigan Notes Lewis Date 12-5-50
Date 12/29/50 Date Map No. Indexed Johnson Date FEB 20 '51

F.B. 1718 PG. 133

PROFILE
and
CROSS-SECTIONS
of
EAST LA VENEZIA
from
FAIR OAKS AVENUE
to
NORTH LA VENEZIA

C.I. 1390

V. Lanigan
C.H. Lewis
H.H. Raphael
E.W. Evans

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

761.298 307 5-49

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 PG. 134

Job No. 4390 Division No. 6 Notes Red. Date Notes Chkd. Date
Survey of Mateusz Avenue Notes Lewis
Survey by Lanigan & C. Tobiason Date 2-1-
Indexed

Profile Plotted Date Checked Date No.
X-Sec. No.

STATION	B. S.	H. I.	F. S.	ELEV.	Foot to Valencia
BM AE 490	5.76	1207.17		1201.41	BM AE 490 El 1201.41 FB 1568 P 124
					Lakeneczia (W) (S. side) at Fair Oaks Ave.
					3" spk. in curb, 7' E of E.P.L. of Fair Oaks Ave.
0+00			6.02	1201.14	℄ Int. Lakeneczia & Fair Oaks Ave.
			11.42	1195.75	℄ of Fair Oaks 100' S'ly
			12.01	1195.16	W gut " " " "
			11.35	1195.82	" cb " " " "
			12.45	1194.72	E gut " " " "
			11.63	1195.54	" cb " " " "
			0.58	1206.59	℄ " " " N'ly
			1.07	1206.10	W gut " " " "
			0.37	1206.80	" cb " " " "
			1.50	1206.67	E gut " " " "
			0.69	1206.49	" cb " " " "
			8.05	1199.13	gut S end SL cb not.
			7.30	1199.87	cb " " " " "
			6.38	1200.79	gut E " " " "
			5.72	1201.45	cb " " " " "
0+46			6.93	1200.24	℄ (across gutter)
			5.80	1201.37	gut N end NE cb not
			4.99	1202.18	cb " " " "

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	East La Verne
		1207.17	5.09	1202.08	gut E. end & NE. cb " "
			4.35	1202.82	cb " " " "
0+57			5.22	1201.95	℄
T.P.			5.75	1201.42	T.P.
0+86	4.94	1206.36	5.0	1201.4	Floor elevation Hse # 8 40' R
"			8.4	1198.0	Elev. on 4" V.C. pipe " " 62' R
"			8.3	1198.4	ground at low cor. " " 80' R
1+12			8.3	1198.1	garage floor elev. " " "
0+86			8.5	1197.9	back lot line " " 100' R
1+00			4.99	1201.37	℄
"			5.62	1200.74	15' R gut
"			4.99	1201.37	" cb
"			5.12	1201.24	15' L gut
"			4.62	1201.74	" cb
1+26			5.0	1201.4	Floor elevation Hse # 16 30' R
"			8.5	1197.9	Elev. on 4" V.C. pipe " " 54' R
"			8.4	1198.0	ground at low cor. (S.W.) " " 80' R
"			9.0	1197.4	back lot line " " 100' R
1+52			8.5	1197.9	garage floor elev - 77' R
T.P.			5.41	1200.95	T.P.
	4.85	1205.80			

Profile Notes Red. Plotted Job No. 1202 Division No. V
No. Date Date Survey of Marengo Avenue
X-Sec. Notes Chkd. Checked Survey by Lewis Notes Lewis Date 12-5-57
No. Date Date Map No. Date

F.B. 1718 PG. 135

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1719 PG. 134 | Job No. 1390 Division No. 1 | Notes Red. | Plotted | Profile
Survey of Valencia Avenue | Date | Date | No.
Survey by Harris & Lewis | Notes Chkd. | Checked | X-Sec.
Indexed L. C. Johnson | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	Fact to	Remarks
1+66		1205.80 ✓	4.5	1201.2	Floor elevation	H&C #22 39' R
"			8.4	1197.4	elev. on 4" V.C. pipe	" " 62' R
"			8.3	1197.5	ground at SW. cor.	" " 80' R
"			8.2	1197.3	back lot line	" " 100' R
1+98			8.2	1197.8	garage floor elev.	" " 85' R
2+00			4.98	1200.82		±
"			5.21	1200.59		15' R gut
"			4.70	1201.09		" c/l
"			5.12	1200.68	15' L gut	
"			4.66	1201.14	" c/l	
2+09			5.3	1200.5	Floor elevation	H&C #30 36' R
"			7.4	1198.4	Elev. on 4" V.C. pipe	" 62' R.
"			8.2	1197.6	ground at low corner	(SW) " 80' R
"			8.4	1197.2	back lot line	" 100' R
2+42			8.2	1197.3	garage floor elev.	" 85' R
T.P.		1	5.01	1200.79 ✓		
	4.81	1205.60				
2+52			5.0	1200.6	Floor elevation	H&C #30 36' R
"			8.5	1197.1	Elev. on 4" V.C. pipe	" " 62' "
"			8.2	1197.4	ground at low corner	" " 80' "
"			8.5	1197.1	back lot line	" 100' "

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	East La	Yonne Ave
2+85		1205.40	7.7	1197.9	garage floor elev. Hse #36	85' R.
2+92.8			5.9	1200.6	Floor elevation to Hse #42	36' R.
"			8.5	1197.1	Elev. on 4" V.C. pipe "	62' R.
"			8.2	1197.4	Low corner (S.W.) "	80' R.
"			8.5	1197.1	back lot line	100' R.
3+00			4.76	1200.84	℄	
"			5.32	1200.28		15' R. gut
"			4.82	1200.78		" C/L
"			4.89	1200.71	15' L gut	
"			4.46	1201.14	" C/L	
3+24			8.4	1197.2	garage floor elev. Hse # 42	85' R
3+33			5.3	1200.4	Floor elevation of Hse " 48	38' R
"			9.2	1196.6	elev. on 4" V.C. line " "	62' R
"			8.9	1197.0	ground at Low cor. (S.W.) "	80' R
"			9.2	1196.4	back lot line "	100' R
3+65			8.9	1197.0	elev. of garage floor " "	85' R
4+00			4.91	1200.69	℄	
"			5.63	1199.97		15' R gut
"			5.17	1200.43		" C/L
"			4.87	1200.73	15' L gut	
"			4.14	1201.46	" C/L	

Profile
Notes Red. ____ Plotted ____ Job No. 1[illegible] Division No. [illegible]
No. ____ Date ____ Date ____ Survey of Maywood [illegible]
X-Sec. Notes Chkd. ____ Checked ____ Survey by Daniels Notes by [illegible] Date 12-[illegible]
No. ____ Date ____ Date ____ Map No. ____ Indexed Johnson Date ____

F.B. 1718 PG. 137

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 PG. 134
Job No. 1390 Division No. V Notes Red Plotted Profile No.
Survey of Maywood Gas Co. Date Date X-Sec. No.
Survey by Lewis Gas Notes Lewis Notes Chkd. Checked
Indexed H. C. Johnson Date Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	
T. P.		1205 60	486	1201 74	
	4 25	1204 99			
			499	1200 00	gut W end S.W. cb int.
			457	1200 42	cb " " " " "
			535	1199 64	gut S " " " "
			508	1199 91	cb " " " " "
			399	1200 90	gut W. " NW " "
			347	1200 52	cb " " " " "
			333	1200 64	gut N " " " "
			282	1200 17	cb " " " " "
4+39 93			400	1200 99	℄ int.
"			760	1199 39	73' S 1° W
			777	1199 22	W gut 73' S 1° W
			741	1199 58	" cb " "
			775	1199 19	E gut " "
			735	1199 59	" cb
4+39 42			110	1200 99	N 1° W 60 ℄
			155	1200 49	W gut " "
			103	1201 06	cb " "
BMAE 489			345	1201 54	BMAE 489 Elev. 1201.549 FB. 1568 P 124 La Venezia (N) at La Venezia (W) B" spk in cb 4'N of ℄ Prod. La Venezia (W)

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Marengo Ave
W.O. 1320 Tape No. Std.
Surveyed by J.J. Lanigan
Notes J.J.L. Date 12-
Indexed C. Johnson

F. B. 1218 PG. 139

FL. 2011

LOCATION
of
IMPROVEMENTS
on
NORTH LA VENEZIA
from
A POINT 80'± S. of EAST LA VENEZIA
to
CALAVERAS ST.
C.I. 1390

J.J. Lanigan
C.H. Lewis
H.H. Raphael
E.W. Evans

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76F3095 247 10M 1-49

F. B. 1218 Pg. 140

CALAVERAS

Sta 27 85.37
Spk. & W.
P.C. of F.B. 1709-39

ST

15.0 15.0

2765.0 2765.0

(30)

VENEZIA

Pav. Const. of Asphalt Macadam Pvmt. 22.0 Wide

14.6

R=10

0+88.0

25.5

14.6

0+72.8

Sta 0+72.33
Spk. & W.
P.C. of F.B. 1709-39

LA VENEZIA
Transit Line

0+57.0

31.7

13.9

0+43.5

R=10

0+46.8

21.8

0+25.3

23.2

14.8

0+02.8

L.A. Transit

(40)

0+02.3

21.8

13.8

0+00.3

Sta 0+00
Spk. L.T.
P.C. F.B. 1709-39

0-06.7

18.9

7.2

0-08.9

RETURN TO
LOS ANGELES COUNTY SURVEYOR
728 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No. | Notes Red. | Plotted | Job No. 1390 | Division No. | F.B. 1718 | Pg. 141

Date | Date | Survey of Marengo Avenue

X-Sec. No. | Notes Chkd. LCM | Checked | Survey by Lanigan | Notes Lewis | Date 12-5-50

Date 12/29/50 | Date | Map No. | Blocked To | Date FEB 20 51

PROFILE
and
CROSS-SECTIONS
of
NORTH LA VENEZIA
from
A POINT 80'± S. of EAST LA VENEZIA
to
CALAVERAS STREET

C.I. 1390

V.V. Lanigan
C.H. Lewis
H.H. Raphael
E.W. Evans

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

76L298 307 5-49

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1778 PG. 142
Job No. 1390 Division No. V Notes Red Date Plotted
Survey of Valencia Avenue Date
Survey by Lawrence Notes Date Checked
Indexed K. C. Johnson Date Notes Chkd Date
Profile No. X-Sec. No.

STATION	B. S.	H. I.	F. S.	ELEV.	
BM AE 489	3 45	1205 00		1201 55	BM AE 489 Elev. 1201.549 FB 1576 & P 124
					La Venezia (N) at La Venezia (W)
					Bt. spk. in curb 4'N of ℄ prod. of La Venezia (W)
0+00			7 60	1197 40	
0-30			8 5	1196 5	
"			8 2	1196 8	
"			9 3	1197 7	70' W'ly
			5 34	1200 27	gut S end S.W. cb not
			5 07	1199 93	cb " " " " "
			4 98	1200 02	gut W " " " "
			4 58	1200 42	cb " " " " "
0+53 4			4 84	1200 16	brk in East curb Bot
0+53 5			4 26	1200 74	" " " Top
0+72 33			4 00	1201 00	℄ int La Venezia S N & W
			3 99	1201 01	gut - W end NW cb not
			3 47	1201 53	cb " " " " "
			3 32	1201 68	gut N " " " "
			2 81	1202 19	cb " " " " "
1+10			2 28	1202 72	
"			2 48	1202 52	15' R gut
"			2 02	1202 98	" cb

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. Division No.
No. Date Survey of Valencia Avenue
X-Sec. Notes Chkd. Checked Survey by Lanigan Notes Lewis Date 12-6-50
No. Date Date Map No. Unrecorded Date F.B. 178 PG. 143

STATION	B. S.	H. I.	F. S.	ELEV.	North by Valencia	
1+10		120500	263	120237	15' L gut	
"			214	120286	" cb	
T.P.			024	120476		
	10 70	121546				
2+00			813	120733		℄
"			864	120482		15' R gut
"			815	120731		" cb
"			840	120706	15' L gut	
"			797	120749	" cb	
2+62			441	121105		℄
"			442	121104		15' R cb (no gut)
"			438	121108	15' L cb (no gut)	
2+65			463	121083		℄
"			470	121076		15' R gut
"			422	121124		cb at end
"			460	121086	15' L gut	
"			414	121132	" cb at end	
			392	121154	℄ int. La Veneza & Calaveras St.	
			463	121083	℄ Calaveras 100' E	
			549	120997	S gut " "	
			505	121041	cb	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 PG. 144
Job No. 1290 Division No. V Notes Red. Plotted Profile No.
Survey of Malibu Canyon Date Date X-Sec. No.
Survey by Lanigan Notes Lewis Notes Chkd. Checked
Indexed C. Johnson Date Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	North La Veneza La	North La Veneza La
		1215 46	336	1213 10	& Calaveras 100' W 1'4	
			391	1213 55	Spot " "	"
			342	1213 04	" ch " "	"
BM AE 364			333	1212 13	BM AE 364 Elev. 1212.134 FB. 1568 P. 28	
					Calaveras St. (N. side) at La Veneza La	
					Bt. spot in curb 5' E of ℄ prod of La Veneza La	

Profile Notes Red. Plotted Job No. 1390 Division No.
No. Date Date Survey of Malonga Tract
X-Sec. Notes Chkd. CCH Checked Survey by Lanigan Notes Lewis Date 10-3-51
No. Date 10/9/51 Date Map No. Indexed Date

F. B. 7718 Pg. 145

PROFILE OF CHIAVERAS STREET

24' N. of CENTER LINE

FROM

FAIR OAKS AVENUE

TO

RAYMOND AVENUE

C.I 1390

V. V. Lanigan
C. H. Lewis
H. H. Raphael
H. Tatoya

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.

96L298 377 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

- Do not extend notes this side of this line.

Profile Plotted Date No. X-Sec. Checked Date No.
Notes Red Date
Notes Chkd Date
Job No. 4390 Division No.
Survey of Alcazar Ave.
Survey by Lanigan Notes Lewis
Indexed Date
Pg 46
4718

STATION	B. S.	H. I.	F. S.	ELEV.	24' N of ℄ of Calaveras St
BM AE 267	3 50	1217 85		1214 35	AE 267 El. 1214.354 FB 1447 P 245
					Fair Oaks Ave. (W. side) at Calaveras St
					Bt. spk in curb, 28' N of ℄ prod.
0 + 40±			2 5	1215 4	
1 + 00			1 8	1216 1	
1 + 50			2 1	1215 8	
1 + 80±			2 35	1215 50	Top of conc. driveway curb
"			3 93	1213 92	bot " " "
1 + 90±			3 76	1214 09	" " " "
"			262	1215 23	Top " " "
"			3 97	1213 88	bot " " "
1 + 98			3 93	1213 92	" " " "
"			261	1215 24	Top " " "
2 + 50			1 9	1216 0	
2 + 88±			3 94	1213 91	Wedge macadam drive
2 + 97±			4 17	1213 68	E " " " bot conc curb
"			3 59	1214 26	Top " "
3 + 00			3 5	1214 4	
3 + 50			3 8	1214 1	
4 + 00			3 6	1214 3	

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ Notes Red. ____ Plotted ____ Job No. 1398 Division No. ____
X-Sec. No. ____ Date ____ Notes Chkd. ____ Date ____ Checked ____ Date ____ Survey of Marengo Ave. Survey by Lanigan Notes Lewis Date 10-5-51 Map No. ____ Indexed ____ Date ____
F.B. 1718 PG. 147

STATION	B. S.	H. I.	F. S.	ELEV.	24' N of ℄ of Calaveras St.
		1217 85			
T.P			6 04	1211 81	
	280	1214 61			
4+50			0 5	1214 1	brk - top of bank
4+51±			1 89	1212 72	Wedge of conc. drive
4+58			1 88	1212 73	E " " " "
4+59			0 9	1213 7	brk Top of bank
5+00			0 7	1213 9	
5+10±			2 24	1212 37	W edge conc. drive
5+19			2 19	1212 42	E " " "
5+25			0 7	1213 9	brk
5+50			0 9	1213 7	
5+68			1 3	1213 3	brk
5+71			2 83	1211 78	W edge conc. drive
5+78			2 80	1211 81	E " " "
5+80			1 4	1213 2	brk
6+00			1 6	1213 0	
6+25			1 6	1213 0	brk
6+28			2 78	1211 83	W edge macadam drive
6+38			2 84	1211 77	E " " "
"			2 34	1212 27	" " " Top conc curb

76L298 307 5-49

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. PG. 148 Job No. 1390 Division No. Profile No. X-Sec. No.
Survey of Marengo Ave
Survey by Lanigan Notes Lewis Plotted Date
Indexed Notes Red. Date
Notes Chkd. Date
Checked Date

STATION	B. S.	H. I.	F. S.	ELEV.	24' N. of ℄ of Calaveras St.
		1214 61			
6+50			24	1212 2	
6+92			25	1212 1	brk
6+94			318	1211 43	W edge conc drive
7+02			325	1211 36	E " " "
7+04			29	1211 7	brk
7+19			293	1211 88	Top of curb } double curb
			300	1211 61	bot
7+21			291	1211 70	Top of curb
			321	1211 40	bot of curb W edge macadam drive
7+32			315	1211 46	bot of curb E " " "
"			299	1211 62	Top " " " " " "
7+50			25	1212 1	
8+00			27	1211 9	
8+11			320	1211 41	W. edge conc. drive
8+29			338	1211 23	E " " "
8+50			26	1212 0	
T.P.		1	467	1209 94	
	456	1214 50			
9+00			19	1212 2	
9+27			23	1212 2	brk

764298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.		
		1214.50				
9+30			3.31	1211.19	W. edge conc. drive	
9+39			3.38	1211.12	E " " "	
9+50			2.7	1211.8	bk	
9+90			2.25	1211.25	W. edge conc. drive	
9+97			3.40	1211.10	E. " " "	
10+00			3.5	1211.0		
10+05			3.52	1210.98	W. edge conc drive	
10+12			3.53	1210.97	E " " "	
10+50			3.0	1211.5		
10+65			2.7	1211.8		
BM. AE363			4.73	1209.77	AE 363 El 1209.781 FB 1568 P. 22	
					Calaveras St. (S. side) at Raymond Ave.	
					Bt. spk in curb 5' W of ℄ prod Raymond Ave.	

Profile Notes Red.____ Plotted____ Job No. 1390 Division No.____ F.B. 7118 Pg. 149
No.____ Date____ Date____ Surv'd Mar 1958 thru
Misc. Notes Clkd.____ Checked____ Survey by Berridge Notes Lewis Date 3-31-58
No.____ Date____ Date____ Map No.____ Indexed____ Date____

F. B. 1718 Pg. 50 Job No. 1390 Division No. Notes Red. Plotted Profile

Survey of Malengo Ave. Date Date No.

Survey by Lanigan Notes Lewis Notes Chkd. Checked X-Sec.

Indexed Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.

Do not extend notes this side of this line.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR

726 Los Angeles County Engineering Bldg.

76L298 307 4-56

Notes Ck'd by	Survey of Malaga Ave.
Map No.	W.O. 4525 Tape No. Std.
Office Work	Surveyed by J.J. Lanigan
Checked	Noted J.J.L. Date 12-1-59
Date	Indexed

F. B. 1115 PG. 37

Notes: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not erase notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County
ENGINEERING BLDG.

LOCATION
of
IMPROVEMENTS
on
S'ely LINE of LOTS #4 TO #7 inc. TRACT #4523
from
RAYMOND AVE.
to
FERRY LINE of LOT #3 TRACT #4523
C.L. 1390

J. J. Lanigan
C. H. Lewis
A. H. Dorham
D. Tafoya

76 5095 847 10M 1-49

F. B. 1718 Pg. 132

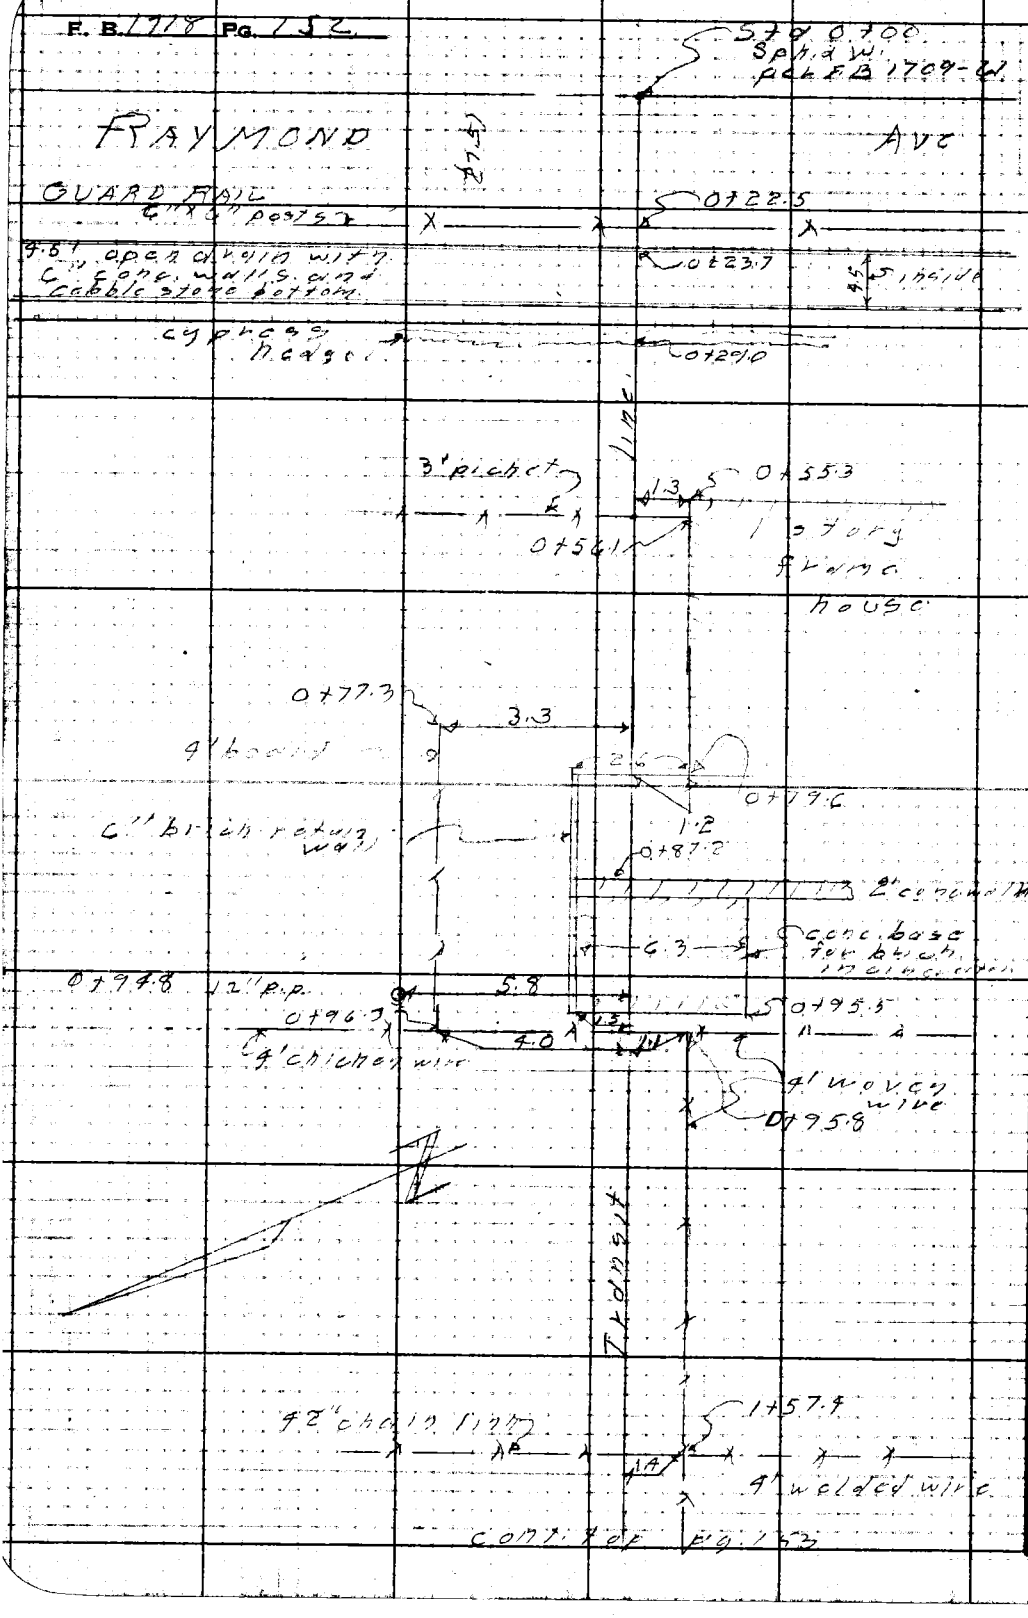

RETURN TO
LOS ANGELES COUNTY SURVEYOR
728 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Noted Ck'd by:	Survey of: Marengo Ave.
Map No.	W.O. 1390 Tape No. Std. °F
Office Work:	Surveyed by: J. J. L. Arriaga
Checked	Notes J.J.L. Date 10-11-57
Date	Indexed

F. B. 1775 PG. 13

Notes: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
720 LOS ANGELES COUNTY
ENGINEERING BLDG.

7SF3D9S 247 10M 1-49

Cont. Bg. 84.134

4" W. oil and wire

1.3 2+15.9

0.9 2+17.9

4.2" chain link

2+33.2 1" orange 5.5

Fence covered with grapevine

2+40.8 2" lemon 3.6

2+57.3 10" Sig. 5.7

2+68.0 2" orange 5.7

0.9 2+77.1

4" power wire

2+80.0 12" pomegranate 2.3

2+91.6 2.1

4 shrubs

3+23.2 shrub 3.0

4" power wire

3+36.3

4" power wire

Trench

3+92 10" shade 1.6

Cont. top pg. 14

F. B. 1218 Pg. 154

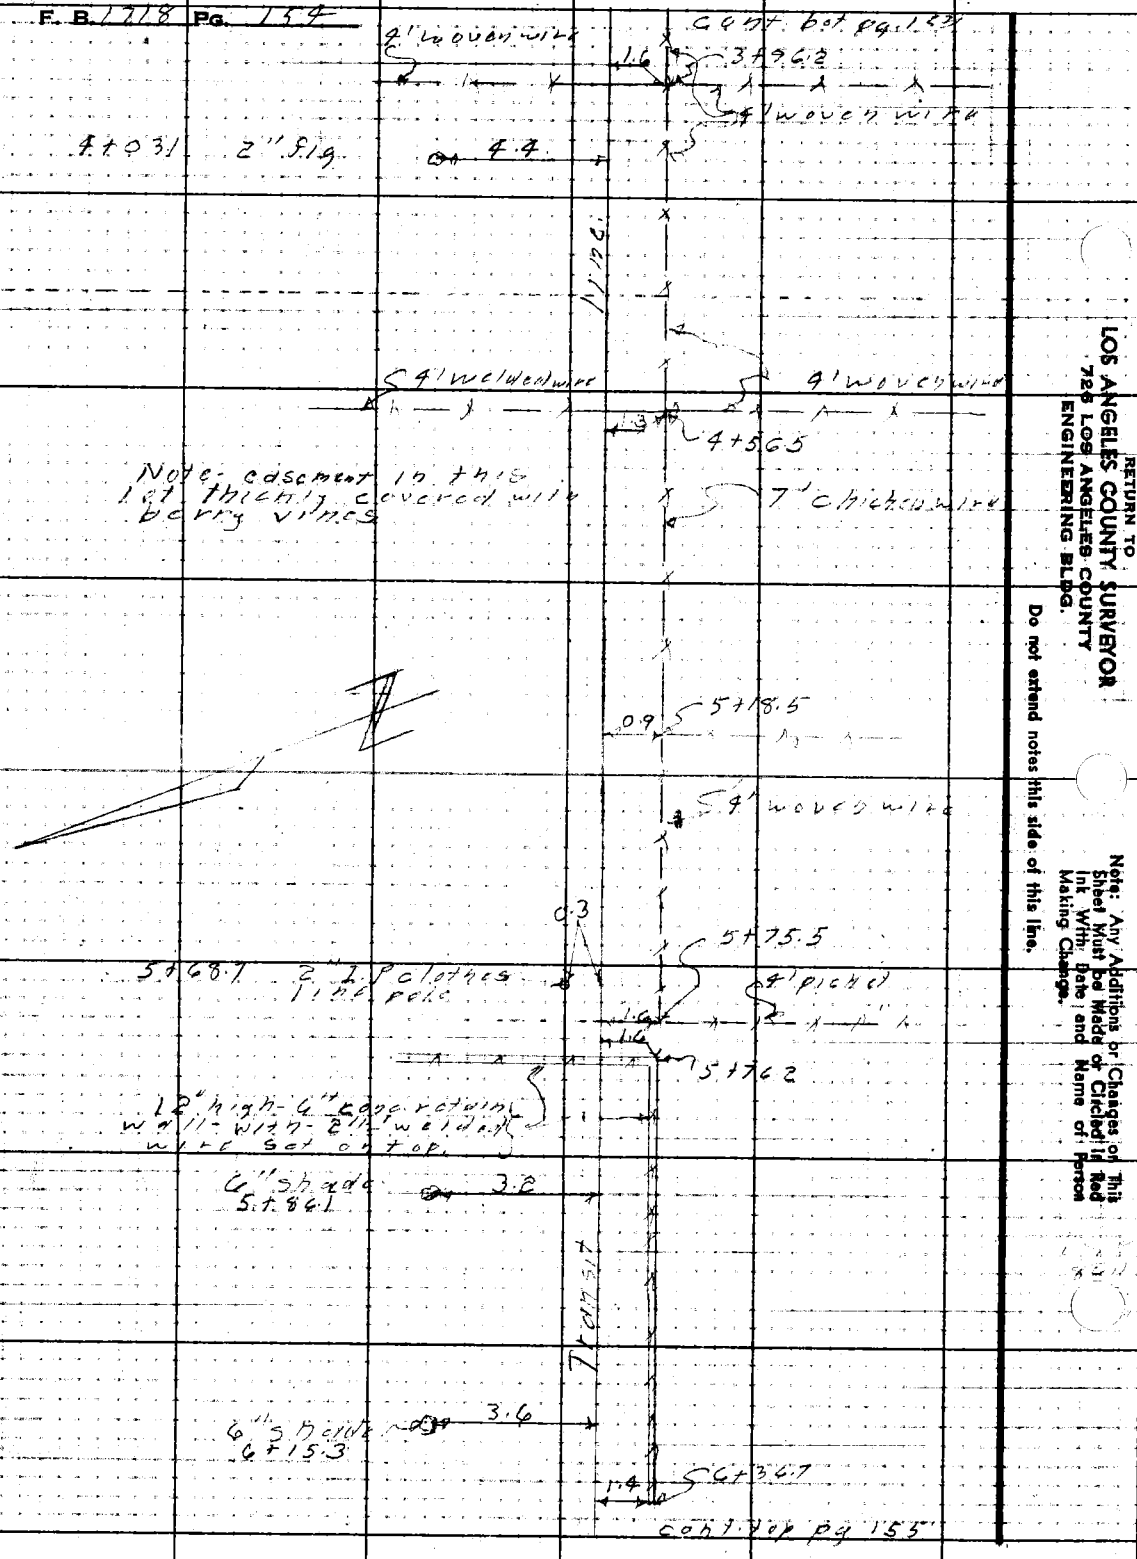

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Maricopa Ave
W. O. 340 Supp. No. Std. "B"
Surveyed by Hall Lanigan
Notes J.V.E. Date 10-11-39
Indexed

F. B. 176 Pg. 154

Notes: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
728 LOS ANGELES COUNTY
ENGINEERING BLDG.

76F3095 247 10M 1-49

Corr. Cor. pg. 153

6+623 3" dead end 1.7

6+926

1.6

9' woven wire

Transit

7154 group of 3 cotton 3.0
9' woven wire

7157.8

5' woven wire

7+837 6' hedge (end line)

7+945.0

8+02.0 6" Sig 5.1

8+08.1

3.3 1.8

brick chamber 1.8

5' woven wire

0.8

8+17.0

5' woven wire

8+23.1 2" I.P. post 4.2

cont. top pg. 155

F. B. 1718 Pg. 154

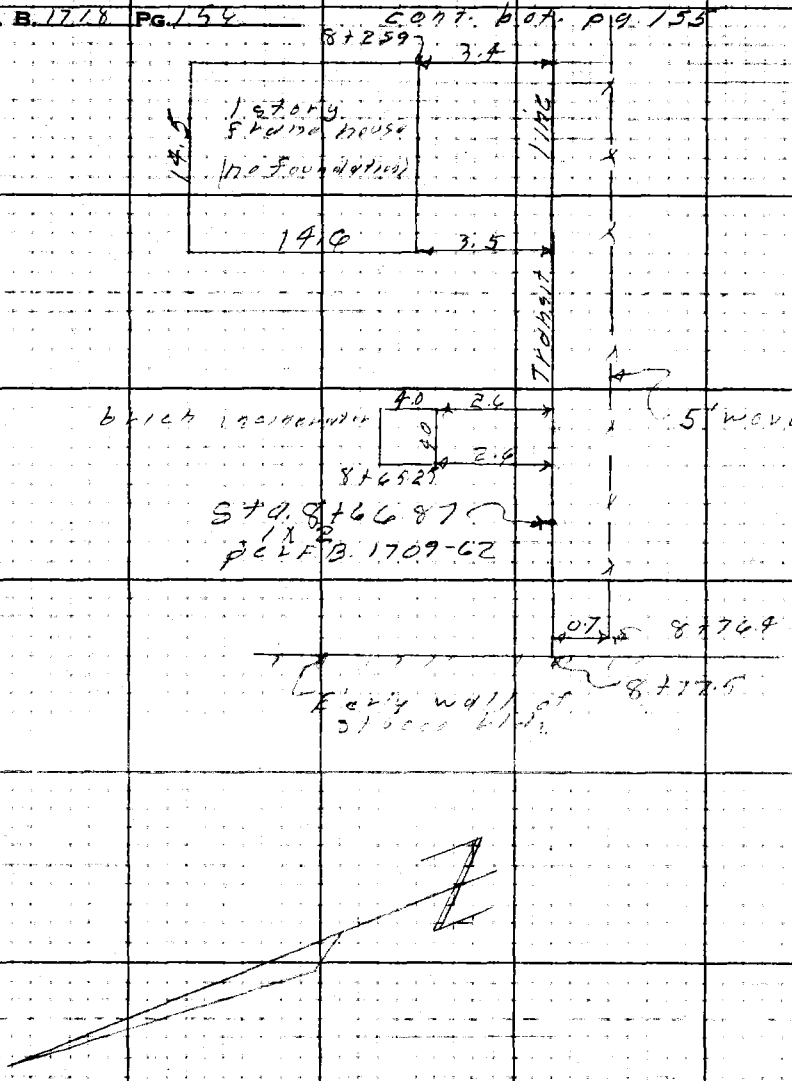

RETURN TO
LOS ANGELES COUNTY SURVEYOR
720 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made in Red Ink With Date and Name of Person Making Change.

Profile No. | Notes Red. | Plotted | Job No. 1390 | Division No. | F. B. 1718 | Pg. 15-7
Date | Date | Survey of Orange Ave. Ext.
X-Sec. No. | Notes Chkd. | Checked | Survey by Hanigan | Notes Lewis | Date 10-17-51
Date 10/23/51 | Date | Map No. | Indexed | Date

PROFILE
AND
CROSS-SECTIONS
OF
SANITARY SEWER R/W
IN
TRACT # 4523

C.I. 1390
S'erly Line of Lots 4 to 17 inc.
Tr. 4523
Raymond Ave to West.

V.V. Hanigan
C.H. Lewis
H.H. Raphael
H. Tafoya

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

764.298 307 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 Pg. 1578 | Job No 2390 Division No. | Notes Red. | Plotted | Profile
Survey of Alameda St & Aliso Ave. | Date | Date | No.
Survey by Lewis & Gan | Notes Lewis | Notes Chkd. | Checked | X-Sec.
Indexed | Date | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	Lot	Line
BM AE 477	0 36	1229 77		1229 41	AE 477 El 1229.441	FB W68 P 112
T. P			991	1219 86	Raymond Ave (E. side) at Harriet St	
	4 58	1224 44			Bt. spk in cut L 5' N. of & prod of Harriet St.	
0 + 00			463	1219 81	Int of Lot Line prod & E of Raymond Ave	
0 + 23			690	1217 54	edge of ditch.	
"			672	1217 72	"	6' R
0 + 25			943	1215 01	Bot of Ditch	
"			917	1215 27	"	6' R
0 + 28			688	1217 56	wedge of ditch	
"			671	1217 73	"	6' R
0 + 50			6 3	1218 1		
"			5 9	1218 5		6' R
1 + 00			5 0	1219 4		
"			4 7	1219 7		6' R
T. P.			2 40	1222 04	TP	
	3 99	1226 03				
2 + 00			4 9	1221 1		
"			4 8	1221 2		6' R
3 + 00			5 2	1220 8		
"			5 1	1220 9		6' R

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. 390 Division No. F.B. 1758 Pg. 159
No. Date Date Survey of Drainage Area
X-Sec. Notes Chkd. Checked Survey by Lanigan Noted Lewis Date 10-14-57
No. Date Date Map No. Indexed Date

STATION	B. S.	H. I.	F. S.	ELEV.	Lot	Line
		1226 03				
4+00			6 0	1220 0	Lot line	
"			5 9	1220 1		6' R
5+00			4 6	1221 4	"	
"			4 4	1221 6		6' R
T.P.			239	122364	T.P.	
	3 84	122748				
5+76 2			5 1	1222 4	bot of conc ret wall at Lot Line	
"			5 1	1222 4		bot of wall 6' R
5+76 8			382	122366	Top of wall at Lot Line	
"			385	122363		Top of wall 6' R
5+77 5			4 3	1223 2	bot of wall 0.5' R	
"			4 4	1223 1		bot of wall 6' R
6+00			393	122355	Top of wall	
"			4 5	1223 0		0.5' R Bot of wall
"			4 5	1223 0		6' R
6+36 7			383	122365	Top of wall on Lot Line	
"			320	122428	Top of wall 6' R	
7+00			3 4	1224 1		
"			3 0	1224 5		6' R

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 1718 Pg. 160 | Job No. 2390 Division No. | Profile | Notes Red. | Plotted | No. | X-Sec. | No.
Survey of Dogwood Ave | Date | Date | Date | Date
Survey by Lewis | Notes Lewis | Notes Chkd. | Checked
Indexed | Date | Date | Date

STATION	B. S.	H. I.	F. S.	ELEV.	Lot	Line
		1227 48				
T. P.			2 34	1225 14	TP	
	4 71	1229 85				
8+00			5 5	1224 4	Lot Line	
"			5 3	1224 6		C / R
8+76.4			4 7	1225 2	" "	
"			4 6	1225 3		C / R
T. P.		1	0 17	1229 68		
	10 72	1240 40				
BM AE 484			2 91	1237 49	AE 484 El 1237.491 Donnally Ave. & Harriet St. NW Cor. at spk in curb 10' N of S. end	FB 1568 P. 122

Notes Ck'd by	Survey of MARENGO AVE
Map No.	W. O. 1390 Tape No. Std. °F
Office Work	Surveyed by J.J. Lonigan
Checked	Notes J.J.L. Date 8-7-57
Date	Indexed

F. B. 78 PG. 61

Note: Any Additions or Changes of This Sheet Must Be Made or Circled in Red Ink, With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
of
IMPROVEMENTS
in
ABANDONED R/W
Between
CALAVERAS ST
and
MENDOCINO ST
From
MARENGO AVE
to
RAYMOND AVE
C.I. 1390

J.J. Lonigan
C.H. Lewis
H.H. Rapinac
H. Tatoya

76F3095 247 10M 1-49

F. B. 1709 Pg. 142

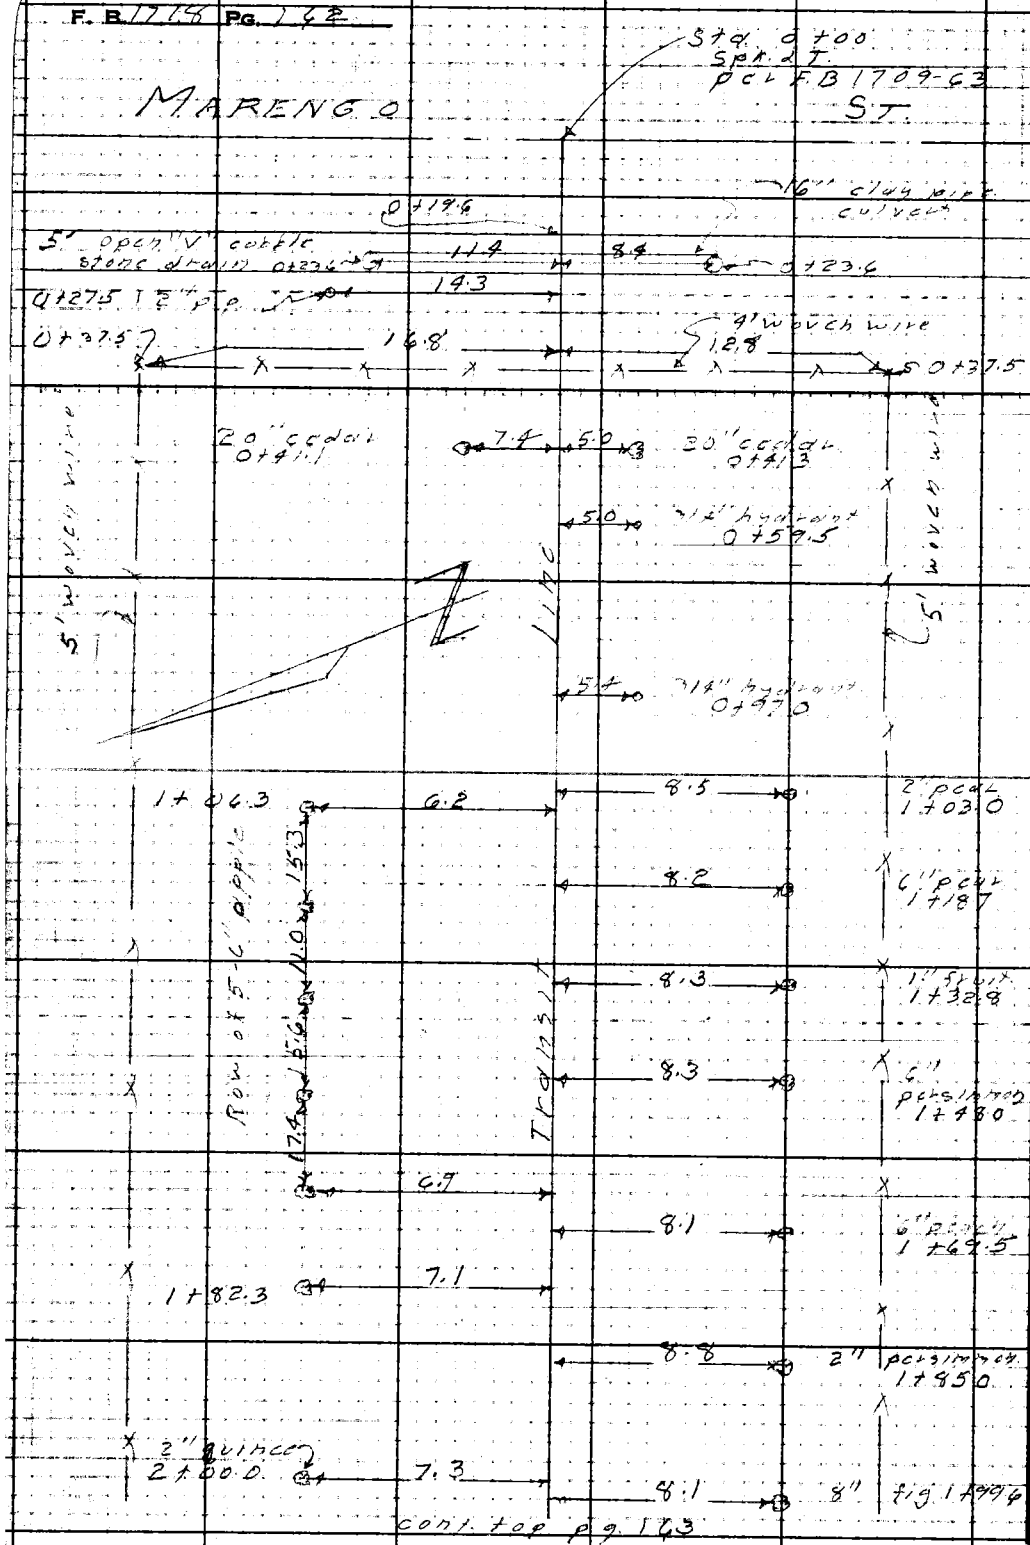

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Alameda Ave.
W. O. 3[illegible] Tape No. Std. °F
Surveyed by V. V. Lapiana
Noted J. L. Date 10/17/39
Indexed

F. B. [illegible] Pg. [illegible]

Notes: Any Additions or Changes of This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

7 6 3 0 9 5 R 4 7 10M -49

1" overcrossing
2+17.3

10" asbestos
2+18.0

12.6 3.5 2+35.6

Lathe house
conc. foundation

80.0

12.6 3.5

3" W.V.C.P.

9.5

3" gum
2+84.0

7.0

3/4" hydrant
3+20.0

8.9

3" gum
3+26.2

9.6

2" gum
3+49.2

3+61.1

6" shade
3+64.0

3.3

8" shade

6.0

11.1

12.8

6.8

3+62.0

3+66.7

3+66.7

pc.g. mine. pav.

Tropisit

cont. top pg. 147

F. B. 1718 Pg. 164 cont. to pg. 163

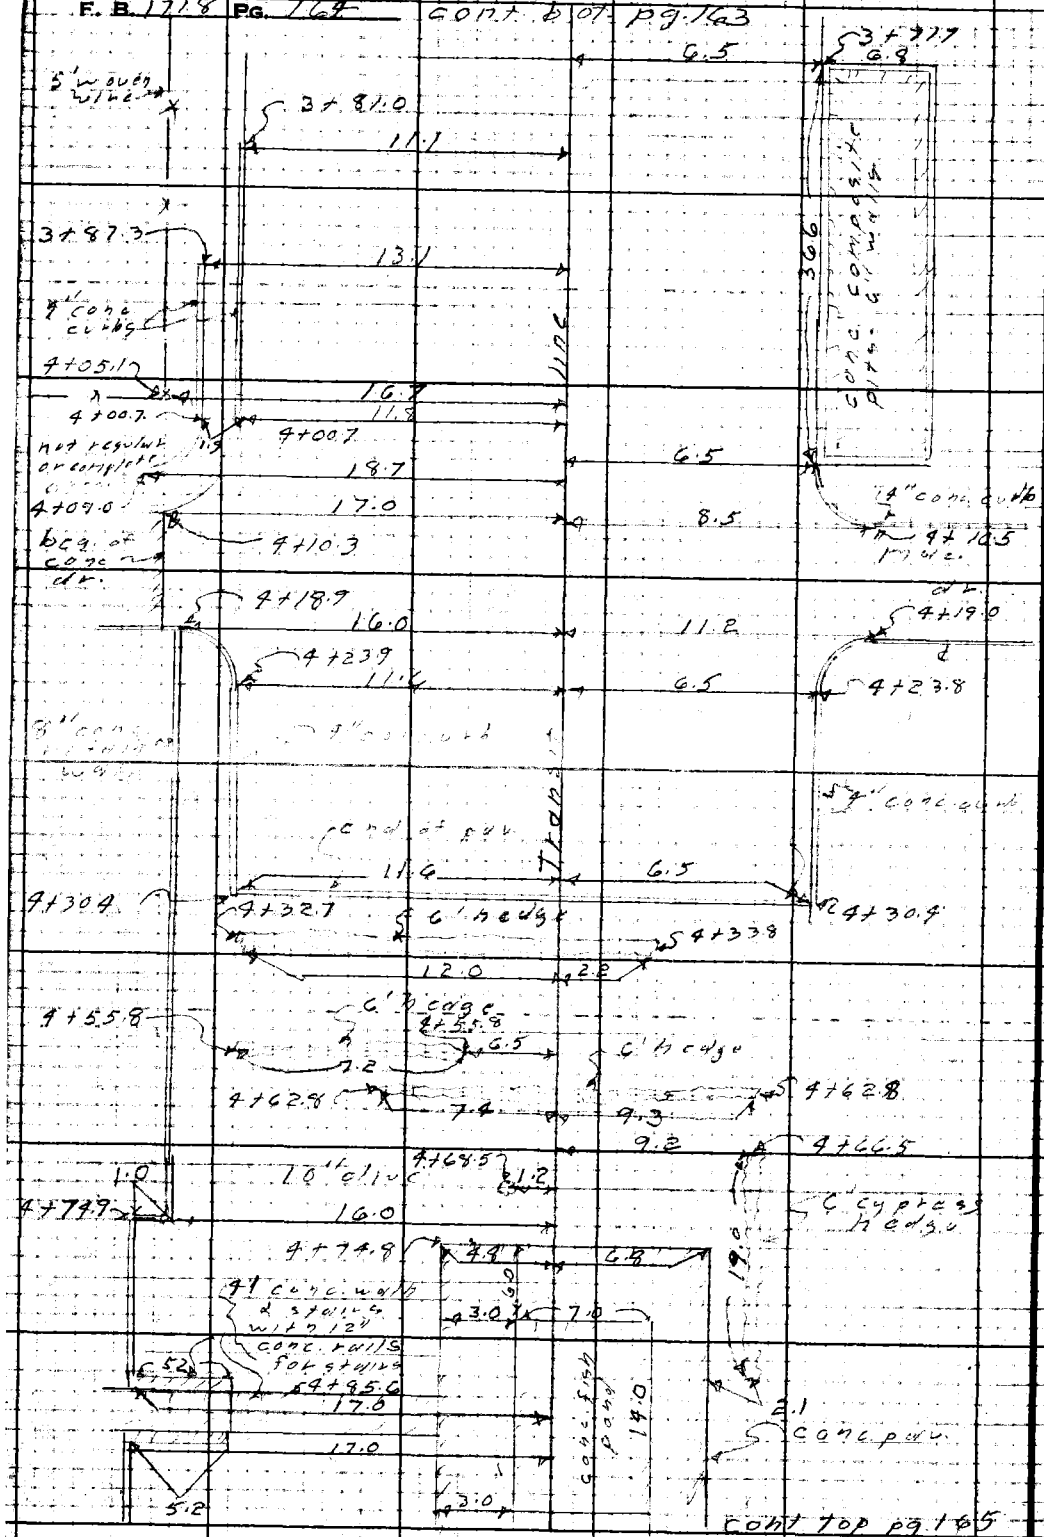

cont. top pg. 165

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by	Survey of Marengo No. 1
Map No.	W. O. 3340 Tape No. Std. °F
Office Work	Surveyed by J. S. Lamm 1944
Checked	Notes Date 10-7-57
Date	Indexed

F. B. 1178 PG. 165

Cont. to of pg 162

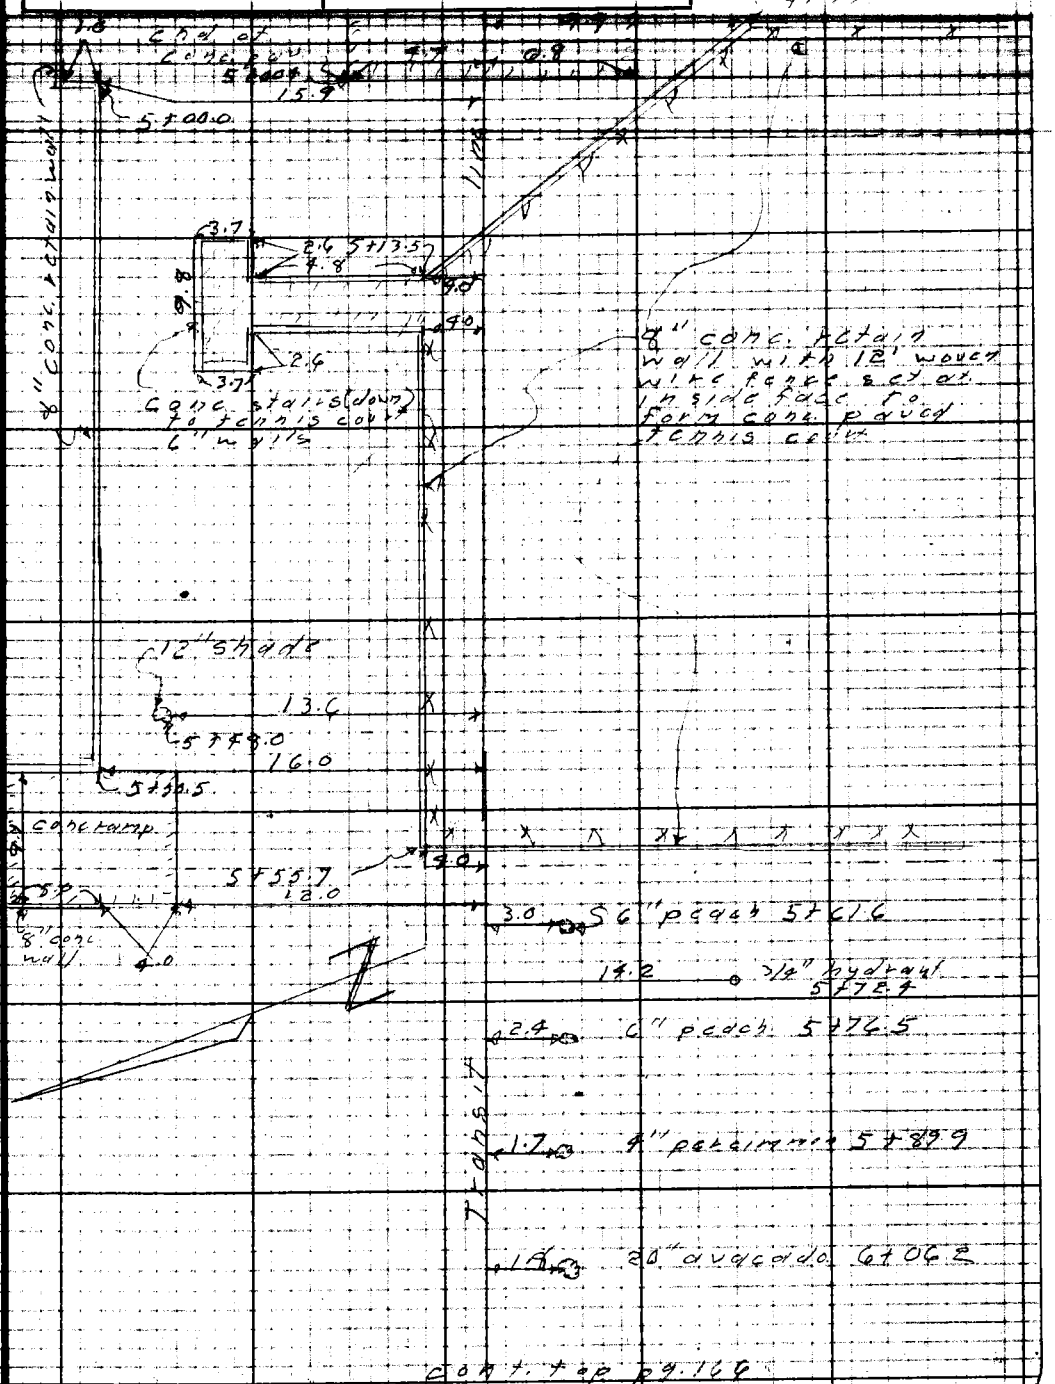

Notes: Any Additions or Changes of This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

767-3088 247 10M 1-49

F. B. 1778 PG. 168

cont. to pg. 169

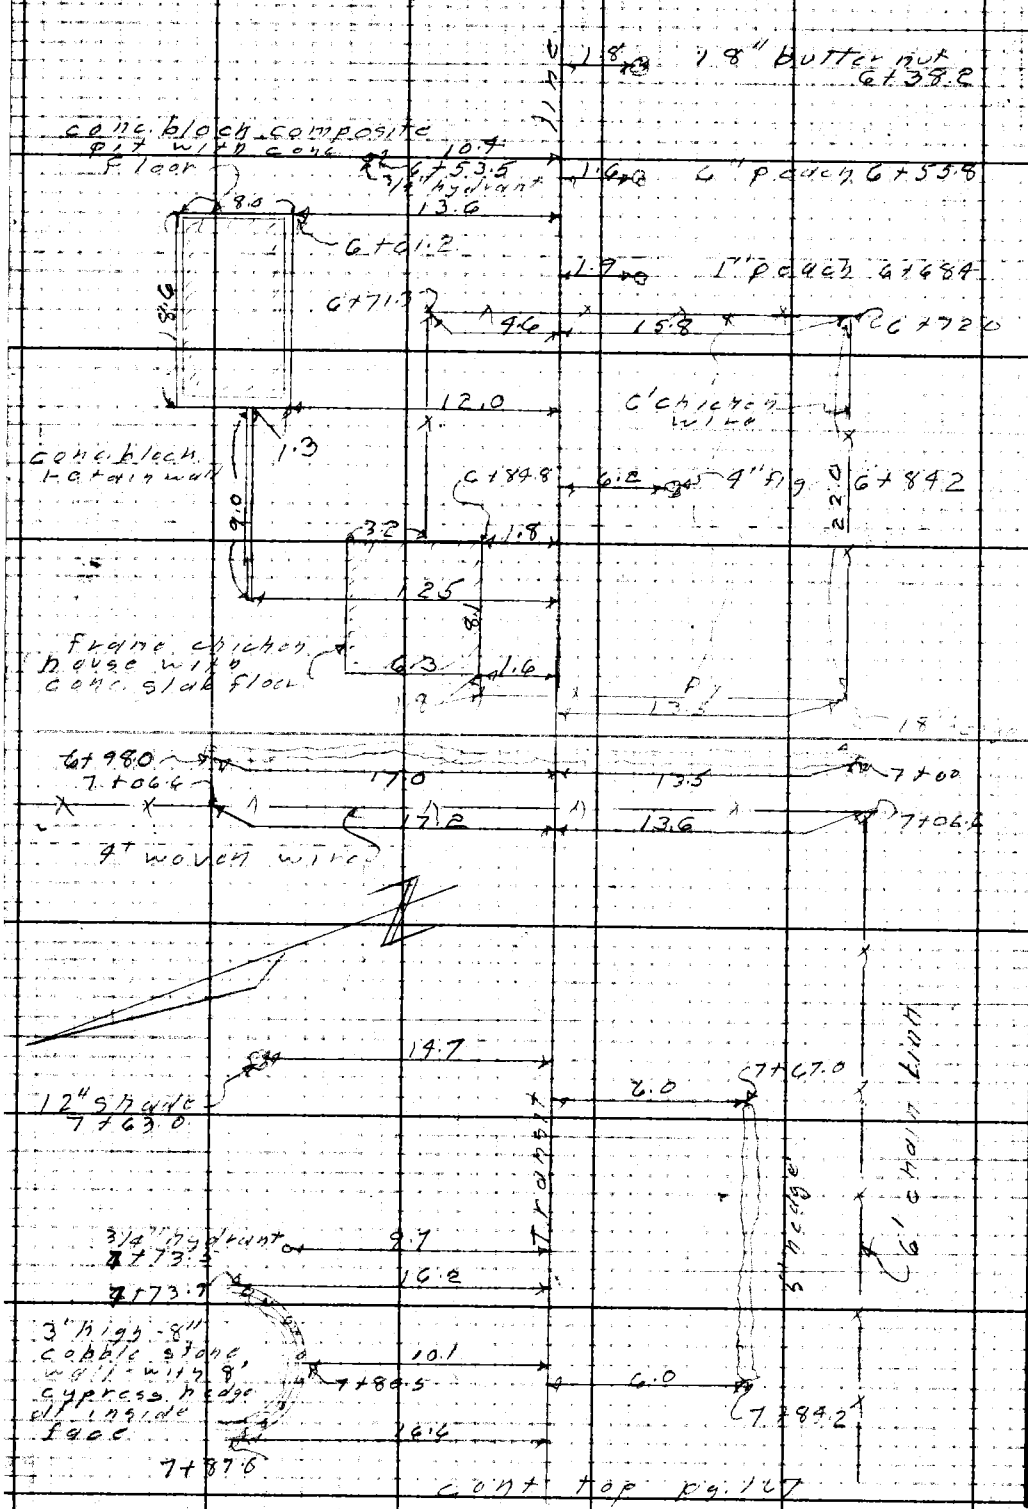

cont. top pg. 167

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Noted Ck'd by	Survey of Mariposa Ave
Map No.	W. O. 5320 Tape No. Std. °F
Office Work	Surveyed by: J.J. Gallagher
Checked	Notes J.J.L Date 10/22/57
Date	Indexed

F. B. 178 Pg. 167

Notes: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

7+87.2
St. P.C.
5+21.6
5'
11.4
10.0
11.4
6" shed
8+01.8
16.5
1.0
1.2 plum
9+02.0
11.4
6.9
5.7
8+19.0
18" oak
8+26.5
Lath & Plaster House
17.0
20.0
N.C. Foundation
Transit
7.1
5.0
8+43.6
2-6" shade
5.2
2.8
2.8
5.0
11.7
2-2" oak
8+49.6
8+49.5
12" cobble retaining wall with 2' woven wire fence on top
13.2
5.9
14" deadard
8+51.3
14" deadard
8+50.8
8+63.1
12½" conc. gutter
RAYMOND
AVE
Sta 8+73.79
Spike in
pc-F.B. 170-24

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

F. B. 7178 Pg. 108

F. B. 1714 PG. 169

Profile No. — Notes Red Lewis — Plotted — Job No. 1390 — Division No.
Date 10-17-51 — Date — Survey of Marengo Avenue
X-Sec. No. — Notes Chkd. — Checked — Survey by [illegible] Notes Lewis Date 10-18-51
Date 10/23/51 — Date — Map No. — Indexed — Date

PROFILE and CROSS-SECTIONS OF ABANDONED RIGHT OF WAY IN BLOCK 27, M.R. 16-45-46

C.I. 1390

Between
Calaveras St & Mendocino Ave
and
Marengo Ave & Raymond Ave.

J.N. Lanigan
C.H. Lewis
H.H. Raphael
H. Tatoya

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

76L298 307 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 1718 Pg. 170 | Job No. 1290 Division No. | Notes Red. | Plotted | Profile
Survey of Mancini-Lemgo Ave. | Date | No. | X-Sec.
Survey by Lerman Notes Keuffel | Notes Chkd | Checked | No.
Indexed | Date | Date | Date

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	℄ Lane
BM AE 470	10 50	1238 65		1228 15	AE 470 El. 1228.15 FB 1568 P. 106 Marengo Ave. (E. side) 260'± N of ℄ of Glenrose St. Bt sph. in drive to Ho # 2484	
0+00			4 24	1234 41	Int. of transit line & ℄ of Marengo Ave.	℄
"			5 15	1230 50	13' L	
"			3 23	1235 42		17' R
0+19 ±			4 83	1233 82	edge of pvmt	℄
"			5 83	1232 82	13' L " " "	
"			4 02	1234 63	" " "	17' R
0+24 ±			4 9/10	1232 8/10	on driveway	℄
"			5 1/10	1233 0/10	9' L " "	
"			7 73	1230 92	13' L bot ditch	
"			4 4/10	1234 3/10		11' R on driveway
"			5 63	1232 02		17' R bot of ditch
0+24 ±			4 7/10	1234 0/10		℄
"			6 53	1232 12	13' L Top storm drain	
"			3 86	1234 79		17' R Top of drain
0+37 ±			4 3/10	1234 4/10	P. L	℄
"			5 6/10	1233 1/10	13' L	
"			3 1/10	1235 6/10		17' R

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red.____ Plotted____ Job No. 1298 Division No.____ F.B. 1718 Pg. 171
No.____ Date____ Date____ Survey of Torrance Sewer
X-Sec. Notes Chkd.____ Checked____ Survey by Lewis Notes Lewis Date 10-17-57
No.____ Date____ Date____ Map No.____ Indexed____ Date____

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
		123865				
1+00			4 3	1234 4		
"			4 5	1234 2	13'L	
"			3 6	1235 1		17'R
2+00			3 3	1235 4		
"			3 6	1235 1	13'L	
"			2 9	1235 8		17'R
T.P.		1	260	123605	T.P	
	606	124211				
3+00			5 9	1236 2		
"			6 0	1236 1	13'L	
"			5 4	1236 7		17'R
3+66 4			577	123634	beginning of	macadam
4+00			444	123767		"
"			459	123752	C 5 L mac. at edge	of compost pit
"			5 3	1236 8	13'L ground	
"			434	123777	macadam	at edge 12'R bot of curb
"			410	123801		" Top " "
"			467	123744		13' bot of gutter
"			397	123814		14'R Top of walk

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 Pg. 172 | Job No. 1390 Division No. | Notes Red. | Plotted | Profile
Survey of Marengo Ave | Date | Date | No.
Survey by Lanigan Notes Lewis | Notes Chkd. | Checked | X-Sec.
Indexed | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
		1242 11				
4+15			4 12	123799		
"			4 86	123725	13' L	
"			3 16	123895		17' R edge of mac. beg conc drive
4+30±			4 04	123807		
"			4 24	123787	7± L edge macadam	
"			5 0±	123701	13' L	
"			3 84	123827		12' R edge mac.
"			3 78	123833		16' R bot ret wall
"			2 57	123954		" Top " "
T.P.			5 20	123791	T.P @ 5+00	
	4 44	1241 35				
4+74±			4 54	123681	NE cor. fish pond slab	
"			4 56	123679	SE " " " "	
5+00±			4 41	123694	NW " " " "	
"			4 49	123686	SW " " " "	
4+88			5 92	123543	Invert of fish pond	
5+00			4 44	123691		
"			4 8	1236 6	6' L ground	
"			5 0	1236 4±	8' L " at bot of wall	
"			4 11	1237 24	8± L Top of wall	

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Rod____ Plotted____ Job No. 1390 Division No.____ F. B. 1718 Pg. 173

No.____ Date____ Date____ Survey of 7th Street Gate

X-Sec. Notes Chkd.____ Checked____ Survey by Lewis Notes Lewis Date 10-17-51

No.____ Date____ Map No.____ Indexed____ Date____

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
5+00		1241 35	7 57	1233 78	13' L bot of wall in tennis court	
"			4 6	1236 8	Ground at NW cor of slab 5' R	
"			4 9	1236 5		17' R bot wall
"			1 75	1239 60		" Top "
5+11			4 61	1236 74		10 8 R ctr Top step
5+16			5 99	1235 36		10 8 " " Landing
5+16			7 41	1233 94		7' R " bot "
"			7 50	1233 85		4' R " gateway
5+13 5			3 98	1237 37		" Top of wall 13 E
5+18 1			4 02	1237 33		" " " " 4
5+55 0			7 48	1233 87	bot of E wall in Tennis court	
5+55 7			4 03	1237 32	Top " " " " "	
5+55			7 46	1233 89	bot of wall at	4' R NW cor " "
5+55 7			4 02	1237 33	Top " " "	" "
5+20 8			4 53	1236 82		10 8 R ctr top step W
5+50 5			4 6	1236 8		16' R bot of wall W
"			1 69	1239 66		16' R top of wall W
"			3 49	1237 86		16' R ramp at wall
"			4 89	1236 46		12' R bot of step
5+59 6			4 91	1236 44		12' R " " "
"			3 52	1237 83		16' R Ramp at wall

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 1218 Pg. 174 Job No. 390 Division No. Profile
Survey of Stevenson Ave. No.
Survey by Lanigan Notes Lewis Date Notes Red. Plotted
Indexed Date Notes Chkd. Date Checked X-Sec.
Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
		1241 35				
5+59.6			1 71	1239 64		16'R Top of wall
5+56			4 9	1226 5	ground on W.	E side tennis court wall
"			5 5	1235 9	13'L " "	" " " "
"			4 9	1236 5	4'R " "	" " " "
T. P.		1	4 03	1237 33	T. P.	
	264	1240 02				
6+00			4 2	1235 8		E
"			4 6	1235 4	13'L	
"			3 9	1236 1		10'R bank
"			1 9	1238 1		17'R Top bank
7+00			3 4	1236 6		E
"			4 1	1235 3	13'L	
"			2 5	1237 35		17'R
8+00			3 4	1236 6		
"			5 7	1234 3	13'L	
"			5 5	1234 5		10'R bank
"			2 5	1237 5		17'R Top bank
T. P.		1	5 48	1234 54	T. P.	
	355	1238 09				
18+46.4			4 64	1232 45	Conc. ret. E. Wall	

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
		1238 09				
8+46 4 ±			4 93	123314	13' L Top of wall	
"			4 15	1233 94		17' R Top of wall
8+46 4 ±			7 5	1230 6		℄ bot of wall
"			7 9	1230 2	13' L bot of wall	
"			6 9	1231 2		17' R bot of wall
8+63 1 ±			9 11	1228 98		℄ Top of curb gutter
"			9 83	1228 26		
8+73 79			931	1228 78	Int Transit line & ℄ of Raymond Ave.	
EMIAB477			8 67	122942	SE 477 E/ 1229.441 FB 1568 P 12	
					Raymond Ave. (E. side) at Harriet St.	
					Rt. spk in curb 5' N of ℄ prod of Harriet St.	

Profile Notes Red. Plotted Job No. 1396 Division No.
No. Date Date Survey of Traverse Ave.
X-Sec. Notes Chkd. Checked Survey by Lewis Notes Lewis Date 10-17-57
No. Date Date Map No. Indexed Date

F. B. 1718 Pg. 175

F. B. 1718 Pg. 176 Job No. 1390 Division No. Notes Red. Plotted Profile

Survey of Florence Ave Date Date No.

Survey by Lanigan Notes Lewis Notes Chkd. Checked X-Sec.

Indexed Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.

Do not extend notes this side of this line.

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR

726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

76L298 307 4-50

177

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Maranga Ave.
W. O. 1372 Tape No. St'd. °F
Surveyed by J. J. Lonigan
Notes J. J. L Date 10-5-51
Indexed

F. B. 1118 Pg. 151

LOCATION
of
IMPROVEMENTS
on
N. SIDE of CALAVERAS
from
CURB LINE
to
PROPERTY LINE
and from
FAIR OAKS AVE
to
RAYMOND AVE.
C.I. 1390

J. J. Lonigan
C. H. Lewis
H. H. Raphael
H. Tafoya

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76F3095 247 2-51

F.B. 1718 PG. 178

comt. bot pg. 153

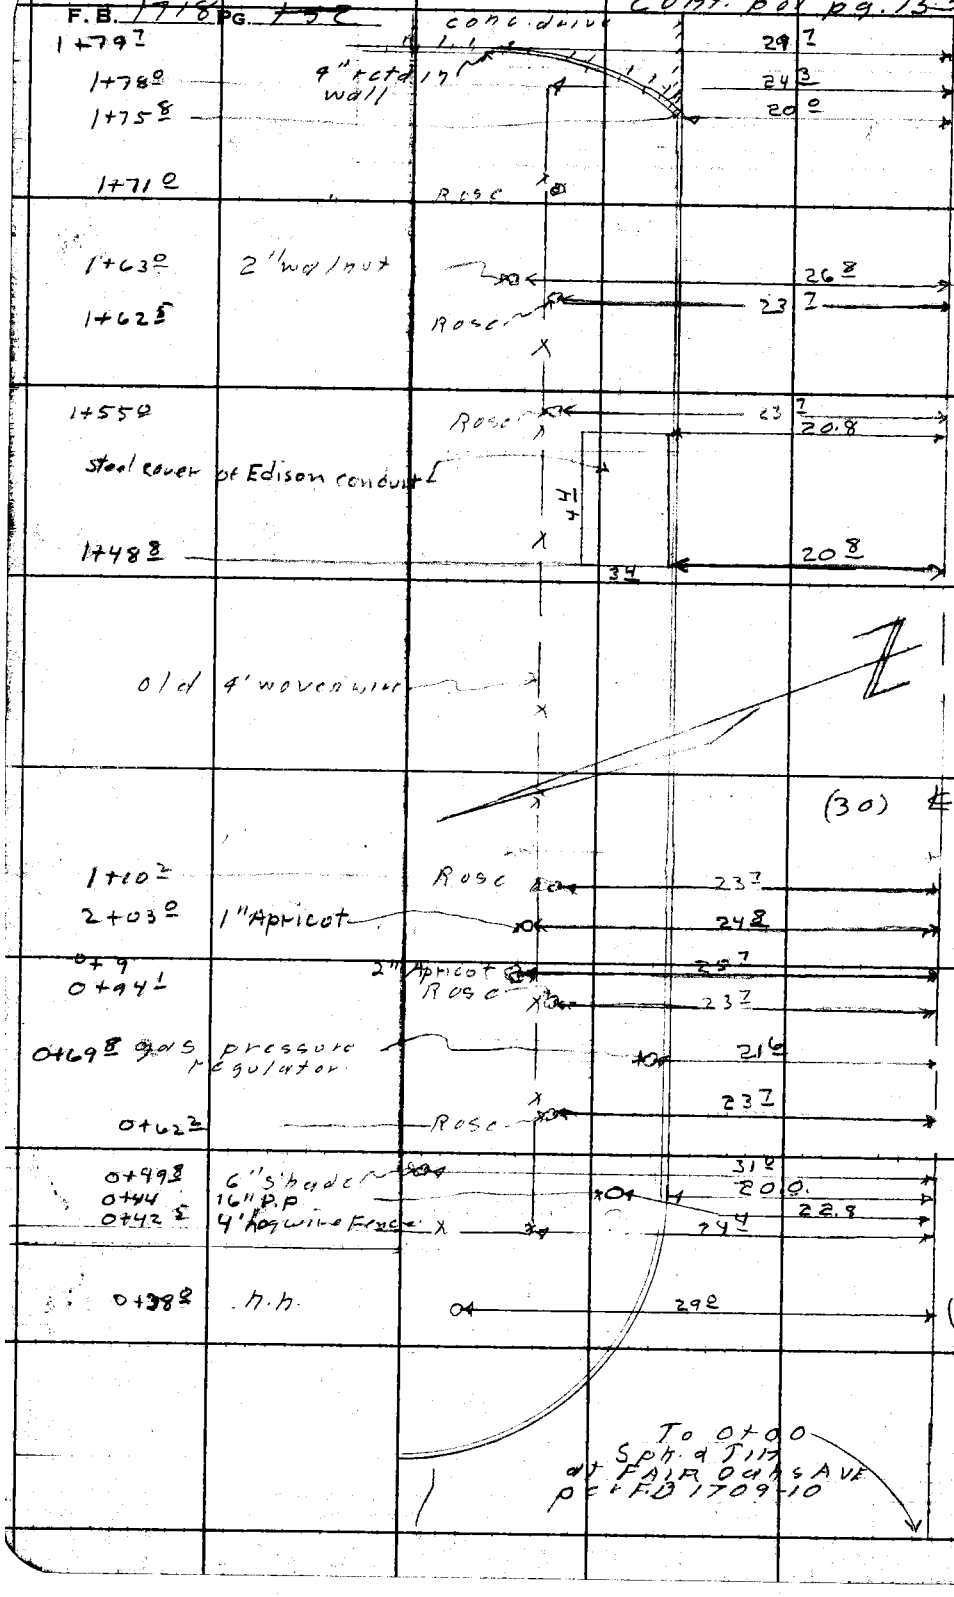

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

(379)

Notes Ck'd by	Survey of Marengo Ave.
Map No.	W. O. 1392 Tape No. St'd. °F
Office Work	Surveyed by J.J.L. Date 10-5-51
Checked	Notes J.J.L.
Date	Indexed

F.B. 1116 Pg. 153

Note: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
720 LOS ANGELES COUNTY
ENGINEERING BLDG.

cont. bot. pg. 154

(30)

2+79 8

9" conc. retaining wall

guard rail

2+56 0

2+48 4

9' conc. steps

2+44 0

2+43 5

2+43 0

end conc. wall

Rose

9' woven wire

2+26 2

18" F/G

Rose

2+23

2+22 2

10" P.P.

2+01 3

2+00 4

9" rail

2+99

Concrete wall

1+98 3

1+98 3

end conc. dr.

1+89 2 12" conc. c.u.p.

CALAVERAS ST

cont. top pg. 152

76F3095 247 2-51

180

F. B. 1718 PG. 154

cont. bot. pg. 155

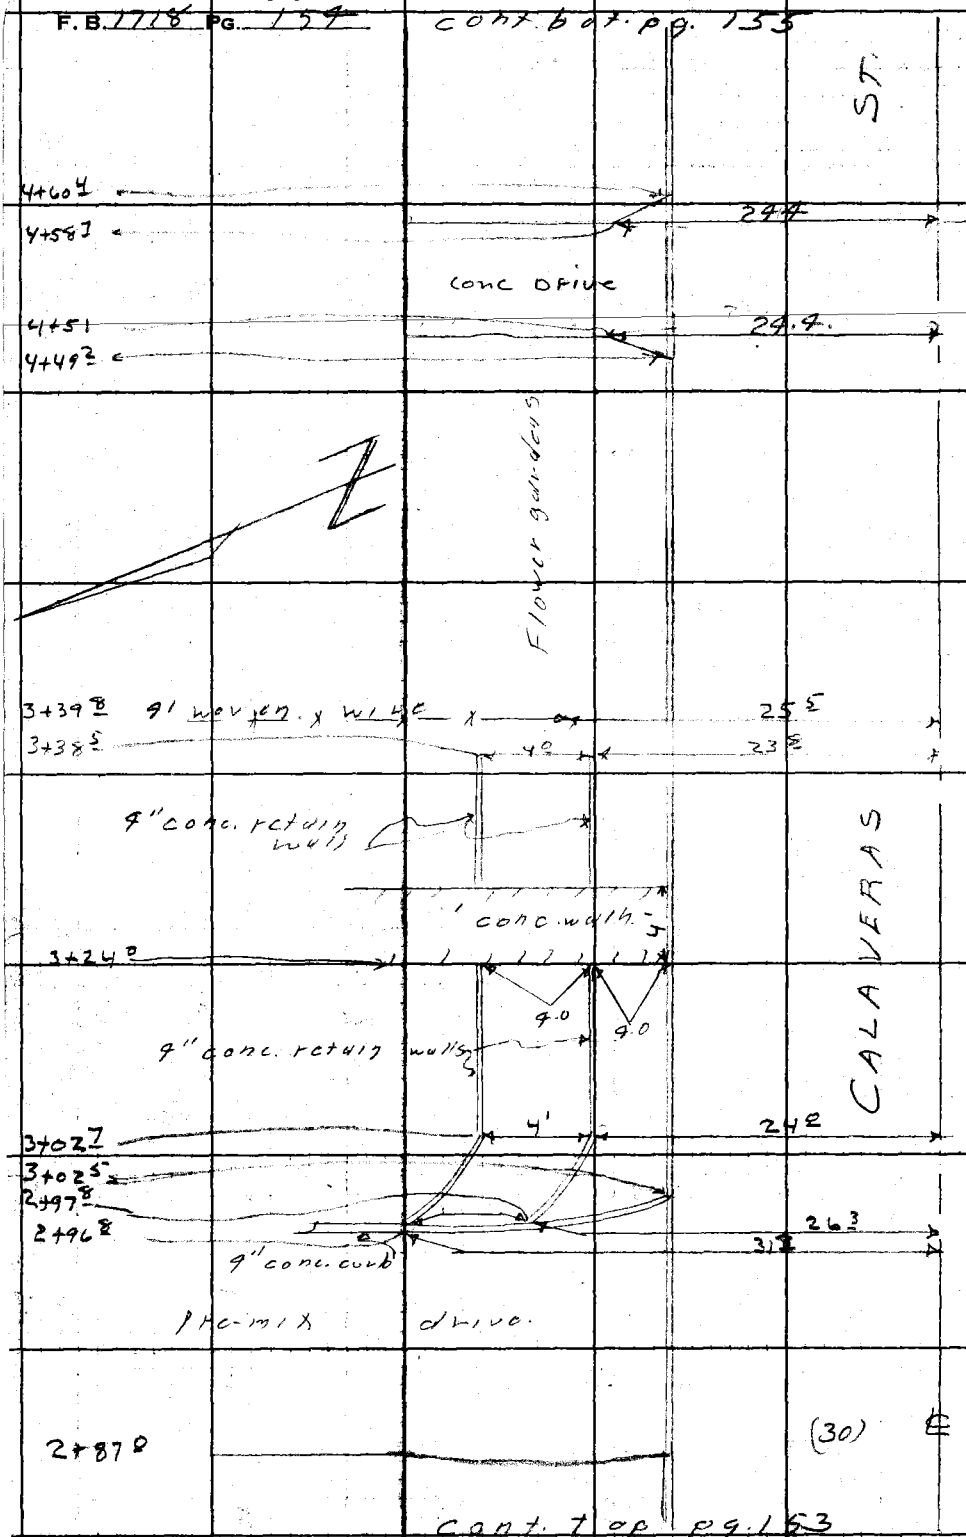

cont. top pg. 153

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

181

F.B. 1116 Pg. 155

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of: Marengo Ave.
W. O. 1390 Tape No. St'd. °F
Surveyed by: J. J. Lanigan
Notes: J. J. L. Date: 10-5-47
Indexed

Cont. from pg. 136

6+35 °

pre-mix drive

6+27 °

ST.

4' hedge

5+77 3

5+77 1

5+74 6

23 °

22 °

24 °

conc. drive

5+67 6

5+65 2

5+63 4

25 3/4

30 1/4

25 1/2

rose bushes

CALAVERAS

5' hedge

5+20 6

5+20

5+19 °

5+15 8

24 8

30 3

29 8

conc. dr.

5+09 2

29 8

5+06

(30)

Cont. to pg. 154

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76F3098 247 2-51

182

F.B. 1778 PG. 156

cont. bef. pg. 157

8+31 Q → 12" walnut

8+30 Q

8+27 Q

conc. drive

8+11 Q

8+08 Q

2" conc. curbs for flower beds

2 1/2" asphalt

7+27 Q

7+27 Q

7+25 Q

pre-mix dr. with 2" conc. curbs

7+25 Q

7+13 Q

2 conc. curbs for flower beds

7+00 Q

6+99 Q

6+97 Q

conc. drive

6+91 Q

6+88 Q

Cont. top pg 155

CLAVERAS ST

RETURN TO
LOS ANGELES COUNTY SURVEYOR
720 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

183

Notes Ck'd by	Survey of Marengo Ave.
Map No.	W.O. 1332 Tape No. Std.
Office Work	Surveyed by J.J. Lanigan
Checked	Notes JJL Date 10-6-52
Date	Indexed

F. B. 1778 PG. 137

Notes: Any Additions or Changes to This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.
Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

7ef3pss 247 10M 1-49

6+96 Conc. pot. pg 156

9+96 3

Conc. drive

9+89 3

9+66 8

20.0

25 ±

9+81 2

7 spreading rose bushes

9+42 8

24 9

9+41 3

29 ±

9+38 8

conc. drive

9+30 5

28 3

9+20 4 → 29" o.d.m.

26 7

9+26 1

conc. walk

conc. steps

9+17 9

9+11

25 °

5 - spreading rose bushes

25 °

8+98 4

8+85 °

25 °

8+78 9

26 5

7' cypress hedge

CALLE VERA

(30)

Cont. top pg 156

F. B. 1718 Pg. 184

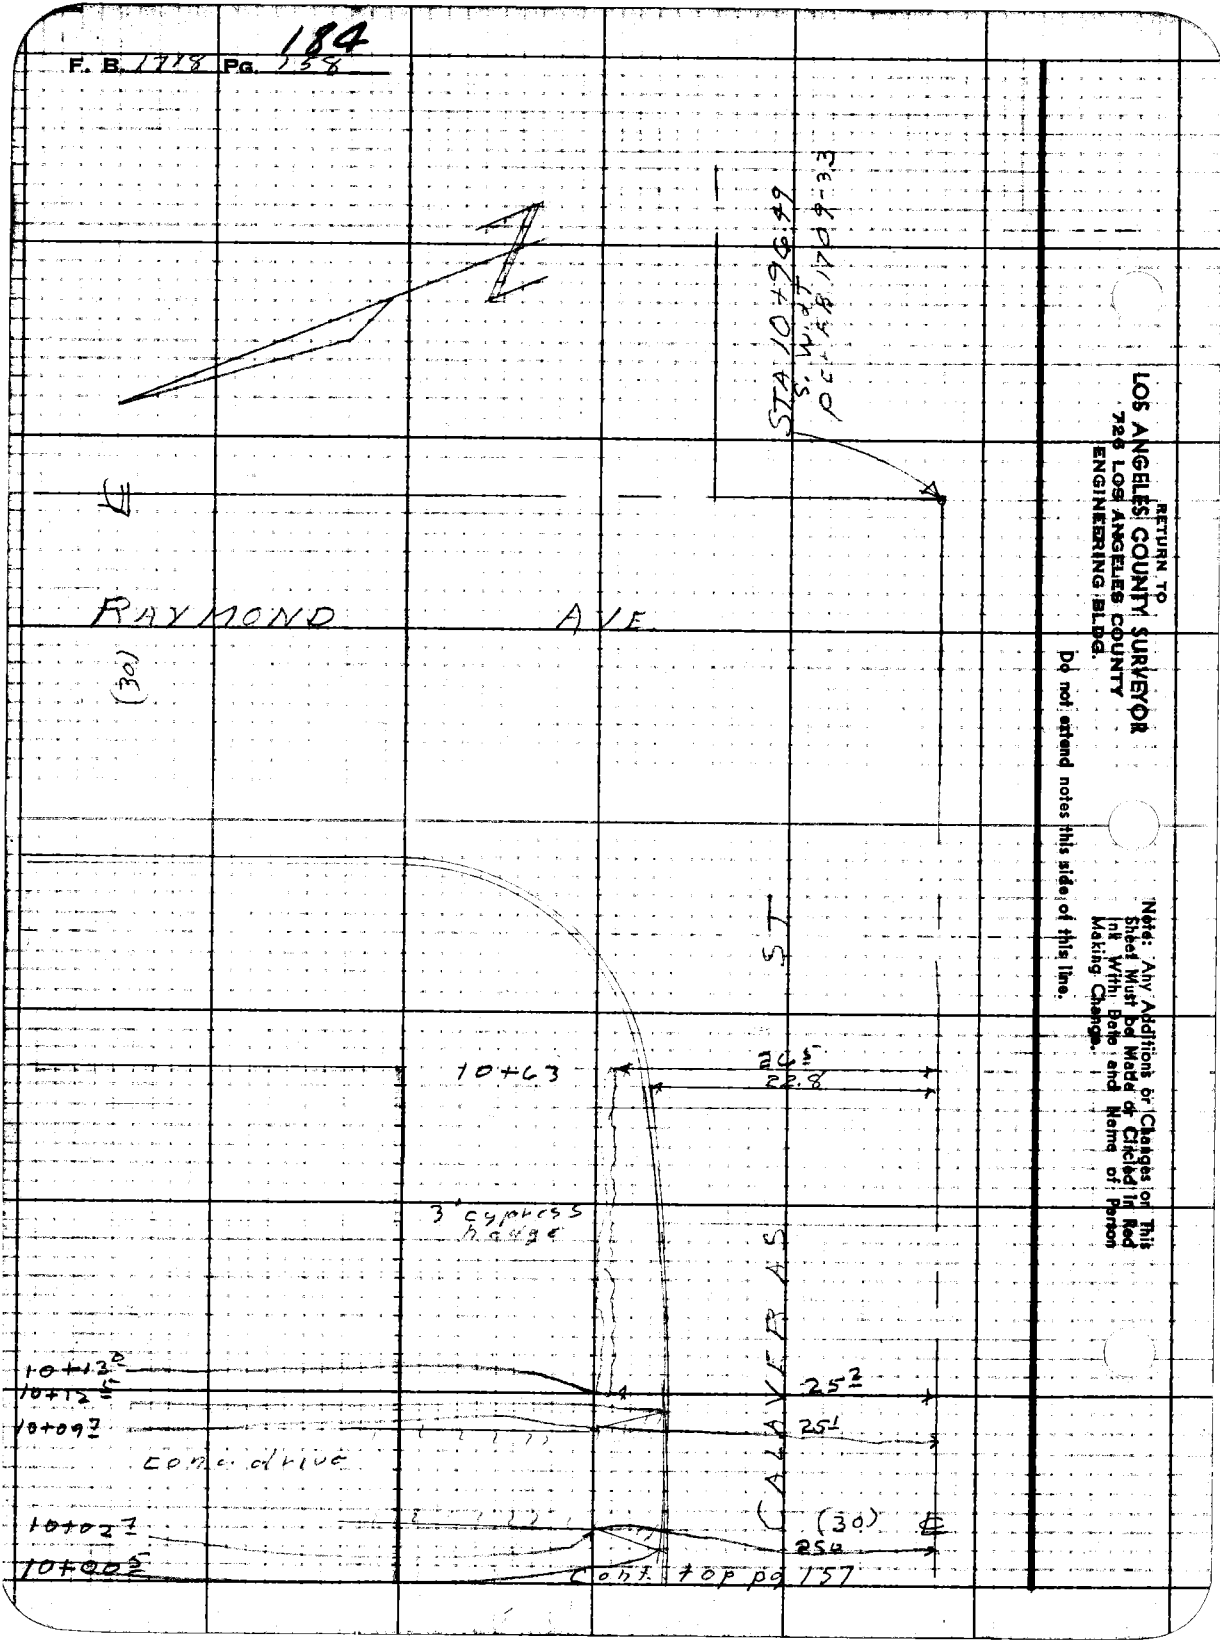

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Review Ck'd by:
Map No.
Office Work:
Checked
Date

Survey of Marengo Ave.
W. O. 1320 Tape No. St'd. °F
Surveyed by J. J. Lanigan
Notes J. J. L. Date 10-24-51
Indexed

F. B. 1718 Pg. 185

Note: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
of
IMPROVEMENTS
on
1ST LOT LINE S. of MARIPOSA ST.
from
MARENGO AVE
to
EASTERLY LINE of TR.* 2147
C.L. 139°

J. J. Lanigan
C. H. Lewis
H. H. Raphael
H. Tafoya

76F3095 247 2-51

F.B. 171 Pg. 186

To S.W. ly ext. int. of Mariposa St pc L.R. 31708-35'

Sta 0+00 SCI spk & tin

173.00

MARENGO AVE (325)

0+20.5

1' open "V" ditch (Sta 6)

90° 00' 18"

3.5 20" pepper 0+28.8

173.00 level @ 68° = 173.00

1) 90° 00' 20"
2) 360° 01' 10"
3) 180° 00' 50"
90° 00' 18 1/3"

line

2.0 dead man 1+12.2

2.6 1+32.6

2.1 8" p.p 1+33.7

1+39.3 4" apple 4.3

1+55.0 2" prune 4.4

1+69.3 2" peach 4.2

1+84.9 4" shade 4.3

2.7 1+92.2

1+76.0 1.1

stucco garage 20.2 24.1 1.1

Triangle

Sta 2+97.19 set 1x2

4' woven wire

1.9 8" p.p. 2+51.0

3.8

2+22.3

2+52.6 9' conc. block wall

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No. | Notes Red. | Plotted | Job No. 1390 | Division No. | F. B. 1718 | Pg. 187

Misc. No. | Notes Chkd. 9/14/51 | Checked | Survey by Lanigan | Notes | Date

Date | Date | Survey of | Date

Map No. | Indexed | Date

PROFILE AND CROSS-SECTIONS

ON

1st LOT LINE S. OF MARIPOSA ST.

FROM

MARENGO AVE. TO EASTERLY LINE TR 2147

C.I. 1390

J.J. Lanigan
C.H. Lewis
H.H. Raphael
H. Tafoya

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

76L298 307 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ Plotted ____ Date ____ Notes Red ____ Date ____ Notes Chkd ____ Date ____ Checked ____ Date ____ X-Sec. No. ____

Job No. 1390 Division No. ____ Pg. 188

Survey of Marengo Ave

Survey by Langan Notes Lewis

Indexed ____ Date ____

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
BM AE 472	11 31	1283 34		1272 03	AE 472 E/ 1272.028 FB 1568 P 105	
T. P.			0 48	1282 86	Marengo Ave. (W. side) 425'± S of Mariposa St	
	11 66	1294 52			Bt spk in conc. drive to No. 2611	
0+00			4 30	1290 22	Init. transit line ℄ of Marengo Ave.	
0+21±			5 25	1281 27	edge of pvmt on ℄	
0+25			6 33	1288 19	bot of drain " ℄	
0+25 5			5 00	1289 52	Top " " " ℄	
0+30			4 0 5	1290 5	" of bank ℄	
0+37 5			4 9	1289 6	3' L	
"			4 4	1290 1		3' R
1+00			5 5	1289 0	3' L	
"			5 1	1289 4		3' R
1+32 6			5 4	1289 1	SE cor Lot #	
1+92 2			4 8	1289 7	SE cor Lot #	
2+00			4 2	1290 3	3' L	
"			3 9	1290 6		1' R
2+47			3 0	1291 5	3' L	
"			2 6	1291 9		3' R
T. P.	9 72	1303 72	0 52	1294 00	BM AE 473 E/ 1301.477 FB 1568 P 105	
BM AE 473			2 25	1301 47	Mariposa St & Marengo Ave S.E. cor Bt spk in curb 5' E of E. end eb. ret	

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Marengo Ave.
W. O. 1390 Tape No. St'd. °F
Surveyed by J. J. Lonigan
Notes J.J.L Date 10-25-47
Indexed

F. B. 115 Pg. 189

Note: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION of IMPROVEMENTS on PRIVATE PAVED Road WEST of MARENGO AVE and NORTH from MARIPOSA ST.

C.I. 1390

J. J. Lonigan
C. H. Lewis
H. B. Raphael
H. Farfaga

76F3096 247 2-51

F. B. 1118 PG. 190

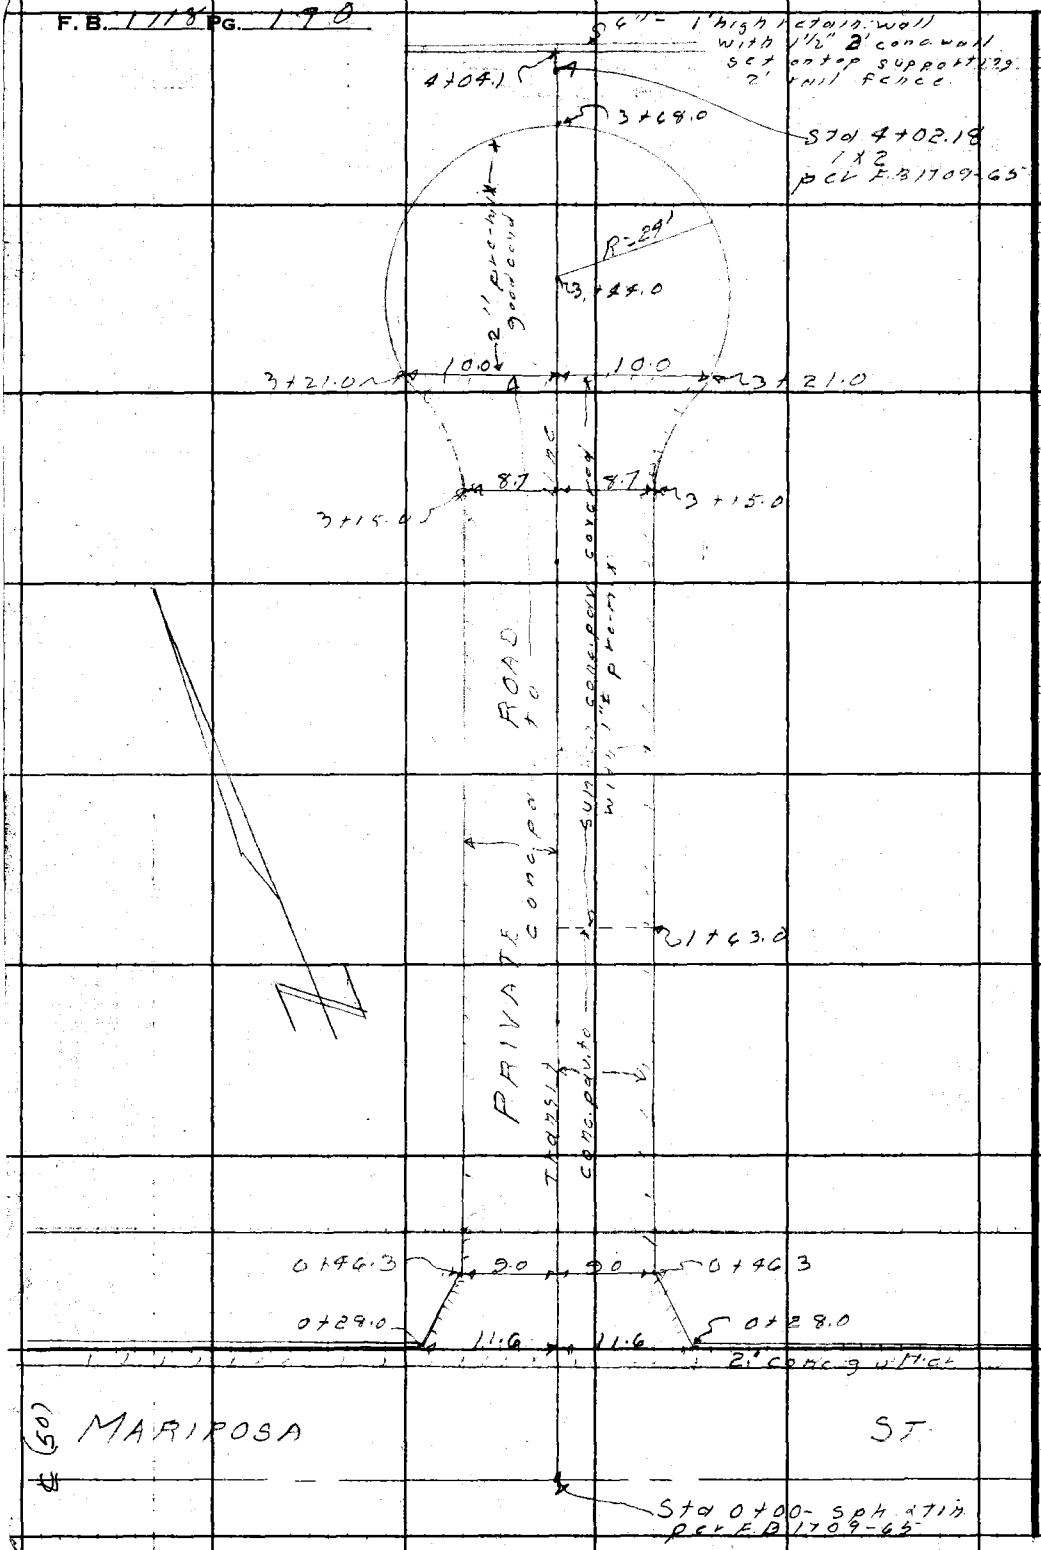

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Marengo Ave
W. O. 1379 Tape No. St'd. °F
Surveyed by J. J. Lanigan
Notes J. J. L. Date 1-8-52
Indexed

F. B. 174 Pg. 191

LOCATION
of
IMPROVEMENTS
on
FIRST LOT (CUT) LINE S. of FOOTHILL BLVD
EASTERLY from PRIVATE ROAD from S.
C.I. 1390

J. J. Lanigan
C. H. Lewis
H. H. Raphael
H. Tafoya

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76F3085 247 2-51

F. B. 1718 Pg. 192

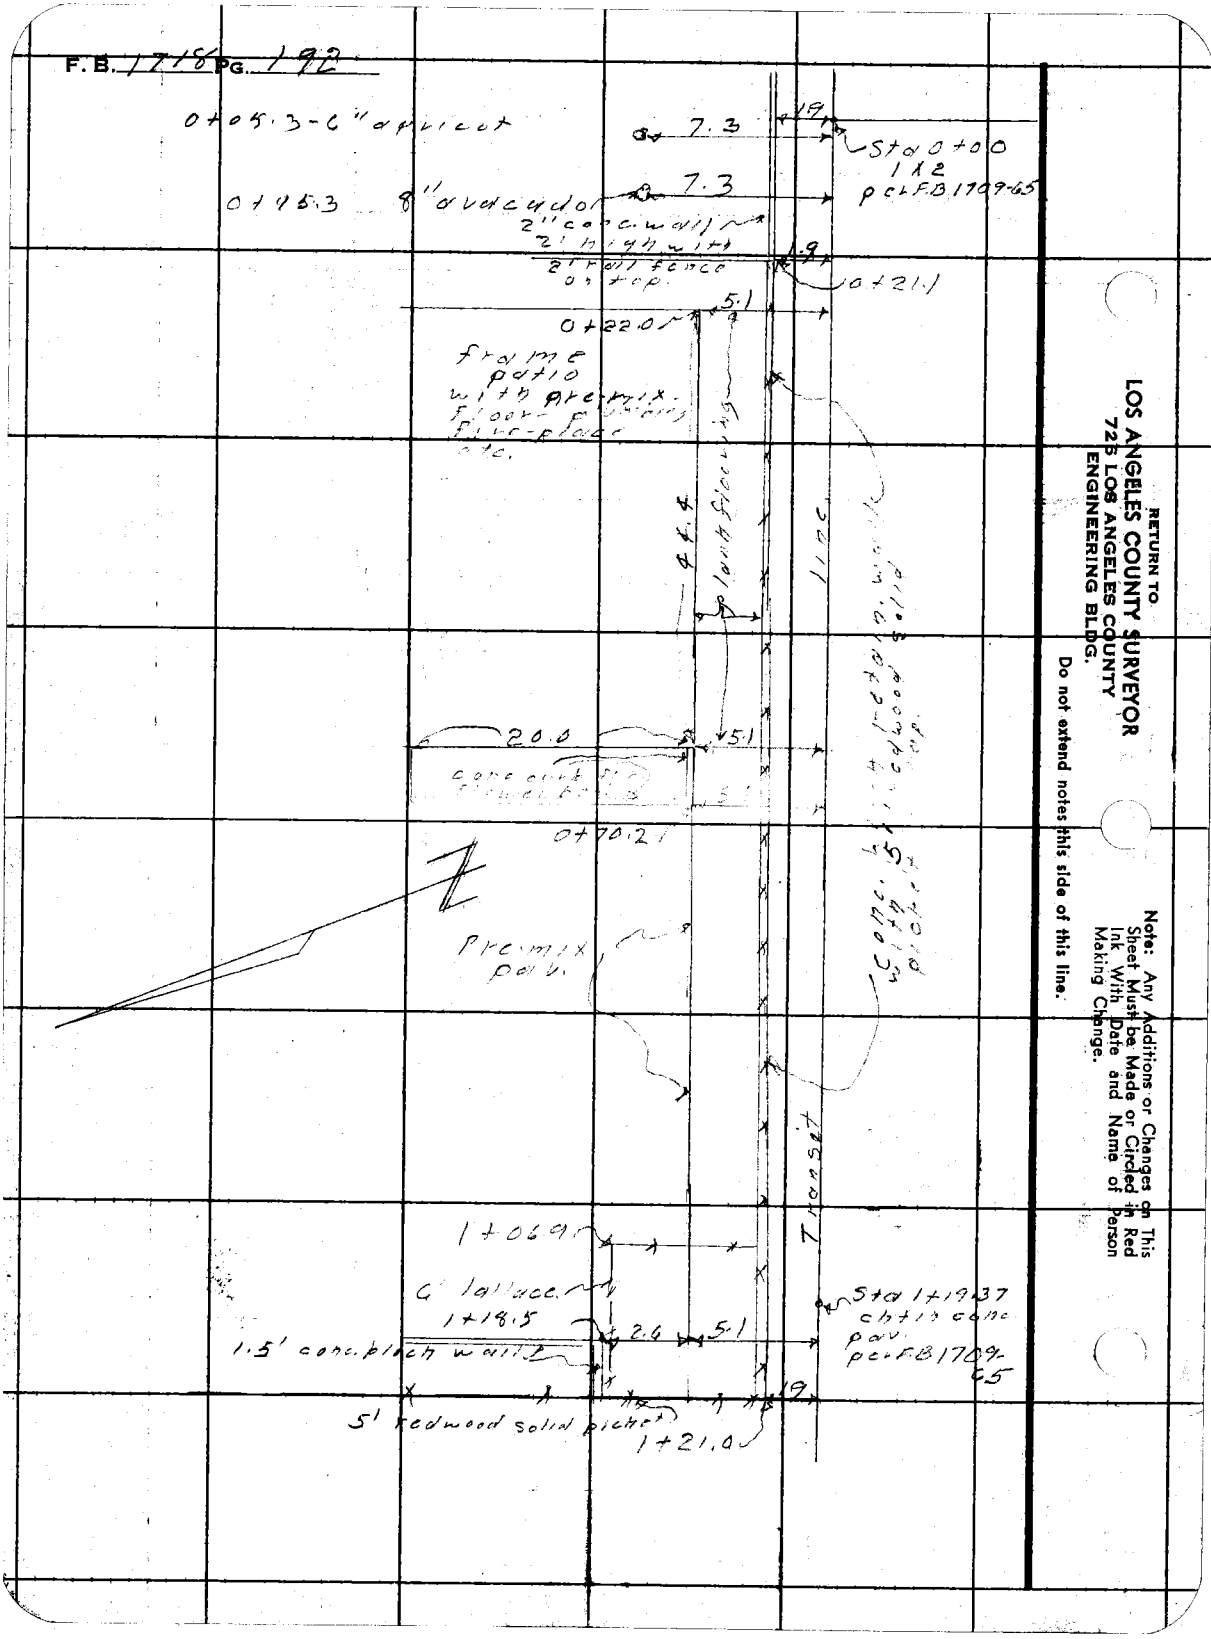

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Marengo Ave.
W. O. 1390 Tape No. St'd. °F
Surveyed by J. J. Lanigan
Notes J. J. L Date 10-25-51
Indexed

F. B. 174 Pg. 193

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76F3095 247 2-51

LOCATION of IMPROVEMENTS

ON

FIRST LOT (CUT) LINE S. of FOOTHILL BLVD

WESTERLY FROM PRIVATE ROAD

C.I. 1390

J. J. Lanigan.
C. H. Lewis.
H. H. Raphael
H. Tafoya.

F. B. 1718 PG. 199

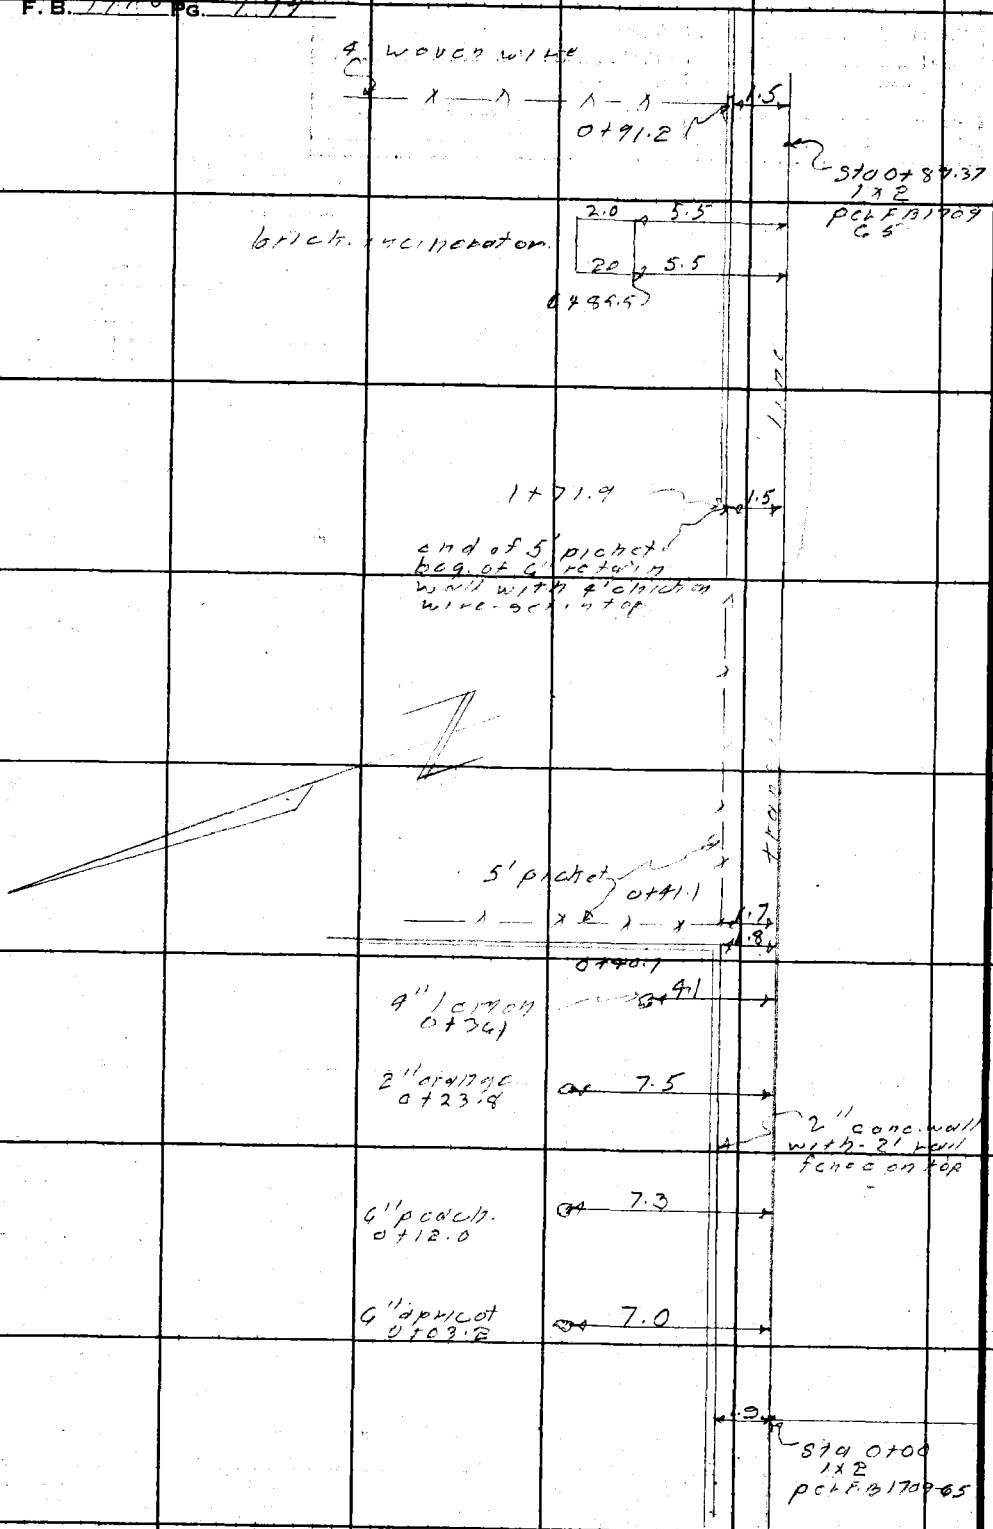

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No. | Notes Red. | Plotted | Job No 1390 | Division No. | F. B. 1718 | Pg. 195

Date | Date | Survey of Marengo Ave.

T-Sec. No. | Notes Chkd. 5-27-51 | Checked | Survey by La H T & H | Notes Lewis | Date IX-3-52

Date 8/9/51 | Date | Map No. | Indexed | Date

PROFILE
AND
CROSS-SECTIONS
OF
PAVED PRIVATE ROAD + ADJACENT WEST OF MARENGO AVE. FROM MARIPOSA ST. NORTHERLY

C.I. 1390

J.J. Lanigan
C.H. Lewis
H.H. Raphael
H. Tatoya

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

%6L298 307 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 1718 Pg. 116 Job No. 1390 Division No. Notes Red Plotted Profile
Survey of Daleng o Ave. Date No.
Survey by Lanigan Notes Lewis Date X-Sec.
Indexed Date Notes Chkd. Checked
Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
BM AE 481	3 76	1308 37		1304 61	AE 481 El. 1304.607 FB 1568 - P. 116	
					Mariposa St. (N. Side) at Visscher Pl.	
					Bt. spk in curb 5' W. of & prod of Visscher Pl.	
0 + 00			5 05	1303 32	Int. transit line & & of Mariposa St	
0 + 28			5 03	1303 34	Cross gutter	E
"			4 97	1303 40	" "	11½' L
"			5 07	1303 30	" "	11½' R
"			4.36	1304 01	Top of curb	11½' L
"			4 42	1303 95	" "	11½' R
0 + 50			3 24	1305 13		E
"			3 15	1305 22	edge pvmt	9' L
"			3 09	1305 28	"	9' R
1 + 00			0 37	1308 00		E
"			0 27	1308 10		9' L
"			0 30	1308 07		9' R
T. P.		/	9 16	1308 21	T P	
	12 27	1320 48				
1 + 50			10 00	1310 48		E
"			9 95	1310 53		9' L
"			9 92	1310 56		9' R
2 + 00			7 23	1313 25		

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. 1390 Division No.
No. Date Date Survey of Laterals Axis
X-Sec. Notes Chkd. Checked Survey by Lanigan Notes Lewis Date 11-25-57
No. Date Date Map No. Indexed Date

F. B. 1718 Pg. 27

STATION	B. S.	H. I.	F. S.	ELEV.	Transit Line
		1320 48			
2+00			7 14	1313 34	9' L
"			7 16	1313 32	9' R
2+50			4 26	1316 22	
"			4 21	1316 27	9' L
"			4 22	1316 26	9' R
3+00			1 07	1319 41	
"			1 09	1319 39	9' L
"			0 99	1319 49	9' R
T. P.		✓	0 32	1320 16	T. P.
	10 63	1330 79			
3+42			8 37	1322 42	
"			8 34	1322 45	24' L
"			7 72	1323 07	24' R
3+67.8			6 58	1324 21	end of pavmt.
4+04			4 7	1326 1	bot of wall
"			5 3	1325 6	24' L " "
"			4 0	1326 8	40' R " "
4+04			1 70	1329 09	top of wall
4+04.5			3 2	1327 1	bot of wall
4+09			3 6	1327 3	

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 7/18 Pg. 198 Job No 1290 Division No. Notes Red. Plotted
Survey of Ornamental Ave. Date Date No.
Survey by Kanigan Notes Lewis Notes Chkd. Checked X-Sec.
Indexed Date Date Date No.
Profile

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
		1330 79				
4+02.18 N = 0+00 To East						
0+4			1 61	1329 18	2' L	Top of wall at corner
"			3 2	1327 6	2.5 L	bot of wall " "
"			3 2	1327 6	8' L	" " "
"			1 55	1329 24	"	Top " "
0+89			1 44	1329 35	2' L	Top of ret wall
"			1 7	1329 1	2.5 L	bot " " "
"			1 5	1329 3	8' L	
0+00 To East = 0+00 To West						
0+21			1 67	1329 12		2' R Top of wall at corner
"			3 2	1327 1		2.5 R bot " " "
"			1 61	1329 18		8' R Top of wall
"			3 8	1327 3		" bot " "
T.P.		1	2 26	1329 53		
	4 46	1332 99				
0+67			7 0	1326 0		2.5 R ground
"			6 84	1326 15		4.7 R Macadam
"			671	1326 28		8' R "
1+18.5			6 8	1326 2		2.5 R ground
"			678	1326 21		4.7 R macadam

96L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
		1332 99 ✓				
1+18 ±			683	326 10		8' R macadam
T.P		✓	034	332 65		
	11 03	1343 68				
			9 97	1333 71	AE 258 El. 1333.714 FB. 1447 P 37 ✓	
					Foothill Blvd + Scripps Lane, S.E. cor	
					Bt. spk. in curb 1.5' E of W end	

Profile Notes Red.____ Plotted.____ Job No. 1390 Division No.____ F. B. 1718 Pg. 99

No. ____ Date ____ Date ____ Survey of 7/19 & 20/60 Date ____

X-Sec. Notes Chkd.____ Checked ____ Survey by Lanigan Notes Lewis Date 7/19 & 20/60

No.____ Date ____ Date ____ Map No.____ Indexed ____ Date ____

F. B. 1718 Pg. 200 Job No. 1390 Division No. Notes Red. Plotted Profile

Survey of Dalengo Ave. Date Date No.

Survey by Lanigan Notes Lewis Notes Chkd Checked X-Sec.

Indexed Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	

76L298 307 4-56

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR

726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Notes Ck'd by	Survey of Mango Ave.
Map No.	W. O. 1322 Tape No. Std.
Office Work	Surveyed by J. J. Kadrigan
Checked	Notes Date
Date	Indexed

F. B. 1118 PG. 201

LOCATION
of
IMPROVEMENTS
to
SOUTHERLY LINES
of
Lots No. 70-71-72-73
YR 6141
C.T. 1390

J. J. Kadrigan
C. M. Lewis
M. R. Rudder
A. Tatum

Notes: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76F3098 247 10M 1-49

F. B. 1778 Pg. 202.

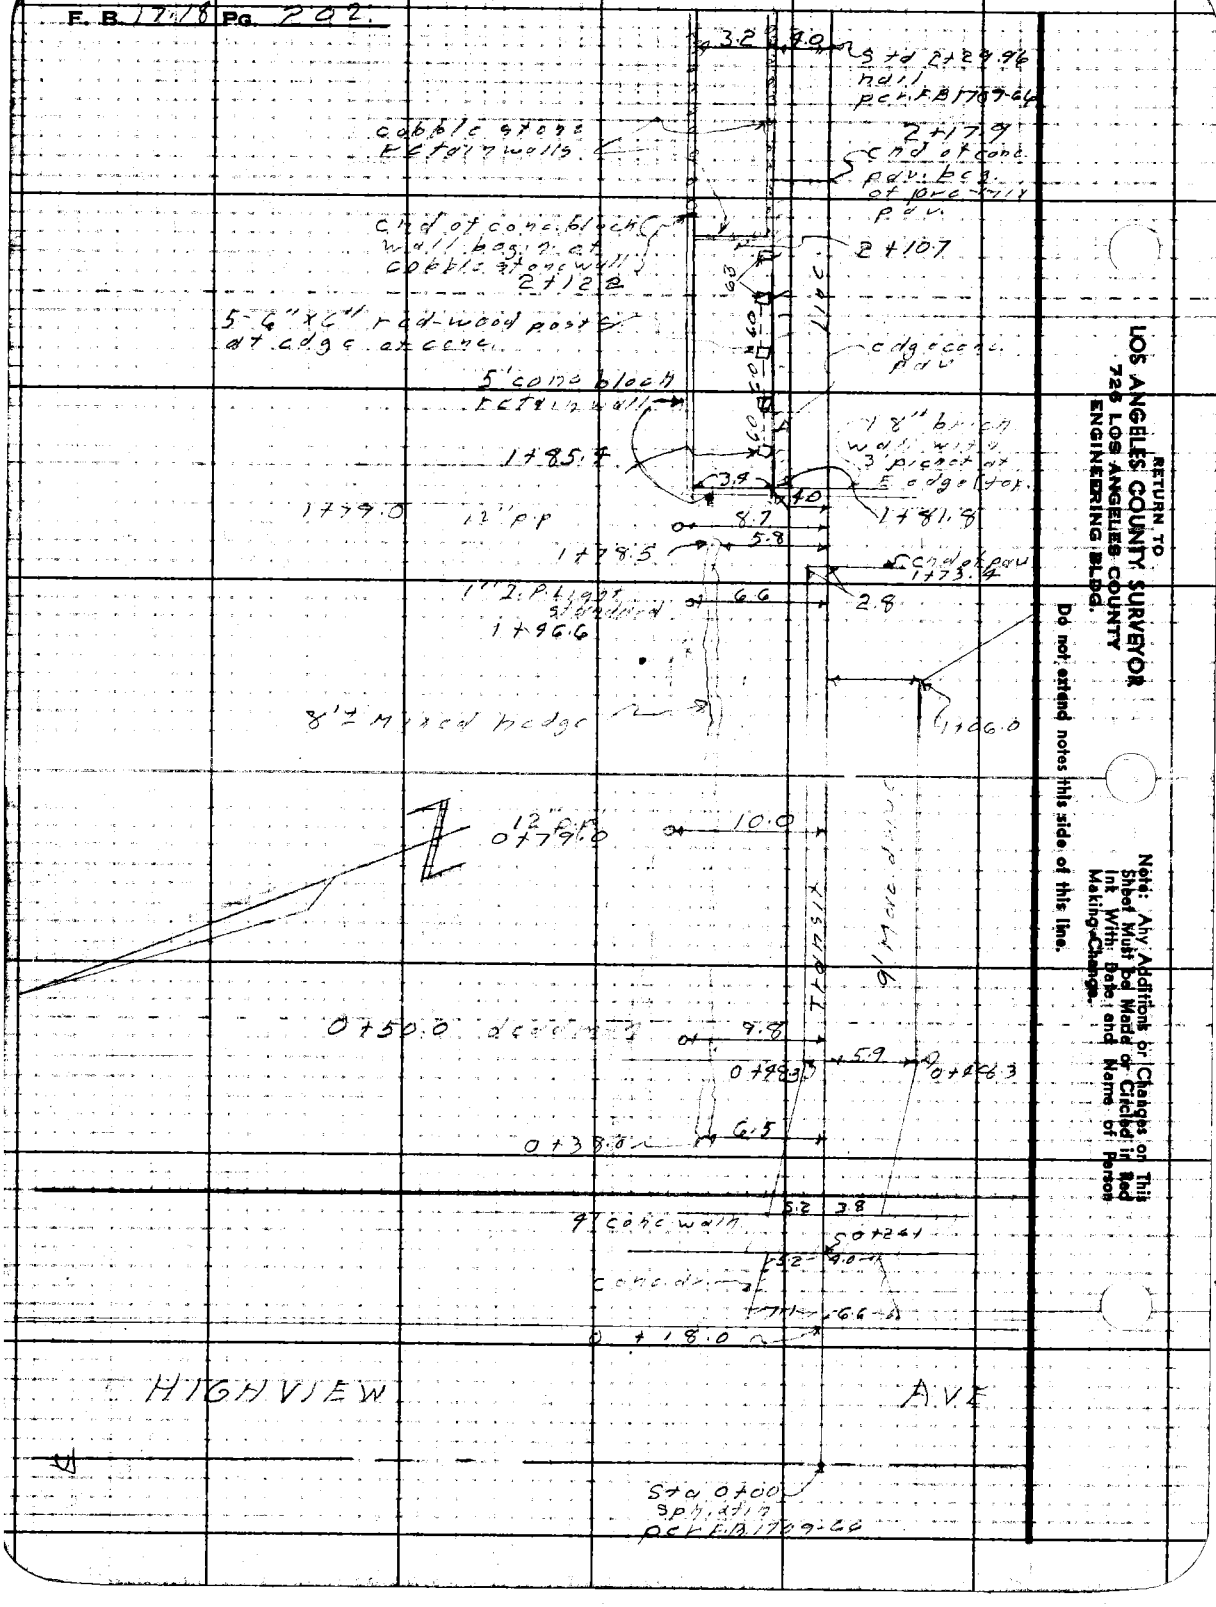

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No. | Notes Red. | Plotted | Job No. 1390 | Division No. | F. B. 7718 | Pg. 203
Sec. No. | Notes Chkd. 11/9/57 | Checked | Survey of | Survey by Langdon | Notes Lewis | Date 11-2-57
Date | Date | Map No. | Indexed | Date

PROFILE
CROSS-SECTIONS
OF
SOUTHERLY LINES of LOTS 70, 71, 72 & 73
TRACT NO. 6161

C.I. 1390

J. Y. Langdon
C. H. Lewis
H. H. Raphael
H. Tafoya
A. B. Barber

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

74L298 307 4-58

76L296 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

2-29-96

Do not extend notes this side of this line.

F. B. 7418 Pg. 204 | Job No. 3320 Division No. | Notes Red | Plotted | Profile
Survey of Mariposa Ave. | Date | Date | No.
Survey by Keenan | Notes Keenan | Notes Chkd | Checked | X-Sec.
Indexed | Date | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
		~~34~~		28	~~29~~	
BM AE 485	8 06	1271		1263 47	AE 485 - El. 1263.468 FB 1568 P. 129	
					Highview Ave (E. side) 250'± S of ℄ of Mariposa St.	
					Bt. spk in curb in front of No. # 2690.	
0+00			5 22	1266 12 ~~31~~	Int. of Transit Line & ℄ of Highview Ave	
"			4 61	1266 ~~73~~	8' L	
0+18			5 75	1265 ~~78~~	gutter	℄
"			5 25	1266 ~~08~~	" 8' L	
"			4 55	1266 ~~79~~	curb 8' L at N end of driveway	
"			5 50	1265 ~~84~~	" " S " " "	
0+30			4 73	1266 ~~61~~		℄ at back of walk
"			4 40	1266 ~~94~~	5± Ledge of macadam " "	
"			4 ±	1267 ~~1~~	8' L ground.	
0+50			4 83	1266 ~~56~~		℄
"			4 89	1266 ~~45~~	4' L ledge of macadam	
"			4 ±	1266 ~~6~~	8' L	
1+00			5 19	1266 ~~65~~		℄
"			5 22	1266 ~~67~~	3± L ledge of macadam	
"			5 ±	1266 ~~5~~	8' L	
1+50			5 45	1265 ~~89~~		℄
"			5 47	1265 ~~87~~	3± L ledge of macadam	
"			5 ±	1266 ~~2~~	8' L	

76L398 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red No. ____ Date ____ Plotted ____ Date ____ Job No. 1360 Division No. ____ F.B. 1715 Pg. 2425
Notes Chkd. ____ Date ____ Checked ____ Date ____ Survey of Downey Area Bike Path
No. ____ Date ____ Survey by Harris & Assoc. Map No. ____ Indexed ____ Date ____

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
		1271 34				
7+81			5 7	1265 6	on W. side of wall	℄ ground
"			5 4	1265 9	8' L " " " "	
1+81 8			6.72	1264 62	4° " E " "	℄ concrete
"			6 7	1264 6	8' L " " " "	ground
2+00			6.9	1264 43		℄
"			6.90	1264 44	4° L edge of conc	
"			6 9	1264 4	7 ½ L ground	
2+10 7			5.70	1265 64	4' L	Top of masonry ret. wall
2+29.96			7.25	1264 09		℄
"			7.24	1264 10	4' L	edge of drive
"			6.31	1265 03	4' L	Top of masonry wall
TP			5.22	1266 BZ		
	11.94	1278 06				
BMAE479			0.62	1277 44	AE 479 E/ 1277.468 FB 1568 P 114	
T.P.	2.63	1280 07			Mariposa St. & Higuera Ave N.W. cor.	
BMAE480			4.92	1275 15	Bt spk in curb 5' W of E.W. end C.R.	
					AE 480 E/ 1275.187 FB 1568 P 116	
					Mariposa St & McNally Ave. S.W. cor.	
					Bt spk in curb 10' W of E.W. end C.R.	

F. B. 1718 Pg. 206 Job No. 1292 Division No. Notes Red. Plotted Profile

Survey of 177th-Emgo Ave. Date Date No.

Survey by Lanigan Notes Lewis Notes Chkd. Checked X-Sec.

Indexed Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	

761-298 307 4-60

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR

726 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Marengo Ave
W. O. 1390 Tape No. St'd. °F
Surveyed by J. J. Lonigan
Notes J. J. L Date 11-6-51
Indexed

F. B. 1116 Pg. 207

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION of IMPROVEMENTS on ABANDONED R/W in BLOCK 22 M. R- 16-45-46 C.I. 1390

J. J. Lonigan
C. H. Lewis
H. H. Raphael
H. Tafoya
A. B. Barker

76F3095 247 2-51

F. B. 1714 PG. 208

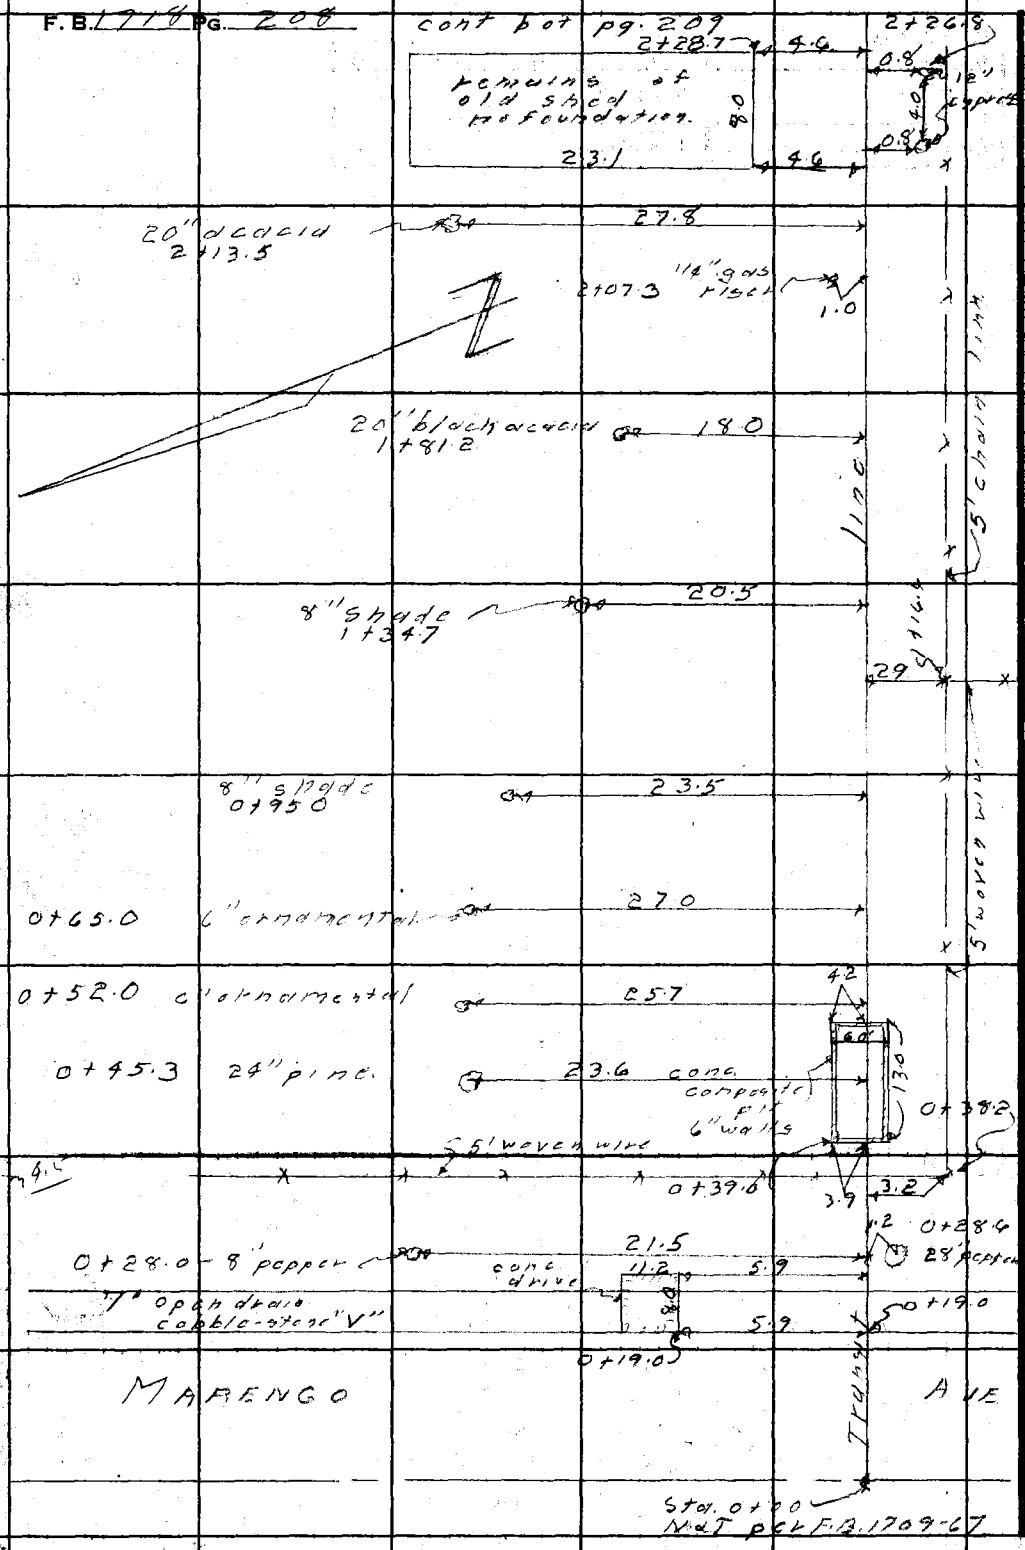

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date, and Name of Person Making Change.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Mckenzie Ave
W. O. 1390 Tape No. St'd °F
Surveyed by J. J. Lanigan
Notes J. J. L. Date 11-6-51
Indexed

F.B. 1718 PG. 209

Note: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76F3095 247 2-51

C 2177 bk pg 218

8" Thick conc. gut. with openings as shown

3+55.2
3+46.9
3+43.6
3+39.6
3+29.7
3+25.8
3+19.8
3+15.6
3+13.8
3+13.9
3+13.2
3+12.0
3+02.1
2+87.7
2+73.2
2+59.2
2+45.4
2+38.77
2+31.6
2+32.7

24" F.L.
18" F.L.
12" F.L.
14" F.L.
12" P.P.
5" Redwood Board
5" Wooden Wire
Sidewalk
Curb & Gutter
Sta 2+38.77 P.C. of FB 1709-67
cont. top pg. 208

F. B. 1716 PG. 210

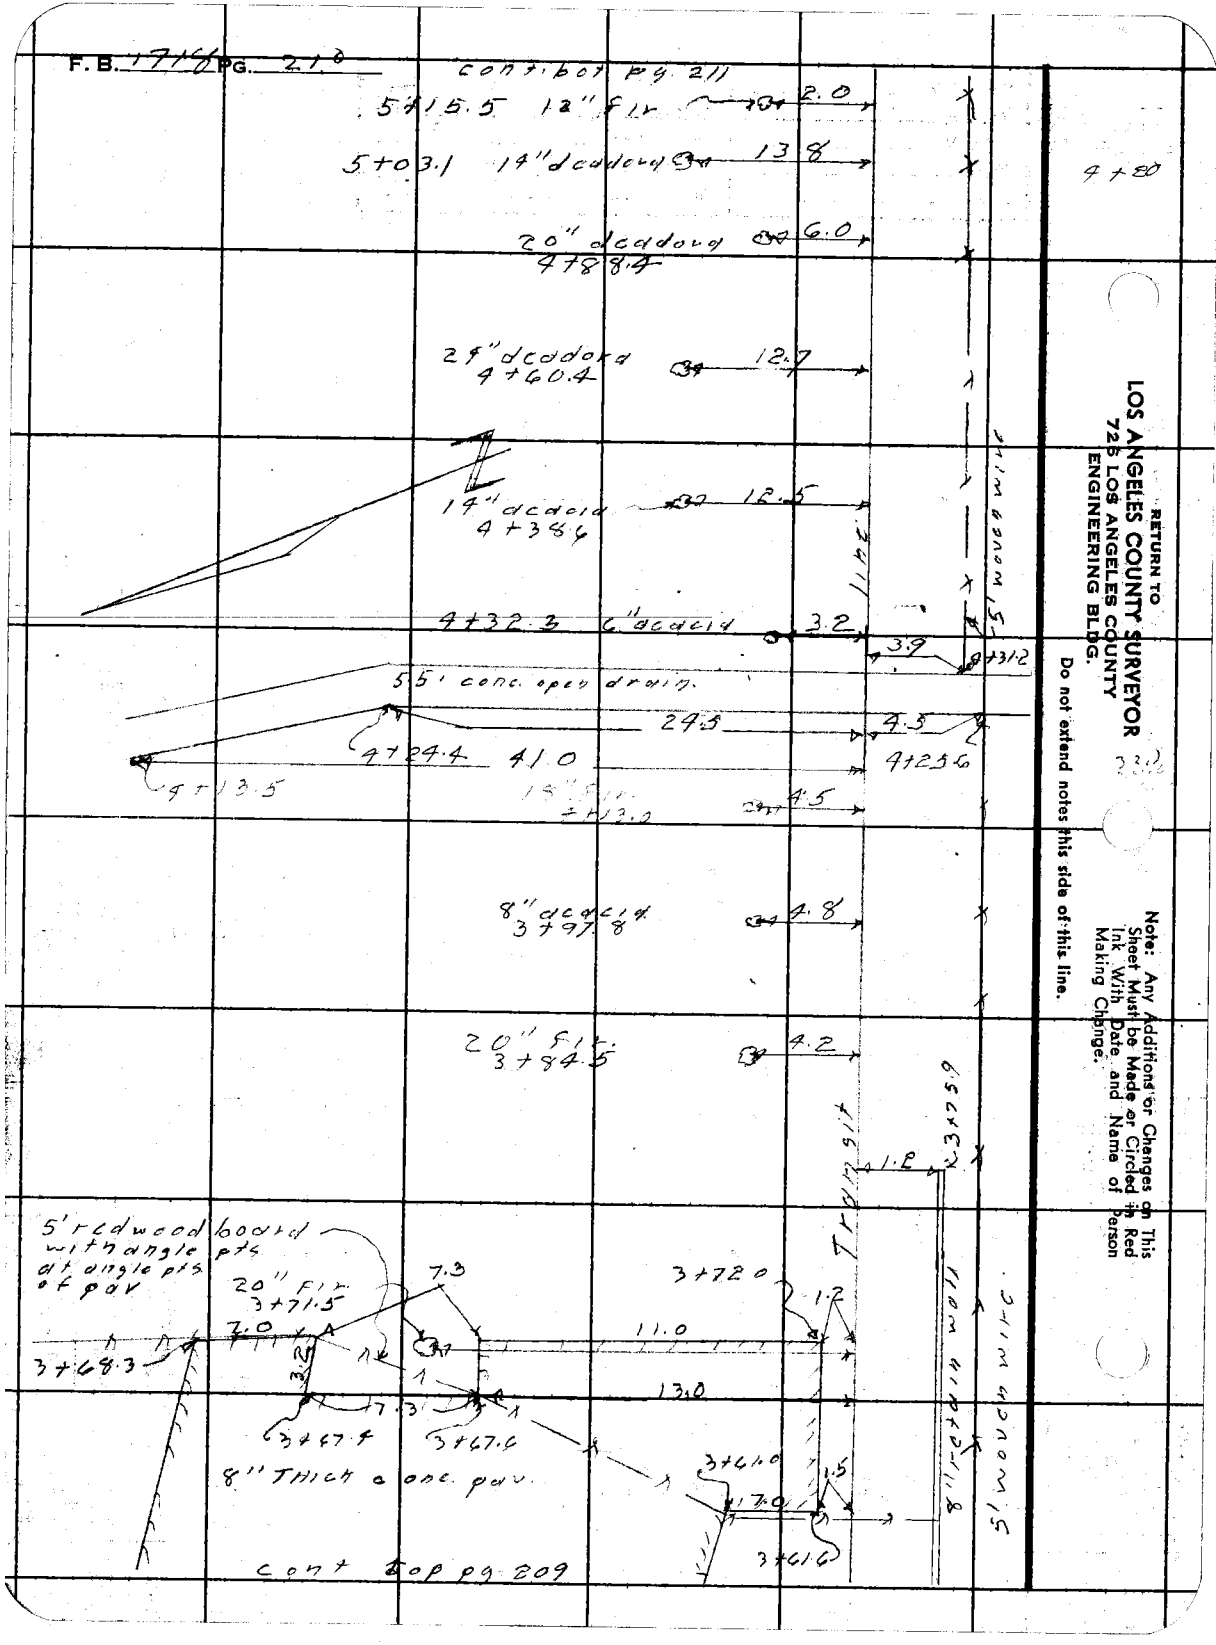

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by		Survey of Marengo Ave	F.B. 1716 Pg. 211
Map No.		W.O. 1390 Tape No.	St'd. °F
Office Work		Surveyed by V.V. Lavrigan	
Checked		Notes V.V.L. Date 11-6-51	
Date		Indexed	

Note: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

cont. bot pg. 212

6+53.7

{8" conc. wall with 5' woven wire in center}

28.8

frame chicken house
no foundation or floor.

6.9

10

22

30" deadora
6+37.6

9.8

20.0

6' chicken wire

6+22.9

28.8

0.8

Sta 6+19.69
per F.B. 1709.68

10" olive
6+12.0

8.8

14.7

20" deadora
5+94.5

5+76.0 18" deadora

5.3

12" deadora
5+58.3

13.9

5+49.0 12" deadora

5.1

5+31.7 18" deadora

15.0

5' WOVEN WIRE

cont top pg. 210

76F3095 247 2-51

F. B. 1718 PG. 212

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

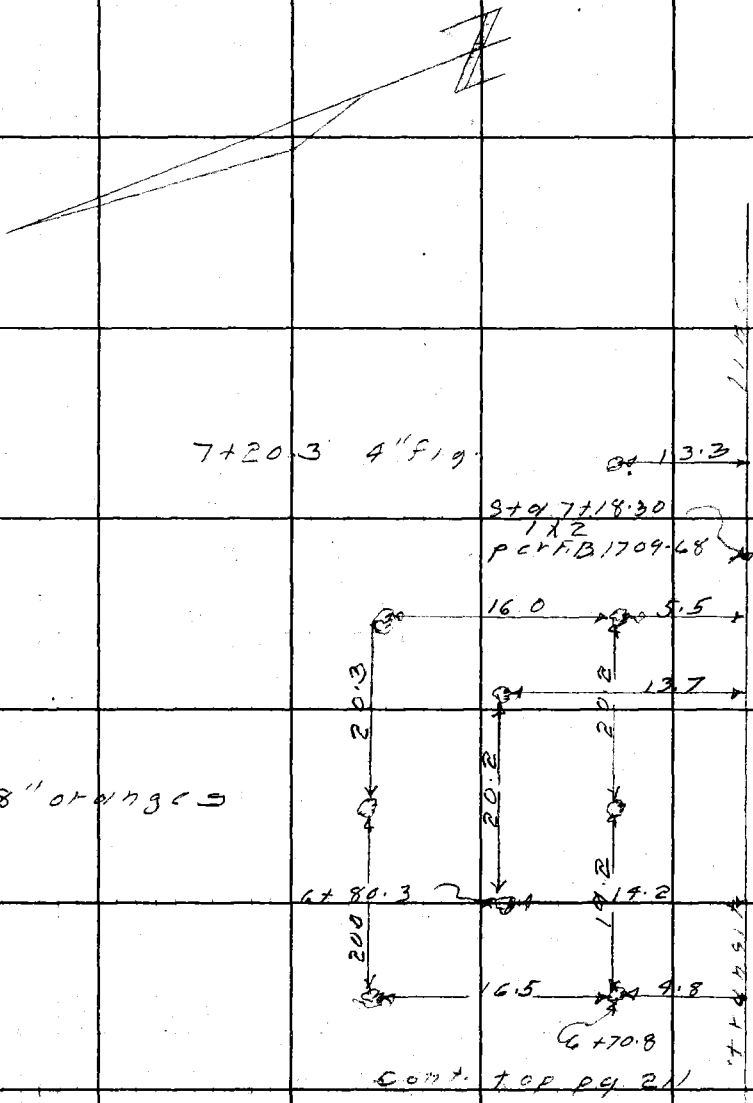

76F3095 247 2-51

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

Tidal Ck'd by_____
Map No._____
Office Work_____
Checked_____
Date_____

Survey of MARENGO AVE.
W.O. 1390 Tape No.____ St'd____ °F
Surveyed by LANIGAN
Notes RAPHAEL Date 11-6-51
Indexed_____

F.B. 17/B Pg. 2/3

F.B. 1718 PG. 214

CONTINUED BOTTOM OF PAGE 215

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes C'd by
Map No.
Office Work
Checked
Date

Survey of MARENGO AVE F.B. 1718 PG. 215
W. O. 1390 Tape No. St'd °F
Surveyed by: ANIGIAN
Notes RAPHAEL Date 1-6-51
Indexed

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

4' REDWOOD FENCE
10.0
2+80.0
4' WOVEN WIRE FENCE
TRANSIT LINE
2+66.0
6" TREE
6.5
2.6
7.5
2+62.6
DEAD MAN
2+58.9
6.3
2.5
11.0
2+45.3
4' REDWOOD FENCE
12" P.P.
2+44.6
6.6
THIS AREA COVERED WITH FLOR. 1" to 6" ACACIAS.
0.1
4.5
2+37.8

STA. 2+34.26 1X2
PER F.B. 1709-67

CONTINUED FROM TOP OF PAGE 214

76F3095 247 2-61

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

F.B. 1718 PG. 214

Profile No. | Notes Red. | Plotted | Job No. 1390 | Division No. | F. B. 1718 | Pg. 217

Date | Date | Survey of 22nd & 23rd AVS.

Notes Card | Checked | Survey by

No. | Date | Date | Map No. | Indexed | Date

PROFILE

AND

CROSS-SECTIONS

OF

ABANDONED RIGHT OF WAY

IN

BLOCK 22, M.R. 16-45-46

C.I. 1390

J.V. Lanigan
C.H. Lewis
H.H. Raphael
H. Tapia
R.B. Baldwin

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

76L298 307 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile | Job No. 3210 Division No. | Notes Red | Plotted | No. | X-Sec.
Survey of Marengo Ave | Date | Date | Notes Child | Checked | No.
Survey by Lanigan Notes Lewis | Date | Date | Date
Indexed | Date | Date

F.B. 1718 P. 21

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
BM AE 470	10 29	1238 44		1228.15	AE 470 El 1228.15	FB 1560 P. 106
					Marengo Ave (E. side)	260'± N of Claremont St.
					Bt. spk. in drive to	No. #2484
0+00			4 72	1233 72	INT. Transit Line	℄ of Marengo Ave
"			4 93	1233 51		3' R
"			2 89	1235 55	27' L	
0+19			5 45	1232 99	edge of pvmt.	℄
"			5 63	1232 81	" "	3' R
"			3 90	1234 54	27' L "	
0+25 5			7 63	1230 81	bot of ditch	℄
"			7 80	1230 64	" " "	3' R
"			6 50	1231 94	" " " 27' L	
0+26			5 33	1233 11	Top of ditch wall	℄
"			5 50	1232 94	" " " "	3' R
"			3 93	1234 51	" " " 27 L	
0+38			4 1	1234 3	P.L.	℄
"			4 2	1234 2		3' R
"			2 9	1235 5	27' L	
1+00			4 0	1234 4		℄
"			4 5	1233 9		3' R
"			3 3	1235 1	27' L	

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted. Job No. 1390 Division No.
No. Date Date Survey of 2224 Entire Area
Notes Chkd. Checked Survey by LA Wilson & Assoc.
No. Date Date Map No. Indexed Date

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
		1238 44				
2+00			4 7	1233 7		℄ b+k
"			6 0	1232 4		3' R
			4 5	1233 2	27' L	
T. P.		✓	6 44	1232 00		
	9 91	1241 91				
2+41.58E = 0+00 N						
0+00 N			9 1	1232 8		℄
"			9 0	1232 9	7 5 L	
1+00 N			5 2	1236 1		℄
"			5 7	1236 2	7 5 L	
2+00 N			0 1	1241 8		℄
"			0 0	1241 9	7 5	
2+34.29		+	1 5	1243 4		℄ Handhole 1
"		+	1 6	1243 5	7 5	" "
T. P		✓	9 30	1232 61		
	5 37	1237 98				
5+00 East			7 4	1230 6		3' R
			5 3	1232 7	2' L b+k	
			4 4	1233 6	27' L	

76L298 307 4-56

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile — Plotted — Notes Red — Division No. 3.90 — Job No. 4 Amms — Page 220 — K.B. 7178
Survey of Maywood — Date — No. — X-Sec. No.
Survey by Langas — Date — Notes Chkd — Checked — Date
Indexed — Date — Notes Lewis — Date

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
		1237 98 ✓				
T. P.			4 32	1233 66		
	5 11	1238 77 ✓				
3+13 8			5 20	1233 57	2'L - S.W. corn. conc.	slab
"			5 04	1233 73	31'L N.W. " "	"
3+68 3			5 01	1233 76	24'L NE " "	"
3+72			5 31	1233 46	1.5'L SE	
4+00			9 5	1229 3		3'R
"			5 5	1233 3	6'L	
"			6 0	1232 8	27'L	
4+20			9 0	1229 8		3'R
"			6 3	1232 5	2'L	
"			6 7	1232 1	27'L	
4+25 6			8 94	1229 83	Top of W. wall of drain	3'R
"			8 10	1230 67	21'L " " "	"
4+28			11 28	1227 49	bot of conc. drain	3'R
"			10 28	1228 49	21'L " " "	"
4+31 2			8 14	1230 63	Top of E wall "	3'R
"			8 09	1230 68	21'L	
4+40			6 6	1232 2		3'R
"			6 2	1232 6	15'L	

76L298 207 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red_____ Plotted_____ Job No. 1390 Division No._____

No._____ Date_____ Notes Chkd_____ Date_____ Checked_____ Date_____ Survey by [illegible] Map No._____ Indexed_____ Date_____

F. B. 771

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
		1233.77				
4+40			7 6	1231 2	27' L	
T.P.		/	552	1233.26	T.P.	
	369	1236 94				
5+00			4 6	1232 3		3' R
"			4 7	1232 2	27' L	
6+00			4 5	1232 4		3' R
"			4 5	1232 4	27' L	
7+00			4 0	1232 9		2' R
"			3 5	1233 4	28' L	
7+18.28			4 0	1232 9		2' R
"			3 6	1233 3	28' L	
T.P.		/	2 70	1234.24	T.P.	
	909	1243 33				
T.P.		/	033	1243.00	T.P.	
	11.94	1254 94				
T.P.		/	133	1253.61		
	726	1260 87				
[illegible]			2 94	1257.93	4E 47' E/ 1257.907 FB 1568 P [illegible] Mendocino St. & Magnolia Ave. [illegible]	
					Brass tack in [illegible] conc. headwall N 24°N 24'E of [illegible]	

7118 P. 22 Job No. 1390 Division No. Notes Red Plotted Profile

Survey of Tarengo Ave. Date Date No.

Survey by Lanigan Notes Lewis Notes Chkd. Checked X-Sec.

Indexed Date Date Date No.

764-398 307 4-60

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR

726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.

Notes Ch'd by
Map No.
Office Work
Checked
Date

Survey of Marengo Ave
W. O. 1329 Tape No. St'd. °F
Surveyed by J. J. Lamigan
Notes J. J. L. Date 11-9-51
Indexed

F. B. 1719 Pg. 223

LOCATION of IMPROVEMENTS in ABANDONED R/W in BLOCK 15 M.R. - 16-45-46 C.I. 1390

J. J. Lamigan
C. H. Lewis
H. H. Raphael
H. Tafoya
A. B. Barker

Note: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76F309S 247 2-51

F.B. 7718 PG. 228

cont. bot pg 225



RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

1 1/2" hydrant 1+69.0

16.8

7.3

1+71.0

1+51.0

10.6

6" olive

11.0

11.0

1+49.0

1+95

1 1/2" hydrant 1+14.8

16.7

9.0

12" oak 1+24.2

Row of 5 cypress 0+74.0

3.0 3.0 3.0 3.0 3.0

4"

8"

4.8

Traffic

0+40.5

11.0

6.5" conc. flat bottom open drain

0+29.2

0+25.0 30" pepper

18.0

S. conc 2' conc. gutter 0+15.3

S cone oak 0+17.3

17.0

11.0

(40) SANTA ANITA AVE.

S.D.M.H. 0+00.6

8.0

Std 0+00

SPH 4-7-70

PCR F.B. 7709-69

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Marengo Ave
W. O. 1399 Tape No. St'd. °F
Surveyed by J.V. Lanigan
Notes J.V.L. Date 11-15-51
Indexed

F. B. 1175 Pg. 225

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Cont. bot. pg. 226

Storm Inclinerator

3+78.8

3+78.2

3+67.6

3+45.2

5' woven wire

18.2

3+55.7

9" conc. retain wall

15.7

3+57.0

38" RCP

5' woven wire

9.5

3+60.8

6" conc. head wall

8" V.C. pipe at wedge drain

21.0

3+36.4

3+36.7

3+30.7

19.0

10" R.C.P.

3+21.5

dead man

3+17.3

200

5' woven wire

5.2

6.8

18" C.C.P.

2+71.4

Trench

1.2

8.0

Concrete ditch

1.3

2+41.5

2+95.0 4" gum

4" gum

7.9

42.8

Frame & cover to be adjusted to grade

9.6

6" gum

2+40.0

15.5

Frame & cover to be adjusted to grade

6.3

6.3

2+35.9

1.2

2+33.7

Cont. top pg. 224

76F3098 247 2-51

F.B. 1118 PG. 226

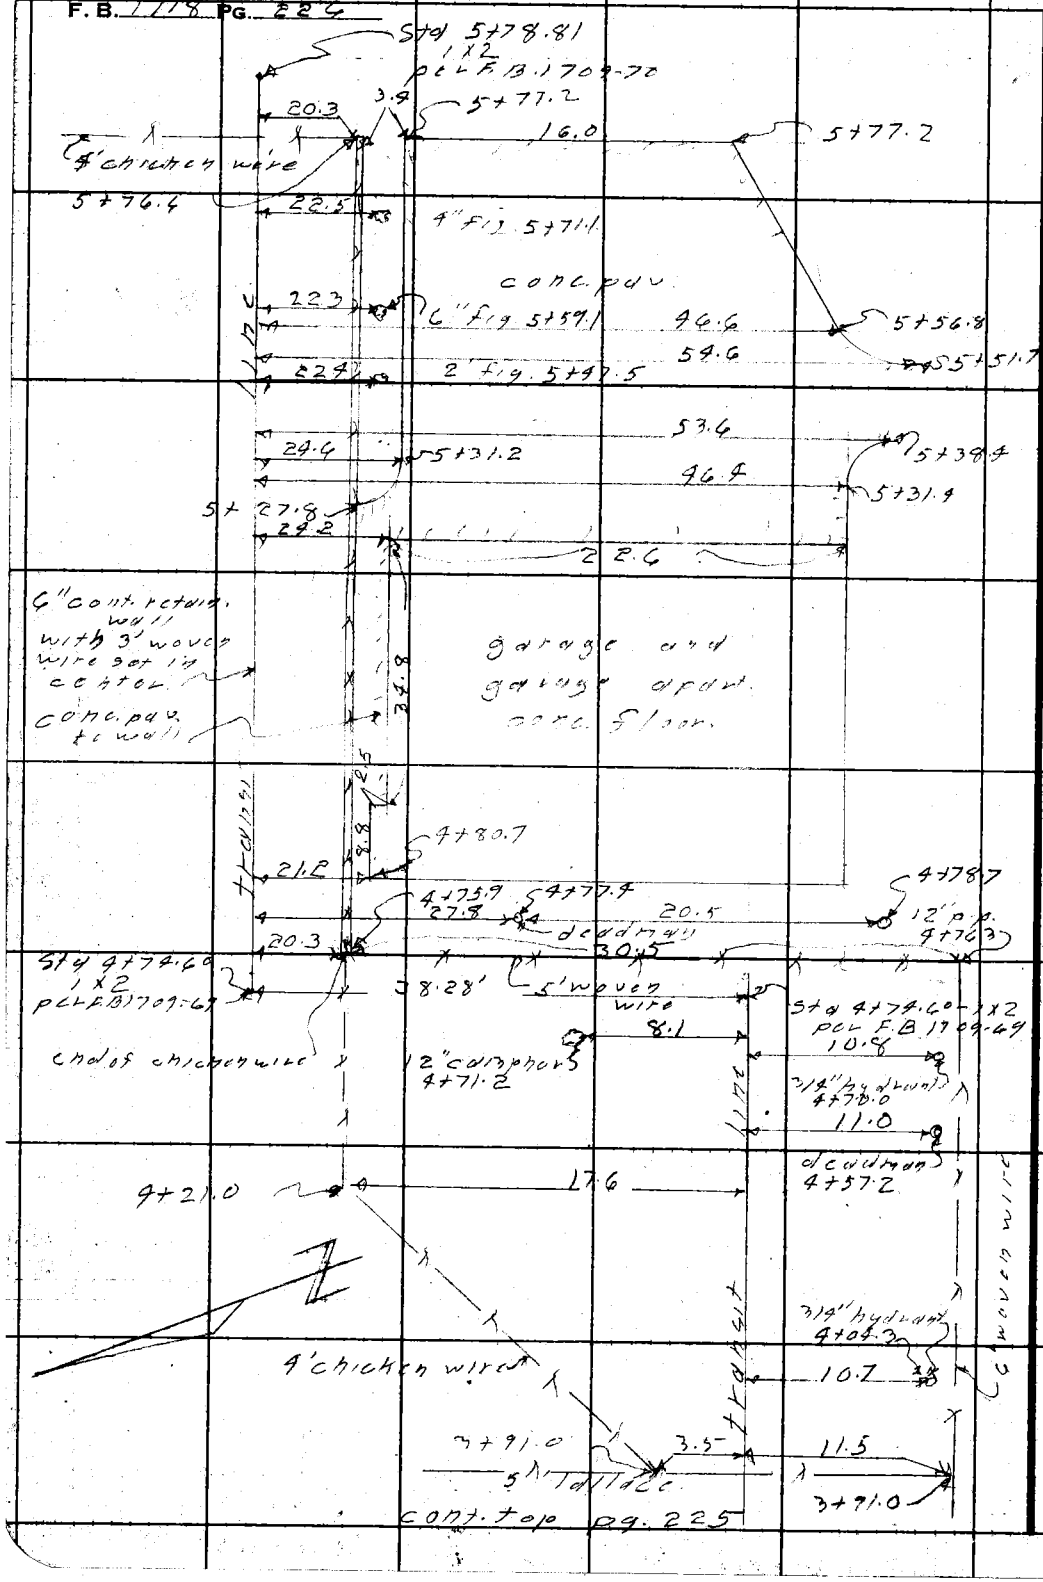

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by	Survey of Marengo Ave.
Map No.	W. O. 1392 Tape No. St'd. °F
Office Work	Surveyed by J. J. Lanigan
Checked	Notes Rejected Date 12-13-51
Date	Indexed

F. B. 1110 PG. 227

Note: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION of IMPROVEMENTS on WESTERLY LINE of 546 2ND LOTS FROM EAST. in BLOCK "15" M.R. 16-45-46 C.I. 1390

J. J. Lanigan
C. H. Lewis
H. H. Raphael
H. Tafoya
A. B. Barbon

76F3095 247 2-51

F. B. 1718 PG. 228

cont. bon pg. 229

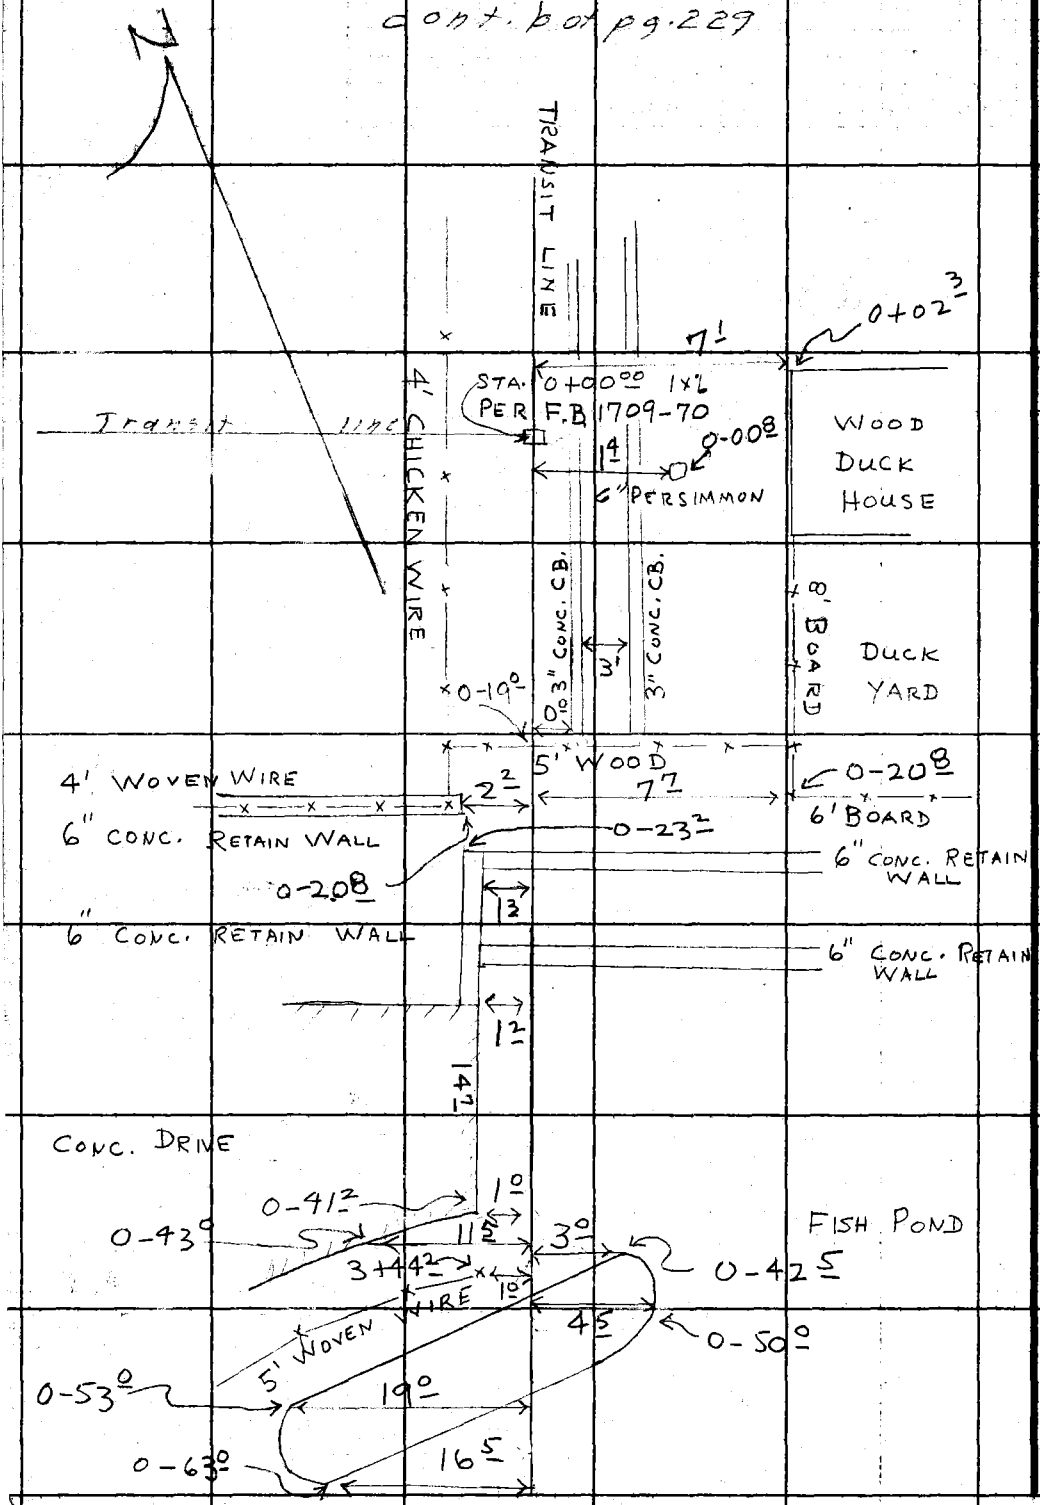

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of MARENGO AVE
W. O. 1390 Tape No. St'd. °F
Surveyed by LANIGAN
Notes RAPHAEL Date 11-13-51
Indexed

F.B. 1718 PG. 229

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

76F3005 247 2-51

TO STA. 3+14.67
SPK & TIN
PER F.B. 1709-70

TRANSIT LINE

4' WOOD

0+57 2 SHADE TREE

0+48 6 CYPRESS TREE

3" CONC. C.B.

0+44 6 HEDGE

0+42 6

0+35 9 BRICK INCIN.

WOOD SHED

0+28 5

8" WALNUT

0+23 8

0+20 8 WOOD GARAGE AND STORAGE SPACE

0+16 9

3" ACACIA TREE

0+13 2

0+02 3

41 CHICKEN WIRE

3" CONC. C.B.

3" CONC. C.B.

cont. top pg. 228

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

F.B. 1716 PG. 230

Profile No. ____ Notes Red. ____ Plotted ____ Job No. 1390 Division No. ____ F. B. 1718 Pg. 231

Date ____ Date ____ Survey of Maywood Area

Notes Chkd. 1247 Checked ____ Survey by ____ Notes ____ Date ____

No. ____ Date 11/26/57 Date ____ Map No. ____ Indexed ____ Date ____

PROFILE AND CROSS-SECTIONS OF PROPOSED SEWER EASEMENT IN BLOCK 15, M.R. 16-45-46

C.I. 1390

J.V. Lanigan
C.H. Lewis
H.H. Raphael
H. Tagaya
A.B. Barber

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

764298 307 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

1259.20

F. B. 718 Pg. 234 Job No. 4390 Division No. Notes Bkd. Plotted
Survey of Duarte 90 Ave. Date Date No. Profile
Survey by Lonigan Notes Lewis Notes Chkd Checked X-Sec.
Indexed Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
BM AE 469	2.97	1238 21		1235 24	AE 469 E 1235.236 FB 1568 P 102	
					Santa Anita Ave (E. side) 320' ± S of ℄ of Mendocino St.	
					Bt. spk in curb across street from Ho. # 2449	
0+00			388	123 433	Int of transit line & ℄ of Santa Anita Ave.	
"			454	123367		10' R
"			263	123558	20' L	
0+17			531	123290	conc. gutter at ℄	
"			592	123229	" " at Sta 1+11' R	
"			402	123419	" " 20' L	
"			320	123501	Top of curb "	
0+18			500	123321		℄ Top of macadam berm
"			538	123283		11' R " " "
0+29			462	123359		℄ Top of drain wall
"			586	123235		11' R " " " "
"			371	123450	19' L	" " " "
0+32			842	122979		11' R ctr drain.
"			633	123178	19' L ctr of drain	
0+36			552	123269		11' R E wall of drain
"			346	123475	19' L	" " " "
1+00			3 2/3	1235 0		℄

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
		1238.21				
1+00			3 3	1234 9		11' R
"			3 0	1235 2		
2+00			3 2	1235 0		
"			3 5	1234 7		11' R
"			2 7	1235 5	19' L	
T. P.			234	123587	T. P.	
	503	1240 90				
1+71			462	1236 28	Top of drain wall	8' R
"			783	1233 07	bot of drain	"
2+00			605	1234 85	Top of drain wall	"
"			695	1233 95	bot of drain	"
3+00			4 7	1236 2		
"			443	1236 47	Top of drain wall	8' R
"			509	1235 81	bot of drain	"
"			4 2	1236 7	10' L blk	
"			2 2	1238 7	19' L	
3+37			374	123716		8' R Top drain wall
"			4 0	1236 9		" bot drain
"			306	1237 84	19' L Top of drain wall	
"			3 8	1237 1	" bot of drain	

Profile Notes Red _____ Plotted _____ Job No. 4390 Division No. _____ F. B. 1718 Pg. 53

No. _____ Date _____ Survey of _____

No. _____ Date _____ Notes Chkd _____ Date _____ Survey by _____

No. _____ Date _____ Checked _____ Date _____ Map No. _____ Indexed _____ Date _____

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 1718 Pg. 234 Job No. 1390 Division No. Notes Red. Plotted Profile
Survey of Marengo Ave Date No.
Survey by Lanigan Notes Lewis Date Notes Chkd. Checked X-Sec.
Indexed Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	Transit Line & Transit Line Reduced	
		1240 90				
T. P.			2 92	1237 98	T. P.	
	4 43	1242 41				
4+00			4 4/0	1238		
"			4 9/5	1237		11" R
"			4 0/4	1238	10' L	
"			3 0/4	1239	19' L	
4+75			5 9/5	1236		
"			6 1/3	1236		11' R
"			5 4/0	1237	12' L brk	
"			3 0/4	1239	19' L	
T. P.			6 84	1235 57	T. P.	
	7 77	1243 34				
5+15			6 99	1236 35		16' R
"			6 83	1236 51	18' L bot of wall	
"			4 22	1239 12	19' L top " "	
5+78			7 05	1236 29		10' R
			6 8/5	1236	18' L bot of wall	
			4 40	1238 94	19' L top of wall	
5+78.81 E on 5th Transit Line produced					= 0+00 N	
0+20			4 2/3	1239	3' L	

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
		1243 34				
0+20 N			3 9	1239 4		7' R
T. P.			3 48	1239 86	T. P.	
	10 46	1250 32				
1+00 N			7 L	1243 2	3' L	
			7 R	1243 1		7' R
2+00			082	1249 50	3' L	
"			110	1249 22		7' R
T. P.			068	1249 64	T. P.	
	11 75	1261 39				
T. P.			181	1259 58	T. P.	
	592	1265 50				
BM AE 149			631	1259 19	AE 149 El 1259.202 FB 1447 - P. 157 Santa Rosa Ave. & Mendocino St. S.W. cor. BT. Spk in curb 6' W of E. end.	

Profile Notes Red. Plotted. Job No. 1380 Division No.
No. Date Date Survey of
No. Date Date Checked Survey by
No. Date Map No. Indexed Date

F. B. 1718 Pg. 235

F. B. 1718 Pg. 236 Job No. 1390 Division No. Notes Red. Plotted Profile

Survey of 227th-Longo Ave. Date Date No.

Survey by Lanigan Notes Lewis Notes Chkd. Checked X-Sec.

Indexed Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.

Do not extend notes this side of this line.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR

726 Los Angeles County Engineering Bldg.

761298 307 4-60

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Marengo Ave.
W. O. 1390 Tape No. St'd. °F
Surveyed by J. J. Lanigan
Notes J. J. L. Date 11-15-51
Indexed

F. B. 744 PG. 237

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
of
IMPROVEMENTS
on
PROPOSED SEWER EASEMENT
in
BLOCK 23
M.R. 16-45-46
C.I. 1390

J. J. Lanigan.
C. H. Lewis
H. H. Raphael
H. Tafoya.
A. B. Barber

76F3095 247 2-51

F.B. 1718 PG. 239

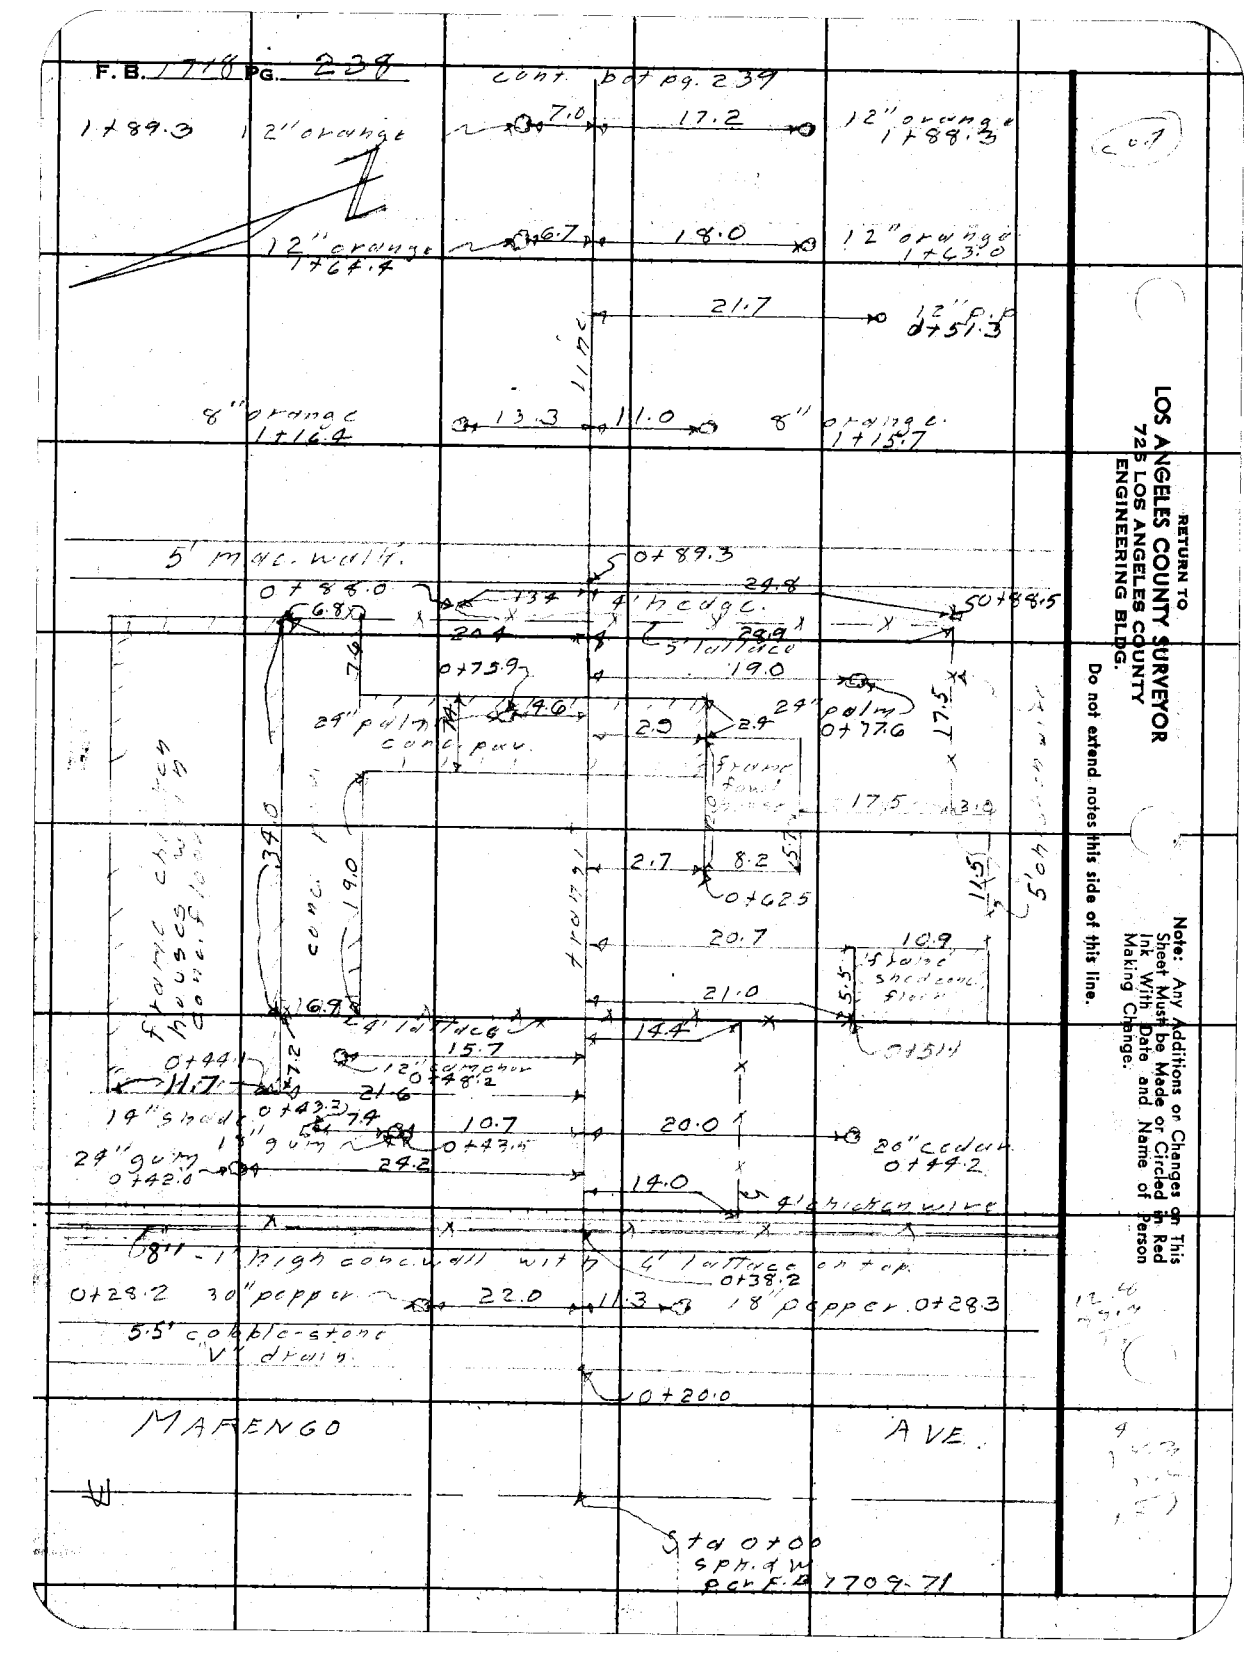

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by	Survey of Marengo Ave
Map No.	W. O. 1390 Tape No. St'd °F
Office Work	Surveyed by V. J. Lanigan
Checked	Notes V.J.L. Date 11-15-51
Date	Indexed

F. B. 1116 PG. 239

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink, With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76FSOS 247 2-51

cont from pg. 240

14.2
13.8
13.2
8" acacia
8" acacia
8" acacia
4+44.9
4+38.2
4+32.5
8.3
6.8
6.0
4" acacia
4" acacia
4+36.0
4+32.5
4+30.5
18" acacia
10" acacia
4+30.0
19.7.2
11.3
24" shade
3+86.5
6.6
14.3
30" laurel
3+82.7
14" carob
3+46.5
21.5
30" acacia
3+49.7
2.8
5
3+38.2
7.2
5" woven wire
10" shade
3+15.8
19.3
12" pine
3+20.0
3+09.7 8" pine
15.0
2+99.0 shrub
13.0
2+96.0 shrub
14.8
9' mac wall
with 3" concrete cubs
2+87.5
21.8
2+88.5
12" cypress
2+78.4
23.0
14" cypress
2+77.6
12.0
mac wall
2+75.7
12" cypress
2+69.7
19.0
3' hedge
2' inside
wall
5.8
34.7
4" orange
2+71.0
2+74.0
20.0
18.4
12" orange
2+60.0
2+58.0
1" avocado
2+56.8
14" orange
2+37.5
18.3
5.7
14" orange 2+34.0
trunk
12.8
1" avocado
2+12.2
12" orange
2+17.8
10.7

F. B. 1716 PG. 240

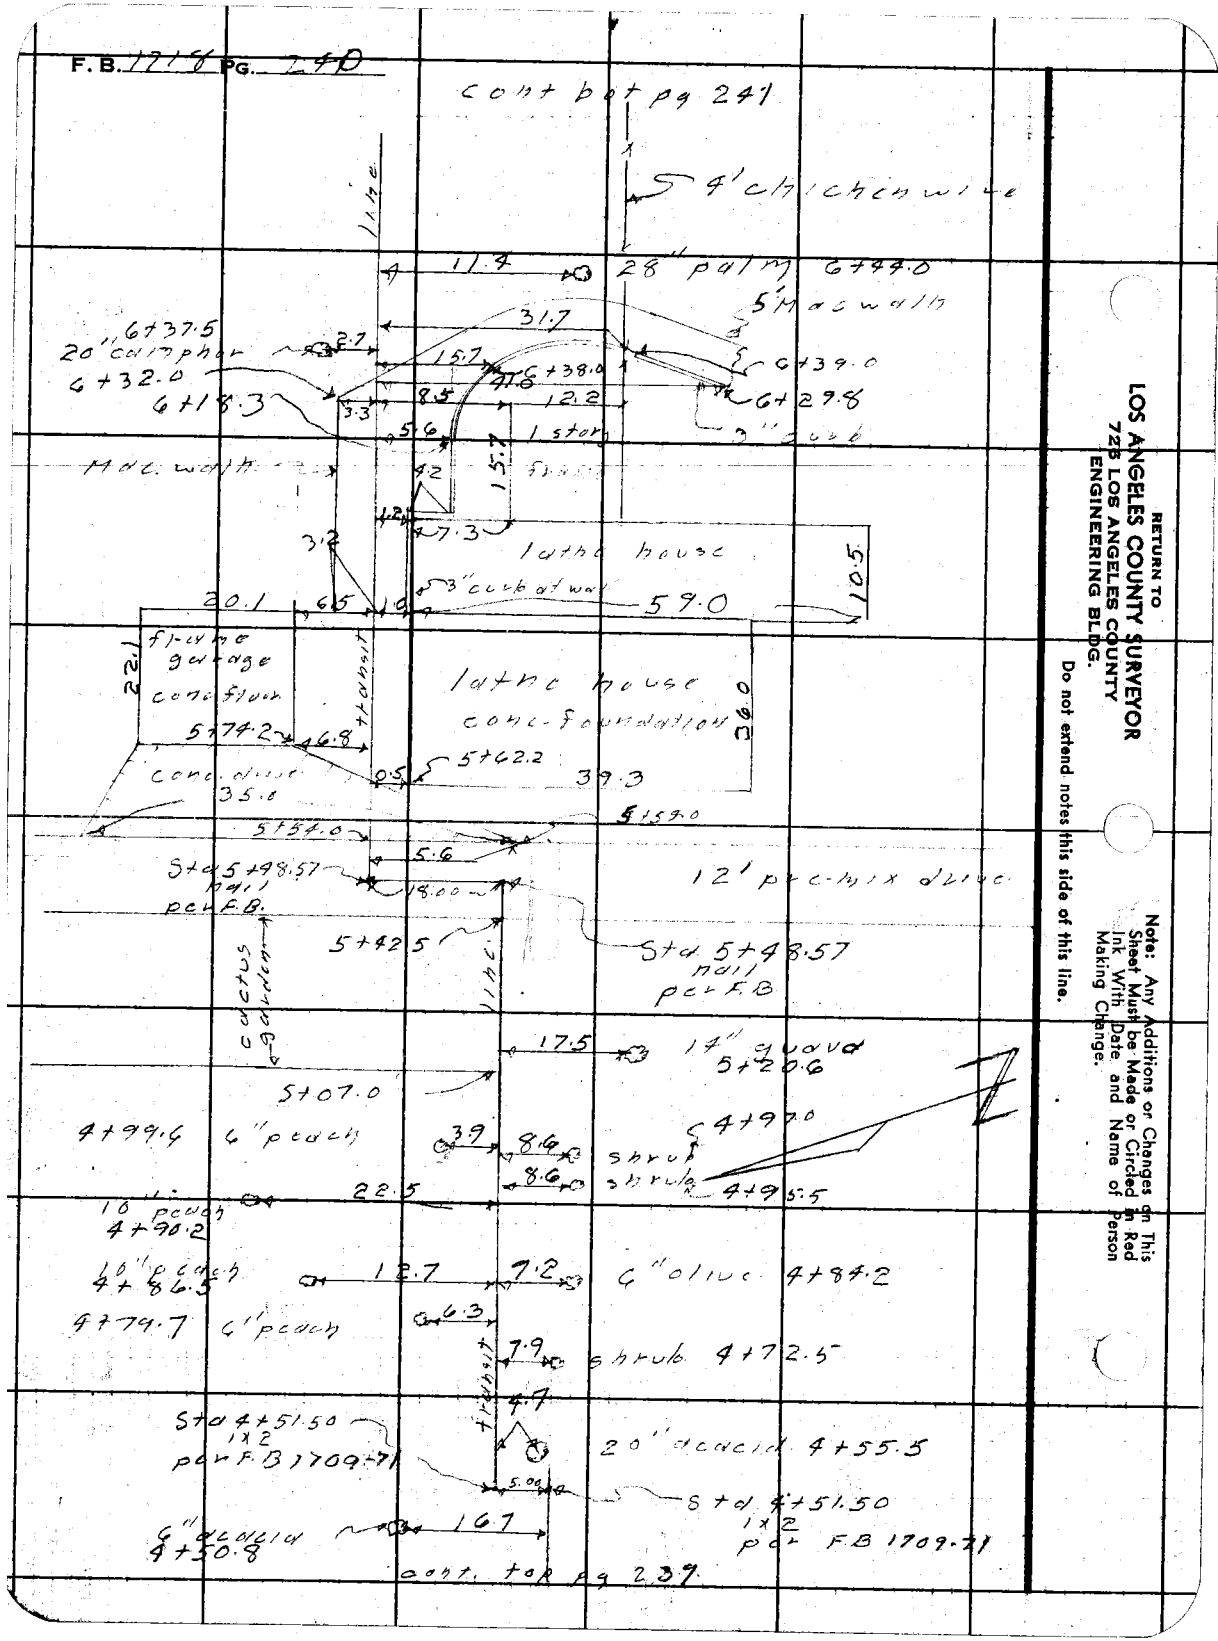

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by
Map No.
Office Work
Checked

Survey of Mahenge Ave. F.B. 1746 Pg. 29 L.
W. O. 1390 Tape No. St'd. °F
Surveyed by J. J. Lamiggs
Notes J.J.L. Date 11-15-54
Indexed

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.



4' chain link

22.7

7+51.4

4' chain link

22.7

7+47.4

4' woven wire

Bg. 7+46.23

1.X 2 pcl F.B. 1709-71

12.2

28.5

14" cedar 7+43.6

8" shade 7+40.8

15.7

20.8

18" palm 7+32.0

24" palm 7+28.7

WARNING - This wall is a property line.

4' chicken wire

9.9

12.6

30" palm 6+88.5

30" palm 6+79.4

T+W 5.1+

cont. top pg. 24D

76F3095 247 2-51

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

F. B. 1716 PG. 242

Profile No. | Notes Red. | Plotted | Job No. 1390 | Division No. | F. B. 1718 | Pg. 243
Date | Date | Survey of MARSHALL AVE.
Misc. No. | Notes Chkd. | Checked | Survey by J. J. Hanigan, C. H. Lewis | Date 11-14-46
Date | Date | Map No. | Indexed | Date

PROFILE AND CROSS-SECTIONS OF BACK LOT LINES IN BLOCK 23, M.R. 16-45-46

C.I. 1390

J. J. Hanigan
C. H. Lewis
H. H. Raphael
H. Tafoya
A. B. Barber

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

761298 307 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line. 29 — 21 R

F. B. 1718 Pg. 244 | Job No. 1390 Division No. | Notes Red | Plotted | Profile
Survey of Inglewood Ave. | Date | No. | X-Sec.
Survey by Lanigan Notes Lewis | Notes Chkd. | Checked | No.
Indexed | Date | Date | Date

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
BM AE 472	9 25	1281 28		1272 03	AE 472 El 1272.028 FB 1568 P 105	
					Marengo Ave. (w. side) 425'± S of ℄ of Mariposa St.	
					Bt. spk in conc. drive to Ho # 2611	
0 + 00			4 63	1276 65	Int. of Transit Line & ℄ of Marengo Ave.	
"			6 03	1275 25		21' R
"			2 74	1278 54	29' L	
0 + 20			5 18	1276 10	edge of pvmt ℄	
"			6 62	1274 66	" " "	21' R
"			3 36	1277 92	" 29' L "	
0 + 25			6 90	1274 38	bot of ditch ℄	
"			8 18	1273 10	" " "	21 R
"			4 94	1277 34	29' L " " "	
0 + 25 ±			5 34	1276 94	Top of wall ℄	
"			6 62	1274 66		21 R
"			3 24	1278 04	29' L	
0 + 38			5 4	1275 9	Fence Line (P.L.±) ℄	
"			6 5	1279 8	" " "	21 R
"			3 0	1278 3	29' L " " "	
T. P.			595	1275 33	T. P.	
	7 25	1282 58				
1 + 00			6 3	1276 3		℄

76L296 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

T.P. 493 1277.87

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
		1282.58				
1+00			7.5	1275.1		21' R
"			4.4	1278.2	29' L	
2+00			5.5	1277.1		℄
"			6.1	1276.5		21' R
"			2.0	1280.6	29' L	
T.P.			2.67	1279.91	T.P.	
	2.89	1282.80				
3+00			4.9	1277.9		℄
"			6.5	1276.3		21' R
"			1.9	1280.9	29' L	
3+80			5.0	1277.8		℄
"			6.9	1275.9		21' R
"			4.2	1278.6	29' L	
4+00			4.5	1278.3		
"			4.4	1278.4		21' R
"			4.0	1278.8	29' L	
4+40			4.8	1278.0		℄
"			4.9	1277.9		21' R
"			4.8	1278.0	29' L	
4+50			5.0	1277.8		℄

Profile Notes Red_____ Plotted_____ Job No. 1390 Division No._____
No._____ Date_____ Date_____ Surveyed Dec. 1950 F. B. 1718 Pg. 24
Notes Chkd._____ Checked_____ Survey by [illegible]
No._____ Date_____ Date_____ Map No._____ Indexed_____ Date_____

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 1718 Pg. 246 | Job No. 1390 Division No. | Notes Red. | Plotted | No. | Profile
Survey of Magnolia Ave | Date | Date | No. | X-Sec.
Survey by Lanigan Notes Lewis | Notes Chkd | Checked | No.
Indexed | Date | Date | Date

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
		1282 80				
4+50			3 0	1279 8		21' R
"			1 1	1281 7	29' L	
T. P.			4 93	1277 87	T. P.	
	6 36	1284 23				
5+00			6 3	1277 9		℄
"			8 3	1275 9		21' R
"			4 1	1280 1	29' L	
6+00			4 3	1279 9		℄
"			6 0	1278 2		21' R
"			2 3	1281 7	29' L	
7+00			3 3	1280 9		℄
"			5 0	1279 2		21' R
"			1 4	1282 8	29' L	
7+46 23			2 9	1281 3		℄
"			3 4	1280 8		21' R
"			0 6	1283 6	29' L	
T. P.	11 69	1295 16	0 76	1283 47		
T. P.	11 29	1305 63	0 82	1294 34	AE 473 El 1301.477 FB 1568 P 105	
T. P.	3 68	1307 39	1 92	1303 71	Maniposa St. & Magnolia Ave S.E cor.	
BM AE 473			5 92	1301 47	Bt. sph in curb 5' E of E end C.R.	

Notes Ck'd by	Survey of Marengo Ave.
Map No.	W. O. 793 Tape No. St'd. °F
Office Work	Surveyed by J.J. Lanigan
Checked	Notes J.J.L. Date 11-19-51
Date	Indexed

F. B. 1718 Pg. 297

Note: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION of IMPROVEMENTS on PROPOSED S.S. EASEMENT in Mc NALLY TRACT (M.B. 6-57) C.I. 1390

J.J. Lanigan
C.H. Lewis.
H.H. Raphael.
H. Taff 99.
A.B. Barber.

76ff3095 247 2-51

F.B. 1718 PG. 246

cont. bot. pg. 247

12" avocado 1+96.6 — 16.3

12" avocado 1+77.0 — 15.1

10" avocado 1+22.5 — 15.2

1+13.0 10" pp — 7.3

10" avocado — 16.0

0+86.5 deadman — 8.5

0+67.6 10" avocado — 15.6

6" fence 0+57.2 — 25.5

0+49.5 8" avocado — 15.7

0+44.8 shrub — 3.8

0+39.4 shrub — 4.0

0+35.2 shrub — 3.6

0+28.3 20" pepper — 1.0

Cobble stone retaining wall

45 Orange gutter

0+21.2

MARENGO AVE.

Sta 0+05

Sph. #14

PCR AP 1709-73

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Maranga Ave
W. O. 1399 Tape No. St'd °F
Surveyed by J. J. L and party
Notes J. J. L Date 11-21-51
Indexed

F. B. 716 PG. 24 9

- cobble-stone

Flag stone retwin
3+82.3 c'pound
conc. walk
3779.6
3+74.3
3770.3
3+70.0 10" plum
cobble-stone walls - 3' high to form flower box
6' boarb.
3+54.2
3+54.0
4" juniper
3741.0
3+33.3 4" loquat
conc. porch
28" palm
3+14.4
3+21.4
6" umbrella
4" magnolia
3716.2
3+06.6
2+68.7 9" lemon
2+59.1 12" p.p.
2+58.5
3" conc. retwin wall
2+43.6
R=9.1+
conc. swimming pool - 12" walls
2+36.9
2+25.0
R=8.5'L
2+15.0 10" avocado
2+09.3
cont. top. pg. 246

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76R3095 247 2-51

F.B. 1118 PG. 250

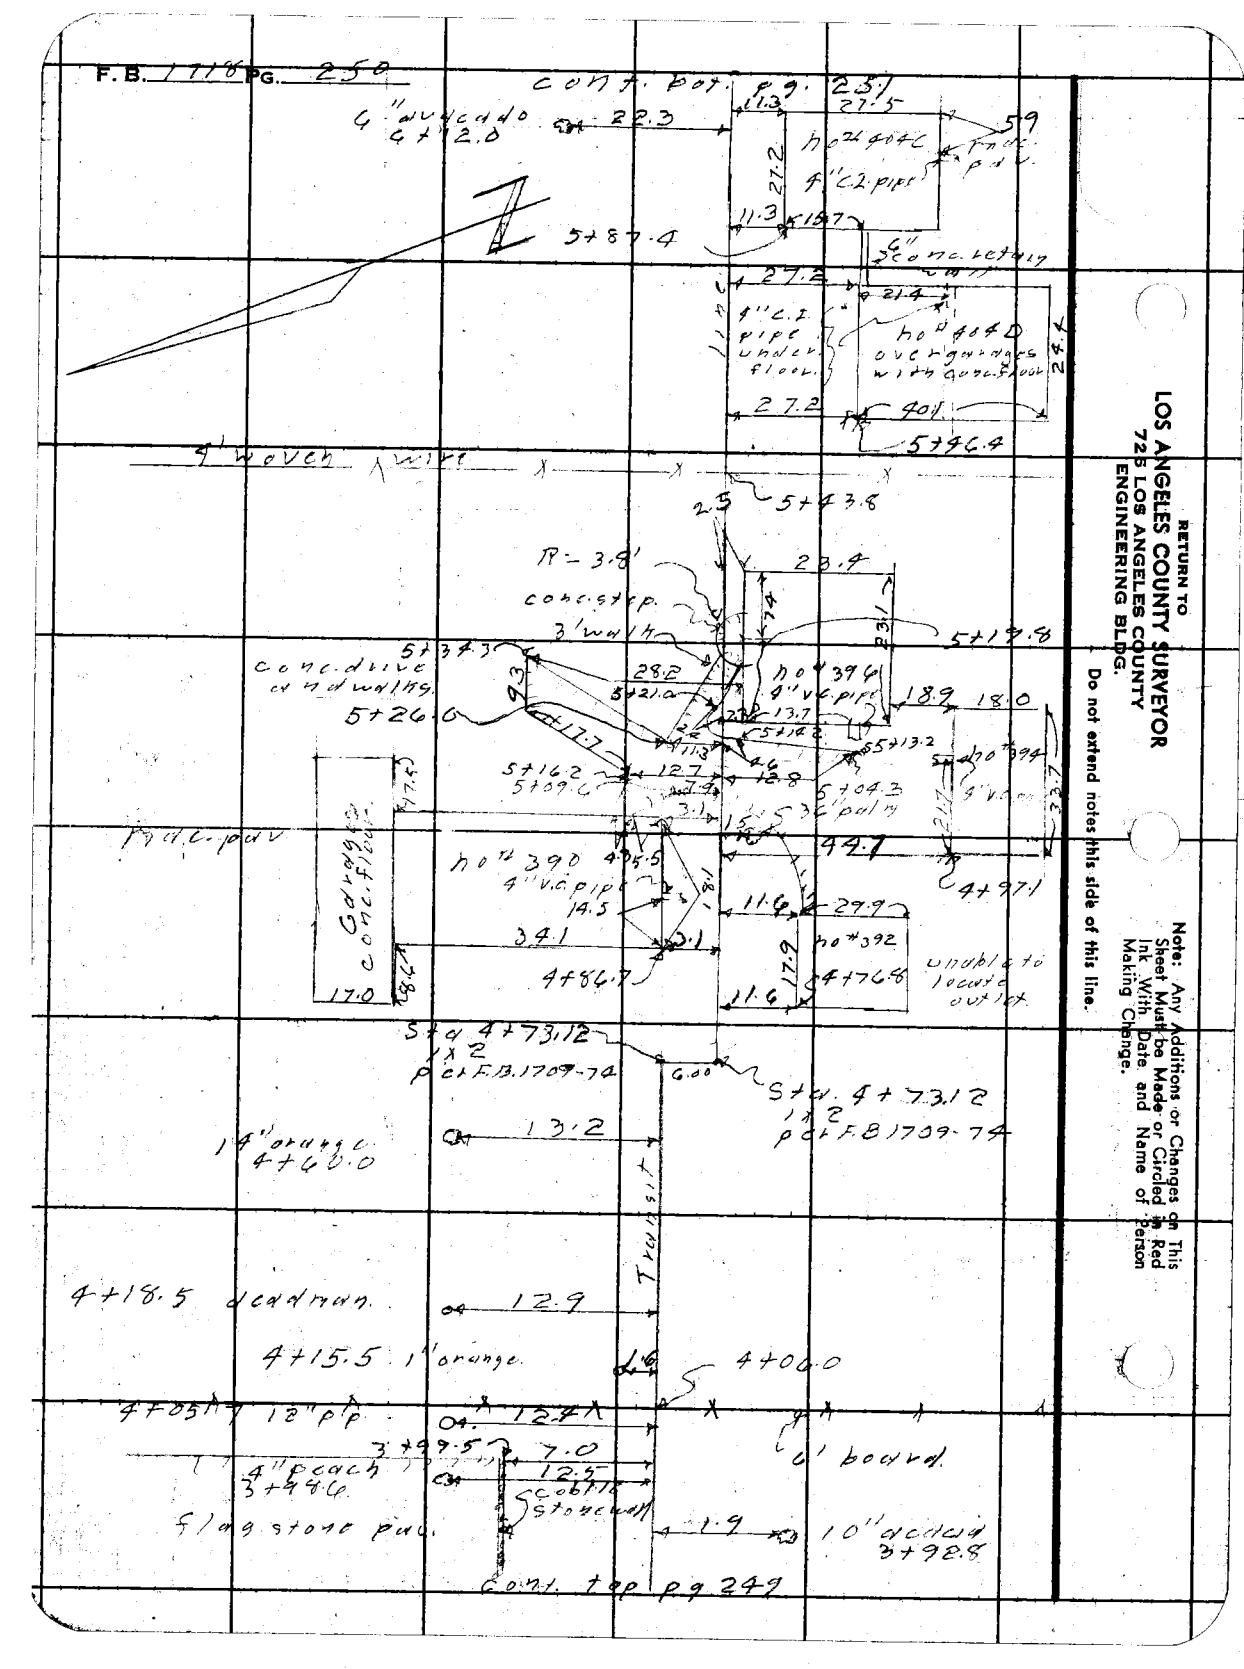

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Montrose Ave
W. O. 1390 Tape No. St'd. °F
Surveyed by J.V.L. & Crew
Notes J.J.L. Date 11-21-51
Indexed

F. B. 1716 Pg. 251

Note: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

5' board
7+35.0
3.0
36.0
7+22.7 18" camphor
Sta-7+11.85
L.T. perp. Bl. 709-75
3.6
10' conc drive with 6" curbs
7+06.9
10" avocado
6+97.5
11.4
42
6" orange 6+97.5
14.7
9.7
18" camphor 6+74.0
4.5
23.7
6+77.0
36.0
25.4
6+72.0
conc. pad
garage
house
33.7
9" c.b. pipe
26.0
18.0
4" conc. retaining wall
12" avocado 6+46.3
18.7
3.6
6+31.2
6" orange
18.4
6+28.0
2.0
6+30.3
5' board
9.4 mac. drive
6+16.0
6" conc. retaining wall
11.2
9.1
6+16.0
CONT. TOP pg. 2.50

FORM 98.247 2-51

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

F.B. 1716 PG. 252

F. B. 1718 Pg. 253

Profile No. | Notes Red. | Plotted | Job No. 1390 | Division No.
Date | Date | Survey of Marengo Avenue
X-Sec. No. | Notes Chkd. 2CM | Checked | Survey by Lanigan | Notes Lewis | Date 11-21-57
Date 11/26/57 | Date | Map No. | Indexed | Date

PROFILE AND CROSS-SECTIONS OF PROPOSED EASEMENT IN McNALLY TRACT - M.B. 6-57

C.I. 1390

J. J. Lanigan
C. H. Lewis
H. H. Raphael
H. Tafoya
A. B. Barber

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

76L298 307 4-58

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 Pg. 254 | Job No. 1390 Division No. | Notes Red. | Plotted | Profile
Survey of Malengo Ave. | Date | No. | X-Sec.
Survey by Lanigan | Notes Lewis | Notes Chkd. | Checked
Indexed | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line (I)
BM AE259	1 47	1346 14		1344 67	AE259 El 1344.671	F.B. 1447-P. 238
T. P.			11 33	1334 81	Foothill Blvd. & Malengo Ave., N.E. cor.	
	1 75	1336 56			Bt. spk. in curb 1' E of W end of catch basin	
0+00			959	132697	Int of Transit line & ℄ of Malengo	℄
"			816	1334 40	21' L	
0+21			1093	132566	edge of pvmt	℄
"			920	1332736	21' L " " "	
0+26			1215	133241	bot of ditch	℄
"			1036	1332620	21' L " "	
0+29.5			906	133250	Top of ditch wall	℄
"			752	1332904	21' L " " "	
0+37			8?	133279		℄
"			7 3/4	133243	21' L	
T. P.			959	132697	T. P.	
	6 13	1333 10				
1+00			543	132767		℄
"			4 5/6	133226	15 L	
"			3 1/2	133200	21' L	
2+10			1 8/3	133213		℄
"			0 1/2	133300	21' L	

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

2.83

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line	Grade
		1333 10					
T. P.			1 73	1331 37			
	7 28	1338 65					
2+12			7 3/4	1331 4/4	at S. base of wall	2'L at corner	
"			5 1/4	1333 6/4	3'L-N. " " "		
"			4 5/4	1334 2/4	21'L		
2+37			12 45	1326 20/4	invert of swimming pool at drain outlet	14.5'L	
2+57			6 6/4	1332 1/4	2'L S. base of wall at corner		
"			4 7/4	1334 0/4	3'L N. base of wall		
"			4 8/4	1333 9/4	21'L		
2+58			5 4/4	1333 3/4	21'L		
3+00			6 3/4	1332 4/4			
"			5 8/4	1332 9/4	10'L		
"			8 0/4	1330 7/4		10' R	
T. P.			5 09	1333 56	T. P.		
	4 52	1338 08					
4+00			3 7/4	1334 4/4			
"			2 7/4	1335 4/4	10'L		
"			5 5/4	1332 6/4		20' R	
4+73			3 10/4	1335 1/4			
"			7 2/4	1330 9/4		75' R	

Profile Notes Red. Plotted Job No. 1390 Division No.
No. Date Date Survey of 22nd street sewer
X-Sec. Notes Chkd Checked Survey by Pearson Notes Lewis Date 11-21-51
No. Date Date Map No. Indexed Date

F. B. 1718 Pg. 2555

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1718 Pg. 25 | Job No. 4390 Division No. | Profile No. | Plotted | Notes Red. | Date | X-Sec. No. | Date
Survey of 223rd St & 90 Ave | Date | Notes Chkd. | Checked | Date
Survey by Ryan & Lewis | Date | Indexed | Date

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line (5th'ly)
		1338 08				
T. P.			2 83	1335 25		
	550	1340 75				
5+01			7 1	133 7	32'L Elev. 4" pipe - HO.	# 390
4+94			6 78	133 97	12'R Floor elev. HO	# 392
5+20			8 6	133 2	44'R Elev. pipe - HO	# 394
"			6 1	133 7	152'R " " "	396
5+43			3 7	133 1		℄
"			8 8	133 0		69'R
T. P.			2 61	133 14		
	053	1337 67				
5+46			4 76	133 91	# 404D Garage floor level where pipe enters	48½'R
5+70			4 98	1332 69	" " "	" " "
5+75			0 5	133 2		℄
"			0 70	133 97		27'R Top of wall
"			5 0	1332 7		28'R Bot of wall
6+08			6 5	133 2	4" pipe outlet to HO	# 404C
6+90			6 4	132 2	" " " "	416½
7+00			0 7	1337 0		℄
"			5 3	1332 4		69'R

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.		
		1337 67				
T. P.			020	1337 47	T. P.	
	12 13	1349 60				
T. P.			028	1349 32	T. P.	
	822	1357 54				
BM AE260			176	135578	AE260 E/1355.797 F.B. 1447 P. 239	
					Foothill Blvd + Santa Anita Ave. S.E. Cor.	
					Bt. Spk. in curb 4' E of E.W. end of Catch Basin	

Profile Notes Red. Plotted Job No. 1390 Division No. V F.B. 718 P.B. 257
No. Date Survey of 1956 thru 60 Etc.
X-Sec. Notes Chkd. Checked Survey by Langan Notes Laws Date 11-26-57
No. Date Date Map No. Indexed Date

Job No. 040 Division No. Notes Red. Plotted Profile

Date Date

Notes Lewis Notes Chkd. Checked

Date Date
