DATE	W.O.				
1-52	1462	TOLA AVE.	Ventura St. to Harriet St.	Topog	5-8
				X-sect	9-14
"	"	CALAVERAS ST.	Tola St. to E'erly Line La Canada Valley Tr.	Topog	15-16
				X-sect	17-20
"	"	MOUNTAIN VIEW RD.	Casitas Ave. to Lincoln Ave.	Topog	21-26
				X-sect	27-36
"	"	MOUNTAIN VIEW RD.	Casitas Ave. to Windsor Ave.	Topog	37-42
				X-sect	43-50
"	"	ROYCE ST.	Lincoln Ave. to E'erly Line of Tr 4702	Topog	51-58
				X-sect	59-70
"	"	CASITAS AVE.	Royce St. to Ventura St.	Topog	71-76
				X-sect	77-86
"	"	LINCOLN AVE.	Royce St. to Foothill Blvd. Location of Basements		87-94
			Back Lot Line & Basement	Elev.	95-96
"	"	STERLING PLACE	Ventura St. to E'erly End of Sterling Pl.	Topog	97-104
				X-sect	105-112
"	"	CALAVERAS ST.	Sterling Pl. to E'erly Line R.S. 17-32	Topog	113-120
				X-sect	121-128
"	"	CRESTVIEW DR.	Mariposa St. to W'erly End of St.	Topog	129-136
				X-sect	137-144
"	"	RIDGEVIEW DR.	Mariposa St. to Foothill Blvd	Topog	145-152
				X-sect	153-160
"	"	WINDSOR AVE.	E'erly Line of Tr 7950 to Ventura St.	Topog	161-168
				X-sect	169-176

OVER

Survey of W.O. [illegible]
Surveyed by [illegible]
Notes [illegible]
Indexed [illegible]

F.B. 1790 Pg. 3

F.B. 1738 Pg. 4

INDEX TO F.B. 1738 (CONT'D.)

DATE	J.N.	DESCRIPTION			NOTES	PAGES
2-52	1462	SCHOOL FOR CEREBRAL PALSIED CHILDREN	Location of Buildings & Furnishings	Outlets		139-140
				Elevations		141-142
"	"	SACRED HEART SCHOOL on Mariposa St.	"	"	"	143-146
"	"	AUDUBON SCHOOL	"	"	"	147-148
5-52	"	SCHOOL FOR CEREBRAL PALSIED CHILDREN	Transit Line Thru the Grounds			149-154
					Profile	155-158
"	"	1st ALLEY W.of LINCOLN AVE	Mer'ly Line Lot 24 Tr6489 to Foothill		Topog	159-160
					Profile	161-164
"	"	Eer'ly Line of Tr.4702	Boyce St. to N'ly Line of 1st Lot N.of Boyce		Topog	165-166
					Profile	167-168
"	"	Boys & Girls Aid Society	Location of Bldg's			169-170
					Elev.	171-172
"	"	Lot 37 M.R. 52-50	Mariposa St. North		Profile	173-174
12-52	"	R/W Between HARRIET ST. & CRESTFORD DR.			℄ & Ties	175-176
					Topog	177-182
					X-sect	183-186
5-53	"	MOUNTAIN VIEW RD.	C sitas Ave. to Windsor Ave.	Low House Loc.& Elev,		187-192
		"	" " Lincoln Ave.	"		193-198
"	"	VENTURA ST.	Windsor Ave. to Lincoln Ave.	Low Houses Loc.& Elev.		199-206
6-53	"	CASITAS AVE.	Calaveras St. to Mariposa St.	"		207-214
"	"	FOOTHILL BLVD.	Lincoln Av to City Bdry.	"		215-218
"	"	CRESTFORD DR.	Foothill Blvd. to N'ly Line Tr.14309	"		219-222
"	"	DEVIRIAN PL.	C sitas Ave. to Lincoln Av .	"		223-226
"	"	HARRIET ST.	Casitas Ave.	"		227-230
"	"	Lot Lines Tr.12677	From Crestford Dr.		℄	231-232
					Topog & X-sect	233-250

RETURN TO
LOS ANGELES COUNTY SURVEYOR
728 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by:		Survey of: Eastern Ave.	F.B. 1738 PG 5
Map No.		W. O. 1462 Tape No.	St'd. °F
Office Work		Surveyed by: J. J. Lanigan	
Checked		Notes J.J.L. Date 1-9-32	
Date		Indexed	

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION of IMPROVEMENTS on TOLA AVE from VENTURA ST to HARRIET ST C.I. 1462

J. J. Lanigan
C. H. Lewis
H. H. Raphael
H. Tafoya

76F3095 247 2-51

F. B. 1738 PG. 9

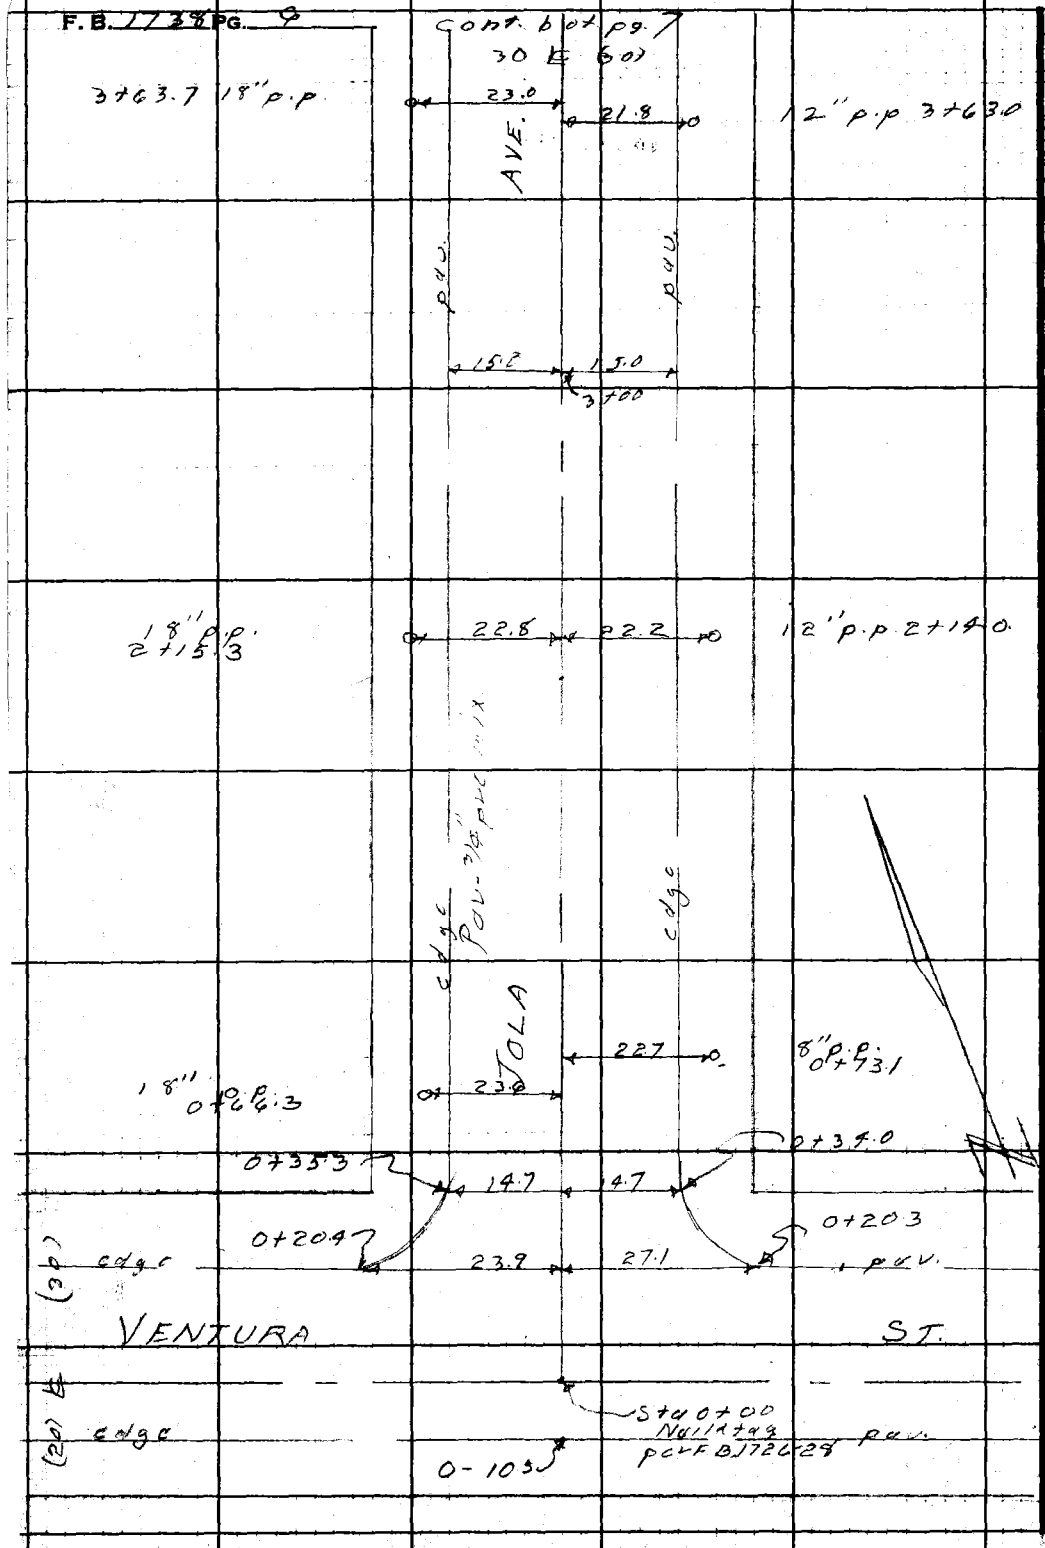

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.
Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Office Ck'd by
Map No.
Office Work
Checked
Date

Survey of Capitol Ave.
W. O. 1942 Tape No. St'd °F
Surveyed by V.V. Lanigan
Notes V.J.L. Date 1-2-32
Indexed by Tom Scott

F. B. 1738 Pg. 1

Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

7873095 247 1981

1942 P 2497 p. 24

HARRIET ST.

(45') E (25')

Sta 7+79.45
S.W.ST.
P.C.V.F.B. 1726-46

7+69.8
21.6
23.0
7+65.4
7+59.4
15.0
15.4
7+53.1
W.I.V. 7+59.8

12" p.p 6+66.8
23.9
22.3
12" p.p 6+62.6

AVE.

P.O.C.

P.O.C. 3/4" pre-mix

Edge

5+29.3
12" p.p 5+28.6
15.1
22.3
Sta-5+07.95
SPH. & W.
P.C.V.F.B. 1726-59
30.2
5+22.0

18" R.F. 5+13.3
23.0
15.0
CALAVERAS ST. (80')

29.3
4+94.0
14.5
4+83.3

Edge

TOLA

12" p.p. 4+62.6
17.5
(30') E (30')

Cont. top pg. 6

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

F.B. 1138 PG. 8

Notes Red. Plotted Job No. Casting Ave.

Map 2129-1 Date Map No.

PROFILE
and
CROSS SECTIONS
on
TOLA AVE.
from
VENTURA ST.
to
HARRIET ST.
C.I. 1962

J.J. Lamigan
H.H. Raphael
A.B. BARBER.

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

76L298 307 4-58

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile ____ Plotted ____ Notes Red. ____ Division No. V Job No. 4U Pg. 10
Survey of Easterly 5 Ave. Date ____ No. ____ Notes Chkd. ____ Date ____ X-Sec. ____ No. ____
Survey by Lundgren Notes Lamigan Checked ____ Date ____
Indexed K. C. Johnson Date ____

STATION	B. S.	H. I.	F. S.	ELEV.		
						Elev. 1179.230 - F.B. 1568 - Pg 10
BM AE507		✓		1177 23	BM AE507 Ventura St & Tolo Ave, N.E. cor. B.S. Sph. in W. side of P.R. & 53 ± GD N.	
	4 12	1183 35				
0+00			7 06	1176 29	19+ ℄ s of Tolo Ave ℄	Ventura St.
			6 50	1176 85	100' E. on ℄ of	Ventura St.
			7 24	1176 11	100' W. "	"
0+06.2			6 72	1176 62		℄ crown of pav.
0+21.4			6 96	1176 39		℄ cross gutter
1+00			382	1179 53		℄
"			418	1179 17		15' R. edge pav.
"			31	1180 3		21 R.
"			29	1180 5		30' R P/L.
"			4 00	1179 35	15' L edge pav.	
"			34	1180 0	17 L.	
"			34	1180 0	30' L P/L.	
T.P		✓	0 12	1183 23	T.P.	
	5 37	1188 60				
2+00			537	1183 23		℄
"			561	1182 99		15' R. edge pav.
"			45	1184 1		18' R.
"			44	1184 2		30' R - P/L.
"			550	1182 10	15' L - P/L.	

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Total	Ave.
		1				
		1188 60				
2+00			47	1183 9	17'L-	
"			50	1183 6	30' L P/L.	
2+10			42	1184 7		265± R- Back lot
2+20			49	1183 7	180'± L back lot.	
3+00			176	1186 84		℄
"			184	1186 76		15' R. edge pav.
"			13	1187 3		17' R.
"			08	1187 8		30' R - P/L.
"			204	1186 56	15' L. edge pav.	
"			13	1187 3	17' L	
"			13	1187 3	30' L P/L.	
T.P.		1	025	1188 35	T.P.	
	1112	1199 47				
4+00			888	1190 59		℄
"			900	1190 47		15' R - edge pav.
"			82	1191 3		18' R.
"			74	1191 9		30' R - P/L.
"			908	1190 39	15' L. edge pav.	
"			82	1191 3	18" L	
"			74	1192 1	30' L P/L.	

Profile Notes Red. Plotted. Job No. 1462 Division No. V F. B. 1735 Pg. 11
No. X-Sec. Date Date Survey of Contract
Notes Chkd. Checked Survey by L. Gilliam Notes by J. Johnson
No. Date Date Map No. Indexed Date

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1738-Pg. 12 | Job No. 4422 Division No. V | Profile | Notes Red. | Plotted | No. | X-Sec.
Survey of Calvillas Lane | Date | Date | No.
Survey by Lawrence Notes L. Griffing | Notes Chkd. | Checked | No.
Indexed A. C. Johnson Date | Date | Date

STATION	B. S.	H. I.	F. S.	ELEV.	Tola	AVC.
		11994.7				
4+94			52	1194.3		30' R P/L
5+07.95			491	1194.56	Inc. E's TOLA AVE & Calavellas ST	
			514	1194.31	15' E. on E of Calavellas ST.	
			548	1193.79	30' E. on E of Calavellas ST - 14' S. gutter	
			526	1194.21	" "	" 14' S. curb
			452	1194.95	30' "	" 14' N. gutter
			404	1195.43	" "	" 14' N. curb
			457	1194.90	100' E. on Calavellas ST - E.	
			557	1193.90	"	" 14' S. gutter
			496	1194.51	"	" 14' S. curb
			430	1195.17	"	" 14' N. gutter
			372	1195.75	"	" 14' N. curb
5+07.95			523	1194.24	15' L edge pav.	
"			48	1194.7	18' L.	
"			95	1195.0	30' L. edge pav.	
"			64	1193.1	246'± L back Lot line.	
5+22			37	1195.8		30' R. P/L.
T.P			165	1197.82	T.P.	
	10.37	1208.19				

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. No. Date
Plotted Date
Job No. 146 2 Division No. V
Survey of
Sec. Notes Chkd. No. Date
Checked Date
Survey by V.V.L. Notes V.V.L. Date 1-10-62
Map No. Indexed C. Johnson
F. B. 1733 Pg. 13

STATION	B. S.	H. I.	F. S.	ELEV.		
		120819				
6+00			1034	119785		℄
"			1052	119767		15' R edge pav.
"			99	11983		17' R
"			94	11988		30' R - P/L
"			1065	119754	15' L edge pav.	
"			99	11983	18' L	
"			96	11986	30' L P/L.	
7+00			669	120150		℄
"			708	120111		15' R. edge pav
"			60	120220		18' R
"			59	120223		30' R - P/L
"			705	120119	15' L edge pav.	
"			64	120178	18' L.	
"			60	120222	30' L P/L	
7+54.5			35	12047		30' R - P/L.
"			39	12043	30' L P/L.	
7+60			452	120367		℄
7+79.45			348	120471	Int. of E's Fola Ave & Harriet St.	
			315	120504	100' E'erly on ℄ at	"
			383	120436	100' W'erly	"

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 1738 Pg. 14-1 Job No. 1442 Division No. V. Notes Red. Plotted. Profile
Survey of C.S. 1745 Date. No.
Survey by L. Cartwright Notes C.S. 1745 Date. X-Sec.
Indexed R. C. Johnson Date. Notes Chkd. Checked. No.
Date.

STATION	B. S.	H. I.	F. S.	ELEV.		
		1209 19				
BM AE 527			1 67	1206 52	BM AE 527 Elev. 1206.530 - FB. 1568-14 / Hollister St (N. side), 81'± W. of E of Told Ave: B.F. sph. in conc. d.m. to ho # C 25.	

Notes Ck'd by:
Map No.
Office Work
Checked
Date

Survey of Casitas Ave.
W. O. 1462 Tape No. St'd. °F
Surveyed by V.J. Lonigan
Notes V.J.L. C. Johnson Date 1-9-52
Indexed

F. B. 1738 Pg. 15

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION of IMPROVEMENTS on CALAVERAS ST. from TOLA AVE. to THE EASTERLY LINE of LA CANADA VALLEY VIEW TR. C.T. 1462.

J.J. Lonigan

H.H. Raphael

76F3095 247 2-51

F.B. 1726 PG. 16

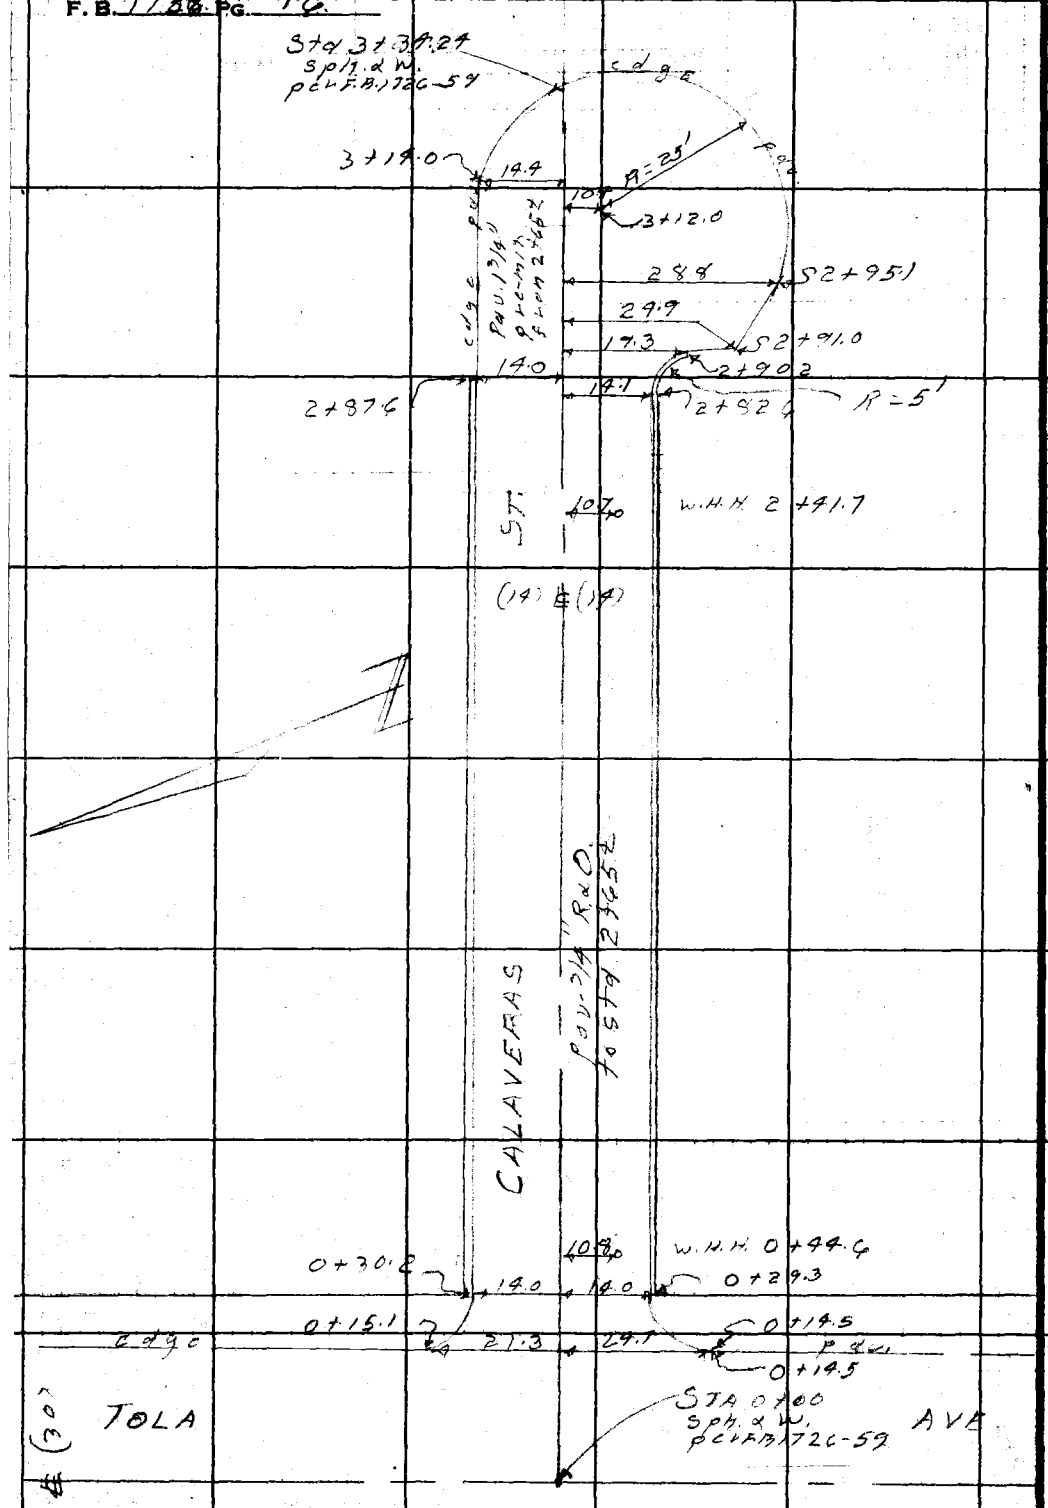

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Notes: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No. | Notes Red | Date | Notes Checked | Date | Platted | Date | Checked | Date | Job No. 1462 | Division No. V | Survey of Calaveras Ave. | Survey by [illegible] | Map No. | Indexed C. Jones

PROFILE
and
CROSS-SECTIONS
of
CALAVERAS ST.
from
TOLA AVE.
to
THE EASTERLY LINE of LA CANADA VALLEY VIEW TRACT.
C.I. 1462.

J.J. Lambiase
H.H. Ruppel
A.B. Barbee

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

761.298 SCT 4-50

76L298 307 4-60

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ Plotted ____ Date ____ X-Sec. No. ____ Checked ____ Date ____

Book 1798 Pg. 18 | Job No. L442 Division No. V. Notes Red ____ Date ____ Notes Chkd ____ Date ____
Survey of Culvers Ave. Notes 4/12/62
Survey by Long and C. Johnson Date ____
Indexed ____

STATION	B. S.	H. I.	F. S.	ELEV.		
					Elev. 1195.45 USC&GS B.M.	
BMAE.525		1		1195 45	BMAE525 Culvers St. & Tola Ave. N.E. cor. BF. SPH. in N. curb of Culvers St. 7' E. of W. end	
	301	1198.46				
0+00			386	119458	int. of E'ly Tola Ave & Culvers St.	
			752	119094	100' S. on E of Tola Ave.	
			062	119789	100' N. " "	
0+15			410	119436		℄ Cross-gutter
0+30			374	119472		℄
"			465	119381		14' R gutter
"			424	119422		14' R curb
"			347	119499	14' L gutter	
"			302	119544	14' L curb	
T.P.			393	119453	T.P.	
	558	1200 11				
1+00			521	119490		℄
"			621	119391		14' R gutter
"			557	119454		14' R curb
"			500	119511	14' L gutter	
"			438	119573	14' L curb	
1+34			75	11926		81' R - S.W. cor. (Floor not 590 not 100)
"			93	11908		140'± R - back lot.
"			22	11979	60' L	

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. 1462 Division No. V. F. B. 1239 Pg. 17
No. Date Date Survey at
X-Sec. Notes Chkd. Checked Survey by Notes Date
No. Date Date Map No. Indexed C. Johnson

STATION	B. S.	H. I.	F. S.	ELEV.		
		1200 11				
1+81			66	11935		65'R - S.W. cor ho
2+00			475	11953		
"			558	11945		14'R. gutter
"			514	11949		14'R curb
"			456	11955	14'R gutter	
"			393	11961	14'L curb	
T.P		✓	512	11949 ✓	T.P	
	582	1200 81				
2+26			77	11931		65'R - S.W. cor ho
"			102	11906		140'±R - back of walk
2+82.6			560	11952		14'R - W. end S.W.
"			522	11959		14'R - " " curb
2+88			104	11904		140'±R - back of walk
T.P.		✓	496	11963 ✓		
	392	1200 27				
2+86			405	11962	14'L gutter	
"			361	11964	14'L end curb	
"			29	11979	50'L	
2+90.2			506	11952		19.3R - gutter
"			464	11956		19.3R - S. end S.W.

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 1738 Pg. 20
Job No. 1462 Division No. V
Survey of Cos. Tas Ave.
Survey by Langley Notes Langley
Indexed K. C. Johnson Date
Profile Plotted Date No.
Notes Red. Date
Notes Chkd. Date
X-Sec. Checked Date No.

STATION	B. S.	H. I.	F. S.	ELEV.		
		1200 27				
3+12			4 38	1195 89		℄ prod
"			5 31	1194 96		35'S R. edge pvt
"			392	1196 35	14.5'L. edge pvt	
3+34.5			425	1196 02		℄ prod.
3+37			459	1195 68		10.5'R edge pvt
BMAE526			5 10	1195 17	BMAE526 Elev. 1195.174 - F.B. 1568+41 Calvucchas St. (S. side) 237'± E. of Toluca Ave. - B.T. spk. in curb in front of No. 576.	

Notes Ck'd by:	Survey of: Casitas Ave.
Map No.	W.O. 2742 Tape No. Std.
Office Work:	Surveyed by: J.J. Lanigan
Checked:	Noted: J.J.L. Date: 2-8-62
Date:	Indexed: C. Jones

F. B. 738 PG. 21

Notes: Any Additions or Changes of This Sheet must be Made or Checked in Red Ink With date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
of
IMPROVEMENTS
on
MOUNTAIN VIEW RD.
from
CASITAS AVE.
to
LINCOLN AVE.
C.2. 1962.

J. J. Lanigan
C. H. Lewis
H. V. Raphael
A. B. Bartee

7673098 247 10M 1-49

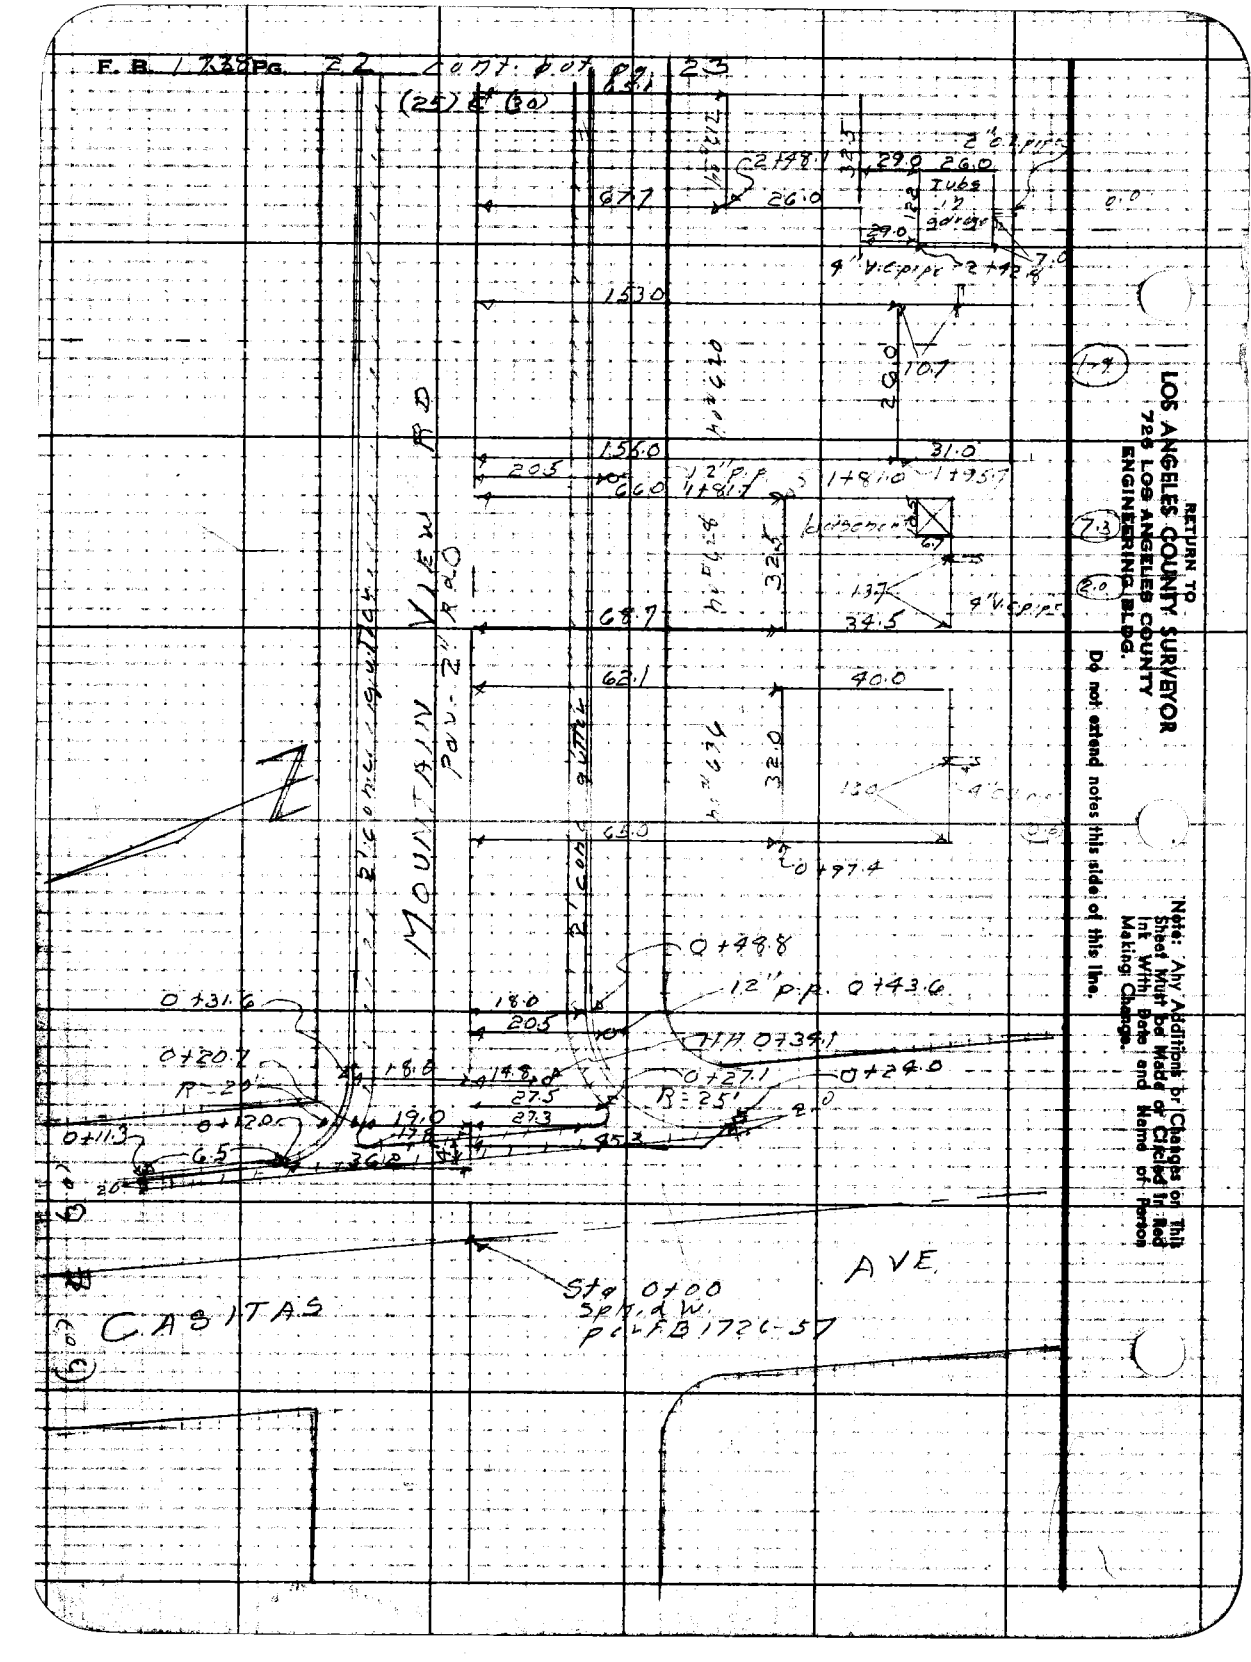
F. B. 1338 Pg. 22
(25) & (30)
MOUNTAIN VIEW AVE
PAV. 21' P.C.C.
CASITAS AVE
Sta 0+00
Spr. d.w.
per F.B. 1721-57
RETURN TO
LOS ANGELES COUNTY SURVEYOR
720 LOS ANGELES COUNTY
ENGINEERING BLDG.
Do not extend notes this side of this line.
Note: Any Additions or Changes to This Sheet Must Be Made or Ciked in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Casitas Ave.
W. O. 7242 Tape No. Std. 'E
Surveyed by J. J. Langan
Notes J.J.L. Date 1-21-52
C. Johnson
Indexed:

F. B. 1738 Pg. 23

Note: Any Additions or Changes of This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

70F3068 247 10M 1-49

125.2 (M)
693
711
671
Cent. Map Pg. 22.
MOUNTAIN VIEW AVE.
12" conc. gutter
Railroad
conc.
665
690
684.2
Cesspool in front.
Basement
29.5
120
240
Elev. 1788.0
Elev. 1785.0
Elev. 1781.0
Elev. 1784.1
Elev. 1783.6
Elev. 1784.0
Elev. 1788.0
121.3
122.7
30.3
9" U.S.P.P.
9" P.P.
37.3
3+51.7
12" P.P. 3+34.6
Unable to locate outlet
Tube in garage not connected
260
185

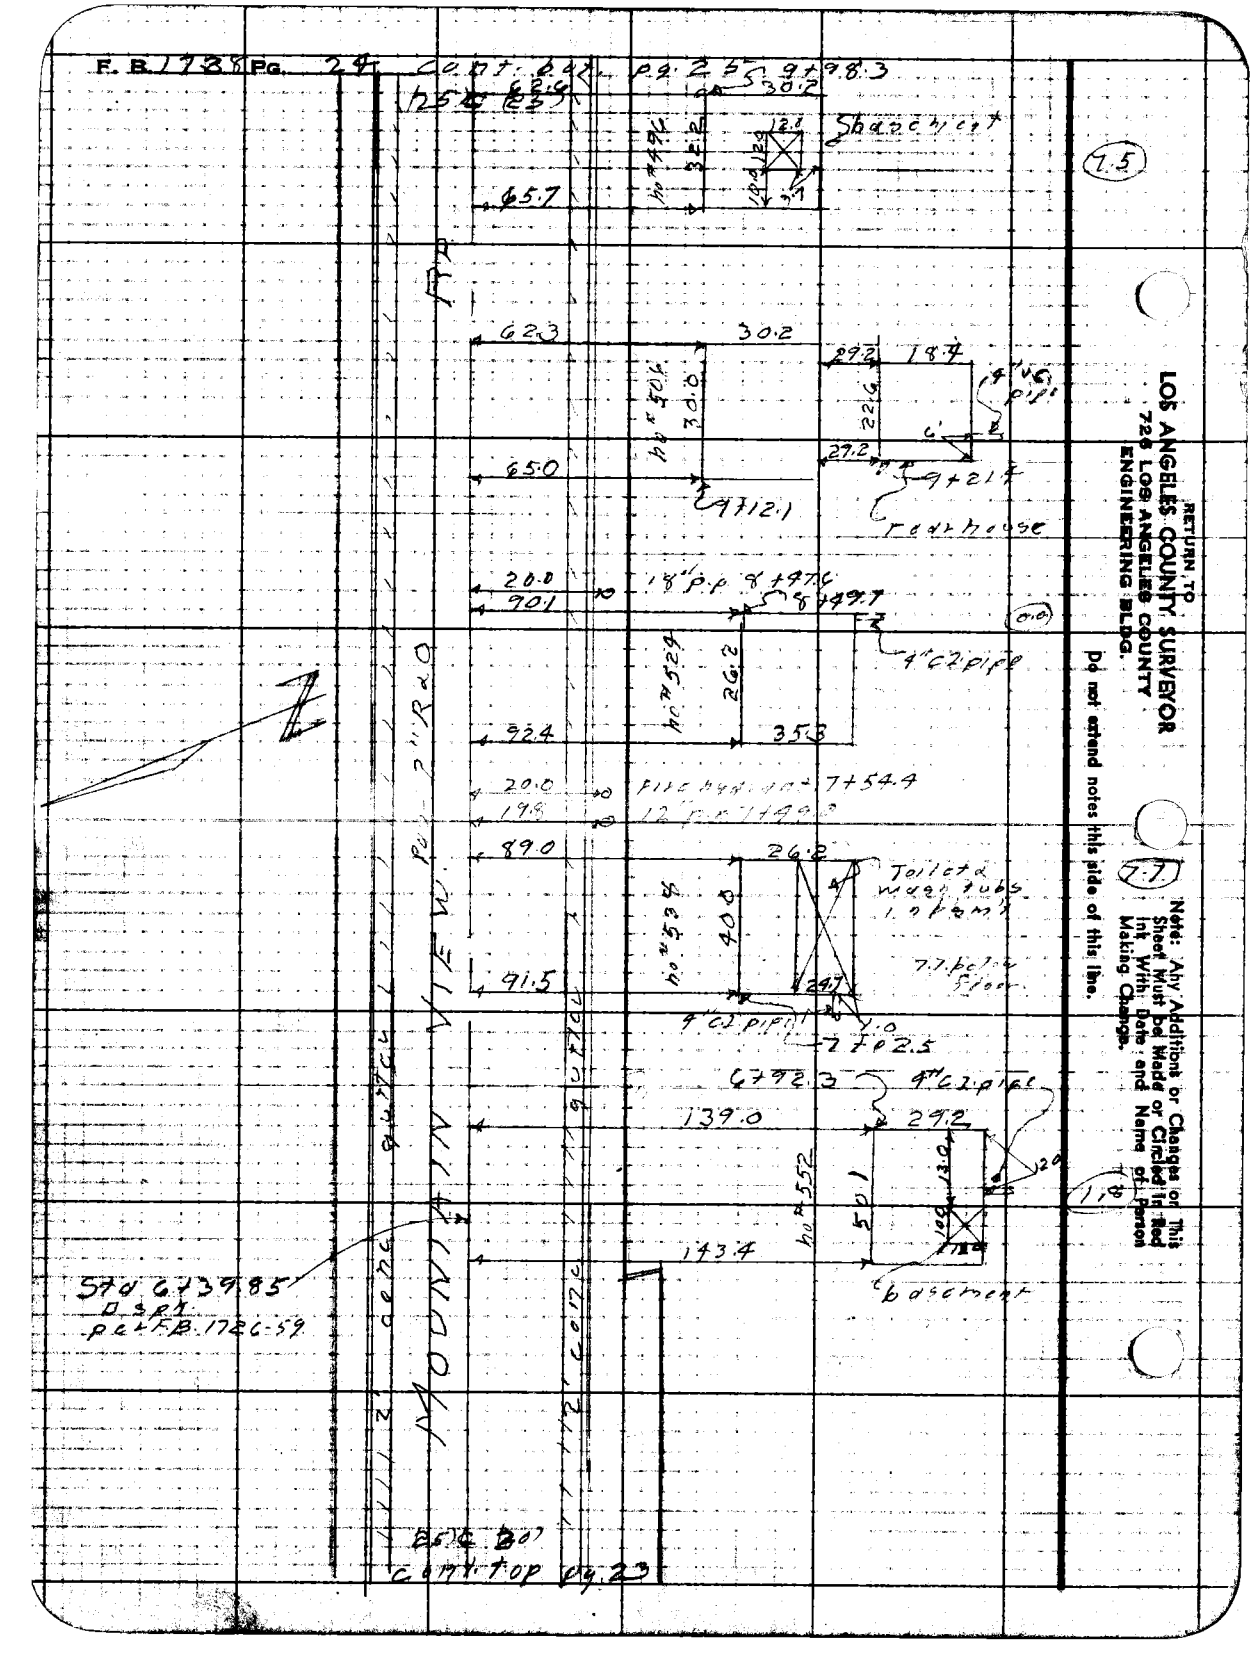

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

F. B. 1738 Pg. 25

Notes Ck'd by:
Map No.
Office Work
Checked
Date

Survey of Castaic Area
W. O. 1962 Tape No. St'd °F
Surveyed by J.C. Lathrop
Notes J.J.C. Date 1-27-52
Indexed

Cont. from Pg 24

12" C.M.P. 12+38.9

59.6

29.6

(1.6)

plan to install plumbing in basement

(6.8)

FD.

57.5

11+91.6

basement

(7.0)

57.9

48 ℄

320 R

90

249

135

(1.3)

75

(2.2)

270

160

9" C.I. Pipe

rear house

26.9

603

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

VIEW

MOUNTAIN

Pav. 2" R&O

9" V.C.P.

9" C.I.P.

10+90.0

399

plumbing in basement

61.6

63.8

19.9

12" A.C.P. 10+53.4

cont. top pg. 24

76F3095 247 2-51

F.B. 1738 Pg. 26

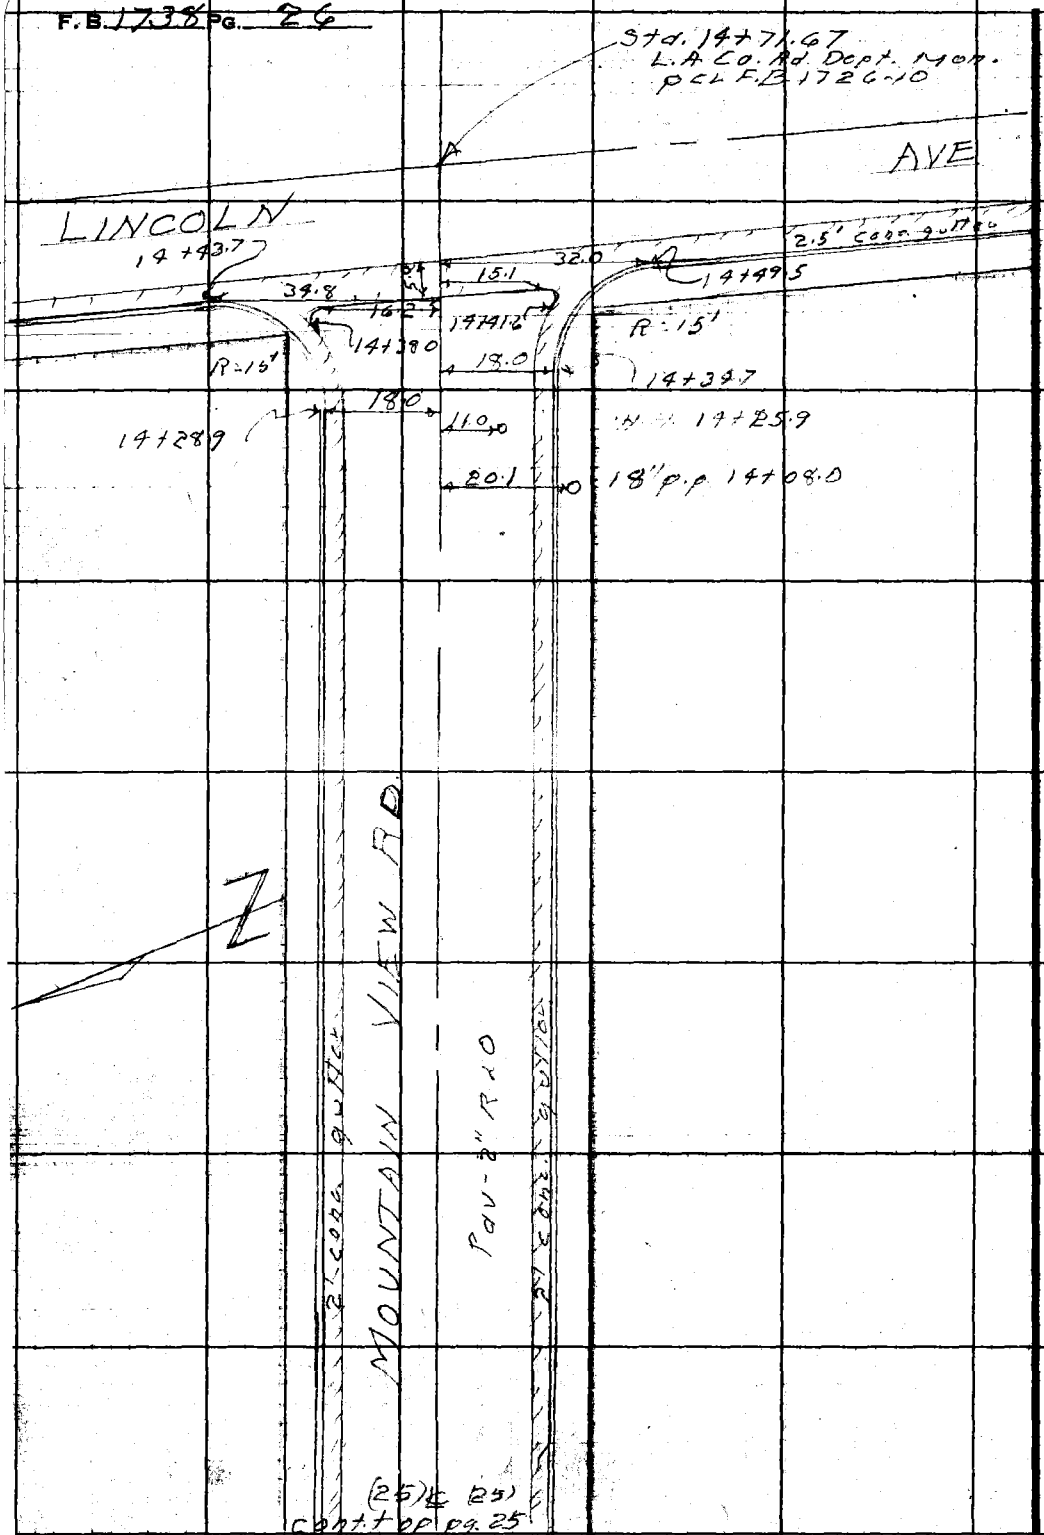

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No. | Notes Red Date | Plotted Date | Job No. 1462 | Division No. | F. B. 1738 | Pg. 77

Notes Ck. Date 2/27/52 | Checked Date | Survey of Casitas Ave | Survey by | Map No. | Traced Date

PROFILE AND

CROSS-SECTIONS

OF

MOUNTAIN VIEW ROAD

FROM

CASITAS AVENUE

TO

LINCOLN AVENUE

C.I. 1462

V.V. Lanigan
C.H. Lewis
H.H. Raphael
H.C. Woodworth

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

764.298 307 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Job No. 1462 Division No. Notes Red Date Plotted Date Profile No.
Survey of Casitas Ave. Date X-Sec. No.
Survey by Lanigan Notes Chkd Checked
Indexed C. Johnson Notes Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	Mountain View Road
BM AE 517	4 58	116340		1158 82	AE 517 El 1158.823 FB 1568 P 149 Mountain View Rd + Casitas Ave. NW cor. @ spk. in curb 5' W of W. end C.R.
0 + 00			596	115744	℄ int. Casitas & Mountain View
			907	115433	100' S'thly on ℄ of Casitas
			130	116210	" N'thly " " " "
			514	115826	gut. N and NE cb Ret
			441	115899	cb " " " " "
			571	115769	gut E " " " "
			505	115835	cb " " " " "
			672	115668	gut " " SE " "
			602	115738	cb " " " " "
			769	115571	gut S " " " "
			710	115630	cb " " " " "
0 + 17			646	115694	cross-gutter ℄
			3 3/4	1160 1/4	NE ppty cor
			6 5/8	1156 9/8	SE " "
1 + 00			561	115779	℄
"			560	115780	18' L gut "
"			494	115846	" " cb

SEL298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Mountain View Road.

STATION	B. S.	H. I.	F. S.	ELEV.		
		116340				
1+00			6.60	115680		18' R g.u.t.
"			5.95	115745		" " c.b.
T.P.			6.51	115689	T.P.	
	6.13	116302				
1+00			10 3/7	115 2 7		170' R ± back lot l. c.
1+13 4/7			8 7/7	1154 3/7		105' R 4" C.I. pipe
1+42 2/7			10 1/7	1152 9/7		104' R 4" V.C. pipe
1+80			11 5/7	1151 2/7		100' R basement flr.
2+00			4.85	115 8.17		℄
"			5.03	1157 99	18' L g.u.t.	
"			4.34	115 8.68	" c.b.	
"			6.02	1157 00		18' R g.u.t.
"			5.36	115 760		" c.b.
T.P.			5.40	115762	T.P.	
	6.21	116383				
2+00			12 7/7	1151 1/7		770 ± R
2+16			12 2/7	1151 6/7		163 7/7 R 4" V.C. pipe
2+49 8/7			9 8/7	1154 0/7		148' R - 2" pipe
3+00			5.64	115 8.19		℄
"			5.68	115815	18' L gutter	

Profile Notes Red_____ Plotted_____ Job No. 1116 Division No. F.B. 1738 PG 27
No._____ Date_____ Date_____ Survey of Easterly Annex
No._____ Date_____ Checked_____ Date_____ Map No._____ Index Date_____

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

8 4

Do not extend notes this side of this line.

F. B. 1932 Pg. 30 | Job No. 462 Division No. | Profile
Survey by Costilla & Avt. | Plotted | Notes Red | No.
Survey by Lonigan | Date | Date | No.
Indexed C. Tolmasoff | Notes Kewis | Notes Chkd. | X-Sec.
Date | Date | Checked
Date | Date

STATION	B. S.	H. I.	F. S.	ELEV.	Mountain View Road
		1163 83			
3+00			5 00	1157 83	18'L cb.
"			6 68	1157 15	18'R gutter
"			6 06	1157 77	" cb.
"			10 1	1155 7	148'R garage floor
"			12 1	1151 7	225'±R
T. P.		1	6 23	1157 60	T. P.
	5 58	1163 18			
3+51 7			5 1	1158 1	Floor elev. Ho. #596 69'R
"			8 3	1154 9	ground at S.W. cor. 107'R
4+00			4 79	1158 39	℄
"			4 85	1158 33	18'L gutter
"			4 18	1159 00	" cb
"			5 87	1157 31	18'R gut.
"			5 19	1157 99	" cb
T. P.		1	5 26	1157 92	T. P.
	5 38	1163 30			
4+00			11 2	1151 6	225'± R
4+05 4			12 0	1151 3	On 4" V.C. pipe 122'R
5+00			4 34	1158 96	℄
"			4 46	1158 84	18'L gutter

Form 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red_____ Plotted_____ Job No. 1446 Division No._____ F.B. 1738 Pg. 31
No._____ Date_____ Date_____ Survey of Mountain View Road
Notes Chkd_____ Checked_____
No._____ Date_____ Date_____ Map No._____ Ind. Rod C. Jones

STATION	B. S.	H. I.	F. S.	ELEV.	Mountain View Road
		1163.30			
5+00			3 80	115 9 50	18'L cb
"			5 45	115 7 85	18'R gutter
"			4 77	115 8 53	" cb
T. P.			4 74	115 8 56	T. P.
	7 32	1165 88			
6+00			5 93	115 9 95	℄
"			5 86	1160 02	18'L gut.
"			5 22	1160 66	" cb.
"			6 82	1159 06	18' R gut.
"			6 16	1159 72	" cb.
"			12 3	1153 6	Ho #556 100' R basement ±
"			11 9	1154 0	" 225'R ±
6+75			14 5	1151 4	Ho #552 170'R basement ±
6+80			11 8	1154 1	" 171'R 4" C.I. pipe
7+00			4 54	1161 34	℄
"			4 53	1161 35	18'L gut
"			3 91	1161 97	" cb
"			5 50	1160 38	18'R gut
"			4 88	1161 00	" cb
"			11 5	1154 4	275'R ±

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 1938 Pg. 32 | Job No. 1462 Division No. | Profile
Survey of Easterly Ave.
Survey by Los Angeles Aerial Surveys
Indexed | Plotted | Notes Red | No. | Date | Checked | Notes Chkd | X-Sec. | No. | Date | Date

STATION	B. S.	H. I.	F. S.	ELEV.	Mountain View Road
		1165 88			
7+04±			12 1	1153 8	HO # 5-38 — 100' R - basement floor
"			11 1	1154 8	" — 116' R 4" C.I. pipe
8+00			333	1162 55	℄
"			338	1162 50	18' L gut.
"			268	1163 20	" cb
"			437	1161 51	18' R gut
"			367	1162 21	" cb
"			11 6	1154 3	275'± R.
8+50			6 2	1159 2	HO # 524 — 126' R 4" C.I. Pipe
9+00			248	1163 40	℄
"			247	1163 41	18' L gut.
"			179	1164 09	" cb.
"			348	1162 40	18' R gut.
"			284	1163 04	" cb.
T.P.			356	1162 32	T.P.
	533	1167 65			
9+00			13 0	1154 7	
9+27½			8 9	1158 8	HO # 506 (real) — 275'± R
9+80			12 5	1155 2	" 496 — 144' R 4" V.C. pipe
					80' R basement

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 1746 Division No. ____
No. ____ Date ____ Date ____ Survey of Castaic Area
Notes Chkd. ____ Checked ____ Survey by Lowery
No. ____ Date ____ Map No. ____ Index C. Jahnke

F. B. 17538 P. 3

Mountain View Road

STATION	B. S.	H. I.	F. S.	ELEV.		
		1167 05				
10+00			3 73	116392		℄
"			3 72	116393	18'L gut.	
"			3 11	116454	" cb	
"			4 75	116290		18'R gut.
"			4 12	116353		" cb
T. P.			0 13	116752	T. P.	
	1 52	1169 04				
10+00			12 3/7	1156 7/		R back [illegible]
10+75			12 0/11	1157 0/	140' 482	70'R basement [illegible]
11+00			5 09	1163 95		℄
"			5 09	1163 95	18'L gut.	
"			4 45	116459	" cb.	
"			6 10	116294		18'R gut.
"			5 53	116357		" cb
"			12 4/	1156 6/		±25±' R back [illegible]
T. P.			5 47	116357	T. P.	
	5 14	1168 71				
11+78			10 9/	1157 8/	140' 466 (front house)	109'R 4" [illegible]
11+84			12 3/	1156 4/	" (rear)	137'R " "
11+85			12 3/	1156 4/	" (front)	86'R basement [illegible]

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

5 5

Do not extend notes this side of this line.

T.B. 1738 Pg. 54 | Job No. 1962 Division No. | Notes Red. | Plotted | Profile
Survey of Castles Add. | Date | No.
Survey by Lanigan Notes Lewis | Notes Chkd. | Checked | X-Sec.
Indexed C. Jamison Date | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	Mountain View Road	
		1168 71				
12+00			5 10	1163 61		℄
"			5 04	1163 67	18'L gut.	
"			4 40	1164 31	" cb	
"			6 06	1162 65		18'R gut
"			5 41	1163 30		" cb
"			13 0	1155 7		225 R. back lot line
12+30			12 3	1155 4	HO # 456	83'R basement
12+53			9 0	1155 7	" "	85'R 4" C.I. Pipe
13+00			5 45	1163 26		℄
"			5 39	1163 32	18'L gut	
"			4 72	1163 19	" cb	
"			6 40	1163 31		18'R gut
"			5 78	1162 93		" cb
14+00			5 54	1163 17		℄
"			5 53	1163 18	18'L gut	
"			4 91	1163 80	" cb	
"			6 53	1162 18		18'R gut
"			5 92	1163 79		" cb
T. P.			5 75	1162 96	T. P.	
	5 58	1168 54				

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. 1462 Division No.
No. Date Date Survey of Cowles Ave
No. Date Date Survey by C. Johnson
No. Date Map No. Index No. Date

F. B. 1738 PG. 25

STATION	B. S.	H. I.	F. S.	ELEV.	Mountain View Road
		1168 54			
14+45			6 15	1162 39	Cross gutter &
			5 67	1162 87	& int Lincoln & Mountain View
			6 53	1162 01	gutter W end SW cb rt
			5 90	1162 64	cb " " " " "
			7 28	1161 26	gutter S " " " "
			6 60	1161 94	cb " " " " "
			5 48	1163 06	gut. W " NW " "
			4 84	1163 70	cb " " " " "
			5 06	1163 48	gut N " " " "
			4 41	1164 13	cb " " " " "
			2 17	1166 37	100' N'ly on ℄ of Lincoln
			2 95	1165 59	" " W gutter "
			2 30	1166 24	" " " cb "
			9 20	1159 34	" 5'N'ly on ℄ "
			9 78	1158 76	" " W gutter
			9 11	1159 43	" " " cb
BM AE 240					AE 240 El. 1161.02 CFB 1447 A 217
			7 55	1160 99	Lincoln Ave & Mountain View Rd. S.E. cor.
					BT. spk in curb 15'S of S. end CR

F. B. 1738 Pg. 36 Job No 1462 Division No. Notes Red. Plotted Profile

Survey of Castas Ave Date Date No.

Survey by Lanigan Notes Lewis Notes Chkd. Checked X-Sec.

Indexed Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	

Do not extend notes this side of this line.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR

726 LOS ANGELES COUNTY ENGINEERING BLDG.

76L298 307 4-56

Maps Ch'd by
Map No.
Office Work
Checked
Date

Survey of Casitas Ave.
W. O. 1462 Tape No. St'd °F
Surveyed by J.J. Lanigan
Notes J.J.L. C. J. Lewis Date 1-27-52
Indexed

F. B. 1738 Pg. 37

Note: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION of IMPROVEMENTS on MOUNTAIN VIEW RD. from CASITAS AVE. to WINDSOR AVE.

C.I. 1462.

J.J. Lanigan
C.H. Lewis
H.N. Raphael
A.B. Barbee

76F3095 247 2-51

F.B. 1738 PG. 38

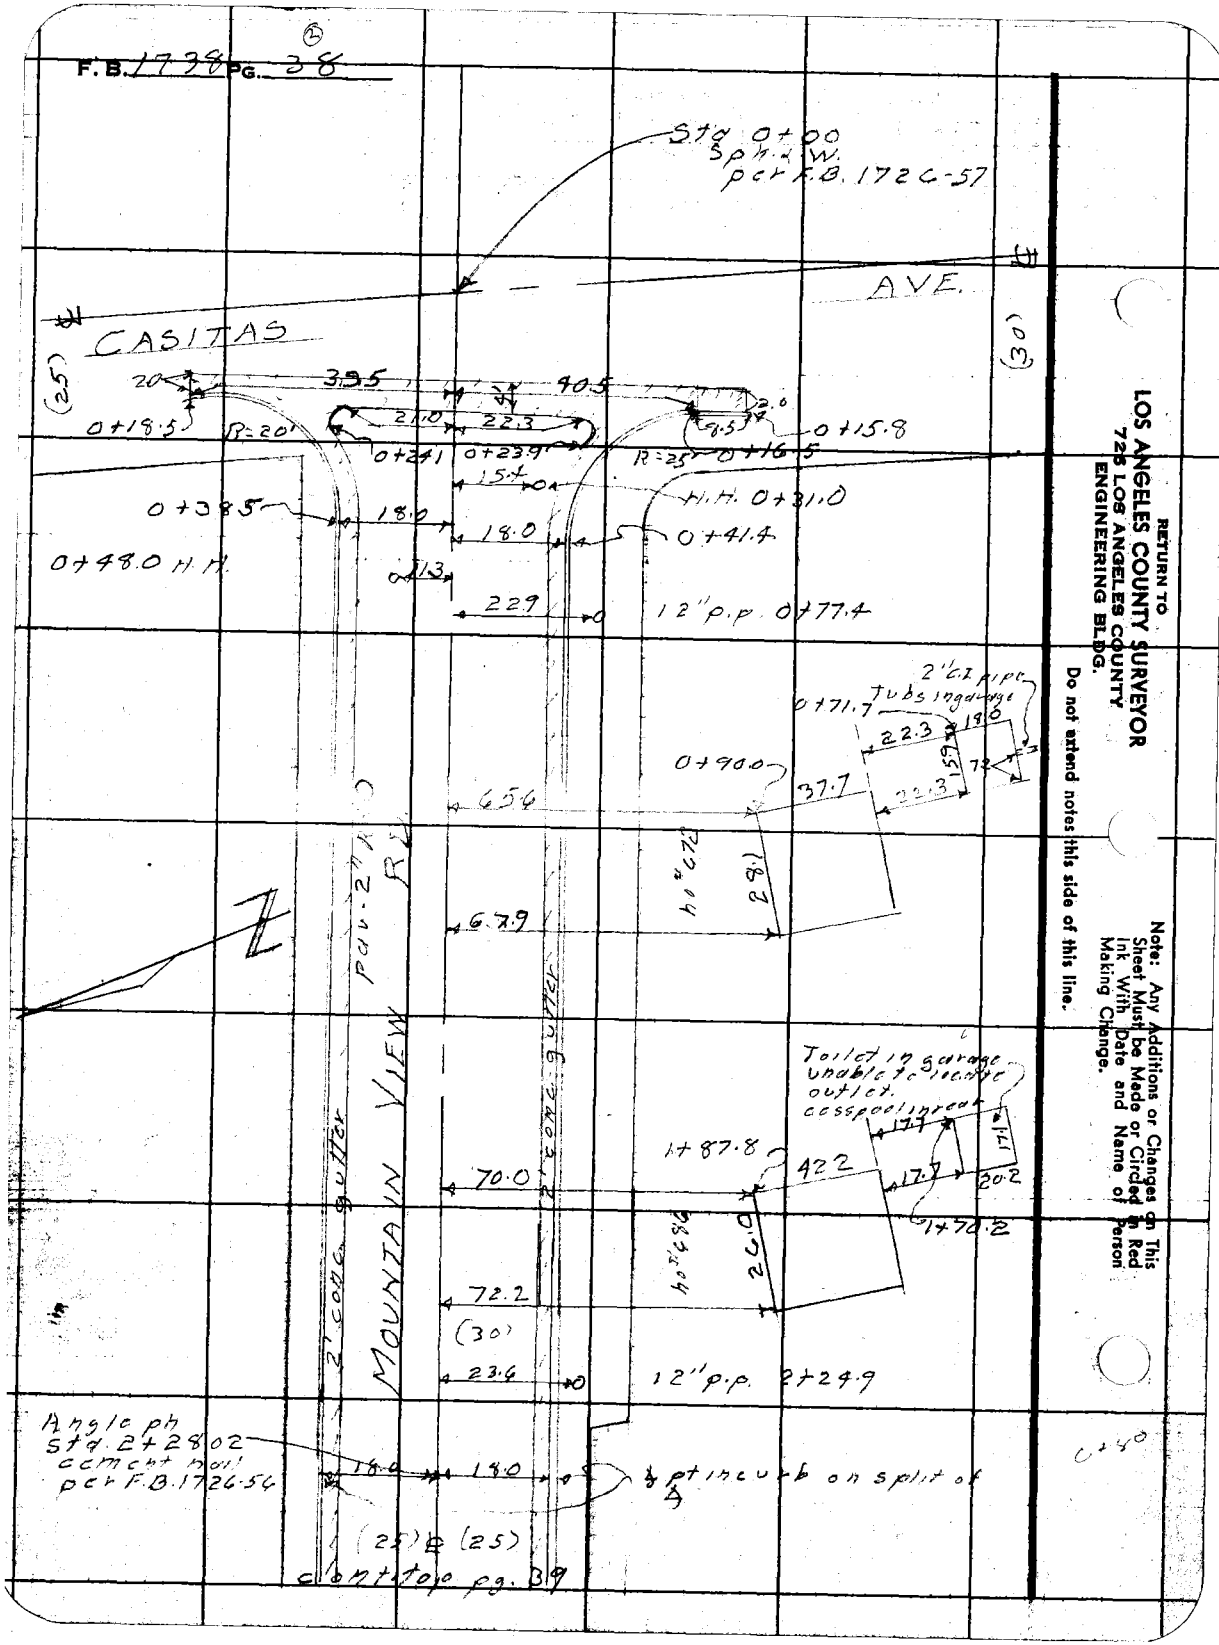

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Casitas Ave.
W. O. 462 Tape No. St'd. °F
Surveyed by Val Lanigan
Notes Date 1-29-52
Indexed E. O. Jenson

F. B. 1738 Pg. 39

Cont. for pg. 38

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76F3095 247 2-51

Rd.

753
763
549
19.6
54.9
60.7
40.7

2+98.7 basement
35.6
38.1
40°27'24"
3+28.6
Wash Room
26.0
26.5
15.7
2" C.I. pipe
18" P.P. 3+78.7
32.2
40°27'12"
25.4
3+92.1
52.3
3+85.2
4" C.I. pipe
Retaining wall
12.4
3+85.7
Identical wall
20.5
27.2
Swimming Pool
40°27'16"
20.3
314
3+80.8
3+92.7
4+55.5
27.6
40°17'34"
340
4+74.98
4" C.I. pipe
40.7
32.1
4+50.0
40°17'29"
10.3
4+46.3
4+59.7
Identical wall
4+40.5
4+40.6
39.9
32.0
17.4
31.9
25.7
10.3
22.0
25.6
40°17'28"
4" C.I. pipe
4" C.I. pipe
MOUNTAIN VIEW
12" Cond. gutter
24" Cond. gutter
(25) & (25)
Cont. top pg. 40

F. B. 1738 PG. 40

cont bot. pg 39

(25) ℄ (25)

17.8 → 5+14.2 - 12" p.p.

200 → 903. H.H. 5+70.1

19.8 → 14" p.p 5+99.2

MOUNTAIN VIEW RD

Poly - 2" 18 x 0.

2" Conc. gutter

2' Conc. gutter

17.9 → 7+01.8 12" p.p

Boys AID BUILDINGS

Sch

pg 140

For Girls

℄ pt. sta 8+43.52
314.1 L.P.
per FB. 1726-55.

21.1
15.6
20.4
10.2
19.6

Fire hy drant 8+42.9

h.h 8+43.7

14" p.p. 8+46.8

(30) ℄ (30)

cont top pg 41

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Maps Ck'd by
Map No.
Office Work
Checked
Date

Survey of Casitas Ave.
W. O. 1942 Tape No. St'd. °F
Surveyed by J. J. Lanigan
Notes Lanigan Date 2-5-52
Indexed C. O. Johnson

F. B. 1796 Pg. 41

Note: Any Additions or Changes on This Sheet Must Be Made or Checked in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76F3095 247 2-51

(5)

cont bot pg 40

9+29.7 12 e.p.

MOUNTAIN VIEW RD.

12" conc gutter

727

750

192

1826

1894

1817

6.3.7

66.1

66.1

690

18.8

1367

(30) & (30)

1385

cont top pg 42

40 x 820 26.5 28.4

basement

(7.5)

(1.1)

1.0+95.3

gutter upstr.

10+71.9 12" p.p.

48.0 14.2 39 20.0 48.0

10+57.0

32.8

40 x 832 24.8

cesspool in front unable to locate outlet

10+94.9 11+18.8 11+20.0

(1.9)

20.0 2' 4"C.I. pipe 36.1

40 x 848

11+75.7 26.3

11+86.4

40 x 820 30.0

36.4 42.3 24.8 11.6 4"C.I. pipe

(8.0)

426

basement with plumbing

19.0 7.0 7.0 31.5

(7.7)

basement

46.7

10+95.5

12+65.6 12+91.4

12" 12 p.p. 81.0

unable to locate outlet

40 x 814

20.1 38.0

F. B. 1136 PG. 42

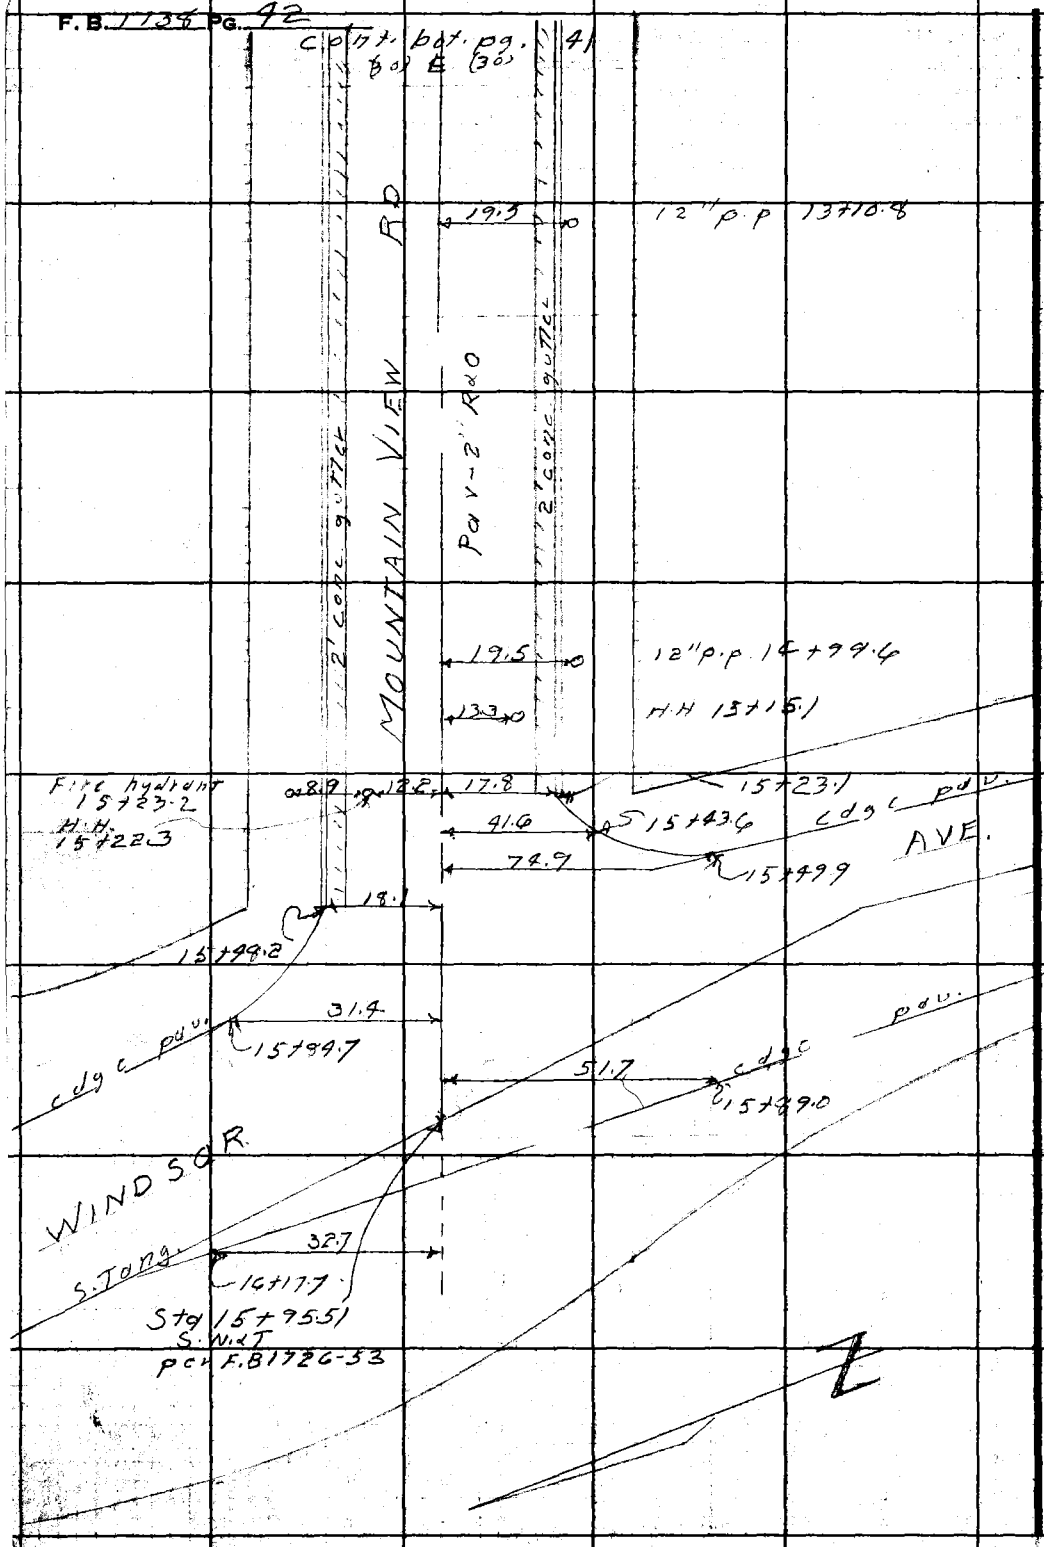

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No. ____ Notes Red. ____ Date ____ Plotted ____ Date ____ Job No. 1462 Division No. ____ Survey of Casitas Avenue

P. B. 1738 Pg. 43

No. ____ Date 2/27/52 Date ____ Map No. ____ Indexed C. Johnson Date ____

PROFILE AND CROSS SECTIONS OF

MOUNTAIN VIEW ROAD

FROM

CASITAS AVENUE

TO

WINDSOR AVENUE

C.I. 1462

V. V. Lanigan
C. H. Lewis
H. H. Raphael
H. C. Woodworth

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

761.298 307 4-50

76L298 307 4-50

0+17.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Plotted Date Notes Red Date
No. X-Sec. Checked Date Notes Chkd Date
No. Job No. 1962 Division No. Notes Lewis Date
Survey of Casitas Ave. Survey by Lanigan & O. Johnson Indexed
F.B. 1738 Pg. 44

STATION	B. S.	H. I.	F. S.	ELEV.	Mountain View Road	
BM AE 517	4 8 2	1163 64		1158 82	AE 517 El 1158.823	FB 1568 P. 149
					Mountain View Rd. + Casitas Ave. N.W. cor.	
					Bt. spk. in curb, 5' W of W. end C.R.	
0+00			6 20	1157 44	℄ int. Casitas & Mountain View	
			1 96	1161 68	100' Nly on ℄ of Casitas Ave	
			9 00	1154 64	" Sly " " "	" "
			7 70	1155 94	gutter S end SW	cb. ret.
			6 90	1156 74	cb " " "	" "
			6 52	1157 12	gutter W " "	" "
			5 64	1158 00	cb " " "	" "
			5 06	1158 58	gutter N " NW	" "
			4 46	1159 18	cb " " "	" "
			5 50	1158 14	gutter W " "	" "
			4 84	1158 80	cb " " "	" "
0+17±			6 28	1157 36	cross-gutter	℄
1+00			5 35	1158 29		℄
"			5 38	1158 26		18' R gutter
"			4 73	1158 91		" R cb
"			6 42	1157 22	17± L gutter	
"			5 72	1157 92	" cb	

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted. Job No. 1743 Division No.
No. Date Date Date Survey of Cascade Terrace
No. Notes Chkd. Checked Survey by C. Tanner
No. Date Date Map No. Index

P.B. 177 Pg. 45

STATION	B. S.	H. I.	F. S.	ELEV.	Mountain View Road
		1163 64			
1+00			10 5	1153 1	175'± L back lot line
0+75±			10 3	1153 4	144'± L 2" C.I. pipe at garage Ho 11 6
T.P.		1	577	1157.87	T.P.
	581	1163 68			
1+87			10 3	1153 4	160'± L ground at rear of garage Ho 11 6
2+00			550	1158 18	℄
"			561	1158 07	18' R gutter
"			492	1158 76	" cb.
"			658	1157 10	17 2 L gutter
"			594	1157 74	" cb.
"			11 4	1152 3	235'± L back lot line
3+00			583	1157 85	℄
"			584	1157 84	18 3 R gutter
"			515	1158 53	" cb.
"			683	1156 85	17 2 L gutter
"			610	1157 58	" cb.
T.P.		1	610	1157 58	T.P.
	580	1163 38			
3+00			12 1	1151 3	100' L basement floor - Ho 11 7
3+42			9 3	1154 1	138' L 2" C.I. pipe at washhouse

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile — Plotted — Date — No. — Notes Red — Date — X-Sec. — Notes Chkd — Checked — No. — Date

Job No. 1962 Division No. — Date — Survey of Cassitas Ave.

Survey by Flanagan Notes Lewis

Indexed C. Johnson Date

STATION	B. S.	H. I.	F. S.	ELEV.	Mountain View Road
		1163 38			
T. P.		1	602	1157 36	
	463	1161 99			
3+86			8 5	1153 5	152'± L 4" C.I. pipe to HO # 714
3+81			10 8	1151 2	203'± L " " " " " " 716
3+80			21 4	1140 6	272'± L drain at bottom of swimming pool
4+00			4 28	1157 71	℄
"			4 32	1157 67	18 6 R gutter
"			3 65	1158 34	" cb
"			5 37	1156 62	17 3 L gutter
"			4 69	1157 30	" cb.
"			12 7	1149 3	293'± L back lot line
T. P.		1	3 67	1158 32	T. P.
	436	1162 68			
4+66			11 3	1151 4	260'± L 4" C.I Pipe to HO # 726
4+71			9 5	1153 2	200'± " " " " " " 728
4+76			13 1	1149 6	139'± L " " " " " " 724
5+00			5 17	1157 51	℄
"			5 26	1157 42	19 1 R gutter
"			4 60	1158 08	" cb
			6 25	1156 43	162 L gutter

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. Notes Red. Plotted. Job No. 1462 Division No.
No. Date Date Date Survey of
No. Date Date Map No. Ind. Co. Jobbers

F.B. 1738 Pg. 47

STATION	B. S.	H. I.	F. S.	ELEV.	Mountain View Road
		1162.68			
5+00			5.56	1157.12	16 L. cb
6+00			5.39	1157.29	℄
"			5.45	1157.23	19 R gutter
"			4.77	1157.91	" cb
"			6.45	1156.23	16 L gutter
"			5.75	1156.93	" cb.
7+00			5.55	1157.13	℄
"			5.61	1157.07	19 R. gutter
"			4.98	1157.70	" cb
"			6.68	1156.00	16 L gutter
"			5.97	1156.71	" cb
T.P.			5.90	1156.78	T.P. BM AE 516 El. 1156.784
	5.30	1162.08			
8+00			5.39	1156.69	℄
"			5.20	1156.88	20 R gutter
"			4.56	1157.52	" cb.
"			6.26	1155.82	15 L gutter
"			5.55	1156.53	" cb.
9+00			5.57	1156.51	℄
"			5.43	1156.65	20 R

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

110

12½

Do not extend notes this side of this line.

Profile No. X-Sec. No.
Plotted Date
Notes Red Date
Notes Chkd Date
Checked Date

Job No. 1962 Division No.
Survey of Cresita Acres
Survey by
Notes
Indexed Date

STATION	B. S.	H. I.	F. S.	ELEV.	Mountain View Road	
		1162.08				
9+00			4.75	1157.33		20½ R cb.
"			6.41	1155.67	15⅝ L. gutter	
"			5.73	1156.35	" cb.	
"			12.4	1149.7	295'± L back lot line	
10+00			5.70	1156.38		℄
"			5.59	1156.49		19½ R gutter
"			4.96	1157.12		" cb
"			6.63	1155.45	16± L gutter	
"			5.93	1156.15	" cb	
T. P.		1	4.90	1157.18	T. P.	
	4.92	1162.10				
10+00			11.7	1150.4	295'± L back lot line.	
10+30			10.6	1151.5	90' L basement floor - Ho # 820	
10+49			10.5	1151.6	172' L plbg outlet to garage "	
10+70			9.6	1152.5	216 L ground at SW cor Ho # 832	
11+00			5.95	1156.15		℄
"			5.82	1156.28		19½ R gutter
"			5.18	1156.92		cb.
"			6.85	1155.25	16½ L gutter	
"			6.18	1155.92	" cb.	

74L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED IN ITH, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red Plotted Job No. 1436 & Division No.
No. Date Date Date Survey of
No. Date Map No. Indexed

STATION	B. S.	H. I.	F. S.	ELEV.	Mountain View Road
		1162 10			
11+19			10 8	1151 3	203'L 2" C.I. pipe to HO* 840
T.P.		1	6.29	1155.81	T.P.
	5.18	1160.99			
11+89			7 7	1153 3	170'L 4" C.I. pipe to HO* 844
12+00			5.01	1155.98	℄
"			4.92	1156.07	19 3 R gutter
"			4.26	1156.73	cb
"			5.94	1155.05	16 7 L gutter
"			5.27	1155.72	" cb
"			10 3	1150 7	80'± L basement floor to HO* 848
"			9 5	1151 5	220'± L back lot line
12+40			11 0	1150 0	95'L basement floor to HO* 836
13+00			5.25	1155.74	℄
"			5.16	1155.83	18 9 R gutter
"			4.51	1156.48	" cb
"			6.15	1154.84	17 0 L gutter
"			5.48	1155.51	" cb
"			7 5	1153 5	140'L Floor elev. HO* 864
"			9 2	1151 8	219'±L back lot line
13+12			8 3	1152 7	177'L ground at S.W. cor HO

F.B. 1738 Pg. 48

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

60

Do not extend notes this side of this line.

Profile No. ____ Plotted ____ Date ____ Notes Red ____ Date ____
X-Sec. No. ____ Checked ____ Date ____ Notes Chkd ____ Date ____
Job No. 1962 Division No. ____ Notes Key 15 ____ Date ____

STATION	B. S.	H. I.	F. S.	ELEV.	Mountain View Road
		1160 99			
14+00			5 39	1155 60	℄
"			5 37	1155 62	18± R gutter
"			4 67	1156 32	" cb
"			6 37	1154 62	17± L gutter
"			5 67	1155 32	" cb
"			7 ±	1153 8	100'± back lot line
T. P			5 65	1155 34	T. P.
	5 72	1161 06			
15+23			5 97	1155 09	℄
"			8 79	1152 27	18' L gutter at end
"			6 04	1155 02	cb " "
15+48			5 73	1155 33	18' R gutter at end
			5 06	1156 00	" cb " "
15+68			6 13	1154 93	℄ brk
15+95.51			5 52	1155 54	℄ int of Windsor Ave. & Mountain View
			3 31	1157 75	100' N'ly on ctr of pvmt on Windsor
			7.61	1152 45	" S'ly " " " " " "
BM AE 496			5 01	1156 05	AE 496 El 1156.048 FB 1568 P133 Windsor Ave & Mountain View Rd NE cor BT spk in cb 5' E of W end.

Plotted, Ck'd by
Map No.
Office Work
Checked
Date

Survey of Castle Ave.
W. O. 1422 Tape No. St'd. °F
Surveyed by J. J. Lanigan
Notes J. J. L. C. Jones Date 2-1-52
Indexed

F. B. 1738 Pg. 31

Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION of IMPROVEMENTS on ROYCE ST. from LINCOLN AVE to THE EASTERLY LINE OF TR # 4702. C.I. 1962.

J. J. Lanigan
C. N. Lewis
H. H. Raphael
H. C. Woodworth

76FBOBS 2-67 2-51.

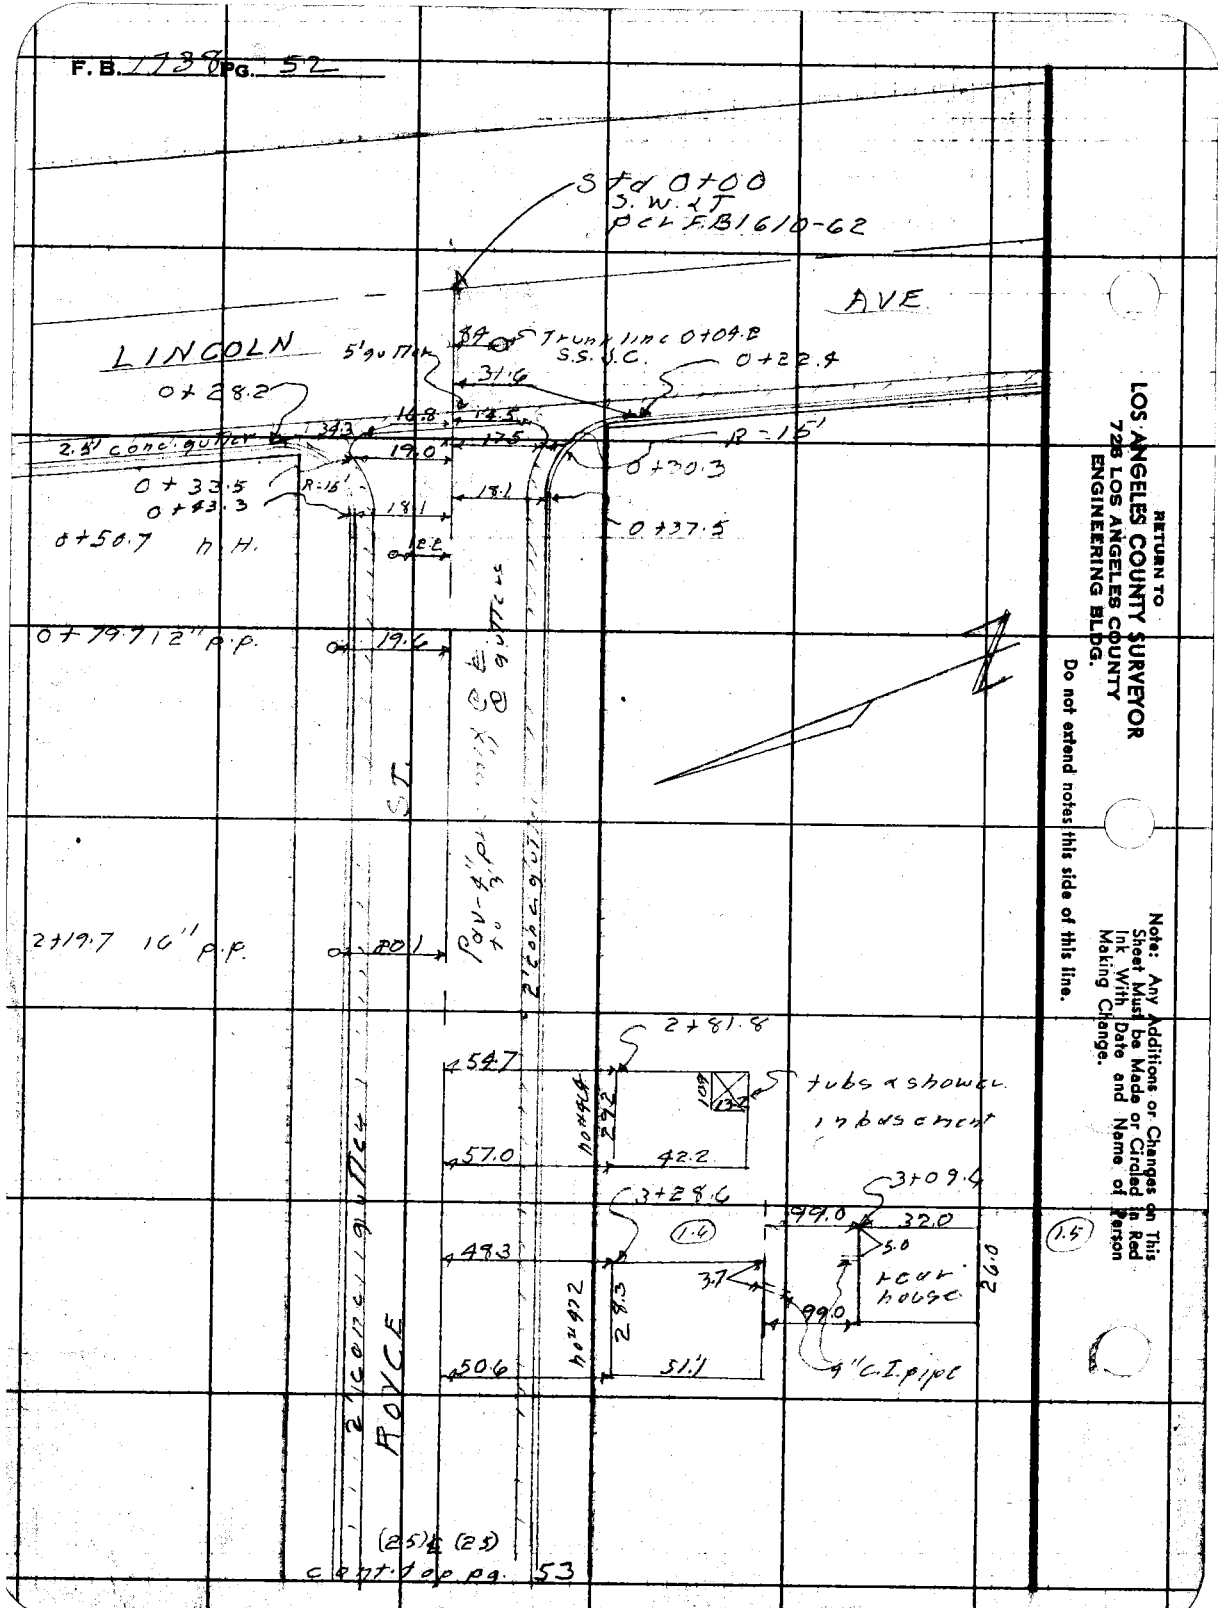
F. B. 1198 Pg. 52
Std 0+00
S. W. I. T.
pc L F.B 1610-62
AVE
LINCOLN
5'sw 17th
Trunk line 0+09.8
S.S.S.C.
0+22.4
0+28.2
31.6
10.8
12.5
2.5' conc. gutter
33.3
19.0
17.5
R=15'
0+30.3
0+33.5
0+43.3
18.1
18.1
0+37.5
0+50.7 h.H.
1.2.2
0+79.7 12" R.P.
19.6
ST.
POV-4" P.C. to 9.0 ft.
2+19.7 10" P.P.
20.1
2+81.8
54.7
tubs & shower in basement
57.0
42.2
3+09.4
3+28.6
(1.4)
99.0
32.0
5.0
49.3
3.7
rear house
99.0
26.0
28.3
50.6
51.1
9" C.I. pipe
ROYCE
(25½) (25)
cont. to pg. 53
(1.5)
RETURN TO
LOS ANGELES COUNTY SURVEYOR
7226 LOS ANGELES COUNTY
ENGINEERING BLDG.
Do not extend notes this side of this line.
Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Casitas Ave.
W. O. 762 Tape No. St'd °F
Surveyed by J. J. Lanigan
Notes J. J. L. Date 2-7-52
Indexed

F. B. 778 Pg. 53

Note: Any Additions or Changes to This Sheet Must be Made in Ink and Circled in Red With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

12" P.P.
3+69.5

20.1

107.8

71.0

2.16

4+22.2

37.6

50.8

53.9

ST.

19.6

12" P.P.
4+74.9

4" C.I. pipe

basement

51.0

5+01.5

5+06.1

5+11.2

4" C.I. pipe

5+23.9

47.9

16.0

basement

4" C.I. pipe

56.1

59.6

PAV. 4" P.C. to 3" P.C. & C. & G.

Fire hydrant
5+71.4

20.0

5+84.2

118.3

62.2

120.0

2" CONC.

12" C.I. P.P.
3+74.8

19.9

ROYCE

2" C.I. Pipe above ground not connected.

4" C.I. pipe

25 & (25)
Cont. for Pg. 54

78F3098 247 2-51

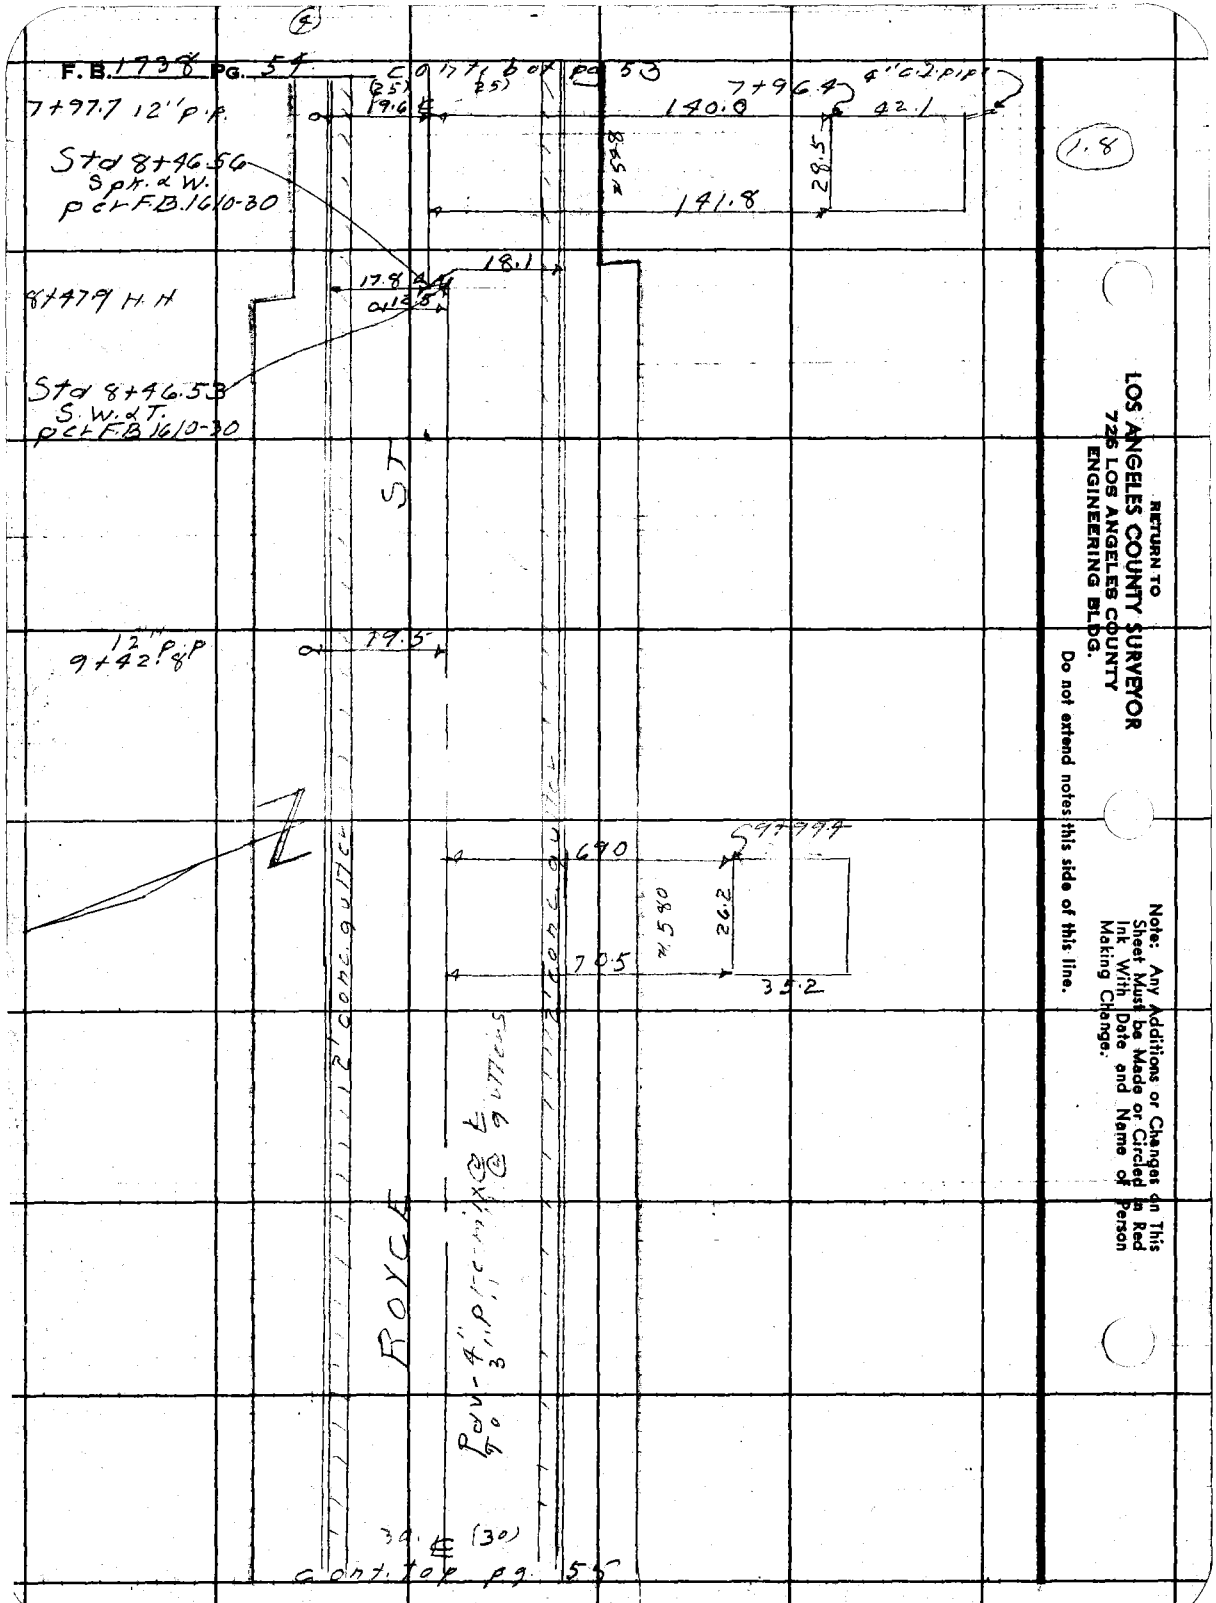

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

1.8

Notes Ck'd by:
Map No.
Office Work
Checked
Date

Survey of: 60th St & 94th Ave
W. O. 1962 Tape No. St'd. °F
Surveyed by: J. J. Lonigan
Notes: J. J. L. Date: 2-7-52
Indexed: C. Johnson

F. B. 1738 Pg. 55

cont. bot. pg 57

11+73.3 P.C.

69.8

St.

69.5

26.2

basement

11+39.3

61.0

31.5

11+62.9

2" C.I. pipe

37.8

64.0

30.9

19.1

30.9

20.0

Tubs in garage

Gutter

Gutter

Gutter

12" R.C.P.

20.3

Pav-To Cobblestone Ave - 5" pipe-mix @ 10 3.11

Edge

ROYCE

12+42.4 P.I.

20.3

13+82.1 P.I.

(30) & (30)

cont top pg 56

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76F3095 247 2-51

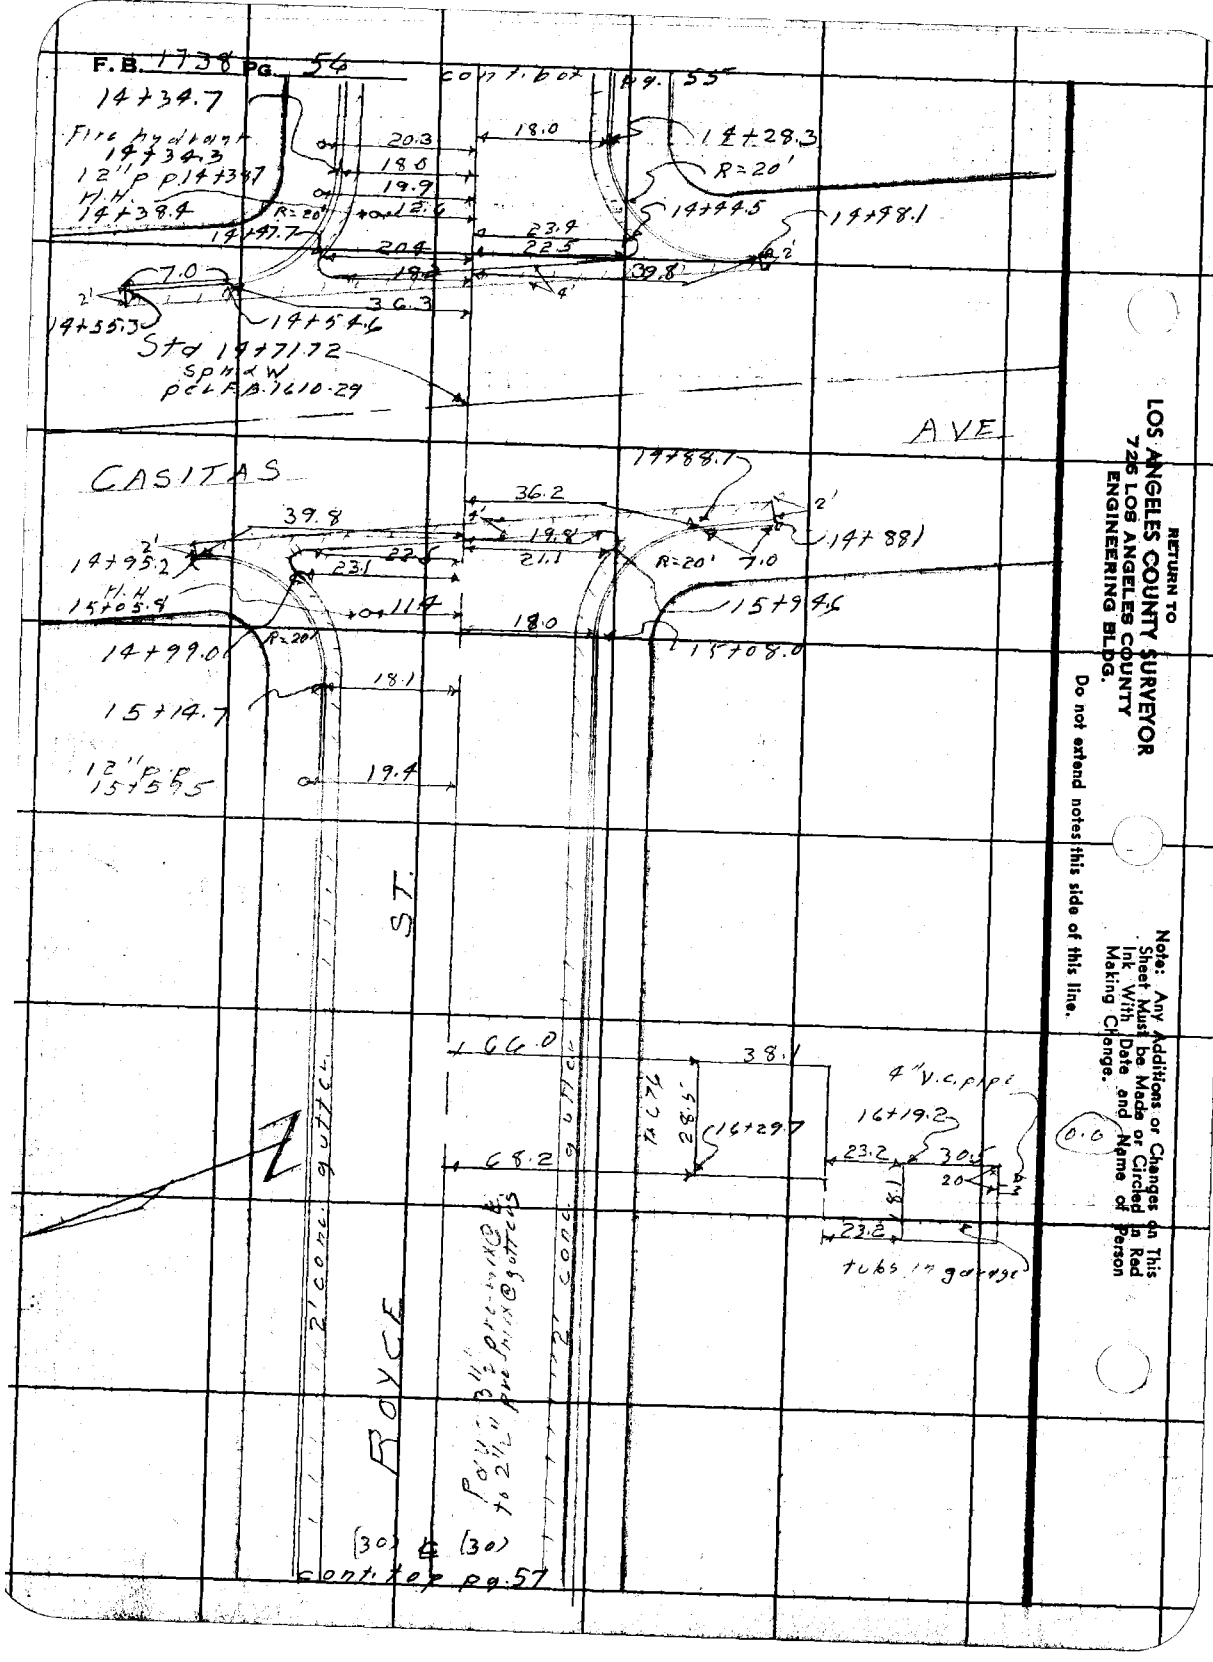

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

0.0

(9)

F. B. 1774 PG. 57

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Gayley Ave
W. O. 1424 Tape No. St'd. °F
Surveyed by V. V. L. Wright
Notes V. V. L. Date 2-7-52
Indexed

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

12" R.C.P. ± 3

Conc. gutter

19.9

6.9

17702.0

17705.1

25.8

16.2

12

1A

17682.9

2" C.I. pipe

7.0

6.0

basement

ST.

Pav. - 3½" ± to 2½" ± at gutter

ROYCE

12" R.C.P. ± 5

19.5

2' conc. gutter

6.5.0

will build garage with plumbing at back lot line

28.2

2" C.I. pipe

6.8.1

26.7

19+23.9

19+28.0

basement

tubs in garage

19+38.9

19+64.6

59.7

33.3

2" C.I. pipe

29.0

6.2.4

Sta 19+82.80 nail in P.C. of F.B. 1610-29

19+89.9

18.2

18.1

19+86.8

Tubs in garage

conc. curb

Easterly line of Tr. 44702

76F3095 247 2-51

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

F.B. 1738 PG. 58

Profile No. ____ Notes Red. ____ Plotted ____ Job No. 1462 Division No. ____ F. B. 1738 Pg. 59

Date ____ Date ____ Survey of Lincoln Ave.

Notes Chkd. [illegible] Checked ____ Survey By [illegible]

No. ____ Date 2/27/52 Date ____ Map No. [illegible] Date ____

PROFILE AND CROSS SECTIONS

ROYCE STREET

FROM

LINCOLN AVENUE

TO

THE EASTERLY LINE of TR. # 4702

C.I. 1462

J. V. Lanigan
C. H. Lewis
H. H. Raphael
H. C. Woodworth

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

764.298 307 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile
Plotted
Date
No.
X-Sec.
Notes Red
Date
Notes Chkd
Date
Checked
Date
No.
Job No. 462 Division No.
Survey of Castle Ave.
Survey by Gallagher Notes Lewis
Indexed C. Johnson Date
Pg. 60
T.S. 1738

STATION	B. S.	H. I.	F. S.	ELEV.	Royce St.
BM AE 241	6 12	1151 63		1145 51	AE 241 El 1145.514 FB 1447 P. 22.7 Lincoln Ave. & Royce St. S.W. cor. Bt. spk. in curb 3' S of S. end. C. R.
0+00			5 11	1146 52	℄ int of Royce St & Lincoln Ave.
			1 55	1150 08	100' N'th'ly on ℄ of " "
			2 15	1149 48	" " " W. gutter " "
			1 55	1150 08	" " " cb " "
			8 25	1143 38	100' S'th'ly " ℄ of " "
			8 87	1142 76	" " " W gutter " "
			8 23	1143 40	" " " " cb " "
0+253			5 58	1146 05	cross-gutter ℄
			4 42	1147 21	gutter N end NW cb. ret.
			3 74	1147 89	cb " " " " "
			4 74	1146 89	gutter W " " " "
			4 08	1147 55	cb " " " " "
			6 68	1144 95	gutter S " SW " "
			6 05	1145 58	cb " " " " "
			5 76	1145 87	gutter W " " " "
			5 11	1146 52	cb " " " "
1+00			4 52	1147 11	℄

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red Plotted Job No 446 Division No
No Date Date Date Survey of
Notes Chkd Checked Survey by
No Date Date Map No. Inked C. Jones

F.B. 7238 Pg 61

STATION	B. S.	H. I.	F. S.	ELEV.	Royce	St.
		1151 63				
1+00			4 59	1147 04		18' R gutter
"			3 98	1147 65		" cb
"			5 51	1146 12	18' L gutter	
"			4 89	1146 74	" cb	
2+00			4 31	1147 32		℄
"			4 46	1147 17		18' R gutter
"			3 82	1147 81		" cb
"			5 35	1146 28	18' L gutter	
"			4 71	1146 92	" cb.	
T. P.			4.71	1146.92	T. P.	
	4 79	1151 71				
2+00			6 ±	1145 ±	80' ± L back lot line	
2+85			10 ±	1140 ±	90' L basement floor to Ho # 46	
3+00			4 26	1147 45		℄
"			4 38	1147 33		18' R gutter
"			3 74	1147 97		" cb
"			5 33	1146 38	18' L gutter	
"			4 68	1147 03	cb	
"			12 0	1139 7	245' ± L. back lot line	
3+14 ±			11 7	1140 0	4" C.I.P. to Ho # 47	

FSL398 307 4-56

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. Plotted Date
Notes Red Date
X-Sec. No. Checked Date
Notes Chkd Date
Job No. 1462 Division No. Date
Survey of Castles Ave.
Survey by Lewis Notes Lewis
Indexed C. Jackson Date
P.B. 138 Pg. 12

STATION	B. S.	H. I.	F. S.	ELEV.	Royce St.
		1151 71			
3 + 33			9 8	1141 9	100'± R 4" C.I. Pipe to HO # 472
T. P.			4.67	1147 04	T. P.
	5 85	1152 89			
3+68			11 5	1141 4	177' R 4" c.I pipe to HO # 480
4+00			5 53	1147 36	℄
"			5 63	1147 26	18' R gutter
"			4.99	1147 90	" ch.
"			6 53	1146 36	18' L gutter
"			5.90	1146 99	ch.
"			13 4	1139 5	255'± back lot line
4+40			12 2	1140 7	80' L. basement floor to HO # 488
4+78			9 0	1143 9	92' L 4" C.I pipe to HO # 496
4+83			13 0	1139 9	104' L. Basement floor " "
T. P.			6.06	1146 83	T. P.
	5 45	1152 48			
5+00			5 23	1147 25	℄
"			5 40	1147 08	18' R. gutter
"			4 75	1147 73	" ch
"			6 30	1146 18	18' L gutter
"			5 64	1146 84	" ch.

764.298 387 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted. Job No. 1462 Division No.
No. Date Date Date Survey of Royce St.
No. Date Map No. Inked C. Johnson F.B. 17338 Pg. 63

Royce St.

STATION	B. S.	H. I.	F. S.	ELEV.	
		1152 48			
5+00			12 9	1139 6	265'± L back lot line
5+13±			9 9	1142 6	161'± L 4" C.I. pipe HO # 5900 (-00)
5+44±			8 5	1144 0	108' L 4" C.I pipe to HO # 5900
5+60			12 3	1140 2	100' L basement floor to HO # 5900
6+00			5 35	1147 13	℄
"			5 49	1146 99	18' R gutter
"			4 81	1147 67	" cb
"			6 37	1146 11	18' L gutter
"			5 72	1146 76	" cb
"			12 1	1140 4	245'± L back lot line
6+03±			10 5	1142 0	184' R 4" C.I. Pipe to HO # 5900
6+10±			9 4	1143 1	135' R 4" " " " " "
7+00			5 61	1146 87	℄
"			5 73	1146 75	18' R gutter
"			5 05	1147 43	" cb
"			6 65	1145 83	18' L gutter
"			6 03	1146 45	" cb
"			12 7	1139 8	245'± L back lot line
7±96			13 5	1139 0	183'± L 4" C.I. Pipe to HO # 5900

76L298 307 4-56

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

11 3/

Do not extend notes this side of this line.

Profile
Survey of Castle Ave. Job No 7462 Division No.
Plotted
Notes Red.
No.
Date
Survey by Lanigan Notes Lewis
Checked
Notes Chkd
X-Sec.
Indexed C. Johnson
Date
Date
No.
B.B. 1738 Pg. 64

STATION	B. S.	H. I.	F. S.	ELEV.	Boyce St.
		1152 48			
8+00			627	1146 21	℄
"			645	1146 03	18'R gutter
"			576	1146 72	" cb
"			743	1145 05	18'L gutter
"			686	1145 68	" cb
"			12 7	1139 8	225'±L back lot line
T.P.		1	679	1145 69	T.P.
	497	1150 66			
9+00			536	1145 30	℄
"			539	1145 27	18'R gutter
"			478	1145 88	" cb
"			640	1144 26	18'L gutter
"			580	1144 86	" cb.
"			11 0	1139 7	225'±L back lot line
10+00			610	1144 56	℄
"			621	1144 45	18'R gutter
"			551	1145 15	" cb
"			722	1142 44	18'L gutter
"			659	1144 07	" cb
"			11 3	1139 4	215'±L back lot line

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted. Job No. 4 & 2 Division No. F. B. 1738 Pg. 65
No. Date Date Date Survey of Easton
No. Date Map No. Indexed C. Johnson

STATION	B. S.	H. I.	F. S.	ELEV.	Royce St.
		1150 CG			
10+15			5 8	1144 9	75'R Floor Level of House with basement at open door entry
11+00			6 36	1144 30	℄
"			6 43	1144 23	18' R gutter
"			5 82	1144 84	" CL
"			7 42	1143 24	18' L gutter
"			6 77	1143 89	" CL
"			11 6	1139 1	205'± L back lot line
11+03			5 9	1144 8	90' L basement floor to HO ℄ 5.9
T.P.			6 70	1143 96	T.P.
	5 32	1149 28			
11+62			8 6	1140 1	140'± R 2" C.I. pipe at garage to HO ℄ CL
12+00			5 16	1144 12	℄
"			5 21	1144 07	18' R gutter
"			4 61	1144 67	" CL
"			6 21	1143 07	18' L gutter
"			5 59	1143 69	" CL
"			10 1	1139 2	195'± L back lot line
13+00			5 32	1143 96	
"			5 35	1143 93	18' R gutter
"			4 75	1144 53	" CL

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

1144.467

Profile No. ____ Plotted ____ Date ____
X-Sec. No. ____ Checked ____ Date ____
Notes Red. ____ Date ____
Notes Chkd ____ Date ____
Job No. 1462 Division No. ____
Survey of Casitas Ave. Notes Lewis
Survey by ____
Indexed ____ Date ____
F.B. 1738 Pg. 66

STATION	B. S.	H. I.	F. S.	ELEV.	Royce	St.
		1149 28				
13+00			6 35	1142 93	18' L gutter	
"			5 65	1143 63	" cb	
"			10 3	1139 0	185± L back lot line	
T. P.		1	5 82	1143 46	T. P.	
	5 39	1148 85				
14+00			5 05	1143 80	℄	
"			5 14	1143 71		18' R gutter
"			4 50	1144 35		" cb
"			6 09	1142 76	18' L gutter	
"			5 53	1143 32	cb	
"			8 4	1140 5	175'± L back lot line	
T. P.		1	4 38	1144 47	T.P. on BM AE 403	El 1144.467
	3 94	1148 41				
14+71.72			4 94	1143 47	℄ int. Royce St. &	Casitas Ave.
			4 20	1144 21	gutter N end	NE cb tot.
			3 43	1144 98	cb " "	" " "
			4 75	1143 66	gut. E "	" " "
			4 07	1144 34	cb " "	" " "
			5 74	1142 67	gut. E "	SE " "
			5 14	1143 27	cb " "	" " "

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted. Job No. 1446 2 Division No.
No. Date Date Survey of
Notes Checked Survey by
No. Date Map No. Inspected Date

F. B. 1738 Pg. 67

STATION	B. S.	H. I.	F. S.	ELEV.	Royce St.
		1148 41			
			6.18	1142 23	gutter Send SE cb ret
			5.60	1142 81	cb " " " " " "
			5.99	1142 42	gut. " " SW " "
			5.36	1143 05	cb " " " " "
			5.55	1142 86	gut W " " " "
			4.92	1143 49	cb " " " " "
			4.60	1143 81	gut " " NW " "
			3.96	1144 45	cb " " " " "
			3.93	1144 48	gut N " " " "
			3.21	1145 20	cb " " " " "
			1.64	1146 77	100' Nthly on ℄ of Cosita Ave
			6.82	1141.59	" Sthly " " " "
14+51 ?			5.22	1143 19	CROSS-gutter (E) ℄
14+91 ℄			5.16	1143 25	" " (W) ℄
16+00			4.25	1144 16	℄
"			4.43	1143 98	18'R gutter
"			3.78	1144 63	" cb
"			5.43	1142 98	18'L gutter
"			4.80	1143 61	" cb
"					

76L298 307 4-58

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

7 3/2

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Royce St.
T.P.		1148 41	3 95	1144 46	T.P.
	4 82	1149 28			
16+00			8 9/4	1140 4/	200± L back lot line
16+21			8 3/	1140 0/	161' R 4" VC pipe at garage to Ho #676
17+00			4 89	1144 39	℄
"			5 08	1144 20	18' R gutter
"			4 44	1144 84	" cb
"			6 07	1143 21	18' L gutter
"			5 42	1143 86	" cb
"			8 8/	1140 5/	190'± L back lot line
17+01			7 2/	1142 1/	142' R 2" C.I. pipe at garage to Ho # 994
17+18			11 1/	1138 2/	90' R basement floor to " "
T.P.			5 48	1143 80	T.P.
	5 74	1149 54			
18+00			4 96	1144 58	℄
"			5 15	1144 39	18' R gutter
"			4 47	1145 07	" cb
"			6 14	1143 40	18' L gutter
"			5 44	1144 10	" cb
"			8 6/	1140 9/	± R back lot line

P. B. 74/38 Pg. 68 Job No. 1462 Division No. Profile
Survey of Castle Gate Ave. Plotted
Survey by Langlan Notes Lewis Notes Chkd. Checked
Indexed C. Johnson Date Date Date
Notes Bad. Date No.
Date No.
X-Sec.

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

7-3 1145

Profile Notes Red. Plotted Job No. 442 Division No.
No. Date Date Survey of
No. Notes Chkd. Checked Survey by Lewis Lewis
No. Date Date Map No. Inked C. Johnson

F. B. 1738 Pg. 69

STATION	B. S.	H. I.	F. S.	ELEV.	Rogce	St.
		114954				
19+00			478	114476	℄	
"			495	114459		18'R gutter
"			428	114526		" cb
"			580	114374	18'L gutter	
"			511	114443	" cb	
"			82	1140±	back lot line	
T. P.			523	114431	T. P.	
	568	114999				
19+15			12 4	1137 4	90'R basement floor to Ho 722	
"			8 0	1142 0	124'R 2" C.I. pipe & gutter to Ho 722	
19+64			7 5	1142 5	122'R " " " " " to Ho 732	
19+80±			620	114379	18'L gutter at end	
"			548	114451	" cb "	
19+89±			516	114483		18'R gutter at end
"			450	114549		cb " "
19+90			98	1140 2	±L back lot line	
BM AE 519			454	1145 45	El. 1145.459	

F. B. 1738 Pg. 70 | Job No. 1462 Division No. V. Notes Red. Plotted. Profile

Survey of Casitas Ave. Date Date No.

Survey by Lanigan Notes Lewis Notes Chkd. Checked X-Sec.

Indexed Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.

761.298 307 4-50

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR

726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Casitas Ave.
W. O. 1462 Tape No. St'd °F
Surveyed by J. J. Lanigan
Notes Lanigan Date 2-13-52
Indexed C. Jannaco

F. B. 1138 Pg. 71

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION of IMPROVEMENTS on CASITAS AVE from ROYCE ST to VENTURA ST

C.I. 1462

J. J. Lanigan
C. H. Lewis
H. H. Raphael
H. C. Woodworth

76F3096 247 2-51

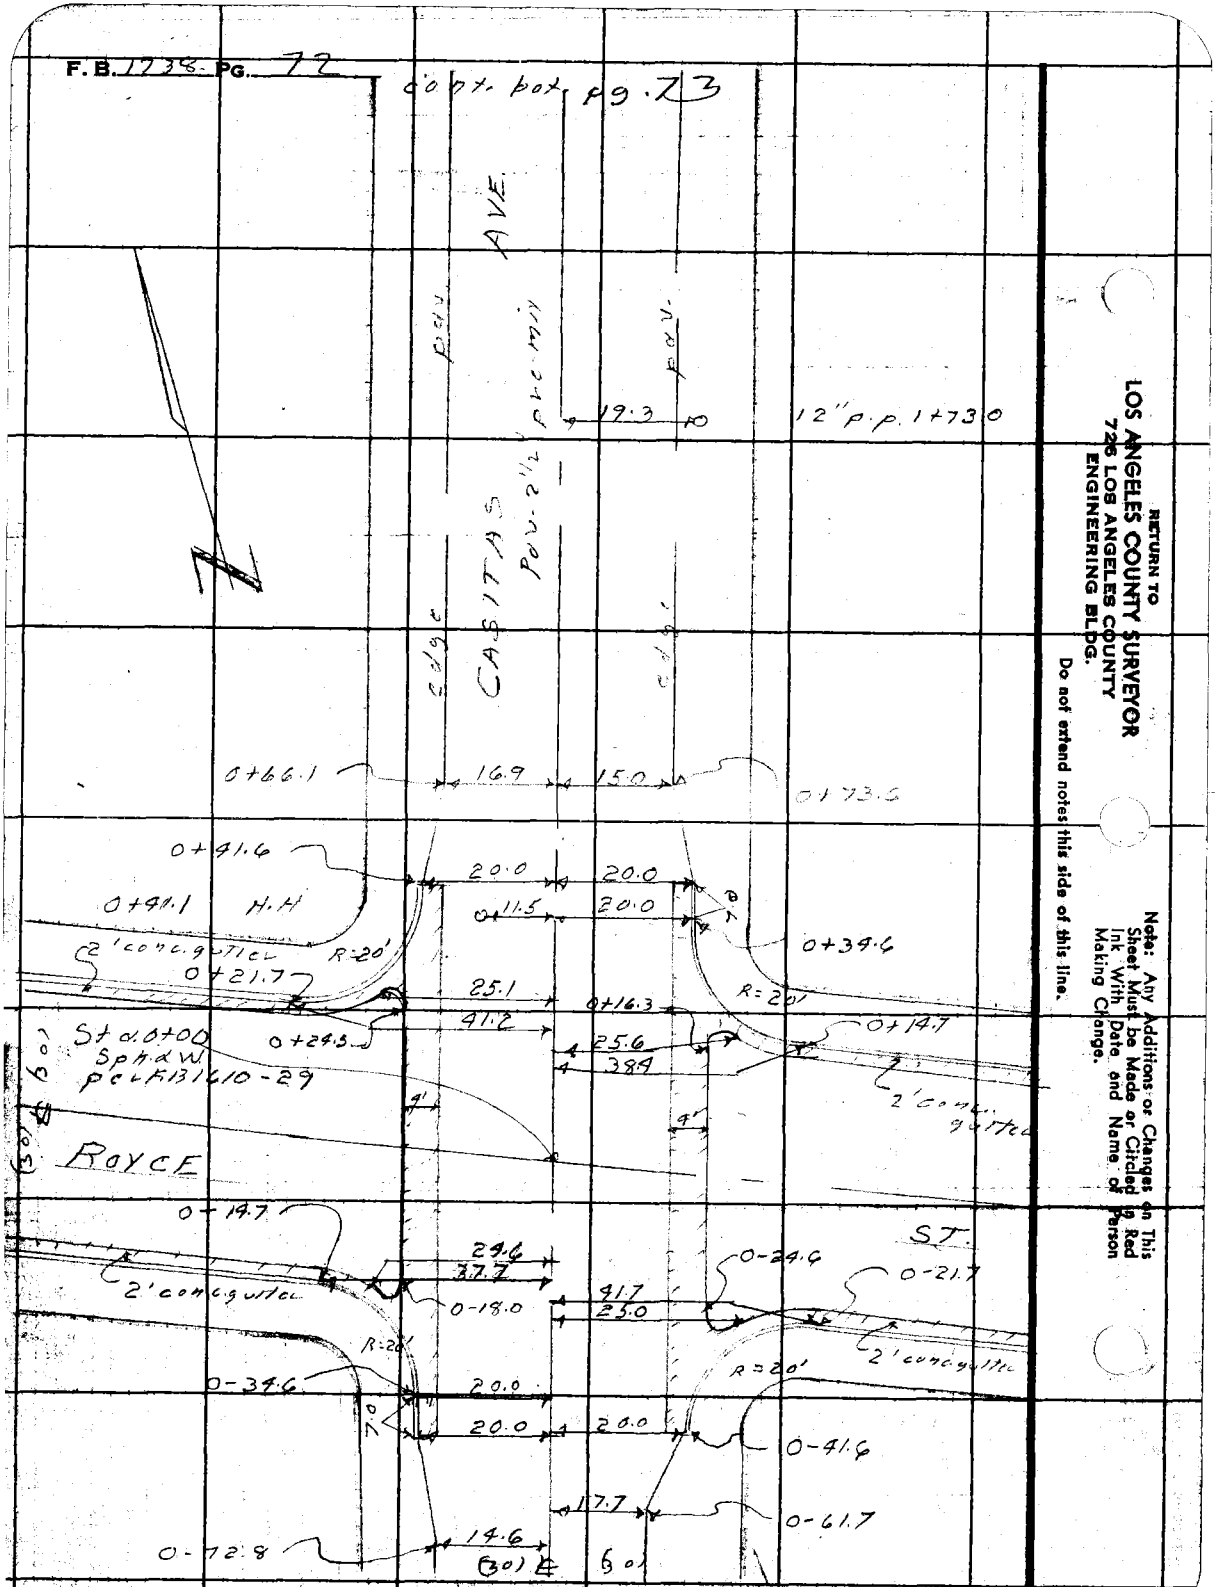
F.B. 1738 PG. 72
cont. bot. pg. 73
AVE.
P.O.C.
P.O.V.
19.3
12" p.p. 1+73.0
CABRITAS
P.O.V. 2½" pipe mon.
0+66.1
16.9
15.0
0+73.5
0+41.6
0+41.1
H.H
20.0
20.0
11.5
20.0
2' conc. gutter
R=20'
0+21.7
0+34.6
25.1
0+16.3
R=20'
41.2
St. 0+00
Sph. W.
pc LA 131610-29
0+24.3
25.6
38.9
0+14.7
2' conc. gutter
4'
4'
ROYCE
0-14.7
2' conc. gutter
29.6
37.7
0-18.0
41.7
25.0
0-24.6
0-21.7
ST
R=20'
2' conc. gutter
0-34.6
20.0
20.0
20.0
0-41.6
17.7
0-61.7
0-72.8
14.6
(30)
60'
Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.
RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.
Do not extend notes this side of this line.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Cosillas Ave
W. O. 1962 Tape No. St'd. °F
Surveyed by J. J. Lonergan
Notes Lonergan Date 2-10-52
Indexed H. C. Johnson

F. B. 1726 Pg. 73

2887 Bor. Pg. 77
Pgs. 80

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

AVE.
19
12" p.p. 5+38.4
5+13.8
13.7
H. H. 4+98.2
10.0
4+91.3
Fire hydrant
4+85.4
15.0
15.0
18.9
16.8
6.5'
4+85.1
C2' conc. gutter
R=20'
22.1
36.7
22.9
33.1
4+71.5
4+72.8
MOUNTAIN VIEW.
4+65.3
4+66.4
2' conc. gutter
R=20'
RD.
60'
Sta. 4+50.13
Spk. 1 W.
pcu F. B. 1726-57
4+29.7
4+35.9
2' conc. gutter
22.7
25.8
47.0
29.6
4+20.9
4+28.0
R=25'
2' conc. gutter
R=25'
4+11.3
H. H. 4+04.8
8.5
20.0
10.8
20.0
20.0
4+02.9
14.8
3+81.5
14.5
3+60.0
CASITAS
Pav. 2½" p.c. 1+77.8
18" P.P. 3+26.7
2+77.8 - 10" guy P.
30.1
30'
Cont. to pg. 72

76F3098 247 2-51

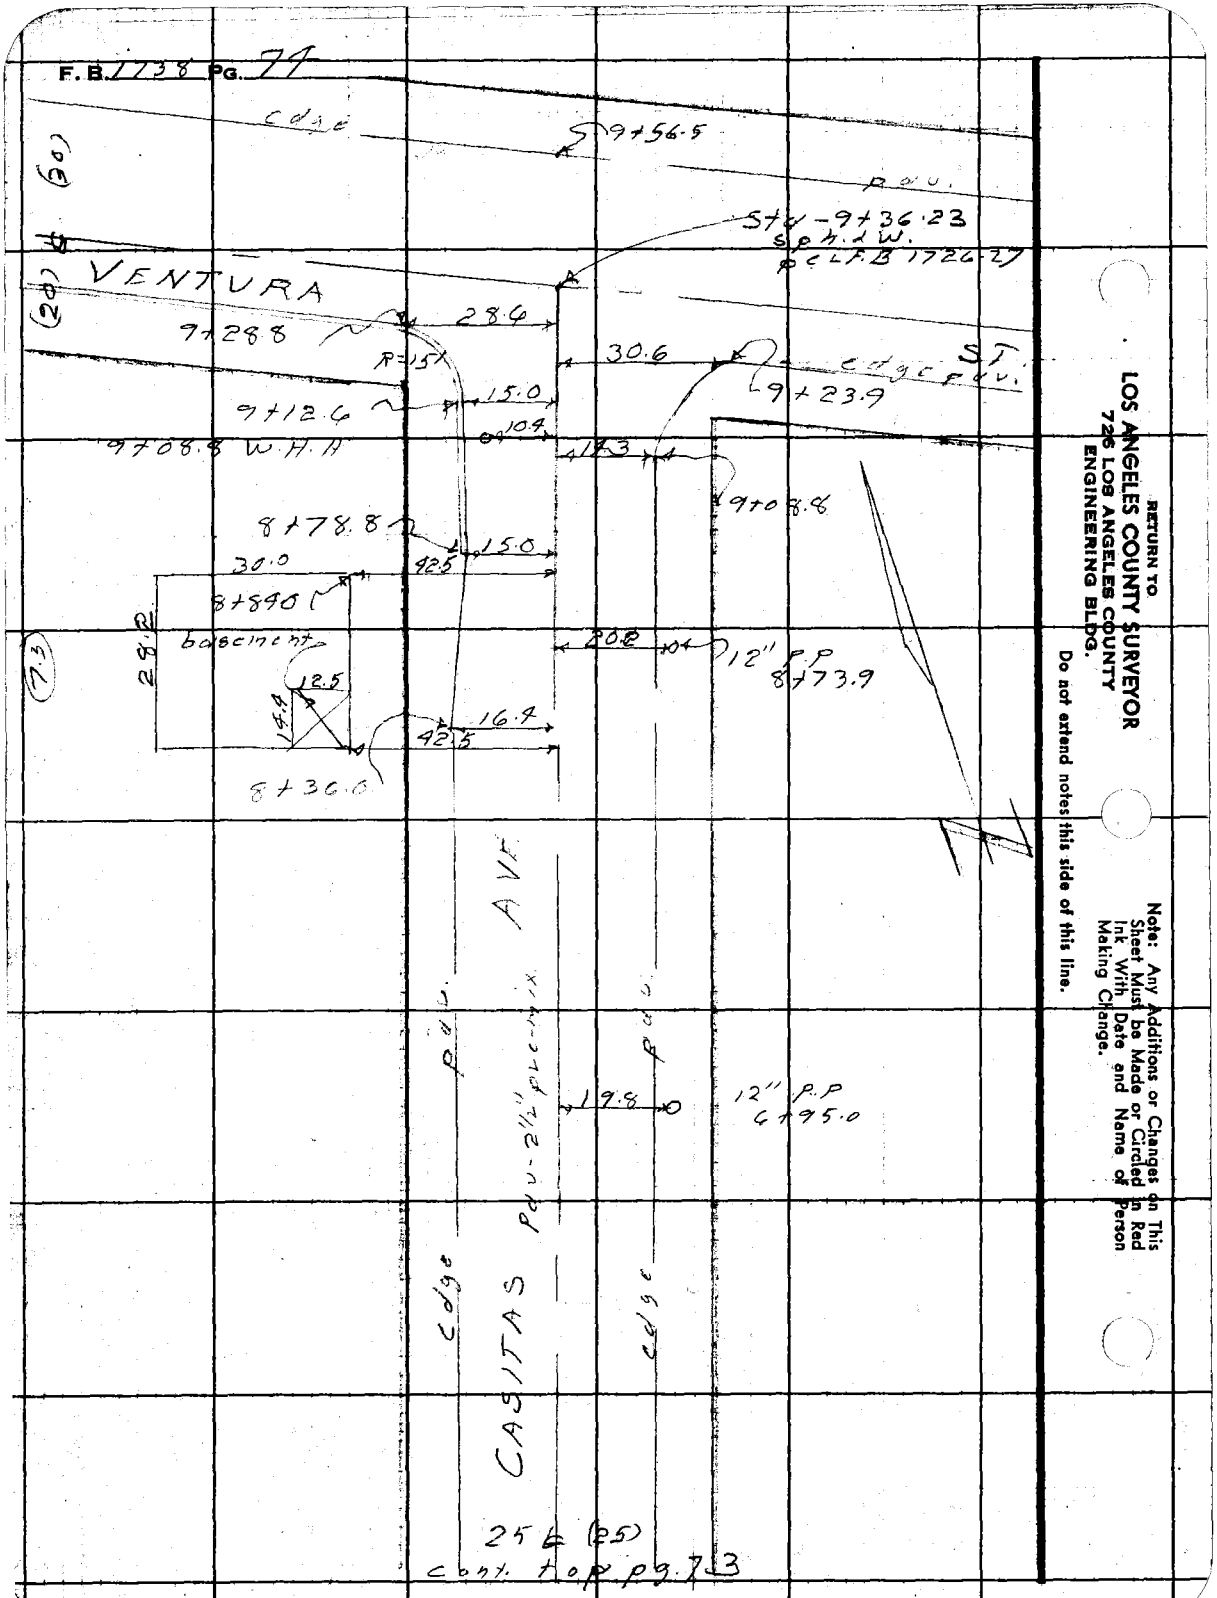
F.B. 1738 Pg. 74
(30)
(28)
VENTURA
9+28.8
9+12.6
9+08.8 W.H.A
8+78.8
8+39.0
8+36.0
28.6
30.6
15.0
10.4
42.5
30.0
29.2
basement
12.5
16.7
20.8
12" P.P
8+73.9
9+08.8
9+23.9
S.T.
edge of Pav.
Sta - 9+36.23
sph. 2 W.
P.C.L.F.B 1726.27
P.C.V.
AVE
Pav. - 2½" P.L. - IX
19.8
12" P.P
6+95.0
CASITAS
Edge
Edge
25 & (25)
Cont. to P. pg. 73
RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.
Do not extend notes this side of this line.
Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No. | Notes Red | Plotted | Job No. 1462 | Division No. | F. B. 1738 | Pg. 75
Date | Date | Survey of Casitas Ave.
Notes Checked | Checked | Survey by [illegible]
No. | Date 2/27/52 | Date | Map No. | Inked C. Johnson | Date

PROFILE AND CROSS SECTIONS

OF

CASITAS AVENUE

FROM

ROYCE ST.

TO

VENTURA ST.

C.I. 1462

J.J. Lanigan
C.H. Lewis
H.H. Raphael
H.C. Woodworth

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

76L398 307 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

P.B. 1738 PG. 47 Job No. 1462 Division No. Profile
Survey of Casitas Ave. Plotted No.
Survey by Lanigan, Notes Lewis Date X-Sec.
Indexed K. C. Johnson Date Notes Red Checked No.
Date Notes Chkd. Date

STATION	B. S.	H. I.	F. S.	ELEV.	Casitas Ave.
BM AE403	3 85	1148 32		1144 47	AE 403 El 1144.467 FB 1568 P50 Casitas Ave. & Royce St., NW. Cor. Bt. spk. in curb 6' W of W. end C.R.
0 +00			4 86	1143 46	℄ int Casitas Ave & Royce St.
			6 66	1141 66	100' S'ly on ℄ of Casitas Ave.
			4 46	1143 86	100' E'ly on ℄ of Royce St.
			5 50	1142 82	" " " S gutter " "
			4 89	1143 43	" " " " cb " "
			4 56	1143 76	" " " N gutter " "
			3 89	1144 43	" " " " cb " "
			4 30	1144 02	100' W'ly " ℄ of Royce St.
			5 36	1142 96	" " " S gutter " "
			4 71	1143 61	" " " " cb " "
			4 39	1143 93	" " " N gutter " "
			3 73	1144 59	" " " " cb " "
			5 65	1142 67	gutter E end SE cb ret
			5 06	1143 26	cb " " " " "
			6 04	1142 28	gut. S " " " "
			5 51	1142 81	cb " " " " "
			5 91	1142 41	gutter S " SW " "

76L298 307 4-50

PLEASE RETURN TO.
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No/462 Division No.____ F.B. 7338 Pg. 77
No.____ Date____ Date____ Survey of Castaic Area
Notes Chkd____ Checked____ Survey by Gantry & Associates
No.____ Date____ Date____ Map No.____ Index C. Johnson Date

STATION	B. S.	H. I.	F. S.	ELEV.	Castaic	Ave
		1148 32				
			5 27	1143 05	cb. S. end S.W.	cb. rot.
			5 46	1142 86	gutter W end "	" "
			4 83	1143 49	c.b. " " "	" "
			4 51	1143 81	gut. " " NW	" "
			3 87	1144 45	cb. " " "	" "
			3 85	1144 47	gut. N " "	" "
			3 11	1145 21	cb " " "	" "
			4 10	1144 22	gut " " NE	" "
			3 33	1144 99	cb " " "	" "
			4 67	1143 65	gut E " "	" "
			3 98	1144 34	" " "	" "
0+41 ℄			3 85	1144 47		20' R gutter
"			3 11	1145 21		" cb
0+66 ℄			2 66	1145 66	℄	
"			2 76	1145 56	9' L bnk	
"			2 42	1145 90	17' " edge pvmt	
0+73 ℄			2 47	1145 85		9' R bnk
"			2 16	1146 16		16' R edge pvmt
1+00			1 55	1146 77	℄	
"			1 75	1146 57		9' R bnk

764398 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

4 8

Do not extend notes this side of this line.

F. B. 1738 Pg. 78 | Job No. 1462 Division No. | Profile
Survey of Casitas Ave. | Plotted | Notes Red | No.
Survey by Lanigan Notes Lewis | Date | Date | No.
Indexed C. Thomas Date | Notes Chkd | Checked | X-Sec.
Date | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	Casitas	Ave.
		1148 32				
1+00			1 13	1147 19		15' R edge pvmt.
"			0 5	1147 8		30' R. P.L.
"			1 68	1146 64	9' L bnk	
"			1 38	1146 94	16' L edge pvmt.	
"			0 7	1147 6	30' L P.L.	
T. P.		1	0 92	1147 40	T. P.	
	8 45	1155 85				
2+00			6 08	1149 77		℄
"			6 20	1149 65		8' R bnk
"			5 71	1150 14		14' R edge pvmt
"			5 5	1150 4		30' R P.L.
"			5 4	1150 5		100' R
"			6 22	1149 63	8 5 L bnk	
"			5 79	1150 06	15' L edge pvmt.	
"			5 4	1150 5	30' L P.L.	
"			5 3	1150 6	100' L	
"			4 8	1151 1	180'± L back lot line	
3+00			2 90	1152 95		℄
"			3 04	1152 81		8' R bnk
"			2 53	1153 32		14' R edge pvmt

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. 1462 Division No.
No. Date Date Survey of Casitas Ave. F. B. 7238 Pg. 29
Notes Chkd. Checked Survey by [illegible] C. Jaramillo
No. Date Date Map No. Inspected

STATION	B. S.	H. I.	F. S.	ELEV.	Casitas Ave.	
		1155.85				
3+00			1.9	1154.0		30' R P.L.
"			2.97	1152.88	8.5' L b+k	
"			2.63	1153.22	15' L edge pvmt	
"			2.3	1153.6	30' L P.L.	
T.P.			2.79	1153.06	T.P.	
	10.69	1163.75				
3+60			8.96	1154.79	8.5' L b+k	
"			8.42	1155.33	14.5' L edge pvmt	
3+81.5			9.06	1154.69		8' R b+k
"			8.63	1155.12		14.8' R edge pvmt
4+00			7.70	1156.05		℄
4+02.5			8.04	1155.71	20' L gutter	
"			7.36	1156.39	" cb	
"			7.0	1156.8	30' L P.L.	
4+02.9			8.05	1155.70		20' R gutter
"			7.47	1156.28		" cb
"			7.3	1156.5		30' R P.L.
4+50.13			6.32	1157.43	℄ int Casitas Ave. & Mountain View Rd.	
			5.96	1157.79	100' E'ly on ℄ of "	" "
			6.96	1156.79	" " S. gutter	

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 1738 Pg. 80 Job No. 1462 Division No. Notes Red. Plotted Profile
Survey of Casitas Ave. Date No.
Survey by Lenigan Notes Lewis Date Notes Chkd. Checked X-Sec.
Indexed C. Johnson Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	Casitas Ave.
		1163 75			
			630	1157 40	100' E'ly on S. cb of Mountain View Rd
			596	1157 79	" " " N gutter " " "
			529	1158 46	" " " " cb " " "
			545	1158 30	" W'ly " on ℄ " " "
			653	1157 22	" " " S gutter " " "
			583	1157 92	" " " " cb " " "
			549	1158 26	" " " N gut. " " "
			483	1158 92	" " " " cb " " "
			664	1157 11	gutter W end & SW cb ret
			577	1157 98	cb " " " " "
			781	1155 94	gut. S " " " "
			708	1156 67	cb " " " " "
			707	1156 68	gut E " SE " "
			637	1157 38	cb " " " " "
			609	1157 66	gut " " NE " "
			542	1158 33	cb " " " " "
			547	1158 28	gut N " " " "
			477	1158 98	cb " " " " "
			536	1158 39	gut " " NW " "
			460	1159 15	cb " " " " "

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Date Plotted Date Job No. 462 Division No. F.B. 1738 Pg. 81
No. 1 Sec. Notes Chkd. Date Checked Date Survey of Cook Tie Survey by [illegible] Map No. Indexed Date

STATION	B. S.	H. I.	F. S.	ELEV.	Casitas Ave.
		1163 75			
			560	1158 15	gut - W end NW cb ret.
			495	1158 80	cb " " " " "
4+91 ℄			524	1158 51	15° R gut
"			457	1159 18	" " cb
5+00			441	1159 34	℄
"			460	1159 15	13' R b+k
"			435	1159 40	15' R edge pvmt
"			3 0	1160 8	30' R P.L.
"			468	1159 07	13' L b+k
"			443	1159 32	15' L edge pvmt
"			3 6	1160 2	30' L P.L.
5+47			192	1161 83	℄
"			204	1161 71	9' R b+k
"			176	1161 99	15' R edge pvmt
"			1 2	1162 1	30' R P.L.
"			203	1161 72	8' L b+k
"			177	1161 98	15' L edge pvmt
"			1 9	1161 9	30' L P.L.
T.P.			181	1161 94	T.P.
	993	1171 87			

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile | X-Sec.
Plotted | No.
Date | Notes Red | No.
Date | Notes Chkd. | Checked
Date | Date
Job No. 1462 Division No. | Notes Lewis | Date
Survey of 295 Freeway 5 Ave.
Survey by Lanigan
Indexed C. Johnson
PG. 92
7738

STATION	B. S.	H. I.	F. S.	ELEV.	Casitas	Ave.
		1171 87				
6+00			8 21	1163 66		℄
"			8 22	1163 65		8'R b-h
"			7 82	1164 05		15'R edge pvmt
"			8 0	1163 9		30'R P.L
"			8 34	1163 53	8'L b-h	
"			7 85	1164 07	14'L edge pvmt	
"			7 7	1164 2	30'L P.L.	
7+00			4 66	1167 21		℄
"			4 63	1167 24		8'R b-h
"			4 28	1167 59		15'R edge pvmt.
"			4 6	1167 3		30'R P.L
"			4 7	1167 2		100'R
"			4 91	1166 96	8'L b-h.	
"			4 35	1167 52	14'L edge pvmt.	
"			4 4	1167 5	30'L P.L.	
"			5 3	1166 6	100'L	
"			6 0	1165 9	210' ±L back lot line	
T.P.			0 43	1171 44	T.P.	℄
	8 46	1179 90				

764.298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Rod_____ Plotted_____ Job No. 4462 Division No._____
No._____ Date_____ Date_____ Survey of Castaic Jct.
Notes Chkd._____ Checked_____ Survey by Lampman & C. Johnson
No._____ Date_____ Date_____ Map No._____ Index No._____
F.B. 1738 Pg. 83

STATION	B. S.	H. I.	F. S.	ELEV.	Cosites	Ave'
		1179 90				
8+00			876	1171 14		℄
			886	1171 04		8'R bk
			843	1171 47		15'R edge pvmt
			9 0	1170 9		30'R P.L.
			895	1170 95	8'L bk	
			858	1171 32	14'L edge pvmt	
			9 4	1170 5	30'L P.L.	
8 +49			712	1172 78		℄
			712	1172 78		8'R bk
			683	1173 07		15'R edge pvmt
			6 8	1173 1		30'R P.L.
			732	1172 58	8'L bk	
			696	1172 94	14'L edge pvmt	
			7 0	1172 9	30'L P.L.	
8+78			652	1173 38		℄
"			682	1173 08	15'L edge pvmt at cb	
"			680	1173 10	" cb at end	
9+00			613	1173 77		℄
"			630	1173 60		14' R edge pvmt
"			5 2	1174 7		16' bk

76L398 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ Plotted ____ Notes Red. ____ Division No. ____
X-Sec. No. ____ Date ____ Date ____ Job No. 1462
Checked ____ Notes Child ____ Survey of Casitas Ave
Date ____ Date ____ Survey by Langlea Notes Lewis
Date ____ Indexed K. C. Johnson

STATION	B. S.	H. I.	F. S.	ELEV.	Casitas	Ave.
		1179 90				
9+00			5 3/5	1174 5		30'R P.L
9+25			585	1174 05	cross gutter ℄	
9+36.23			495	1174 95	℄ int. Casitas Ave. & Ventura ST	
			445	1175 45	100' E'ly on ℄ of " "	"
			549	1174 41	" W'ly " " " " "	"
			613	1173 77	gutter - S end SW cb & et	
			555	1174 35	cb " " " " "	
			586	1174 04	gut. W " " " "	
			539	1174 51	cb " " " " "	
BM AE 506			546	1174 44	AE 506 E/ 1174.446 FB 1568 P141 Ventura St + Casitas Ave, S.W. cor BT spk in curb C'W of W. end C.R.	

Notes Ck'd by:
Map No.
Office Work
Checked
Date

Survey of Easters Ave
W. O. 1962 Tape No. St'd L °F
Surveyed by J. J. Lanigan
Notes J. J. L Date 2-15-62
Indexed K. C. Johnson

F. B. 1738 Pg. 85

Note: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION of BASEMENTS on LINCOLN AVE from ROYCE ST to FOOTHILL BLVD C.I. 1962

J. J. Lanigan
C. H. Lewis
H. H. Raphael
H. S. Woodworth

76F3098 247 2-51

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

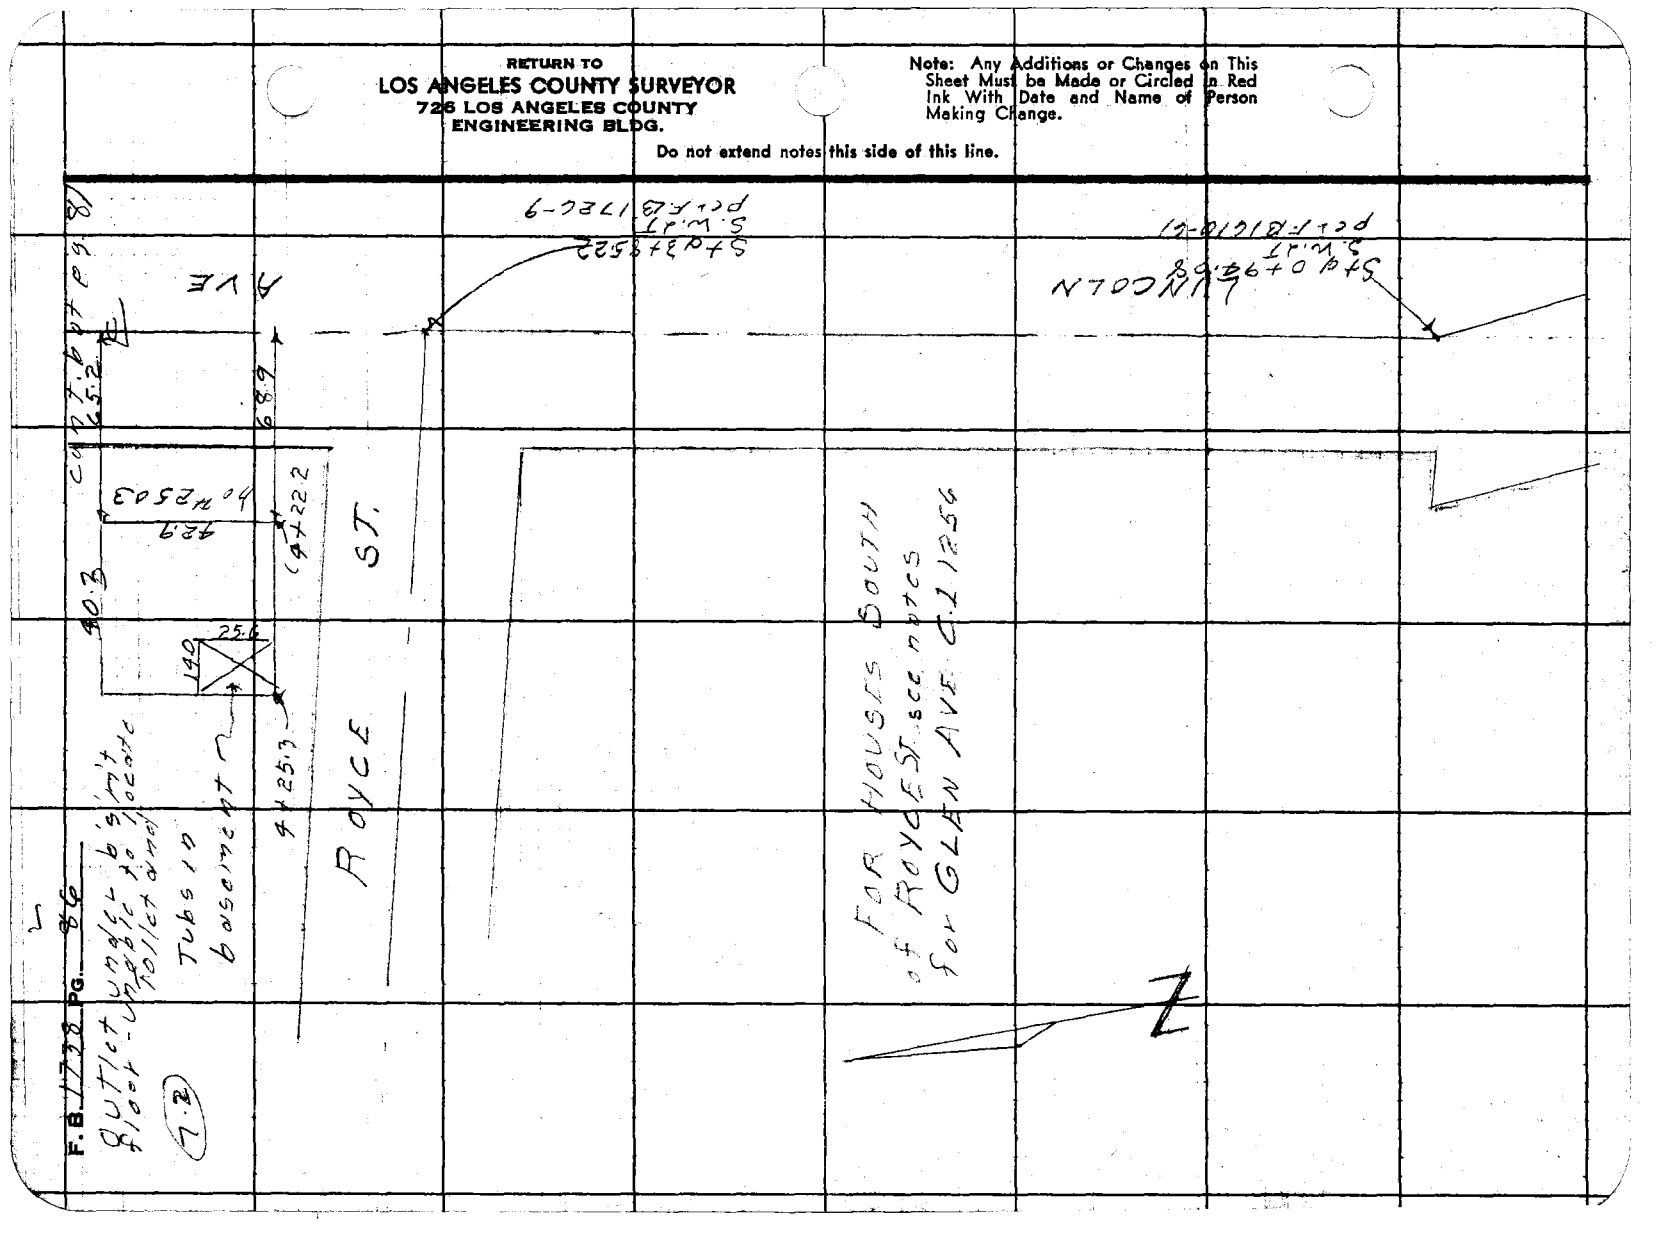

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Casita Ave
W. O. 1962 Tape No. St'd. F
Surveyed by J. J. Lanigan
Notes J. J. L. Date 2-15-32
Indexed C. Johnson

F.B. 1738 Pg. 87
cont. bot pg. 88

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

8.4
basement
92.0
87.4
10.3
38.6
10.0
N 25 83
87.4
9+21.1
Sta 87+35.27
Rd. Dept. Mon.
per F.B. 1738-10
A 12
MOUNTAIN VIEW RD
37.5
61.0
Tubs in basement
13.5
27.0
42.5
N 25 51
61.0
8.1
7.9
5.2
7+34.4
4" C.I. pipe
7+03.7
33.7
63.7
15.0
17.3
36.2
N 0 25 41
66.5
4.0
Tubs in basement
drain goes into floor of bsmt. unable to locate outlet.
LINCOLN
cont. top pg. 86

75F3093 247 2-51

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

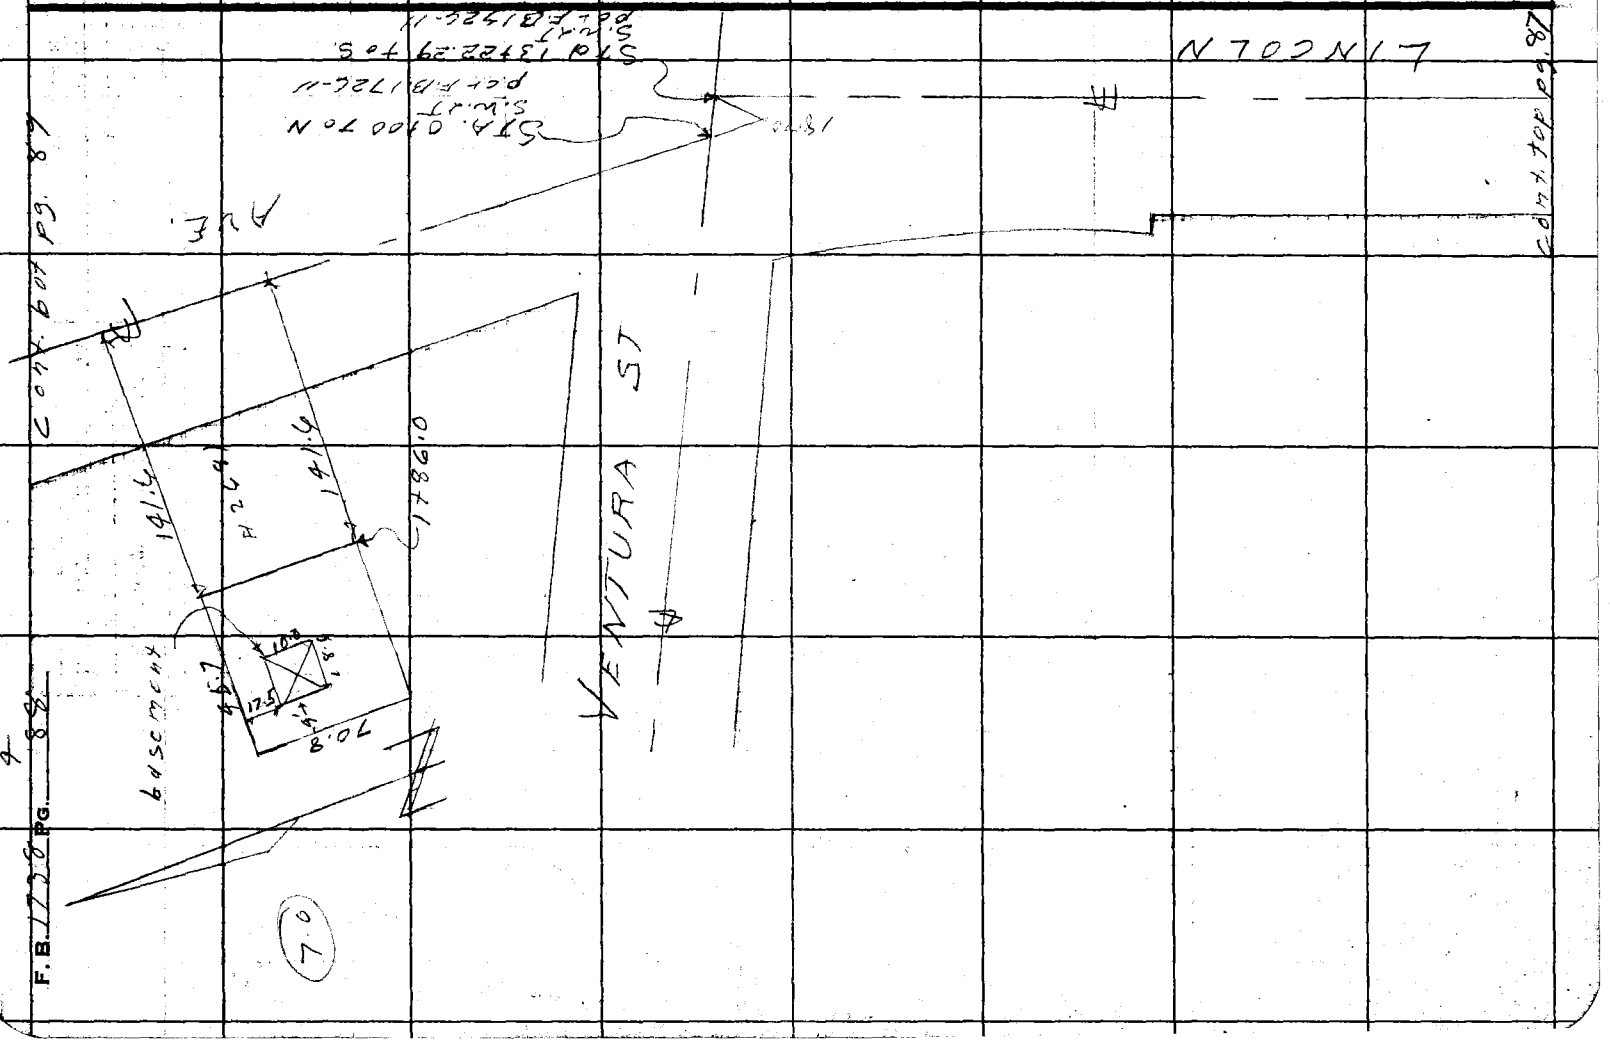

Notes Ck'd by:
Map No.
Office W'prk
Checked
Date

Survey of Gaviota Ave.
W. O. Tape No. St'd. °F
Surveyed by J.J. Lanigan
Notes J.J.L. Date 2-18-57
Indexed C. Johnson

F. B. 1736 Pg. 89

cont. from pg. 7

9+53.3

28.1

58.9

11.5

8.0

basement

39.1

N 27°33' E

9.1

71.4

(6.7)

HARRIET ST.

EST. 8+49.47 ± B.W.L.T. per F.B. 722-12

LINCOLN

cont. top pg. 88

Note: Any Additions or Changes of This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76P3095 247 2-51

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

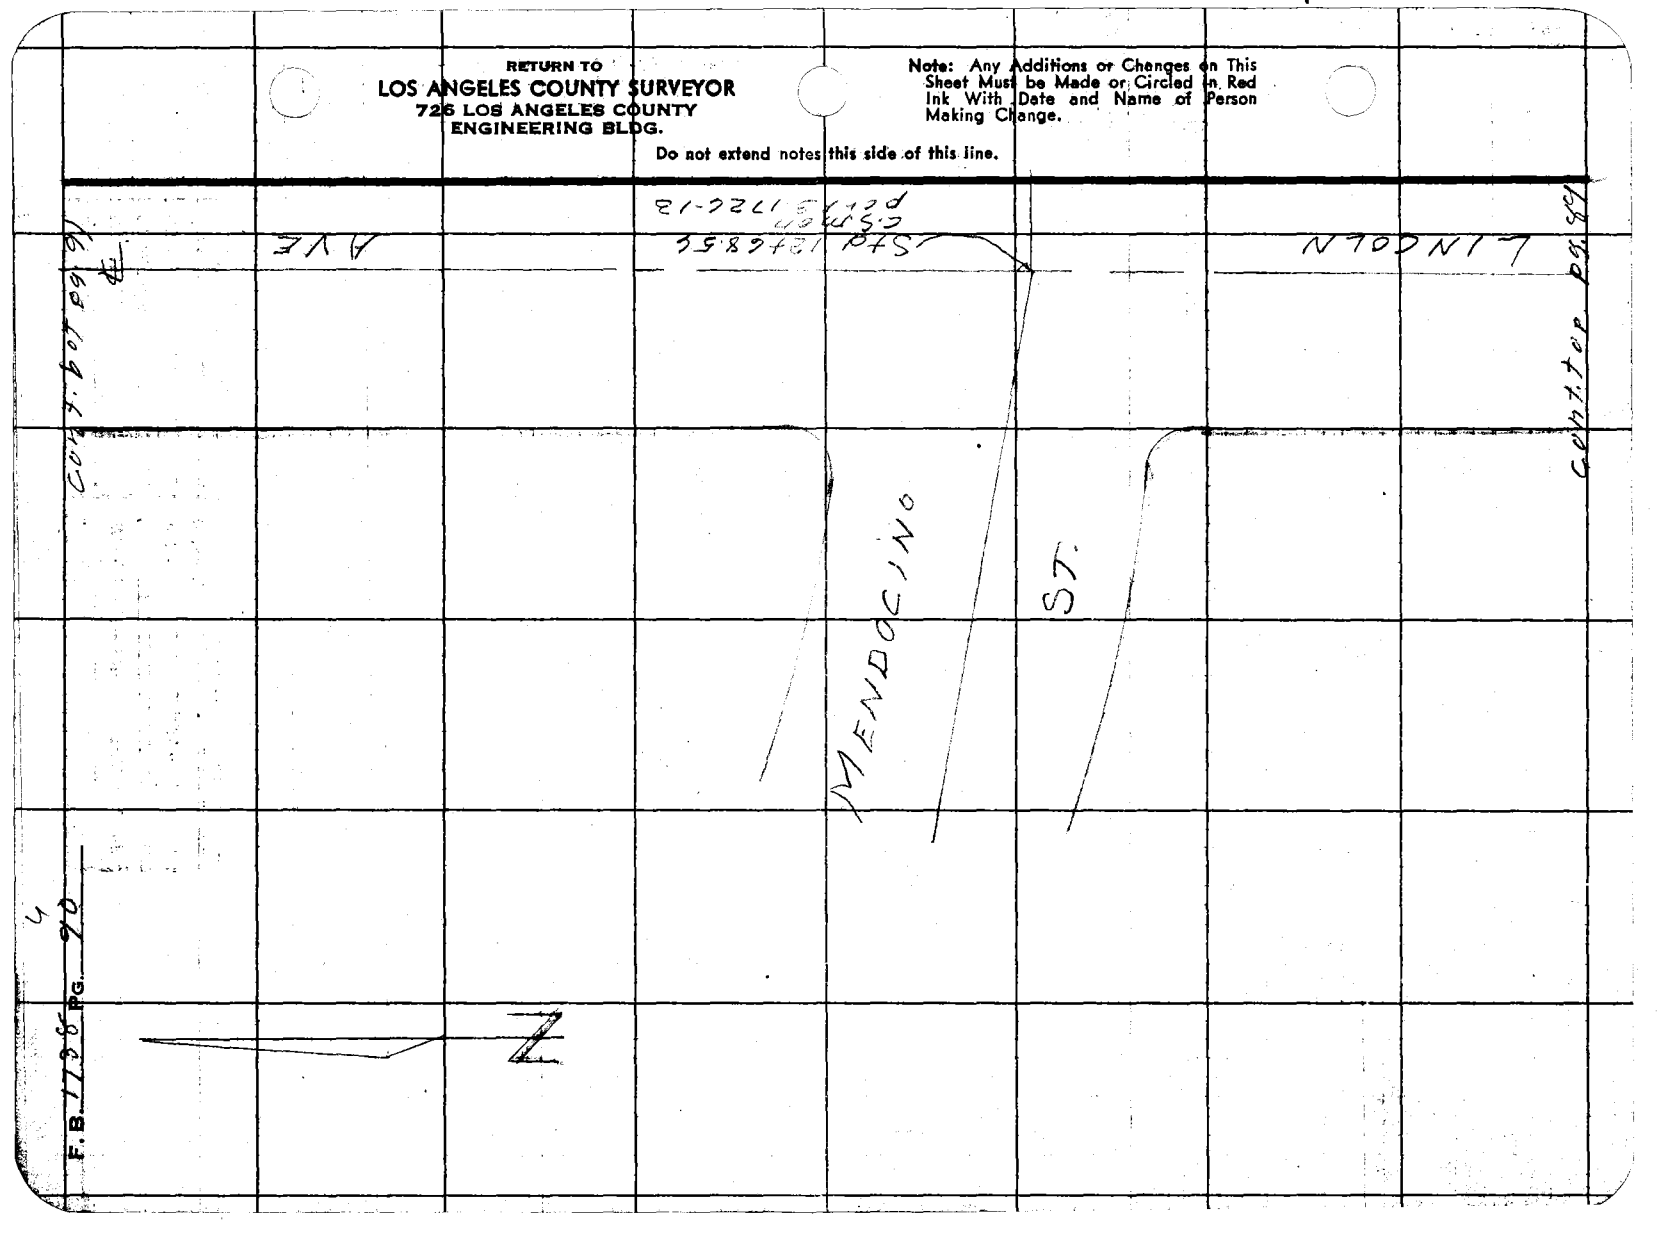

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Garfield Ave
W. O. 1462 Tape No. St'd °F
Surveyed by J. J. L. and Crew
Notes J. J. L. Date 2-15-52
Indexed C. Johnson

F. B. 1735 Pg. 91

-21+877

basement

26.7
46.2
36.1
95.4
#2989

GARFIELD AVE

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

MARIPOSA ST.

Sta 17+53.84
S. W. 1/4
ALLEY
B 1726-14

LINCOLN

76F3095 247 2-51

F.B. 1738 Pg. 92

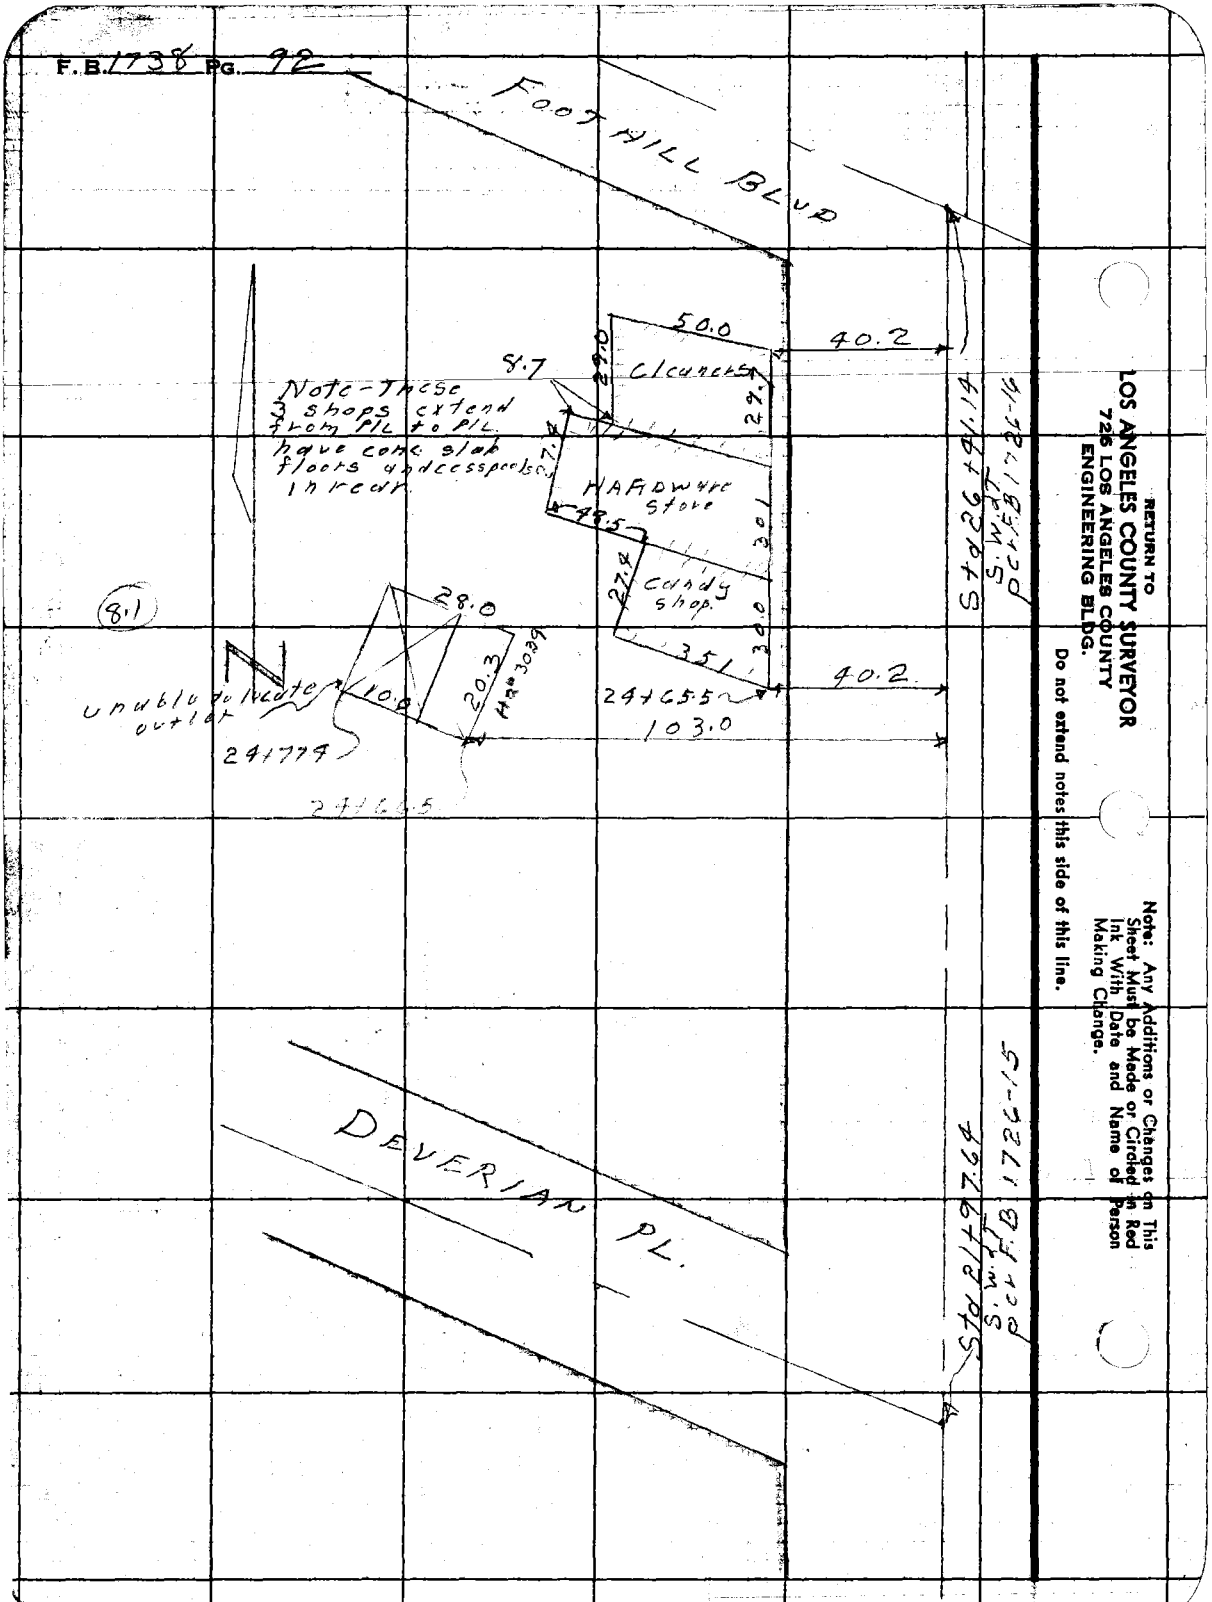

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No. | Notes Red. Date | Plotted Date | Job No. 1462 Division No. | P.S. 1738 P. 9
Notes Cnkd. Date | Checked Date | Survey of Castro Ave | Survey by | Map No. | Date

ELEVATIONS

BASEMENTS and BACK LOT LINES

ON

LINCOLN AVENUE

FROM

ROYCE ST.

to

FOOTHILL BLVD.

C.I 1462

V.V. Lanigan
C.H. Lewis
H.H. Raphael
H.C. Woodworth

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.

761298 307 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

5-7

F. B. 1738 Pg. 94 | Job No. 4242 Z Division No. | Notes Red | Plotted | Profile
Survey of Glassy Ave. | Date | No.
Survey by Lanigan | Notes Levels | Date | Checked | X-Sec.
Indexed C. Johnstone | Date | Notes Chk | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	Lincoln & Ave.
For cross-sections of Lincoln Ave, see notes of C.I. 1256 - Glen Ave.					
BM AE 241	6 27	1151 78		1145 51	AE 241 El 1145.514 FB 1447 P 227 Lincoln Ave. & Royce St. S.W. cor. Bt. spk. in curb 3' S of S. end C.R.
4+30			7 4	1144 4	102'L Basement Floor of Ho # 2503
			2 6	1149 2	SW cor Lot 8 Tr 5823
T. P.			110	1150 68	T. P.
	10 24	1160 92			
			5 6	1155 3	N.W. corner of Lot 5, Tr 5823
6+70			7 5	1153 4	90'L Basement Floor of Ho # 2541
T. P.			018	1160 74	T. P.
	10 50	1171 24	14 2	1157 9	Elev. of 4" C.I. pipe from basement
7+40			14 4	1156 8	90'L Basement floor Ho # 2555
9+50			9 7	1161 5	125'L " " " 2583
T. P.			2 56	1168 68	T. P.
	6 13	1174 81			
10+40			4 1	1170 7	100'L
"			3 2	1171 1	162'L
			3 5	1171 3	230'L

761.398 307 4-80

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. 1446 Division No.____
No. 2564 Date____ Date____ Survey of Cost
Notes Chkd.____ Date____ Checked____ Survey by____
No.____ Date____ Date____ Map No.____ Inked____

F. B. 7382 Pg. 95

STATION	B. S.	H. I.	F. S.	ELEV.	Lincoln Ave
		1174 81			℄
T. P.			0 13	1174 68	T. P.
	10 28	1184 96			
T. P.			0 14	1184 82	T. P.
	8 76	1193 58			
0+00	= ℄ int of Ventura St + Lincoln Ave.				
			11 3/4	1182 3/4	?
2+35			4 3/4	1184 3/4	180' L basement floor to Ho # 26 ?
2+60			6 8	1186 8	285' L
T. P			0 41	1193 17	T. P.
	10 08	1203 25			
5+50			6 1	1197 2	100' L
"			6 7	1196 6	200' L
T. P.			0.15	1203 10	T. P.
	10 57	1213 67	7 8	1205 9	
9+40±			4 1	~~1206~~	80± L basement floor to Ho # 228
BM AE238			6 85	1206 82	AE238 El 1206.84 FB 1447 P 22 Lincoln Ave & Harriet St SW corner BT spk in curb 7' S of Sand C.R.

(over)

76L398 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ X-Sec. No. ____
Plotted ____ Date ____ Checked ____ Date ____
Notes Red ____ Date ____ Notes Cked ____ Date ____
Survey of Lincoln Ave. Sta. 10+00 to 25+00 Div. No. ____ Sta. No. ____
Survey by [illegible] Notes by [illegible] Date ____
Indexed ____ Date ____

STATION	B. S.	H. I.	F. S.	ELEV.	Lincoln Avenue
					℄
BM AE 237	7.64	1228.08		1220.44	AE 237 El. 1220.440 FB 1447 P 225. Lincoln Ave. & Mendocino St. S.E. Cor. Bt. spk in curb, 3' E of E end C.R.
11+87 T.P.			12.1	1216.0	200'± L AE 235 El. 1247.694 FB 1447 P 225
			0.20	1227.88	T.P. Lincoln Ave. & Devilla Pl. S.W. corner Bt. spk. in
	10.13	1238.01			
16+35 T.P.			9.4	1228.6	200' L curb, 25' S. of S end C.R.
			0.20	1237.81	T.P.
	11.82	1249.63			
21+14 T.P.			7.3	1242.3	25' N of SW cor. Lot 20, ~~T.P. 6489~~
			3.03	1246.60	T.P.
	8.35	1254.95			
21+85			13.1 ~~6~~	1241.9 ~~1244.1~~	100'± L basement floor to Ho # 2989
			7.1	1247.9	S.W. corner Lot 21 Tr. 6489
24+07			5.63 ~~9~~	1249.27 ~~1245~~ OK	ground at SW corner of Ho # 3039
24+80			9.9	1245.1 OK	115' L basement floor " " "
			3.2	1251.8	ground at SW corner of candy shop
			1.3	1250.7	" " " " " Hardware Sto
			4.3	1250.4	SW. cor. Lot 19 Tr. 6489
BM AE 235			7.25	1247.70	(1247.69)

Notes Ck'd by	Survey of Casitas Ave
Map No.	W. O. 1962 Tape No. St'd °F
Office Work	Surveyed by J. J. Lanigan
Checked	Notes Lanigan Date 2-21-62
Date	C. Johnson
	Indexed

F. B. 123 X Pg. 97

Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION of IMPROVEMENTS on STERLING PL from VENTURA ST to NORTHERLY END of STERLING PL C.T. 1962

J. J. Lanigan
C. H. Lewis
H. H. Raphael
H. S. Woodworth

76F3095 247 2-51

F. B. 1738 Pg. 98

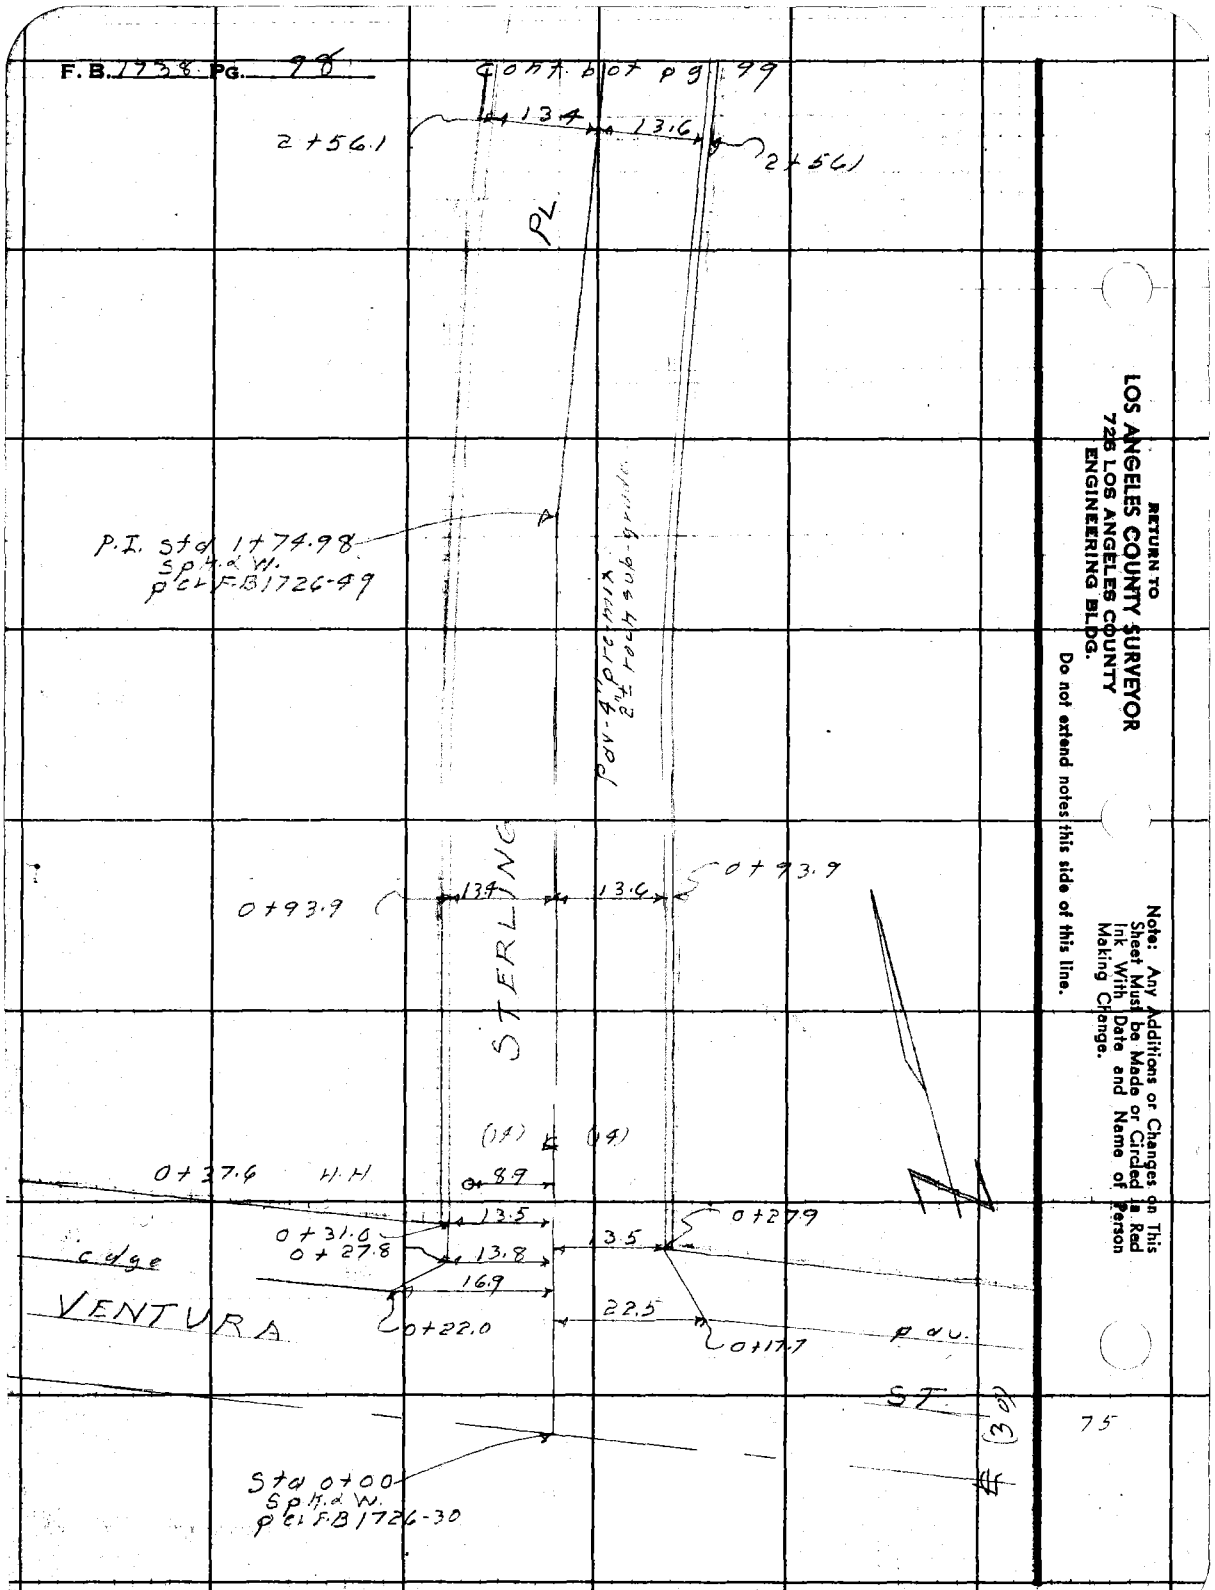

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

75

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Casitas Ave.
W. O. 1422 Tape No. St'd. °F
Surveyed by U.J. Lanigan
Notes 2-27-1952 Date 2-19-52
C. Johnson
Indexed

F. B. 1738 Pg. 99

Cont. on pg. 78

Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

P.L.

Pave - 4" plus or minus
2" ± road-sub-grade

13.6
3+45.1
R=12'
3+33.7
24.7

Sta 3+20.08
W. Sp. Line
per F.B. 1726-50

CALAVERAS

ST.

250
3+06.9
R=12'
13.6
2+94.8

STERLING

Cont. top pg. 78

76F309S 247 2-51

F.B. 1738 PG. 100

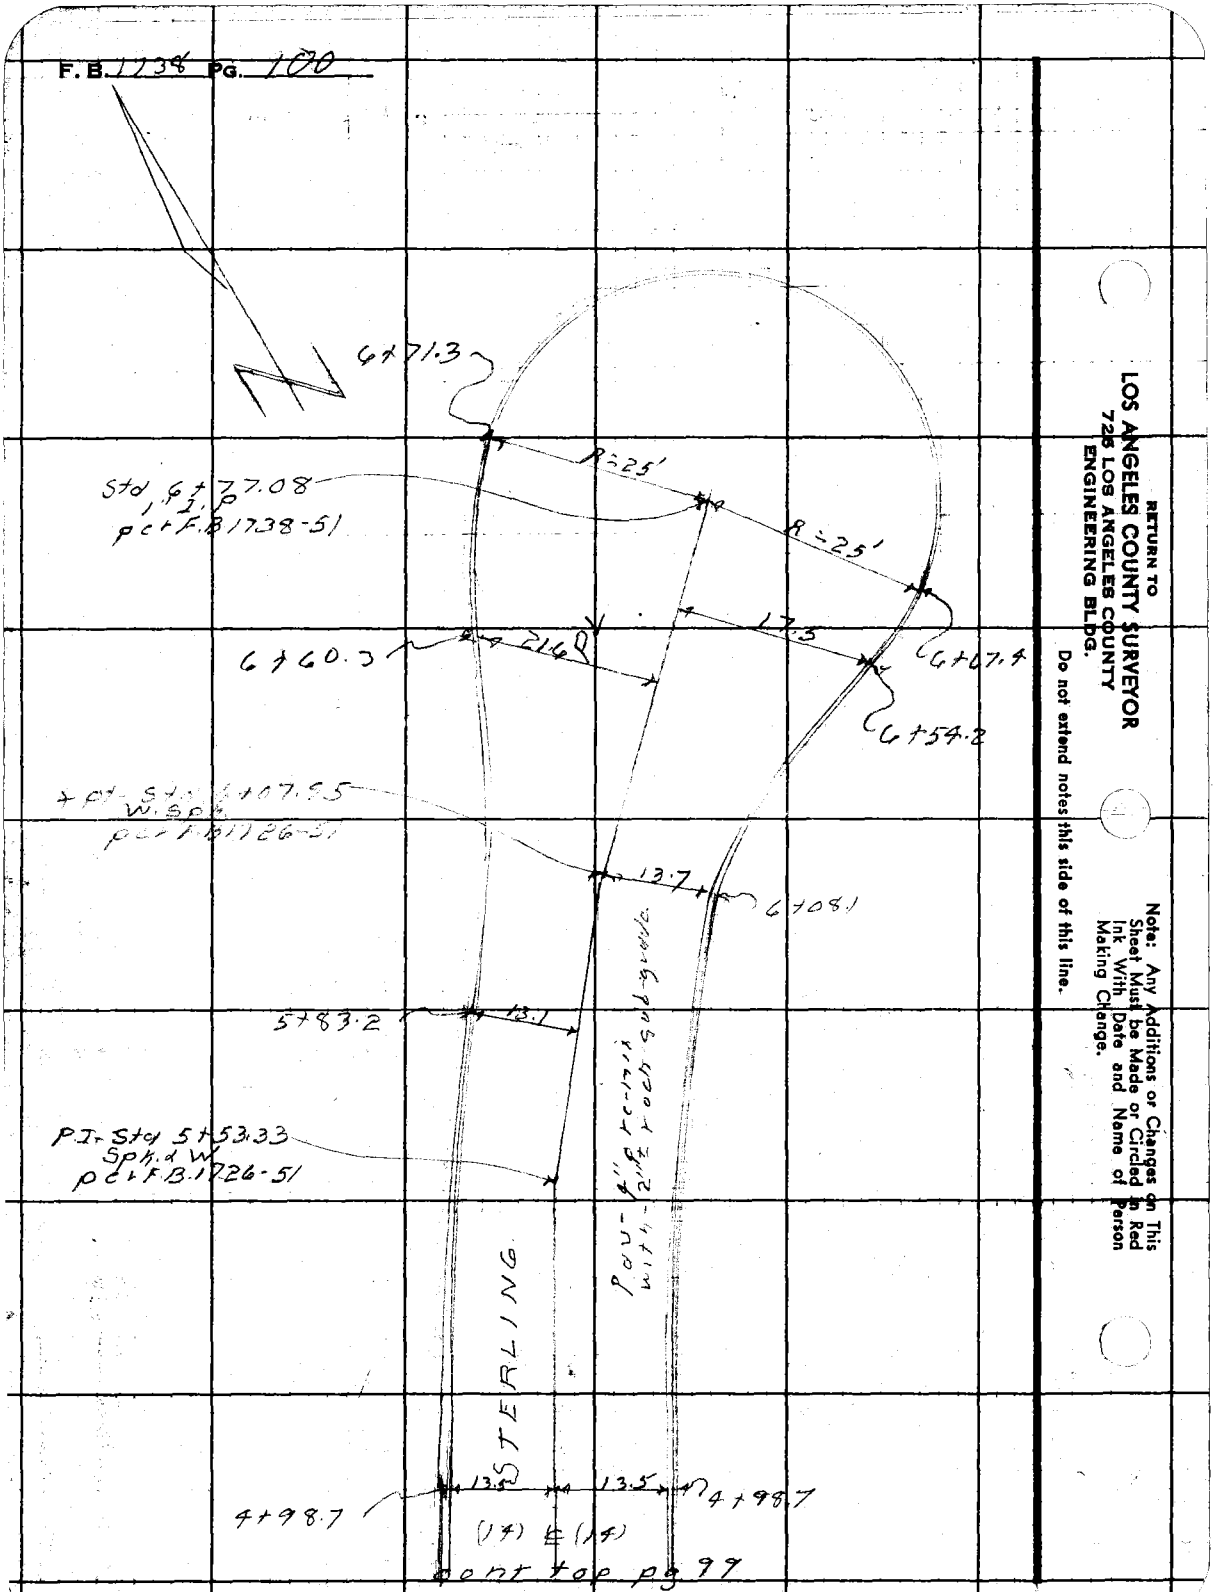

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No. | Notes Red. | Plotted | Job No. 1462 Division No. | F. B. 1738 | Pg. 101

Notes | Date | Date | Survey of Cenitos Hts

Notes Ch[illegible] | Checked | Survey by [illegible] Lewis Date [illegible]

No. | Date 2/27/52 | Date | Map No. | Ind. Ed C. Johnson

PROFILE AND CROSS-SECTIONS

STERLING PLACE

FROM

VENTURA STREET

TO END

C.I. 1462

J.J. Lanigan
C.H. Lewis
H.M. Raphael
H.C. Woodworth

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

764.298 3077 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

P.E. 1936 Pg. 102 | Job No. 1962 Division No. | Notes Red | Plotted | Profile
Survey of Easter Ave. | Date | No.
Survey by Lanigan Notes Louis | Notes Chkd. | Checked | X-Sec.
Indexed C. Johnson Date | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	STERLING	PLACE
BM AE 497	5.16	1173 22		1166.06	AE 497 El 1168.061 Ventura St. & Sterling Pl. NE cor BT spk in curb E of S. end.	FB 1568 P. 134
0+00			6.68	1166.54	℄ int. Sterling Place & Ventura St.	
			7.29	1165.93	75' W'ly on ℄ of	" "
			6.45	1166.77	100' E'ly	
0+04			6.43	1166.79	Crown of pvmt.	℄
0+19.8			6.62	1166.60	Cross-gutter	℄
0+27.9			5.98	1167.24		13.5' R. gutter
"			5.32	1167.90		" cb
0+31			5.78	1167.44	13.5' L gutter	
"			5.24	1167.98	" cb	
"			5.41	1167.81		℄
1+00			4.32	1168.90		℄
"			4.60	1168.62		13.5' R gutter
"			4.15	1169.07		" cb
"			4.54	1168.68	13.5' L gutter	
"			4.12	1169.10	cb	
2+00			2.29	1170.93		℄
"			2.71	1170.51		14' R gutter

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted. Job No. 1462 Division No.
No. Date. Date. Survey of Castle Ave.
Notes Chkd. Date. Checked. Survey by Kenyon & Digert
No. Date. Map No. Inspected C. Johnson Date.

F. B. 1738 Pg. 103

STATION	B. S.	H. I.	F. S.	ELEV.	Sterling	Place
		1173 22				℄
2+00			223	117 099		14⁶ R. cb
"			275	1170 47	12.4 L gutter	
"			228	1170 94	" cb	
T. P.			166	1171 50	T.P.	
	6.96	1178 52				
3+00			548	1173 04		℄
"			594	1172 58	13⁵ L gutter	
"			555	1172 97	" cb	
3+20.08			502	1173 50	℄ int Sterling Pl &	Calaveras St.
			536	1173 16	—	13⁶ R cross gutter
			493	1173 59		25' R bk
			4.46	1174 06	100' E'ly on ℄ of	Calaveras
			5.00	1173 52	" " " S gutter	"
			4.49	1174 03	" " " "	cb "
			4.65	1173 87	" " " N gutter	"
			3.96	1174 56	" " " "	cb "
			6.01	1172 51	gutter s end S ℄	cb ret
			5.60	1172 92	cb " "	" "
			5.55	1172 97	gut. E "	" "
			5.05	1173 47	cb " "	" "

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 1738 Pg. 104 Job No. 1462 Division No. Notes Red. Plotted Profile No.
Survey of Castle St. Ave. Date Date No.
Survey by Lanigan Notes Lewis Notes Chkd. Checked X-Sec.
Indexed C. Tabancon Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	Sterling	Place
		1178 52				℄
			4 81	1173 71	gutter E. end	NE cb. ret.
			4 32	1174 26	cb " "	" " "
			4 88	1173 64	gut. N "	" " "
			4 39	1174 13	cb " "	" " "
3+40			4 ±	1174 5	100'± L	
T. P			3 60	1174 92	T. P.	
	12 23	1187 15				
4+00			11 82	117.533		℄
"			12 19	1179 96		13± R gutter
"			11 78	1175 37		" cb
"			12 33	1177 82	13± L gutter	
"			11 90	1175 25	" " cb	
5+00			9 41	1177 79		℄
"			9 93	1177 22		13± R gutter
"			9 40	1177 75		" cb
"			9 91	1177 29	13± L gutter	
"			9 50	1177 65	" cb	
6+00			7 09	1180 06		℄
"			7 63	1179 52		13± R gutter
"			7 06	1180 09		" cb

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. 4462 Division No.
No. Date Date Survey of Cadillac
Notes Chkd. Checked Survey by
No. Date Date Map No. Indexed

STATION	B. S.	H. I.	F. S.	ELEV.	Sterling	Place
		1187 15				℄
6+00			750	1179 65	13.4 L gutter	
"			706	1180 09	" cb	
6+96.3			473	1182 42		℄ gutter
"			429	1182 86		℄ cb
6+80			4.4	1182 8	100' L	
BM AE 499			439	1182 74	AE 499 El 1182.787 FB 1568 P 13	
					Sterling Place at N end of ℄	
					Bt spk in cb 12'± W of ℄ Pl	

F. B. 1738 P. 16

F. B. 1738 Pg. 106

Job No. 1438 Division No. Notes Red Plotted Profile

Survey of Casitas Ave. Date Date No.

Survey by Flanigan Notes Lewis Notes Chkd. Checked X-Sec.

Indexed Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.

764.298 307 4-50

PLEASE RETURN TO.

LOS ANGELES COUNTY SURVEYOR

726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK. WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Notes Ck'd by	Survey of Calaveras Ave.
Map No.	W. O. 1265 Tape No. St'd. °F
Office Work	Surveyed by J. J. Lanigan
Checked	Notes Lanigan Date 8-14-52
Date	Indexed C. Johnson

F. B. 1238 Pg. 107

Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION of IMPROVEMENTS on CALAVERAS ST from STERLING PL to EASTERLY LINE R.S. 17-33 C.I. 1462

76F309S 247 2-51

F. B. 1726 PG. 108

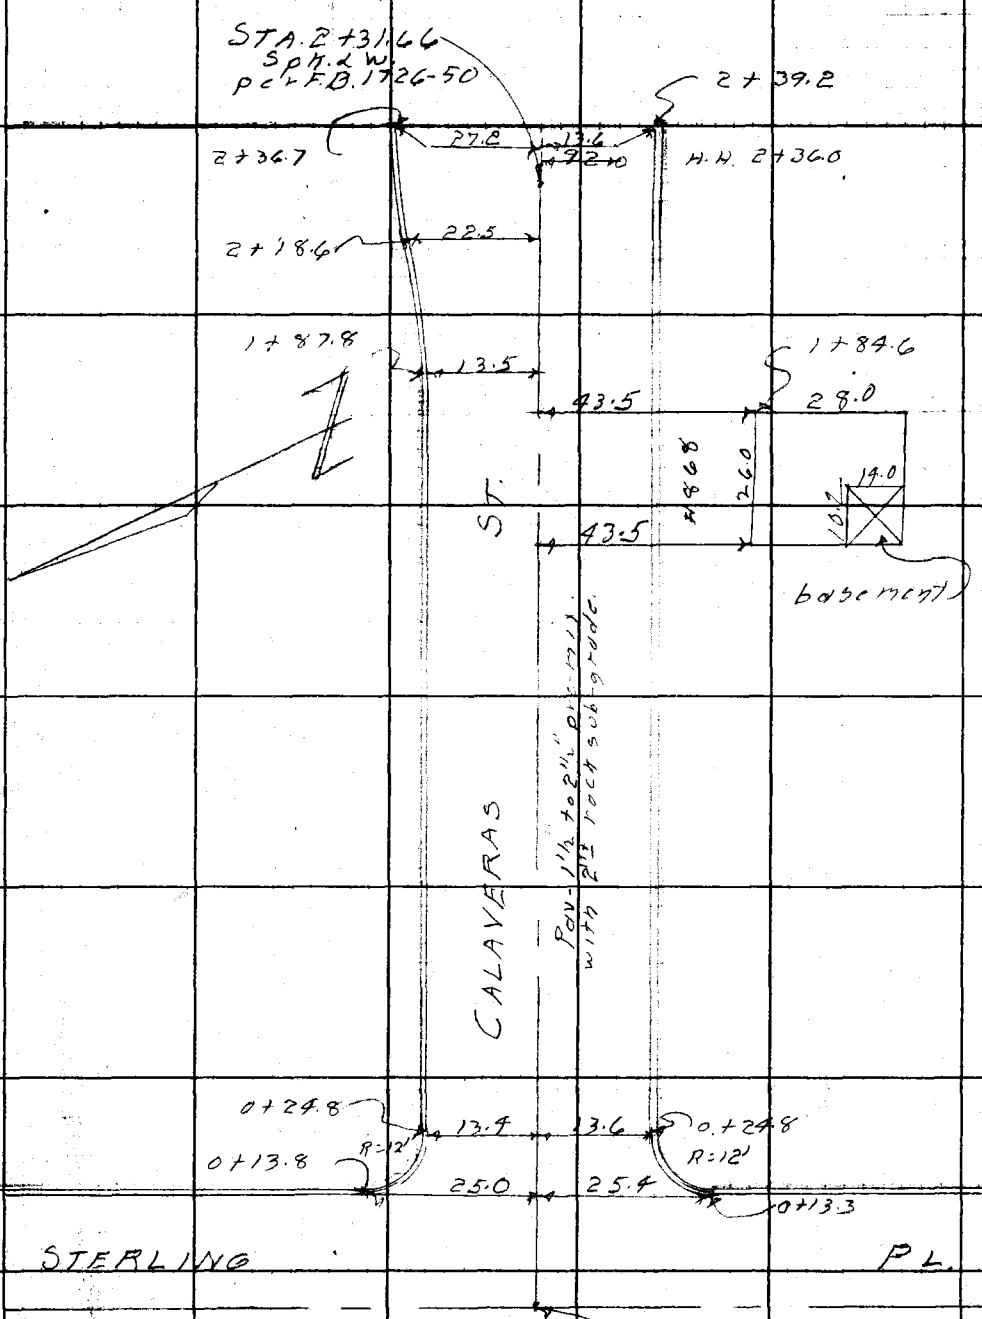

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No. | Notes Red. | Plotted | Job No. 1462 | Division No. | F. B. 1738 | Pg. 109
Sec. No. | Date | Date | Survey of Calaveras
Notes Chkd. ECH | Checked | Survey by Lewis & Notes Rec'd | Date
Date 2/27/52 | Date | Map No. | Indexed C. Johnson | Date

PROFILE AND CROSS-SECTIONS

CALAVERAS STREET

FROM

STERLING PLACE

TO

EASTERLY LINE OF R.S. 17-33

C.I. 1462

J. V. Lanigan
C. H. Lewis
H. H. Rappaport
H. C. Woodworth

STATION	B. B.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

741-298 307 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 10 38 Pg. 10
Job No. 1442 Division No. Notes Red. Plotted Profile
Survey of Calistoga Ave. Date No.
Survey by Leggett & Lewis Notes Chkd. Checked X-Sec.
Indexed C. Fontana Notes Date Date No.
Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	Calaveras	Street
					℄	
BM AE 498	539	1178.37		1172.98	AE 498 E/ 1172.979 FB 1568 P 134 Sterling Place (W side) at Calaveras St. BT Sph in curb 18'S of ℄ prod of Calaveras St	
0+00			4.86	1173.51	℄ Int. Calaveras Sta	Sterling Pl.
			7.09	1171.28	100' S 17th ¼ on ℄ of	" "
			7.55	1170.82	" " " W gutter	" "
			7.08	1171.29	" " " " cb	" "
			7.55	1170.82	" " " E gut.	" "
			7.06	1171.31	" " " " cb	" "
			2.43	1173.94	" N 17th ¼ " ℄	" "
			3.07	1173.30	" " " W gutter	" "
			2.56	1173.81	" " " " cb	" "
			2.85	1173.52	" " " " gut	" "
			2.38	1173.99	" " " " cb	" "
			4.72	1171.65	gutter N end NE cb ret	
			4.22	1172.15	cb " " " " "	
			4.65	1171.72	gutter E " " " "	
			4.16	1172.21	cb " " " " "	

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Calculations	St.
		1178 37				
			538	117299	gutter End	S.E. cb. rot.
			489	117398	cb. " "	" " "
			584	117253	gut. " "	" " "
			546	117291	cb. " "	" " "
0+13.5			517	117320		℄ cross gutter
0+25			470	117367		℄ bk.
1+00			431	117406		℄
"			484	117353		13.5 R gutter
"			433	117404		13.5 R. cb
"			450	117387	13.5 L gutter	
"			381	117456	13.5' L. curb	
T. P.			380	117457	T. P.	
	5.53	1180 10				
2+00			555	117455		℄
"			586	117429		13.5 R gutter
"			539	117471		13.5' R cb
"			87	11719		150'± R back Lot Line
"			557	117459	18' L gutter	
			496	117519	18' L cb.	

Profile Notes Red. Plotted Job No. 1462 Division No. F. B. 1238 Pg. 111
No. Date Notes Chkd. Date Survey of
No. Date Checked Date Survey by Notes Date
No. Date Map No. Indexed Date

76L298 307 4-56

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 17384 Pg. 112 Job No. 1462 Division No. V Notes Red Plotted Profile
Survey of Calistas Ave. Date No.
Survey by Lanigan Notes Lewis Notes Chkd Checked X-Sec.
Indexed C. Johnson Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	Calavetas	St.
		1180.10				
2+28			521	1174.89	27'L gutter	
"			475	1175.35	" cb	
2+39			540	1174.70		℄
"			557	1174.53		13'SR gutter
"			512	1174.98		" cb.
BMAE 533			526	1174.84	BMAE 533 Elev. 1174.830 FB 156 6-156 Calavetas St. (S. side) 220'± E. of ℄ of Sterling Pl. BT. 6 PM. in C & G.	

Notes Ck'd by	Survey of Casitas Ave.
Map No.	W. O. 462 Tape No. St'd. °F
Office Work	Surveyed by J.J. Lonigan
Checked	Notes J Lonigan Date 2-20-62
Date	Indexed C. Johnson

F. B. 1736 Pg. 112

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
720 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
of
IMPROVEMENTS
on
CRESTFORD DR
from
WESTERLY END of STREET IN TR# 12677
to
MARIPOSA ST
C.I. 1962

J.J. Lonigan
C.H. Lewis
H.H. Raphael
H.S. Woodworth

76FSOS 247 2-51

F. B. 1738 PG. 114

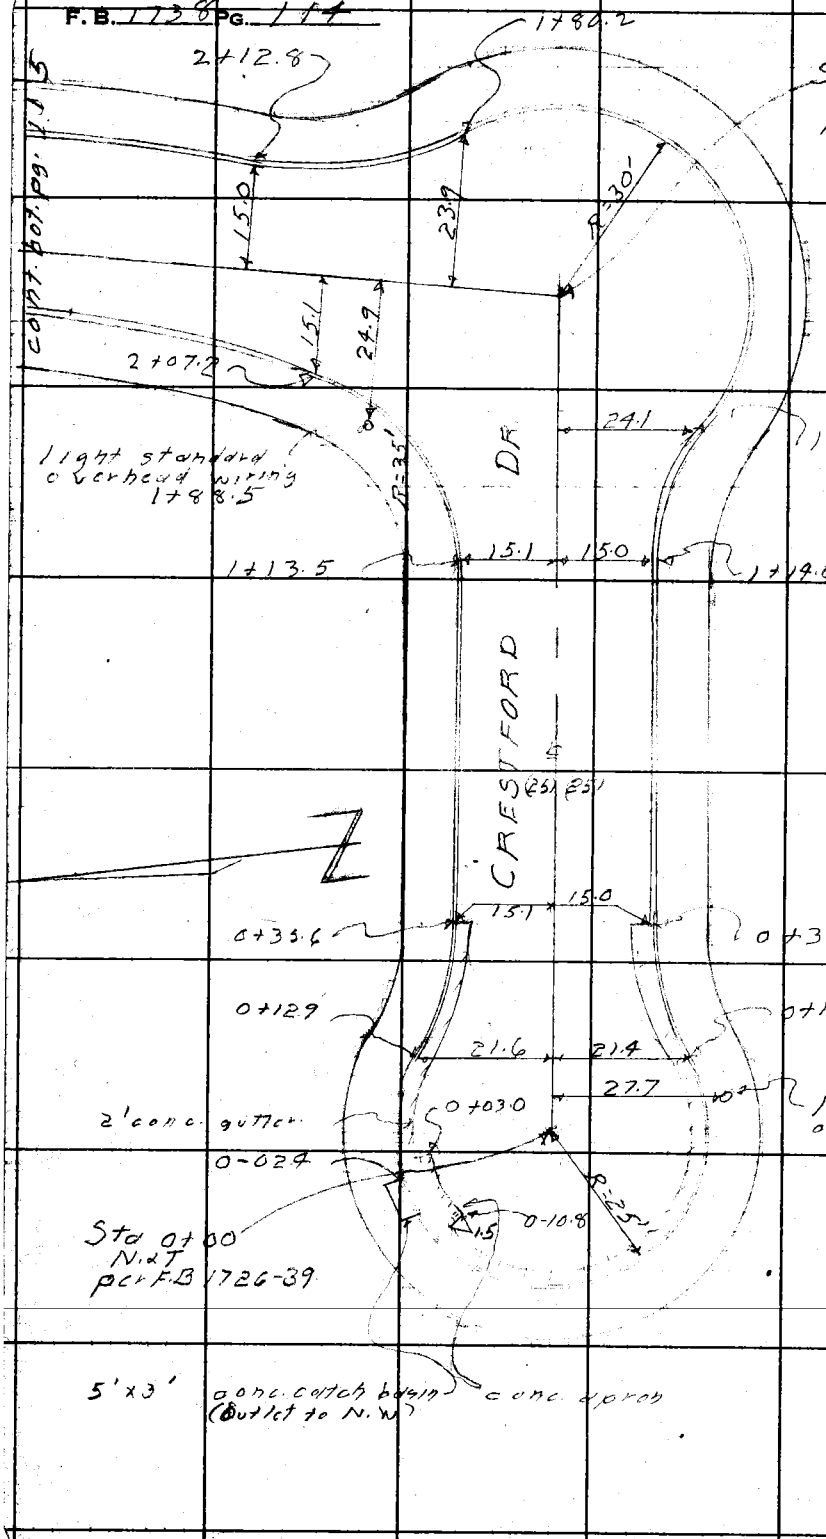

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Station Ck'd by
Map No.
Office Work
Checked
Date

Survey of Crestford Ave.
W. O. 1462 Tape No. St'd. °F
Surveyed by J. V. Lanigan
Notes Lanigan Date 2-20-52
C. John
Indexed

F. B. 1738 Pg. 1-15

cont. for pg. 1146

4+30.9 — 15.1 — 15.0 — 4+30.1

P.I. Sta 3+87.21
S.P.H.A.W.
P.C.C. F.B. 1726-38

DR.

3+45.9 — 14.9 — 14.9 — 3+44.4

(25) ℄ (25)

3+00.8 — 15.1 — 15.0 — 2+87.2

P.I. Sta 2+49.23
S.P.H.A.W.
P.C.C. F.B. 1726-38

CRESTFORD

N

Note: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76F3095 247 2-51

cont. for pg. 1144

F. B. 1739 PG. 116

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

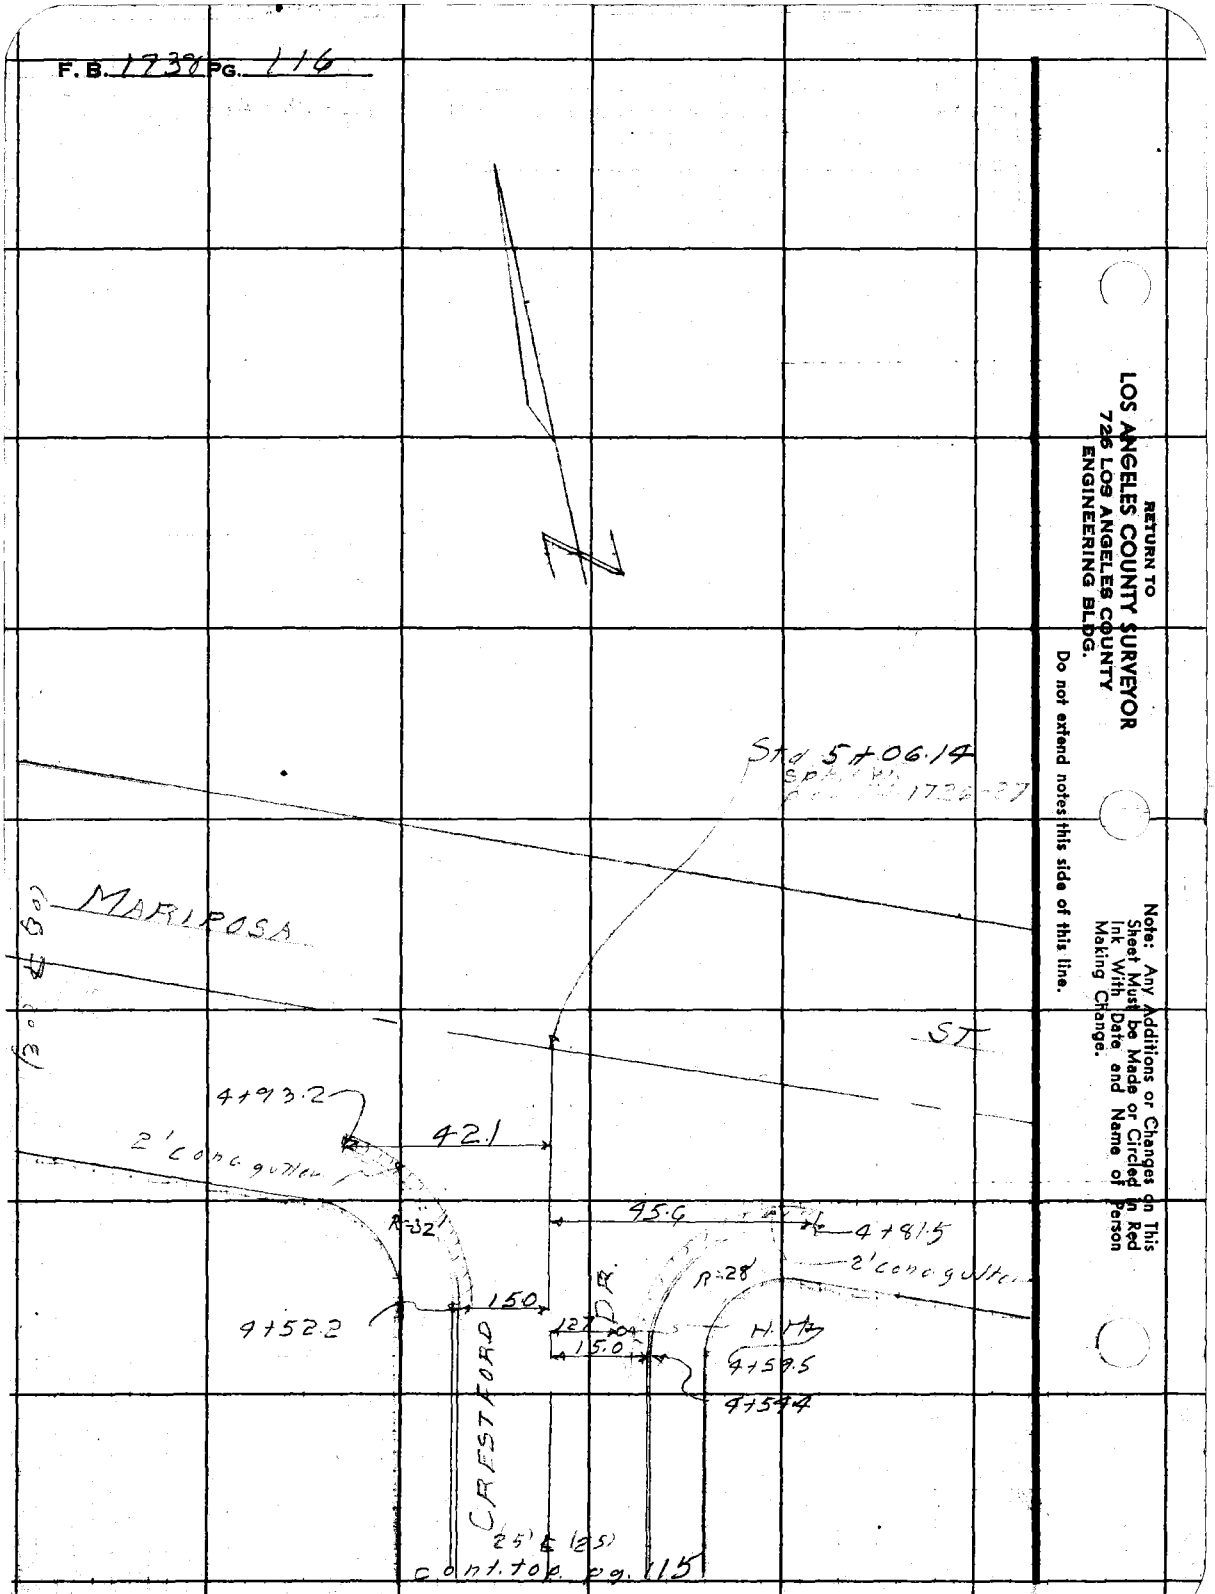

Profile No. | Notes Red. Date | Plotted Date | Job No. 1462 Division No. | F. B. 1738 Pg. 1-7
Survey of County Surveyor
Notes Chkd. [illegible] Checked | Survey by [illegible]
No. | Date 2/27/52 Date | Map No. | Indexed C. Johnson

PROFILE AND CROSS-SECTIONS

CRESTFORD DRIVE

FROM

WESTERLY END of STREET IN TR #12677

TO

MARIPOSA STREET

C.I. 1462

J.J. Lanigan
C.H. Lewis
H.H. Raphael
H.C. Woodworth

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend notes this side of this line.

761298 307 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 1738 Pg. 118 | Job No 4462 Division No. | Notes Red. | Plotted | Profile
Survey of Castles Lake | Date | No.
Survey by Lewis & Gow | Notes Chkd. | Checked | X-Sec.
Indexed C. Johansen Date | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	Crestfold Drive
					℄
BMAE500	5.78	1200.14		1194.36	AE500 El 1194.363 FB 1-68 P 135- Crestfold Dr. at W. end of street BT spk in curb 1' N of ℄ prod
6+00			5.88	1194.26	℄
0-25			6.48	1193.66	gutter ℄ prod w/y
"			5.79	1194.35	" cb ℄ " "
-1+25			6.4	1192.7'	℄ " "
1+00			4.68	1195.46	℄
"			5.01	1195.13	15' R gut
"			4.40	1195.74	" cb
"			4.0	1196.1	75' R
"			4.93	1195.21	15' L gut
"			4.41	1195.73	" cb
2+00			3.04	1197.10	℄
"			2.87	1197.27	16' R gut
"			2.20	1197.94	" cb
"			3.58	1196.56	16' L gut
"			3.03	1197.11	" cb

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red Plotted Job No. 4462 Division No.
No. Date Date Date Survey of Crestcourt Drive
No. Date Date Map No. Indexed C. Jacobsen
F. B. 773 & Pg. 112

STATION	B. S.	H. I.	F. S.	ELEV.	Crestcourt Drive
		1200 14			℄
T.P			1 98	11981 C	T.P.
	10 76	1208 92			
3+00			9 30	11996 2	℄
"			9 39	11995 3	15 R gutter
"			8 78	12004	" " cb.
"			9 95	11989 7	15' L gutter
"			9 29	11996 3	" " cb
4+00			6 67	12022 5	℄
"			6 82	12021 0	13 5 R gutter
"			6 16	12027 6	" " cb
"			7 30	12016 2	16 5 L gut
"			6 71	12022 1	" " cb
5+06.14			4 35	12045 7	℄ int Crestcourt Drive & Tobiasa St
4+87			5 25	12036 7	℄ cross gutter
			2 95	12059 7	100' E'ly on ℄ of Tobiasa St
			5 37	12035 5	" W'ly " " " " "
			5 55	12033 7	gut W. end SW cb inlet
			4 91	12040 1	cb " " " " "
			5 74	12031 8	gut S " " " " "
			5 06	12038 6	cb " " " " "

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 1738 PG 120 Job No. 1432 Division No. Profile
Survey of Castle Ave. Notes Red Plotted No.
Survey by Lanigan Notes Date Date X-Sec.
Indexed C. Johnson Date Notes Chkd. Checked No.
Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	Crestford Drive ℄
		1208.92			
			5.36	1203.56	gut. S end S.E. cb ret.
			4.75	1204.17	cb " " " " "
			4.48	1204.44	gut E. " " " "
			3.86	1205.06	cb E. " " " "
					Changes in green JH 2/26/53
BM AE501			5.25	1203.67	AE501 El 1203.646 FB 1568 P 135 Crestford Dr. & Mariposa St., S.W. cor. Bt. spk. in curb 6'S of S. end C.R.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Castlos Ave.
W. O. 146 Tape No. St'd. °F
Surveyed by J. J. Lanigan
Notes Lanigan Date 2-20-52
Indexed C. Johnson

F. B. 173 Pg. 121

Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
of
IMPROVEMENTS
on
RIDGEVIEW DR
from
MARIPOSA ST
to
FOOTHILL BLVD
C.I. 1962.

J. J. Lanigan
C. H. Lewis
H. H. Raphael
H. S. Woodworth

76F3095 247 2.51

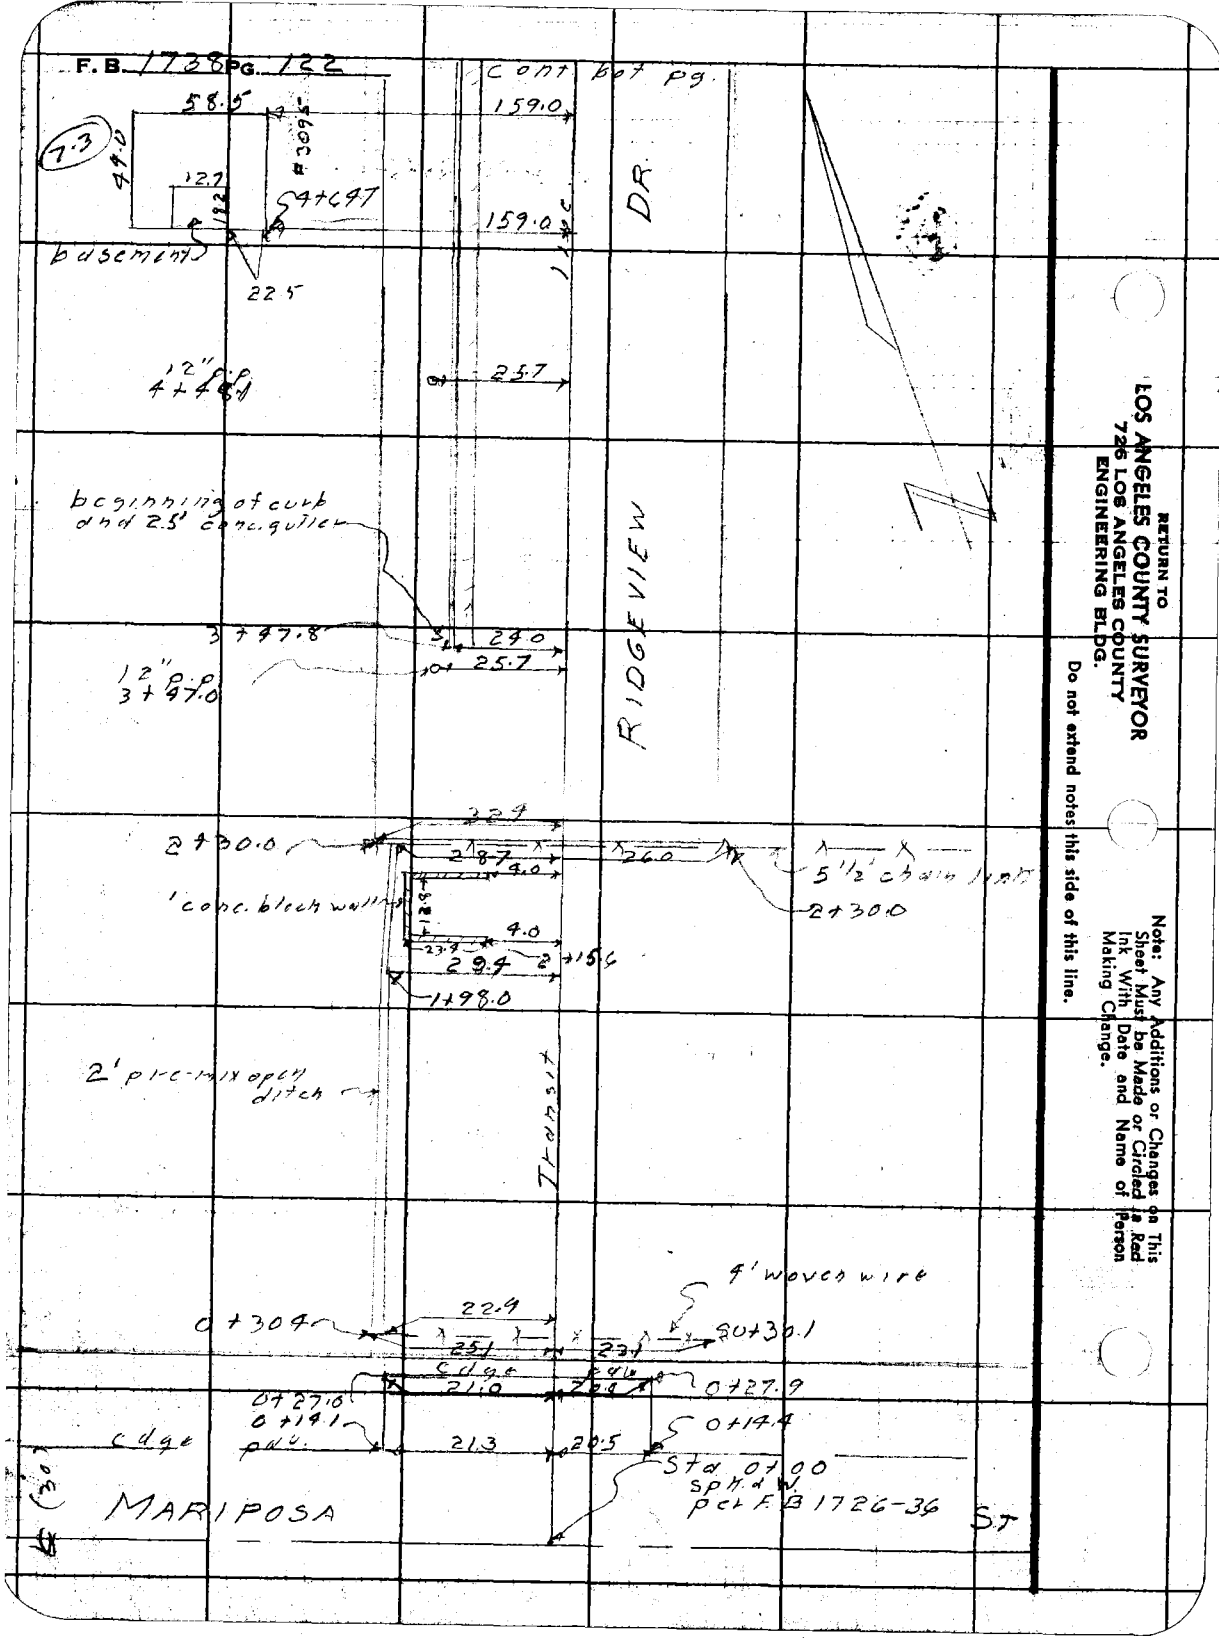
F. B. 1738 PG. 122
cont bot pg.
58.5
159.0
49.0
#309
12.7
12.2
94+69.7
159.0
DR.
basement
22.5
4'12" C.P.
4+48.4
25.7
beginning of curb
and 2.5' conc. gutter
3+97.8
2.40
25.7
12" C.P.
3+97.0
RIDGE VIEW
22.9
2+30.0
21.8.7
26.0
4.0
5 1/2" chain link
2+30.0
1' conc. block wall
4.0
23.9
29.9
2
15.6
1+98.0
2' p-c-c-mix open ditch
THOMAS ST
4' woven wire
0+30.4
22.9
25.1
23.1
30+30.1
edge
21.0
0+27.9
0+27.0
0+19.1
edge
pvt.
21.3
20.5
0+14.4
Sta 0+00
Sp. in W.
pc of B 1726-36
MARIPOSA
ST.
RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.
Do not extend notes this side of this line.
Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Casitas Inc.
W. O. 1962 Tape No. St'd. *F
Surveyed by J. J. Lanigan
Notes Lanigan Date 2-20-52
C. Johnson
Indexed

F. B. 138 Pg. 125

Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

S 48° 13' 00" E

FOOT HILL 7+93.2

7+93.2 BLVD

7+93.6

edge pav.

17.9

30.4

55.0

5.8

12.0

17.3

17.2

7.0

7+85.8

7+79.6 h.h.

7+74.9

7+76.9

12" p.p. 7+55.7

26.0

DR

LANE

25.6

12" p.p. 7+51.8

UNIMPROVED

(5.5)

Swimming pool

6+02.0

24.0

12.0

49.5

49.5

TYLER

RIDGEVIEW

end of curb and 2.5' conc. gutter 5+48.9

8" p.p. 5+47.4

24.0

25.6

conc. top sq.

N

76F3095 247 2-51

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

F.B. 1736 P. 124

Profile No. ____ Notes Red. ____ Date ____ Plotted ____ Date ____ Job No. 1462 Division No. ____ Survey of Ridge View

No. ____ Date 2/27/52 Date ____ Map No. ____ Indexed ____ Date ____

F. B. 1738 Pg. 125

PROFILE OF RIDGE VIEW

FROM MARIPOSA STREET TO FOOTHILL BLVD.

C.I. 1462

V.V. Lanigan
C.H. Lewis
H.H. Raphael
H.C. Woodworth

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

76L298 307 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 1738 Pg. 126 Job No. 1462 Division No. Profile
Survey of Cashio Ave. Notes Red No. Plotted
Survey by Lanigan & Jaramillo Notes Chkd. Date X-Sec.
Indexed A. C. Jaramillo Date Date Checked No.
Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	Ridgeview	Drive
						℄
BM AE 502	6.22	1208.69		1202.47	AE 502 El. 1202.466 FB. 1568 P. 136 Mariposa St. (S. side) at W. end of Street Bt. spk in W. end of conc. catch basin	
0+00			4.78	1203.91	Int. of Mariposa St ℄ & ℄ prod. of Ridgeview	
			3.62	1205.07	100' E'ly on ℄ of Mariposa St.	"
			6.01	1202.68	" W'ly " " "	"
0+14			4.72	1203.97		℄ Cross gutter
"			4.51	1204.18		23' R
"			4.92	1203.77	24' L	
0+30			3.7	1205.9		℄
"			3.8	1204.9		23' R
"			3.25	1205.44	23' L top of ditch wall at end	
"			4.32	1204.37	24' L bot of ditch	
1+00			2.0	1206.7		℄
"			1.8	1206.9		25' R
"			1.75	1206.94	24.5 L top of ditch wall	
"			2.90	1205.79	25.5 " bot of ditch	
T. P.		1214.38	0.68	1204.01	T. P.	
	6.37					

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. 4462 Div. No. F.B. 7238 Pg. 127
No. Date Date Survey of Ridge View Drive
No. Date Map No.

STATION	B. S.	H. I.	F. S.	ELEV.	Ridge View Drive
		1214 38			℄
2+00			5 4	1209 0	℄
"			5 3	1209 1	30' R
"			5 27	1209 11	30' L
"			6 42	1207 96	bot ditch
2+30			4 66	1209 72	Top of ditch wall at end
"			5 85	1208 53	bot of ditch at end
T.P.			3 55	1210 83	T.P.
	7 54	1218 37			
3+00			8 0	1210 4	℄
"			7 1	1210 7	30' R
"			8 0	1210 4	30' L
3+48			7 55	1210 82	24' L gutter at beginning
"			6 88	1211 49	" cb " "
4+00			6 1	1212 3	℄
"			5 5	1212 9	30' R
"			6 74	1211 63	14' L gutter
"			6 05	1212 32	" cb
4+75			8 1	1210 3	185' L basement floor to HO* 10.2
5+00			4 2	1214 2	℄
			4 0	1214 4	30' R

76L298 307 4-56

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

12 21
13 2

Do not extend notes this side of this line.

F. B. 1738 Pg. 128 Job No. 1462 Division No. Profile
Survey of Castro Ave. Plotted No.
Survey by Lewis Notes Red Date X-Sec.
Indexed Date Notes Chkd Checked No.
Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	Ridgeview	Drive
		1218 37				℄
5+00			5 00	1213 37	24'L gutter	
"			4 38	1213 99	cb	
5+48			4 12	1214 25	24'L gutter at end	
"			3 47	1214 90	" cb " "	
6+00			2 2/10	1216 2/4		℄
"			2 0	1216 4		25' R
"			2 6/10	1215 8/10	24'L	
T. P.			0 16	1218 21	T. P.	
	12 31	1230 52				
6+02			19 2/10	1211 3/10	50'L invert of swimming pool	
7+00			11 9/10	1218 6/10		℄
"			11 7/10	1218 8/10		25' R
"			11 8/10	1218 7/10	24'L	
7+80			4 89	1225 63		℄
"			5 2/10	1225 3/10		25' R
"			4 8/10	1225 7/10	24'L	
7+98			5 72	1224 80		℄ CROSS gutter
"			5 88	1224 64		25' R.
"			5 62	1224 90	24'L	

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. 1442 Division No.
No. Date Date Date Survey of Ridgeview Drive
No. Date Date Date Survey by [illegible] & C. Johnson
F.B. 1238 Pg. 129

STATION	B. S.	H. I.	F. S.	ELEV.	Ridgeview Drive
		1230 52			
8+13.60			5 00	122552	℄ int. of Ridgeview Dr & Foothill Blvd
			6 11	122441	100' Easterly on ℄ of " "
			5 46	122506	" " " N gut. of " "
			4 80	122572	" " " " cb " "
			4 17	122635	" W'ly " ℄ " "
BM AE 230			3 66	122680	AE 230 El. 1226.864 AB 1447 P 223 Foothill Blvd & Crestford Dr. NW. cor. Bt. spk. in curb 2' N of N end C.R.

F. B. 1728 Pg. 130 Job No. 1462 Division No. Notes Red. Plotted Profile

Survey of Casitas Ave. Date Date No.

Survey by Lanigan Notes Lewis Notes Chkd. Checked X-Sec.

Indexed Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	

Do not extend notes this side of this line.

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR

726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

76L298 307 4-50

F. B. 17-8 Pg. 131

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Casilla Ave
W. O. 1962 Tape No. St'd °F
Surveyed by J. J. Lanigan
Notes Lanigan Date 2-21-52
Indexed C. Johnson

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION of IMPROVEMENTS on WINDSOR AVE. from SOUTHERLY LINE OF TRACT # 7950 to VENTURA ST C.I. 1962

J. J. Lanigan
O. H. Lewis
H. H. Raphael
H. S. Woodworth

76F3095 247 2-51

F.B. 1738 PG. 132 cont. bot. pg. 133

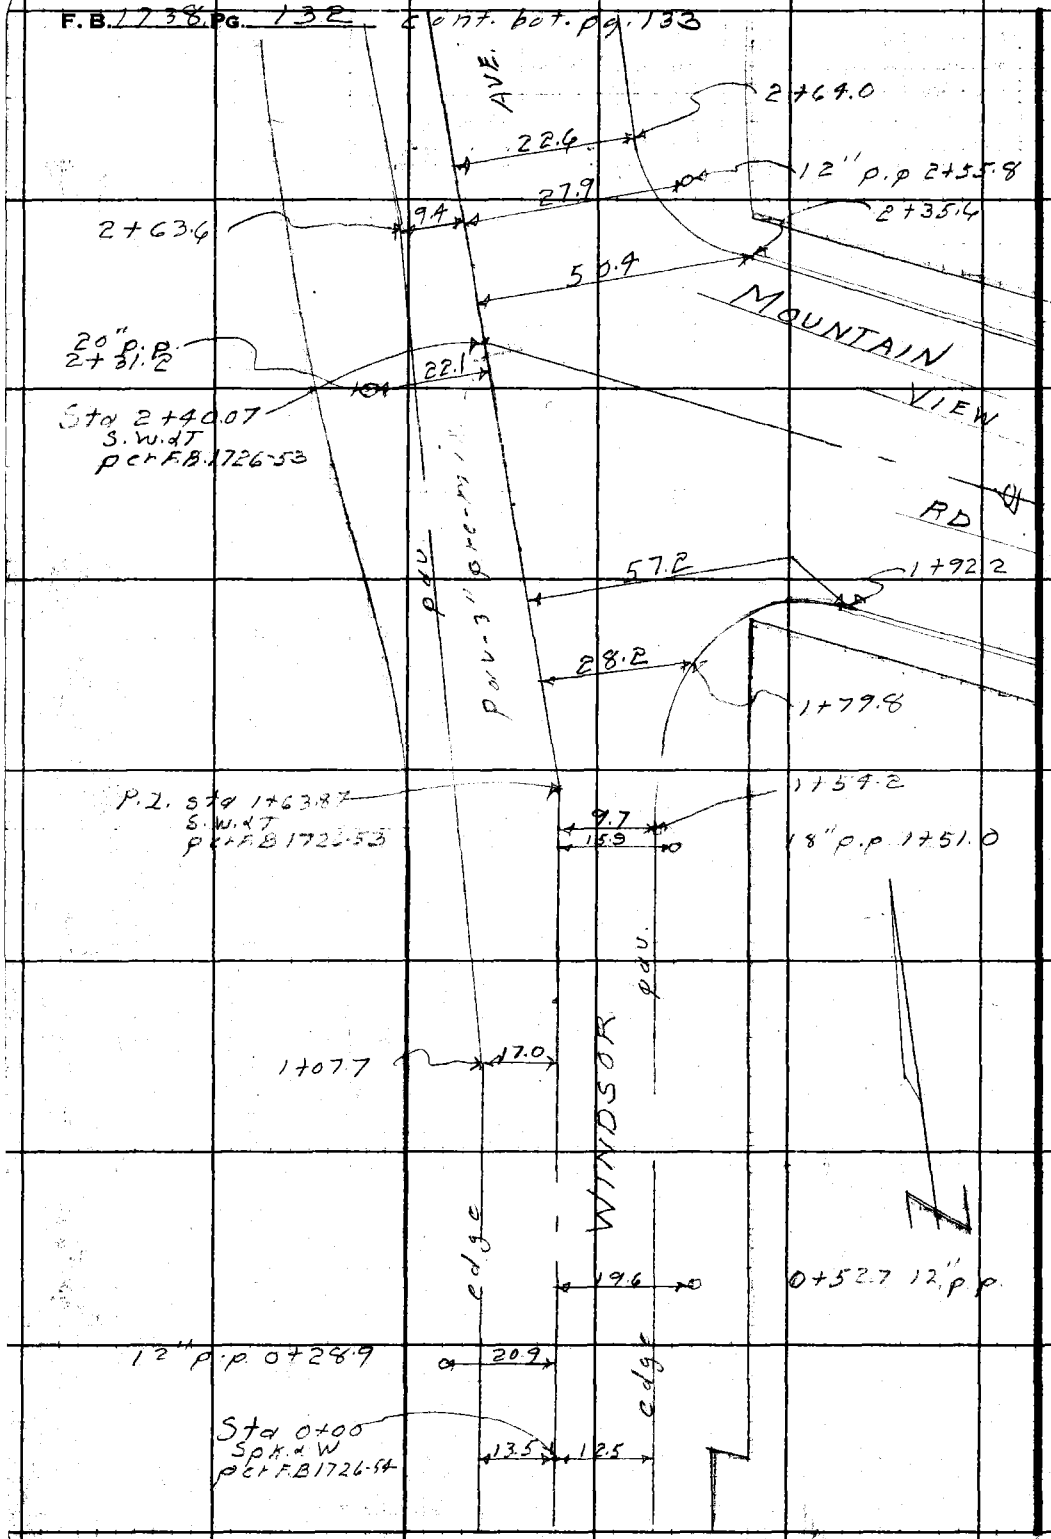

RETURN TO
LOS ANGELES COUNTY SURVEYOR
.726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Cortez Ave.
W. O. 962 Tape No. St'd. °F
Surveyed by J.J. Lanigan
Notes J.J.L. Date 2-27-52
Indexed C. Johnson

F. B. 1738 Pg. 133

Contd. for pg. 131

E.P.S. 6+36.5

60.5

19.7

H.H. 6+22.0

6+00

12.6 20.9 28.7

20" P.P 5+99.8

Edge Pav. 3" bit-mix

AVE.

Pav.

32.5

6.4 26.3

5+00

15.9

18" P.P 5+01.8

20" P.P 4+94.2

P.I. Sta 3+93.17
3/4 I.P.
pc I.F.B 1726-52

4+32.0

37.6

4+32.0

3+74.4

12" P.P 3+73.2

Pav.

5 3+62.4

41.1

46.7

49

2.7

14" P.P. 3+58.2

Edge

WINDSOR

Edge

Contd. for pg. 132

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
720 LOS ANGELES COUNTY
ENGINEERING BLDG.

76FS095 247 2-51

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

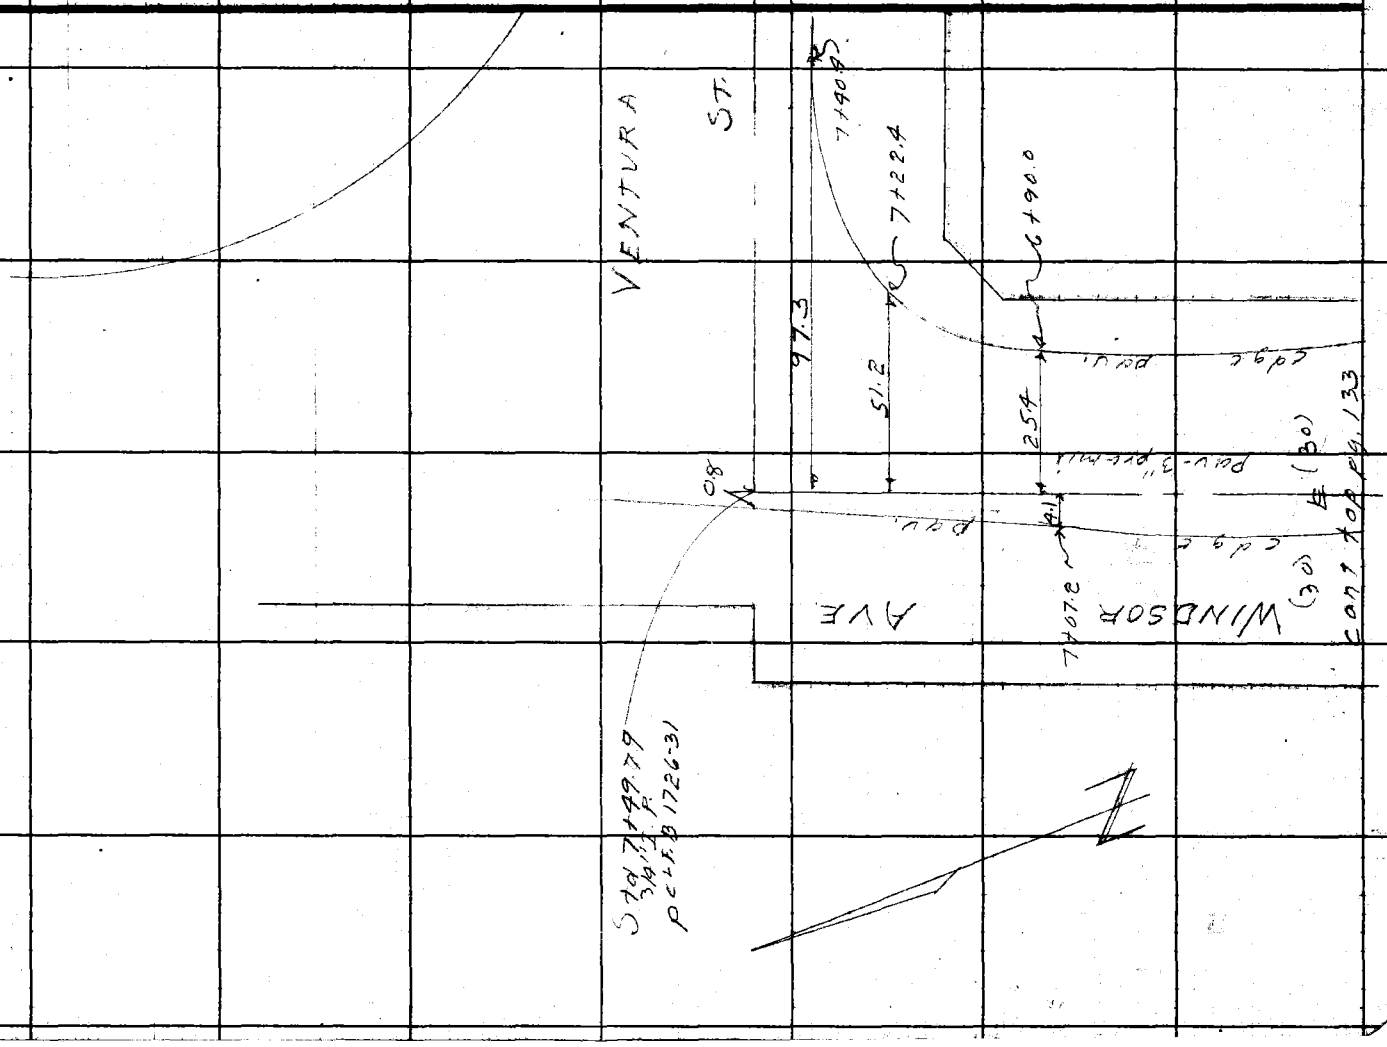

F.B. 1116 Pg. 124

Profile No. | Notes Red. | Date | Plotted | Date | Job No. 1462 | Division No. | F. B. 1738 | Pg. 135
Notes Ch. | Date 2/27/52 | Checked | Date | Survey of Co. Rd. Dept. | Survey by | Map No. | Indexed C. Johnson | Date

PROFILE AND CROSS SECTIONS OF

WINDSOR AVENUE

FROM

SOUTHERLY LINE OF TRACT 7950

C.I. 1462

J. J. Lanigan
C. H. Lewis
H. H. Raphael
H. C. Woodworth

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend notes this side of this line.

761298 377 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 1462 Pg. 136 Job No. 1462 Division No. Notes Red. Plotted. Profile
Survey of Carson Ave Date No.
Survey by Davison Notes Kewis Date X-Sec.
Indexed C. Johnson Notes Chkd. Checked
Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	Windsor Avenue
					℄
BM AE 496	4 14	1160 19		1156 05	AE 496 E/1156.048 FB 1568 P. 133
					Windsor Ave. & Mountain View Pl., NE cor.
					Bt. sph. in curb 5' E of W. end
0 + 00			9 67	1150 52	Int of Tract line & ℄ of Windsor
			11 82	1148 37	190' S'ly on ℄ of Windsor
0 + 00			9 79	1150 40	12.5' R edge pvmt
"			9 6	1150 6	30' R
"			10 10	1150 09	13.5' L edge pvmt
"			9 6	1150 6	30' L
1 + 00			7 59	1152 60	℄
"			7 95	1152 24	11.5' R edge pvmt
"			6 6	1153 6	30' R
"			7 94	1152 25	15.5' L edge pvmt
"			6 88	1153 31	25' L fence line
2 + 00			5 53	1154 66	℄
"			5 88	1154 31	15.5' L edge pvmt
"			4 2	1156 0	25' L
2 + 40.07			4 65	1155 54	℄ Int of Windsor & Mountain View Pl
			5 01	1155 18	100' Easterly on ℄ of " " "

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. 462 Division No.
No. Date. Date. Survey of Windsor Avenue
No. Date. Date. Map No. Indexed C. Jones Date.

F. B. 462 Pg. 137

Windsor Avenue

STATION	B. S.	H. I.	F. S.	ELEV.		
		1160.19				℄
			5.75	1154.44	100' E'ly on S. gutter of Mountainview	
			5.11	1155.08	" " " " cb	" "
			4.72	1155.47	" " " N gutter	" "
			4.08	1156.11	" " " " cb	" "
3+00			3.32	1156.87		℄
"			3.50	1156.69		6.5 R edge pvmt
"			3.4	1156.8		25' R
"			3.06	1157.13	28' L edge pvmt	
"			2.3	1157.9	35' L Fence line	
4+00			1.6	1158.6		℄
"			1.46	1158.73		5.5 R edge pvmt
"			1.75	1158.44		43' R "
"			1.3	1158.9		50' R Fence line
T.P.		1	1.38	1158.81	T.P.	
	9.27	1168.08				
5+00			7.63	1160.45		℄
"			7.94	1160.14		26' R edge pvmt
"			7.0	1161.1		35' R Fence line
"			7.77	1160.31	6.5 L edge pvmt	
"			7.2	1160.9	15' L	

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile — Plotted — Notes Red. — Job No. 1442 Division No. — Pg. 138
X-Sec. — No. — Date — No. — Date — Survey of Castles Ave.
Checked — Notes Chkd. — Notes Lewis — Survey by Lagliegan
Date — Date — Date — Indexed C. Francisco

STATION	B. S.	H. I.	F. S.	ELEV.	Windsor	Avenue
		1168.08				℄
6+00			6.14	1161.94		℄
"			6.36	1161.72		21' R edge pvmt
"			5.0	1162.1		31' R fence line
"			6.26	1161.82	12.5' L edge pvmt	
"			4.8	1163.3	25' L	
7+00			5.09	1162.99		℄
"			5.00	1163.08		30' R edge pvmt
"			2.6	1165.5		35' R fence line
"			5.13	1163.95	3' L edge pvmt.	
"			2.1	1166.0	15' L	
7+49.79			4.76	1163.32	℄ int. Windsor & Ventura St.	
			2.13	1165.95	100' E'ly on ℄ of " "	
			3.54	1164.54	" N'ly on Windsor produced	
			6.0	1162.1	15' W'ly on Ventura ℄ prod. (Top of bank of Arroyo Seco)	
BM AE 497			0.04	1168.04	AE 497 E 1168.06 1 EB 15-68 P. 134 Ventura St. Sterling Place, NE cor. Bt. Spk. in curb 6' N of S. end	

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Castaic Jr. C.
W. O. 4[illegible] Tape No. St'd °F
Surveyed by J. J. Lanigan
Notes J.J.L Date 2-20-52
Indexed C. Johnson

F. B. 1738 Pg. 139

LOCATION of BUILDINGS and PLUMBING OUTLETS at SCHOOL FOR CEREBRAL PALSIED CHILDREN C.I. 1462

J. J. Lanigan
C. H. Lewis
H. H. Raphael
* H. S. Woodworth

Notes: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76F3085 247 2-51

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

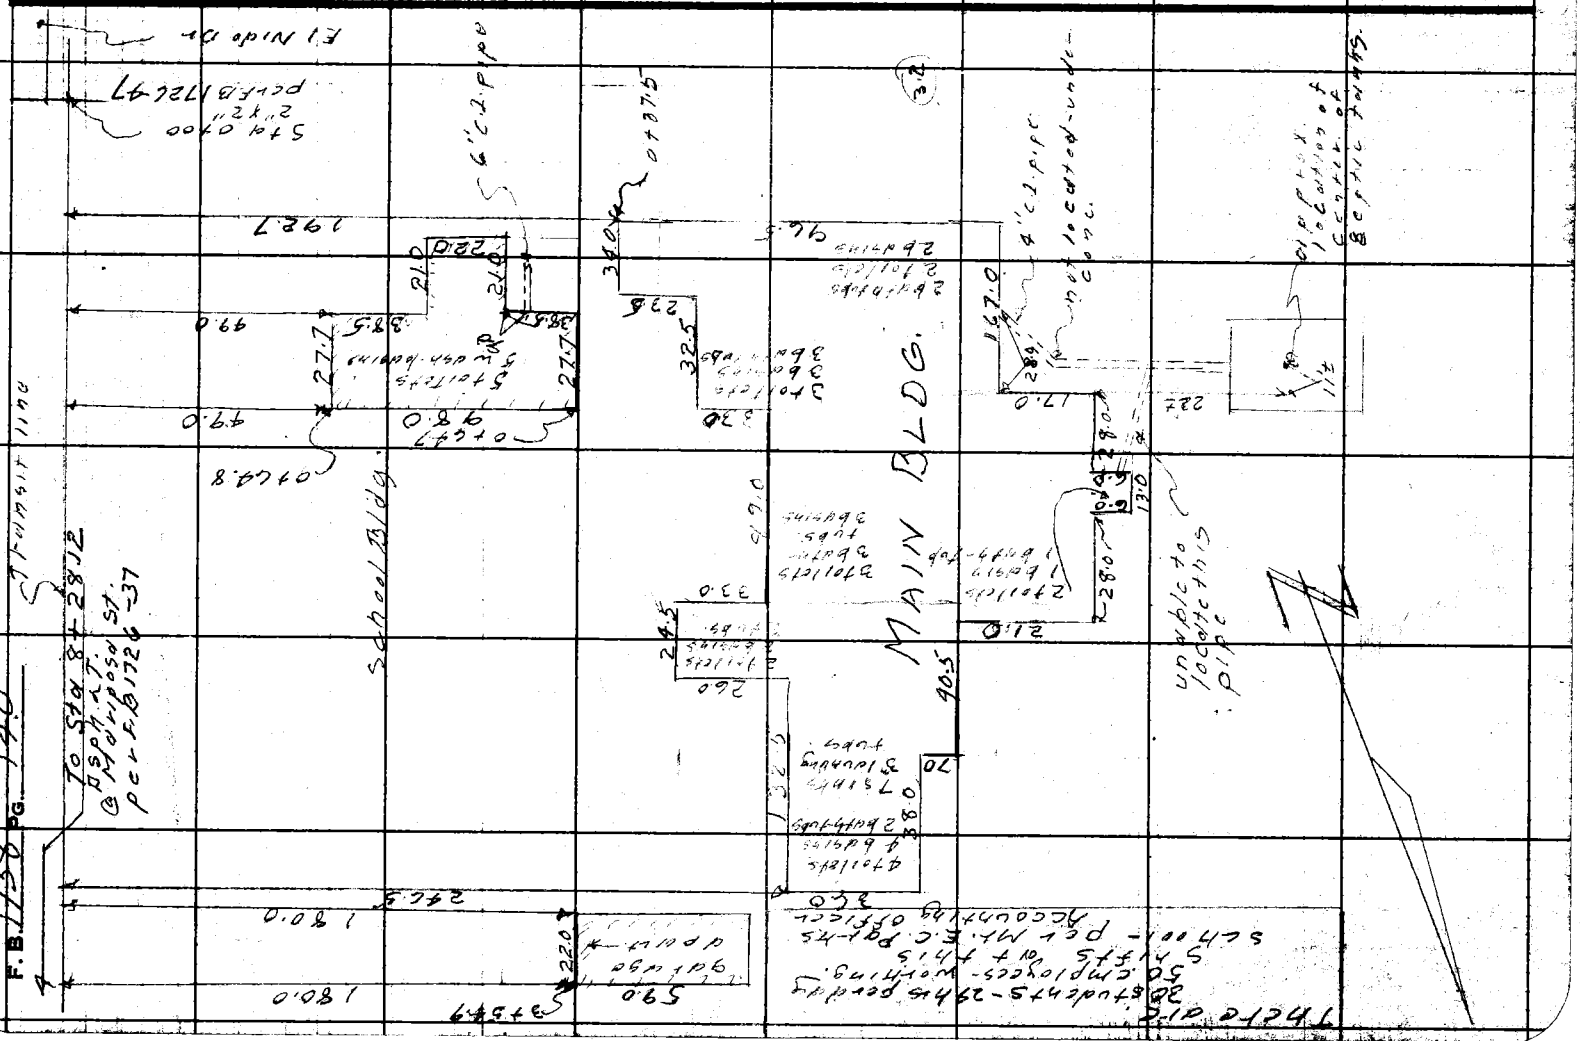

Profile No. | Notes Red. | Plotted | Job No. 1462 | Division No. | F. B. 1738 | Pg. 141

Date | Date | Survey of California

Notes Chkd. | Checked | Survey by [illegible] C. Johnson

No. | Date | Date | Map No. | Indexed | Date

ELEVATIONS

FLOORS AND PLUMBING OUTLETS

OF

CALIFORNIA SCHOOL

For

CEREBRAL PALSIED CHILDREN

C.I. 1462

J. J. Lanigan
C. H. Lewis
H. H. Raphael

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

764.298 377 4-50

76L298 307 4-58

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ Plotted ____ Date ____
X-Sec. No. ____ Checked ____ Date ____
Notes Red ____ Date ____
Notes Chkd ____ Date ____
Job No. 1462 Division No. ____
Survey of Castle Ave.
Survey by: Lanigan Notes: Lewis
Indexed ____ Checked ____ Date ____
F. 1738 P. 142

STATION	B. S.	H. I.	F. S.	ELEV.	California School For Cerebral Palsied Children
BM AE 524	4 28	1191 88		1187 60	AE 524 El 1187.600 FB 1568 P. 156 El Nido Drive (W. Side) at Harriet St Bt spk in conc. walk to Ho # 2909
			4 9	1187 0	Elev. of 6" C.I. pipe, S. side of Classroom Bldg.
			2 2	1189 7	Floor Elevation " " "
0+37 to 1+04			3 4	1188 5	" " SE wing main Bldg.
T. P.			6 16	1185 72	T. P.
	7 70	1193 42			
			5 9	1187 5	Elev 4" C I pipe. W. side of main Bldg.
1+04 to 2+04 5/7			2 7	1190 7	Floor elev. of main Bldg center section
T. P.			2 00	1191 42	T. P
	4 64	1196 06			
			3 9	1192 2	Floor elev. N wing of main Bldg.
			3 8	1193 3	Garage floor elev.
BM AE 500			1 70	1194 36	AE 500 E 1194.363 FB 1568 P 135 Crestford Drive at W. end of St. Bt spk in curb 1' N of & prod.

Notes Ck'd by	Survey of Castlegate Ave.
Map No.	W. O. 7202 Tape No. Std. °F
Office Work	Surveyed by: J. J. Lanigan
Checked	Notes J. J. L. Date 2-28-32
Date	Indexed: C. Johnson

F. B. 738 Pg. 183

Notes: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink with Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
of
BUILDINGS
at
SACRED HEART SCHOOL
on
MARIPOSA ST.
C. I. 1962

J. J. Lanigan
C. H. Lewis
H. H. Raphael
H. S. Woodworth

75F3095 247 10M 1-49

F. B. 738 Pg. 14

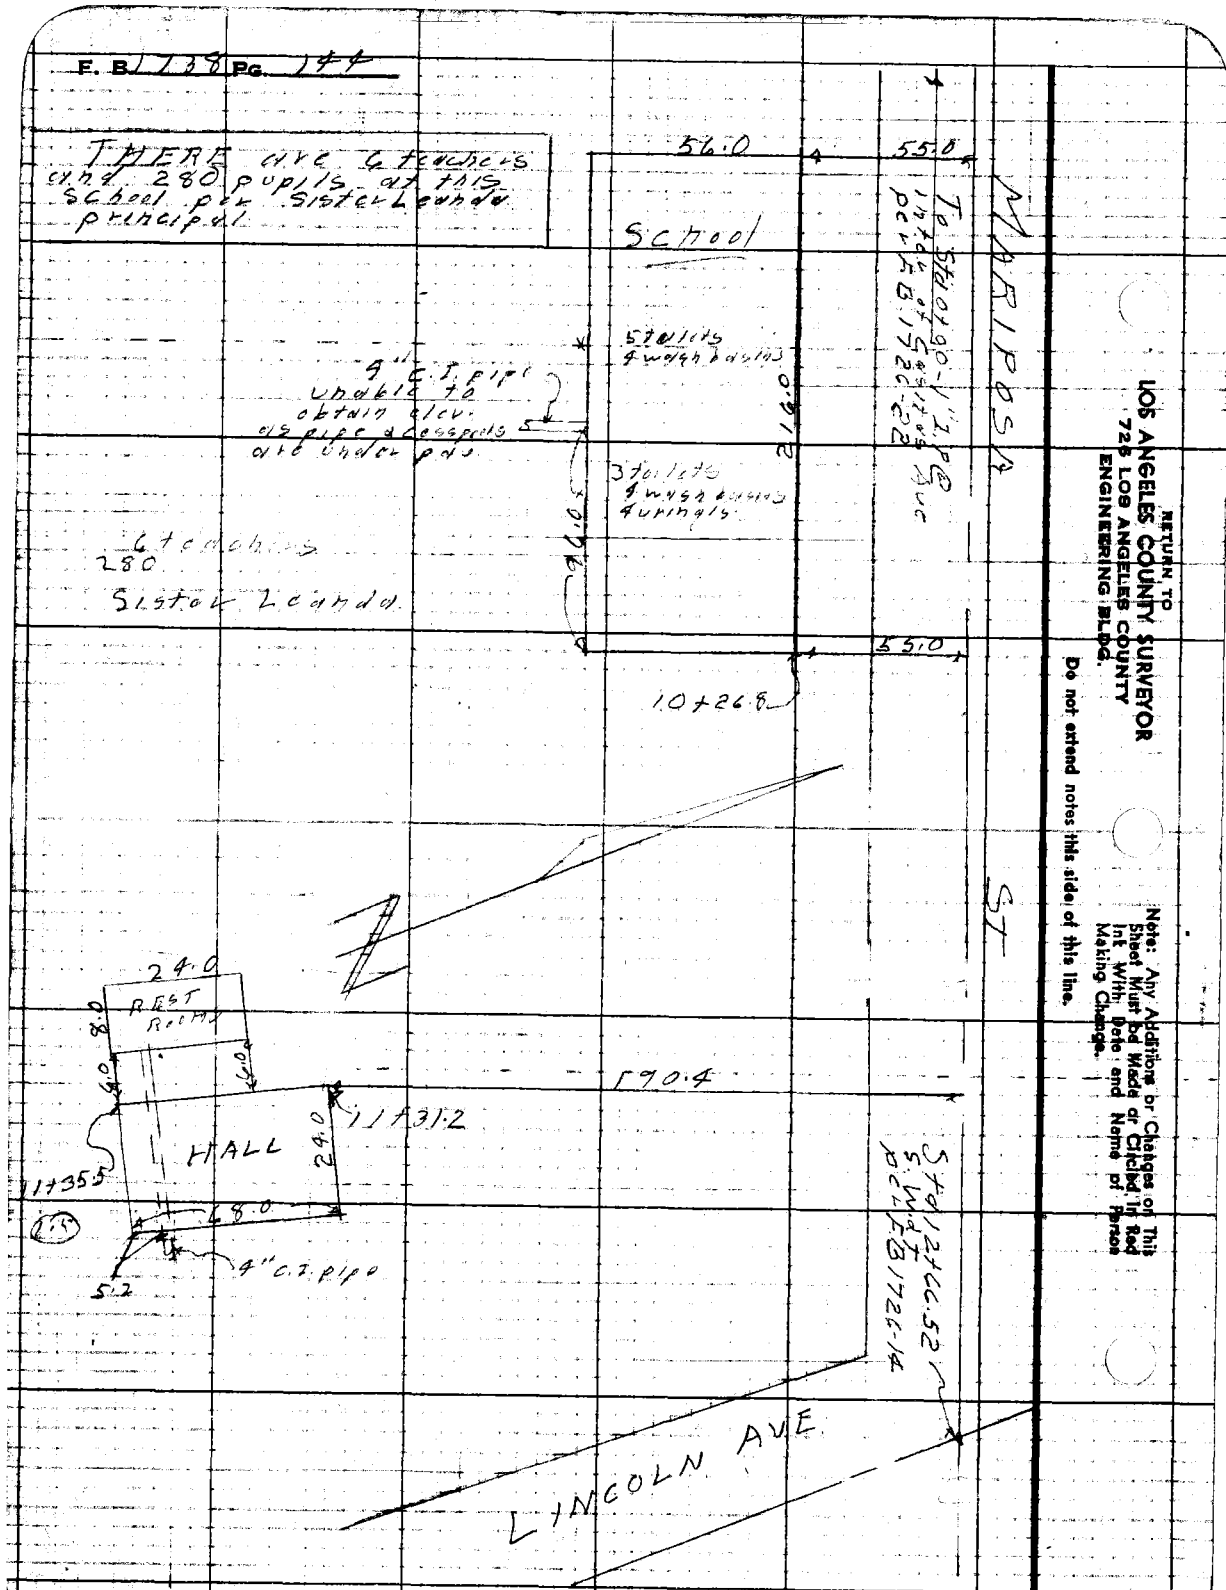

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No. | Notes Red. Date | Plotted Date | Job No. 1462 | Division No. | F. B. 1738 | Pg. 145

Sec. No. | Notes Chkd. Date | Checked Date | Survey of Capitan Ave. | Survey by Lanigan | Notes Chkd. C. Johnson | Date | Map No. | Indexed | Date

ELEVATIONS

PLUMBING OUTLETS and BUILDINGS

OF

SACRED HEART SCHOOL

MARIPOSA STREET

AT

LINCOLN AVENUE

C.I 1462

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend notes this side of this line.

761.298 3M7 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

5.28

Do not extend notes this side of this line.

F. B. 7738 Pg. 144 Job No. 4Le 2 Division No. Notes Red Plotted Profile
Survey of Cost Plus Date No.
Survey by Lagasse Notes Lewis Date X-Sec.
Indexed K. O. Johnson Date Notes Chkd Checked
Date No.

STATION	B. S.	H. I.	F. S.	ELEV.		
BM AE236	1 42	1239.97		1238.55	AE236 El. 1238.548	FB 1447 P 225
T.P.			7 76	1232 21	T.P.	
	4 36	1236 57				
			6 1	1230 5	Ground at SW corner of school	
			4 08	1232 49	Floor elev. at rest rooms.	
			5 5	1231 1	Ground at SE corner of School	
			11 2	1225 4	Elev. of 4" C.I. pipe from hall.	
T.P.			5 51	1231 06	T.P.	
	1 89	1232.95				
BM AE237			12 42	1220 43	AE237 1220.440 FB 1447 P 225	
					Lincoln Ave. & Mendocino St SE cor.	
					BT spk in curb 3' E of E end C.R.	

Notes Ckd by	Survey of Casitas Ave.
Map No.	W. O. 1462 Tape No. St'd. °F
Office Work	Surveyed by J. J. Lanigan
Checked	Notes J.J.L Date 2-28-52
Date	Indexed C. Johnson

F. B. 173 Pg. 147

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Location of Buildings at Audubon School

C. I. 1462

J. J. Lanigan
C. H. Lewis
H. H. Raphael
H. S. Woodworth

76F3095 247 2-51

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

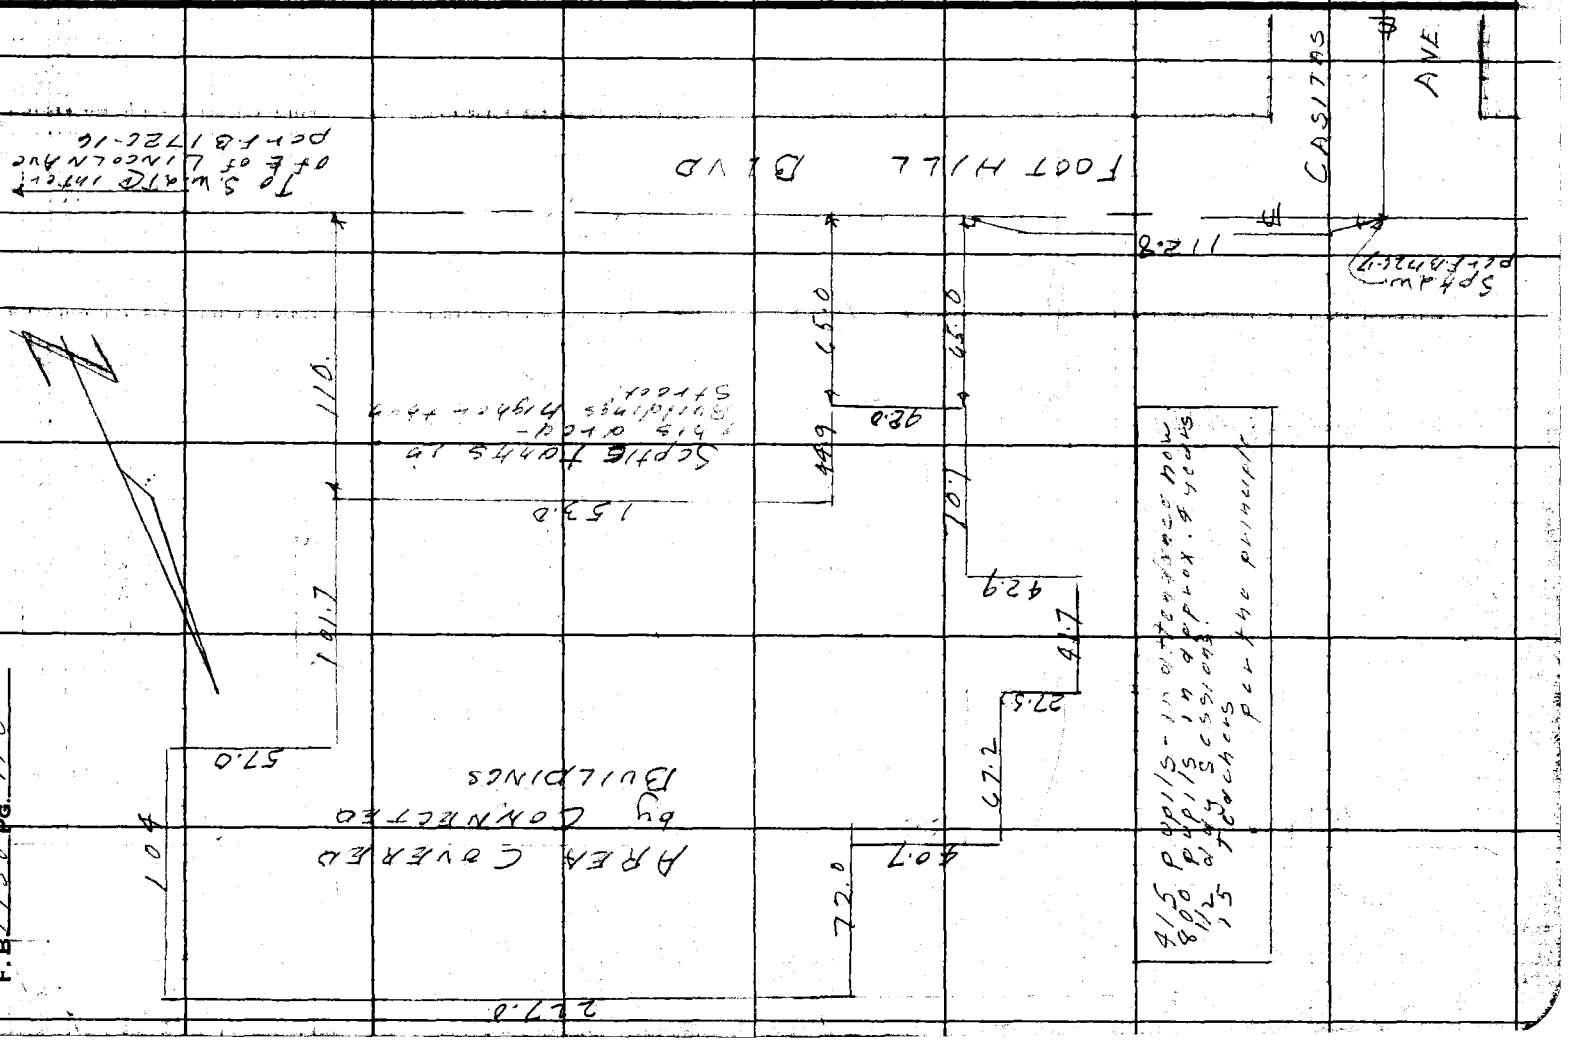

Notes Ck'd by:	Survey of: Castle Axe
Map No.	W. O. 1462 Tape No. St'd. °F
Office Work	Surveyed by: J. J. Lonigan
Checked	Notes J. J. L. Date 5-9-52
Date	Indexed C. Johnson

F.B. 736 Pg. 149

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION of IMPROVEMENTS on TRANSIT LINE THROUGH THE GROUNDS of SCHOOL FOR CEREBRAL PALSIED CHILDREN from STERLING PL. to CRESTFORD DR. C.I. 1462

J. J. Lonigan
C. H. Lewis
H. H. Raphael
H. C. Woodworth

76F309S 247 2-51

F. B. 1737 PG. 150 Cont. bot. pg. 151

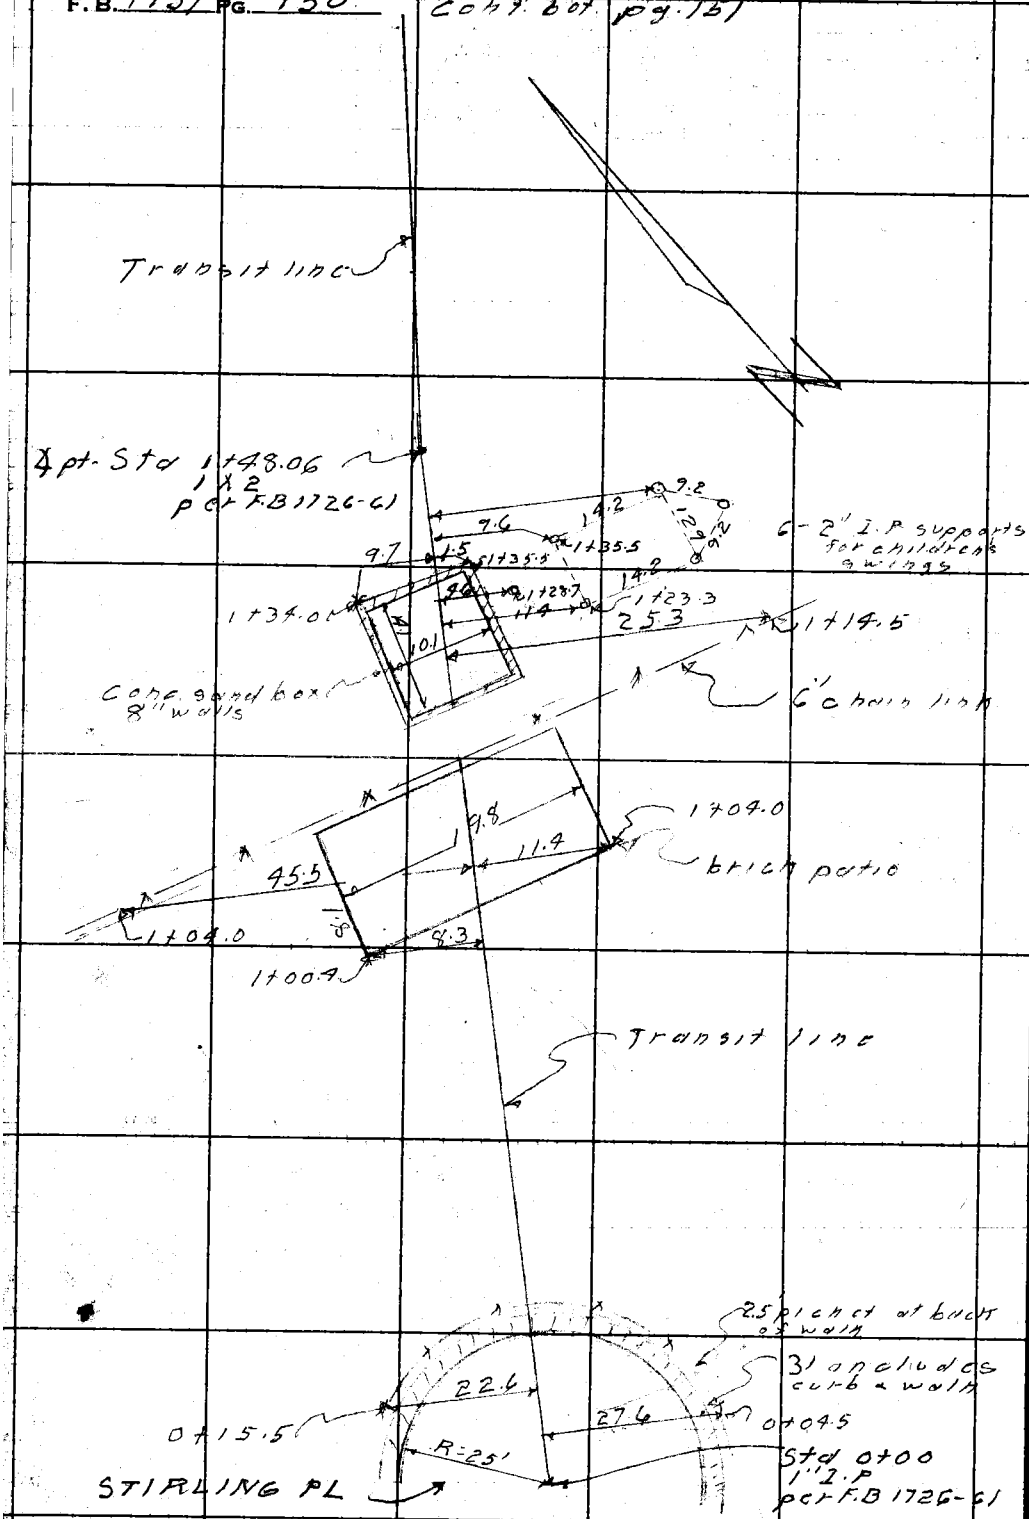

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes C'k'd by:
Map No.
Office Work
Checked
Date

Survey of Cavitas Ave
W. O. 1462 Tape No. St'd. °F
Surveyed by J.J.L. Conigaro
Notes J.J.L. Date 5-8-52
Indexed C. Johnson

F. B. 1139 Pg. 137

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

cont. to pg. 150

cont. to pg. 150

3 off. lowest elev. in gutter 5278.8

conc. p.

18.0

3+03.5

3.4

20'

29'

6.0

3+38.5

11th

conc. walk

3+28.8

54' chain

19.4

3+19.5 p.t.

3.0

23.2

3+22.0

3.1

6.0

5.0

15.5'

Westerly wall of Bldg.

3"ø pipe

3+17.0

18.3

36.7

3+10.8

36.8

4" conc. iron effluent pump house-conc. base

3+00

top of bank

Tr. wall

13.7

3.5

conc. pav.

20.5

18.3

2+74.5

New M.H. 2+70.9

27.3

78F3095 247 2-51

F. B. 1129 PG. 152

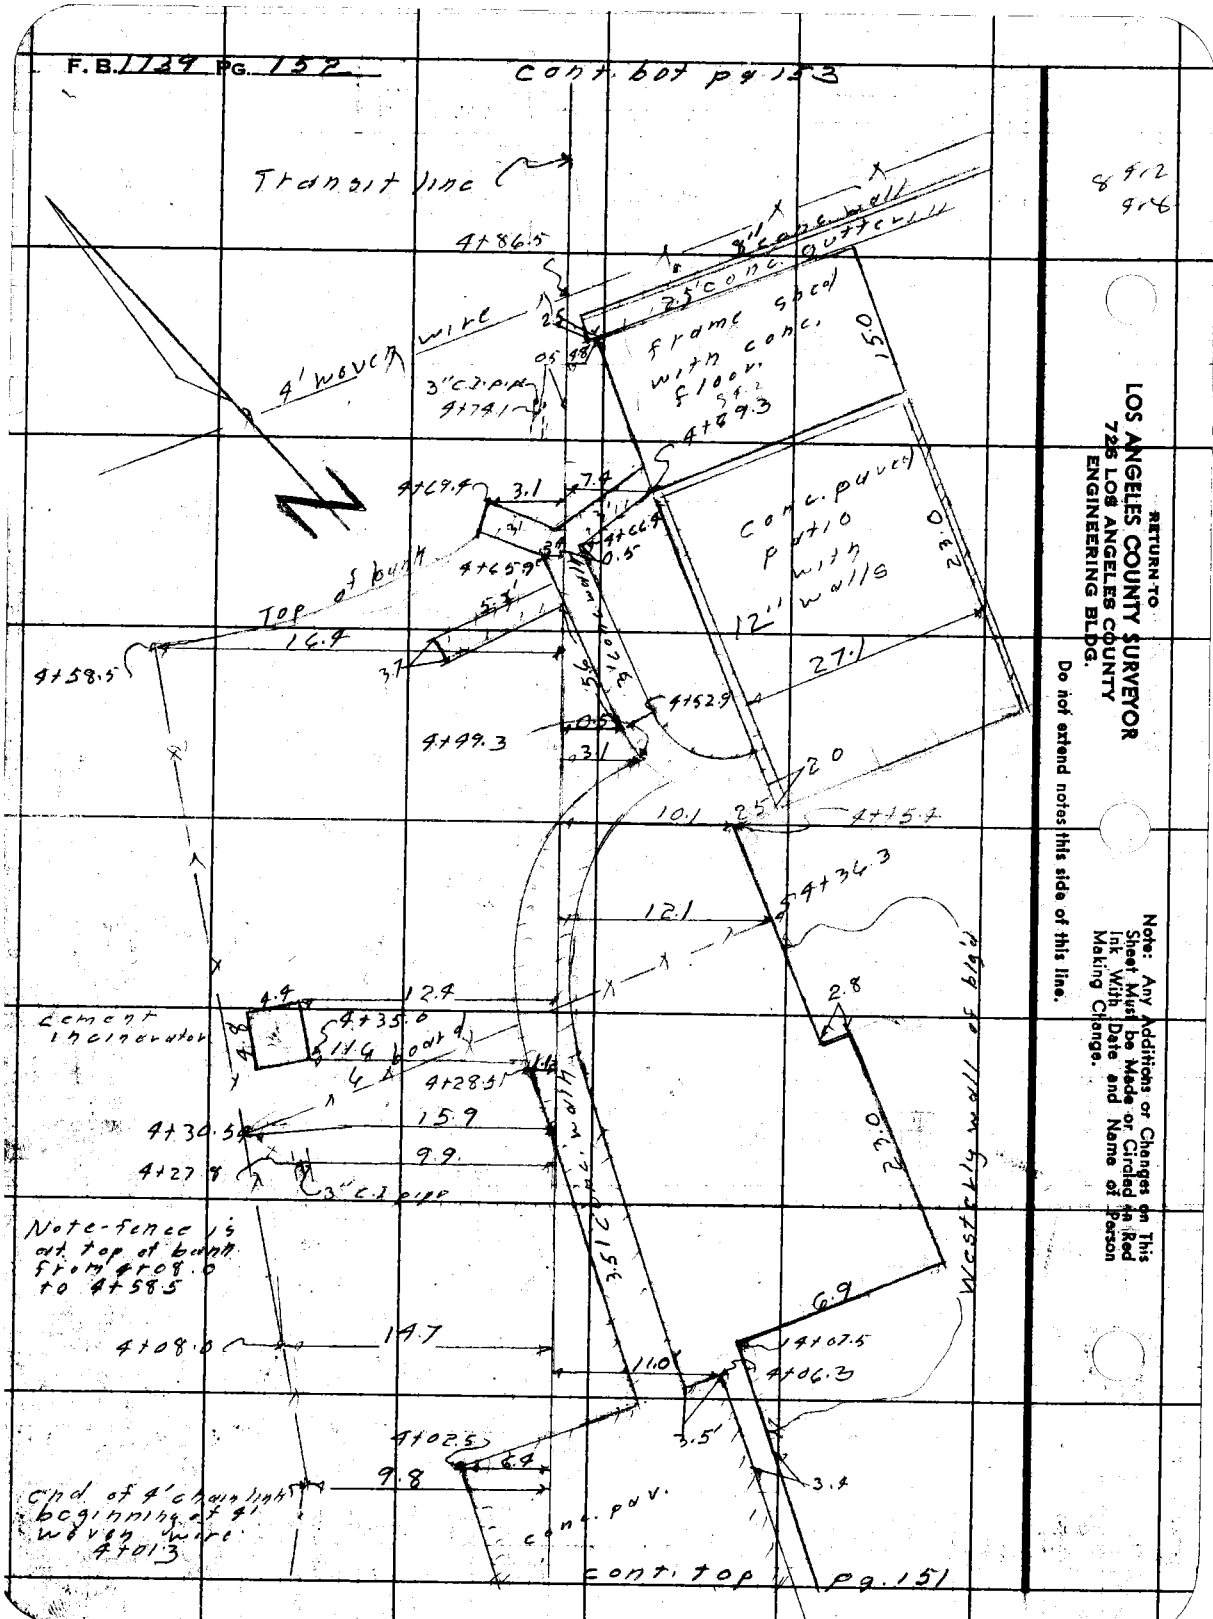

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by:	Survey of Cowles Ave.
Map No.	W. O. 462 Tape No. St'd. °F
Office Work	Surveyed by J. J. Lanigan
Checked	Notes J.J.L. Date 5-8-52
Date	Indexed E. C. Johnson

F. B. 1737 Pg. 153

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Sta 5+71.0 ℄
N.I.T.
P.C. F.B. 1721-62

CREST FORD DR.

1020'

5+42.5 - Jump pos'd

5+43.3

4.8

12" oak
5+21.2

2.2

Transit line

4+92.6
12" gum

3.7

4+89.7
8" gum

2.0

11

4+89.9
6" gum

Cont. top pg. 152

.767309 247 2-51

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

F. B. 1739 PG. 154

Profile No. | Notes Red. | Date | Plotted | Date | Job No. 1462 | Division No. | F. B. 1738 | Pg. 155

X-Sec. No. | Notes Chkd. | Date | Checked | Date | Survey of [illegible] | Survey by Lanigan | Notes Lewis | Date 2-8-52 | Map No. | Indexed C. Johnson | Date

PROFILE
OF
TRANSIT LINE
FROM
STERLING PLACE (N. END)
TO
CRESTFORD DRIVE (W. END)

C.I. 1462

J.J. Lanigan
C.H. Lewis
H.H. Raphael
H.C. Woodworth

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

761.298 307 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 1738 Pg. 156 Job No. 1462 Division No. Profile
Survey of Cesitas Ave. Plotted No.
Survey by Lanigan Notes Lewis Date Notes Red. Date No.
Indexed C. Johnson Date Notes Chkd. Date X-Sec.
Checked Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
BM-AF 499	7.45	1190.24		1182.79	AF 499 El 1182.787 FB 1568 P 134 Sterling Place at N. end of St. on E. Bt. spk in curb 12'± W of ℄ prod.	
0+00			8.36	1181.88	Radius pt. at N. end of	Sterling
0+25			7.85	1182.39		gutter
"			7.39	1182.85		cb
0+50			6.9	1183.3		
1+00			5.9	1184.3		
1+02			5.42	1184.82	Lucile Ave.	
			5.24	1184.90	NE cor. " "	
1+50			4.6	1185.6		
2+00			3.5	1186.7		
2+50			2.4	1187.8		
3+00			1.1	1189.1		
T.P.			0.59	1189.65	T.P.	
	6.47	1196.12				
3+50			6.3	1189.8		
4+00			5.8	1190.3		
4+50			4.9	1191.2		

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
		1196.12				
5+00			4.2	1191.9		
			1.65	1194.47		CL
			2.33	1193.79		Cut
5+71.04			1.76	1194.36	End of Transit Line in Crestford Dr.	
BM AE 500			1.77	1194.35	AE 500 El 1194.863 FB 1568 P 135 Crestford Dr. at W. end of street Bt. sph. in curb 1' N of ℄ Prod	

Profile Notes Red. Plotted Job No. 1462 Division No. F. B. 1738 Pg. 157
No. Date Survey of Easterly Extension
X-Sec. Notes Chkd Date Survey by Lewis Date 5-28-57
No. Date Checked Notes Lewis
Date Map No. Indexed Johnson Date

F. B. 1738 Pg. 13-8 Job No. 1462 Division No. Notes Red. Plotted Profile

Survey of Casitas Avenue Date Date No.

Survey by Lanigan Notes Low is Notes Chkd Checked X-Sec.

Indexed Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.

761.298 307 4-50

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR

725 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Notes Ck'd by	Survey of Cazitos Ave.
Map No.	W. O. 1462 Tape No. St'd. °F
Office Work	Surveyed by J.J. Lanigan
Checked	Notes J.J.L. Date 5-7-52
Date	Indexed C. Jennson

F. B. 1738 Pg. 157

Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION of IMPROVEMENTS on FIRST ALLEY W. of LINCOLN AVE. from N'ERLY LINE LOT # 24 - TRACT # 6489. to FOOTHILL BLVD.

C.I. 1462

J.J. Lanigan
C.H. Lewis
H.H. Raphael
H.C. Woodworth

76F3095 247 2-51

F.B. 1139 PG. 160

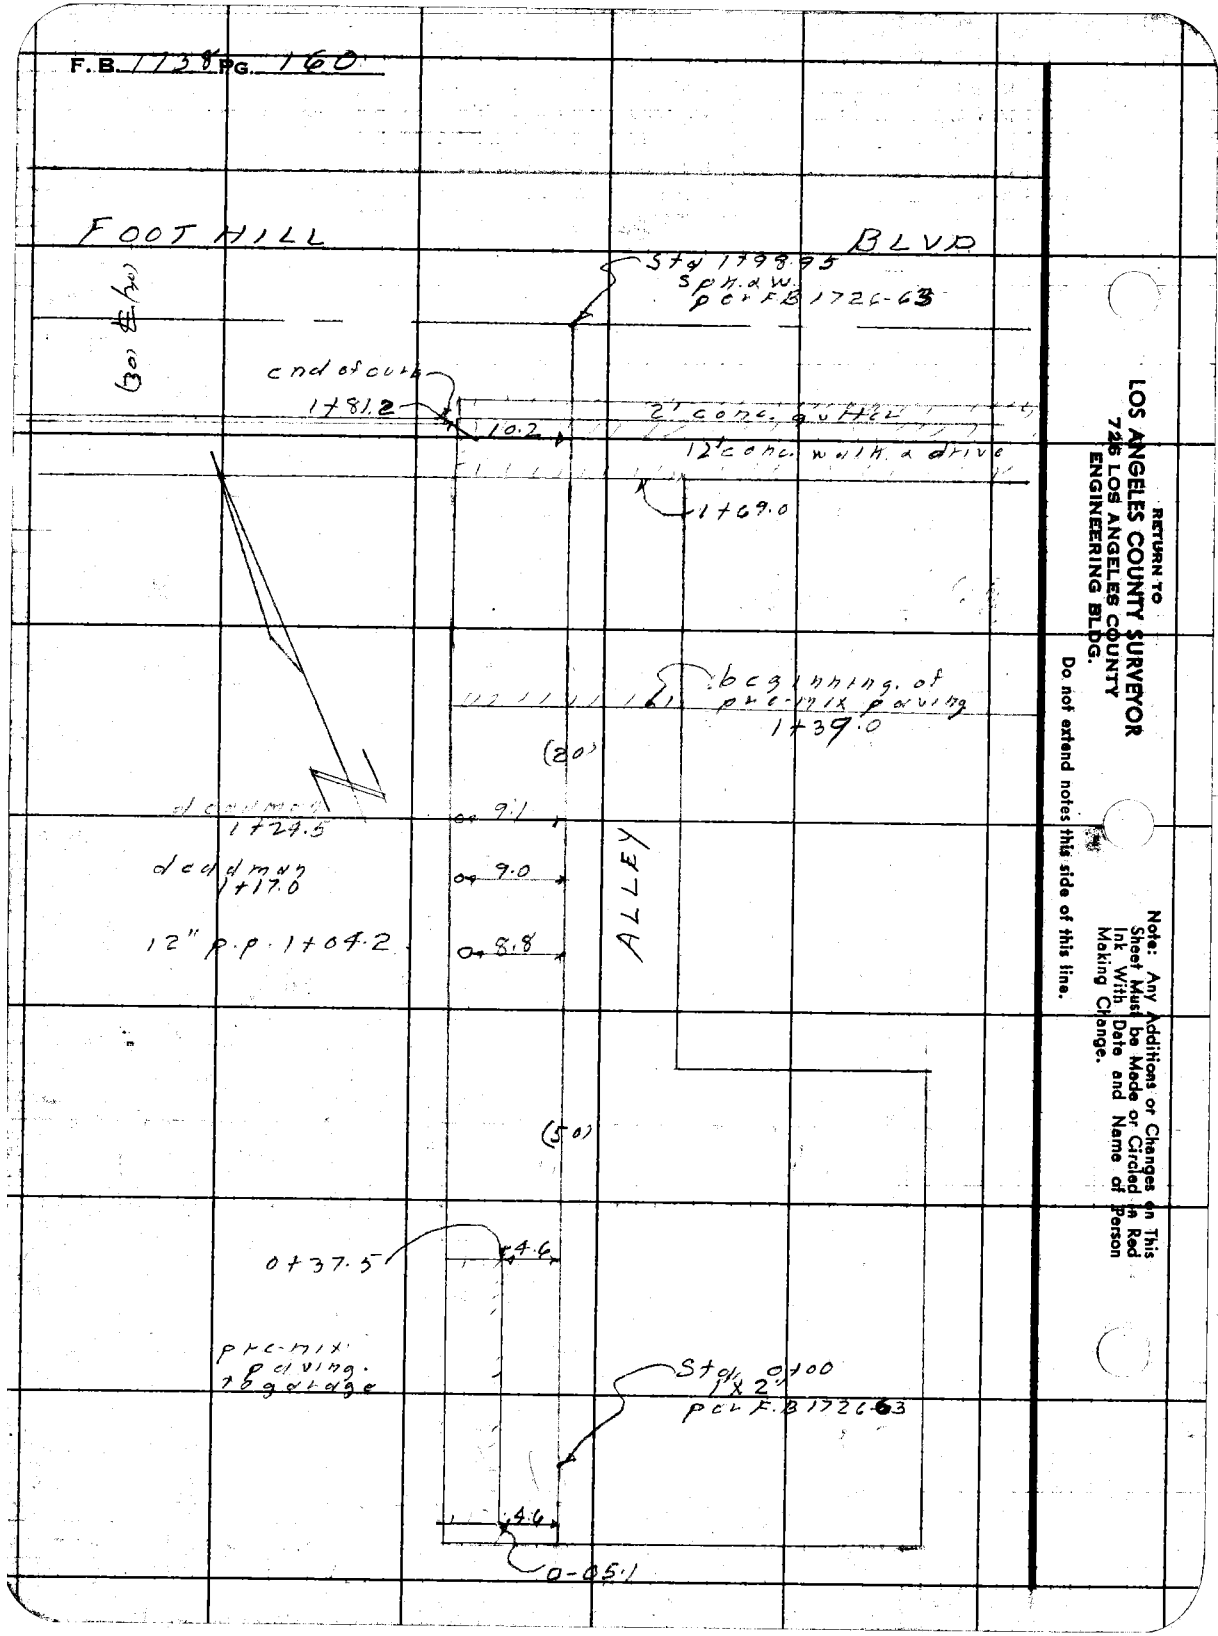

RETURN TO
LOS ANGELES COUNTY SURVEYOR
7215 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No. | Notes Red. Date | Plotted Date | Job No. 1462 Division No. | F. B. 1738 Pg. 161
X-Sec. No. | Notes Chkd. Date | Checked Date | Survey of Castigas Avenue
Survey by Lanigan Notes Lewis Date 5-9-52
Map No. | Index C. Johnson Date

PROFILE AND CROSS-SECTIONS

OF

1st ALLEY WEST OF LINCOLN AVE

BETWEEN

SOUTH END OF ALLEY AND FOOTHILL BLVD.

C.I 1462

J.V. Lanigan
C.H. Lewis
H.H. Raphael
H.C. Woodworth

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

764298 307 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 1738 Pg. 102 | Job No 446.2 Division No. | Profile
Survey of Castle Ave | Plotted | No.
Survey by Lonigan & Notes Lewis | Date | X-Sec.
Indexed C. Johnson | Notes Red | No.
Date | Date | Notes Chkd. | Checked
Date | Date

STATION	B. S.	H. I.	F. S.	ELEV.	Transit Line	
BM AE 233	3 58	1257 96		1254 38	AE 233 El 1254.377	FB 1447 P 224
					Foothill Blvd & Lincoln Ave. L.T. ± S 40.6' E of ℄ Int.	
					L.A. County Survey Control Traverse Stations Altadena El in feet based on	
0+00			10 3	1247 7		℄
"			9 80	1248 16	10' L Premix apron	to garage
			10 1	1247 9		30' R.
0+50			9 2	1248 8		℄
"			9 3	1248 7	10' L	
"			8 3	1249 7		30' R
1+00			7 6	1250 4		℄
"			7 5	1250 5	10' L	
"			7 5	1250 5		10' R
1+40			6 57	1251 39	edge of pvmt	℄
			6 17	1251 79	10' L " "	
			5 88	1252 08	" "	10' R
1+72			4 43	1253 53		℄ ctr of walk
			4 30	1253 66	10' L	" " "
			4 06	1253 90		10' R " " "
1+81 2			5 07	1252 89		℄ gutter
"			5 19	1252 77	10' L	"

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
		1257 96				
1+81 3			501	1252 95	10'L Gutter	
1+99			438	1253 58		E
"			450	1253 46	10'L	
"			426	1253 70		10' R
BM AE 234			118	1256 78	AE 234-E/ 1256.784 FB 1447-P 22 4 Foothill Blvd & Lincoln Ave SE Cor. BT Spk in cb 2' E of E end C.R.	

Profile Notes Red. Plotted Job No 462 Division No. F. B. 738 Pg. 163
No. Date Date Survey of Castle Ave.
X-Sec. Notes Chkd. Checked Survey by Hawkins Notes Lewis Date 5-9-52
No. Date Date Map No. Index C. Johnson
Date

F. B. 1738 Pg. 164

Job No. 1462 Division No. Notes Red. Plotted Profile

Survey of Casitas Ave. Date Date No.

Survey by Lanigan Notes Lewis Notes Chkd. Checked X-Sec.

Indexed Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.

761298 307 4-50

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR

726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Notes Ck'd by:
Map No.
Office Work
Checked
Date

Survey of Cahuenga Ave.
W. O. 1462 Tape No. St'd. °F
Surveyed by J. J. Lanigan
Notes J. J. L. Date 6-14-32
Indexed E. C. Johnson

F. B. 1938 Pg. 165

Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
of
IMPROVEMENTS
on
EASTERLY LINE of Jr 4702.
from
ROYCE ST.
to
NORTHERLY LINE of 1st LOT N. of ROYCE ST.
C. I. 1462.

J. J. Lanigan
C. H. Lewis
H. H. Raphael
H. C. Woodworth

76F3095 247 2-51

F. B. 1738 PG. 166

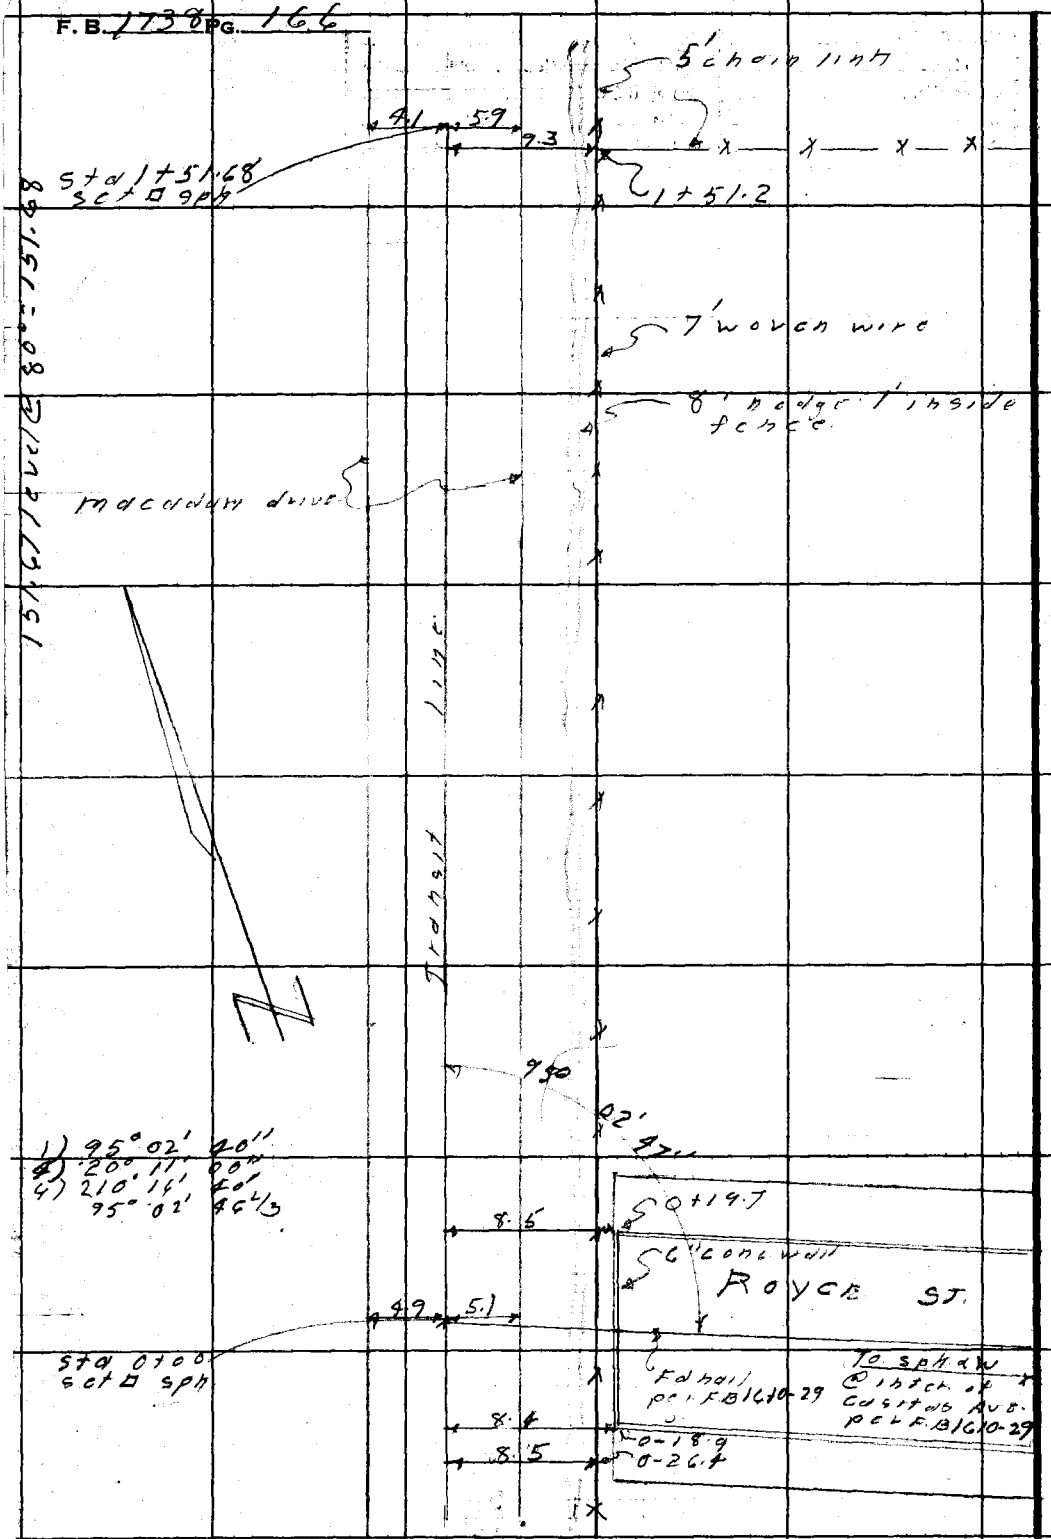

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No. | Notes Red. | Plotted | Job No. 1462 | Division No. | F. B. 7238 | Pg. 167
Date | Date | Survey of Capitan Ave
X-Sec. No. | Notes Chkd. | Checked | Survey by Lanigan | Notes Lewis | Date 5-14-5
Date | Date | Map No. | Indexed C. Johnson | Date

PROFILE

Easterly Line of Tr. 4702

Royce St. to
1st. Lot Line N. of Royce St.

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend notes this side of this line.

761298 307 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 1738 Pg. 168 Job No. 462 Division No. Notes Red. Plotted Profile
Survey of Casitas Ave. Date Date No.
Survey by Lewis & Tomlinson Notes Chkd. Checked X-Sec.
Indexed C. Tomlinson Notes Lewis Date Date No.
Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Line
BM AE519	5 48	1150 94		1145 46	AE519 E/1145.459	FB 1528 P 152
					Royce St. (N. side) 400' W of ℄ of Casitas Ave.	
					13" sph. in curb in front of HO # 733	
0+00			5 43	1145 51	℄	
"			5 3	1145 6		9' R
0+50			4 21	1146 73	℄	
"			4 0	1146 9		9' R
1+00			2 97	1147 97	℄	
"			2 7	1148 2		9' R
1+57.68			1 56	1149 38	℄	
"			1 4	1149 5		9' R
T. P.			6 02	1144 92	T. P.	
	4 70	1149 62				
BM AE519			4 16	1145 46	AE519 - as above.	

F. B. 1738 Pg. 169

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Cortez Ave
W. O. 1462 Tape No. 052 St'd. C & °F
Surveyed by J. J. L & 1/2 1942
Notes J. J. L Date 5-15-52
Indexed C. Johnson

LOCATION
of
BUILDINGS
at
S. END of Boys and Girls Aid Society
in
TRACT # 4702
C. I. 1462.

J. J. Lanigan
E. H. Lewis
H. H. Raphael
H. C. Woodworth

Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76F309S 247 2-51

F. B. 1238 PG. 110

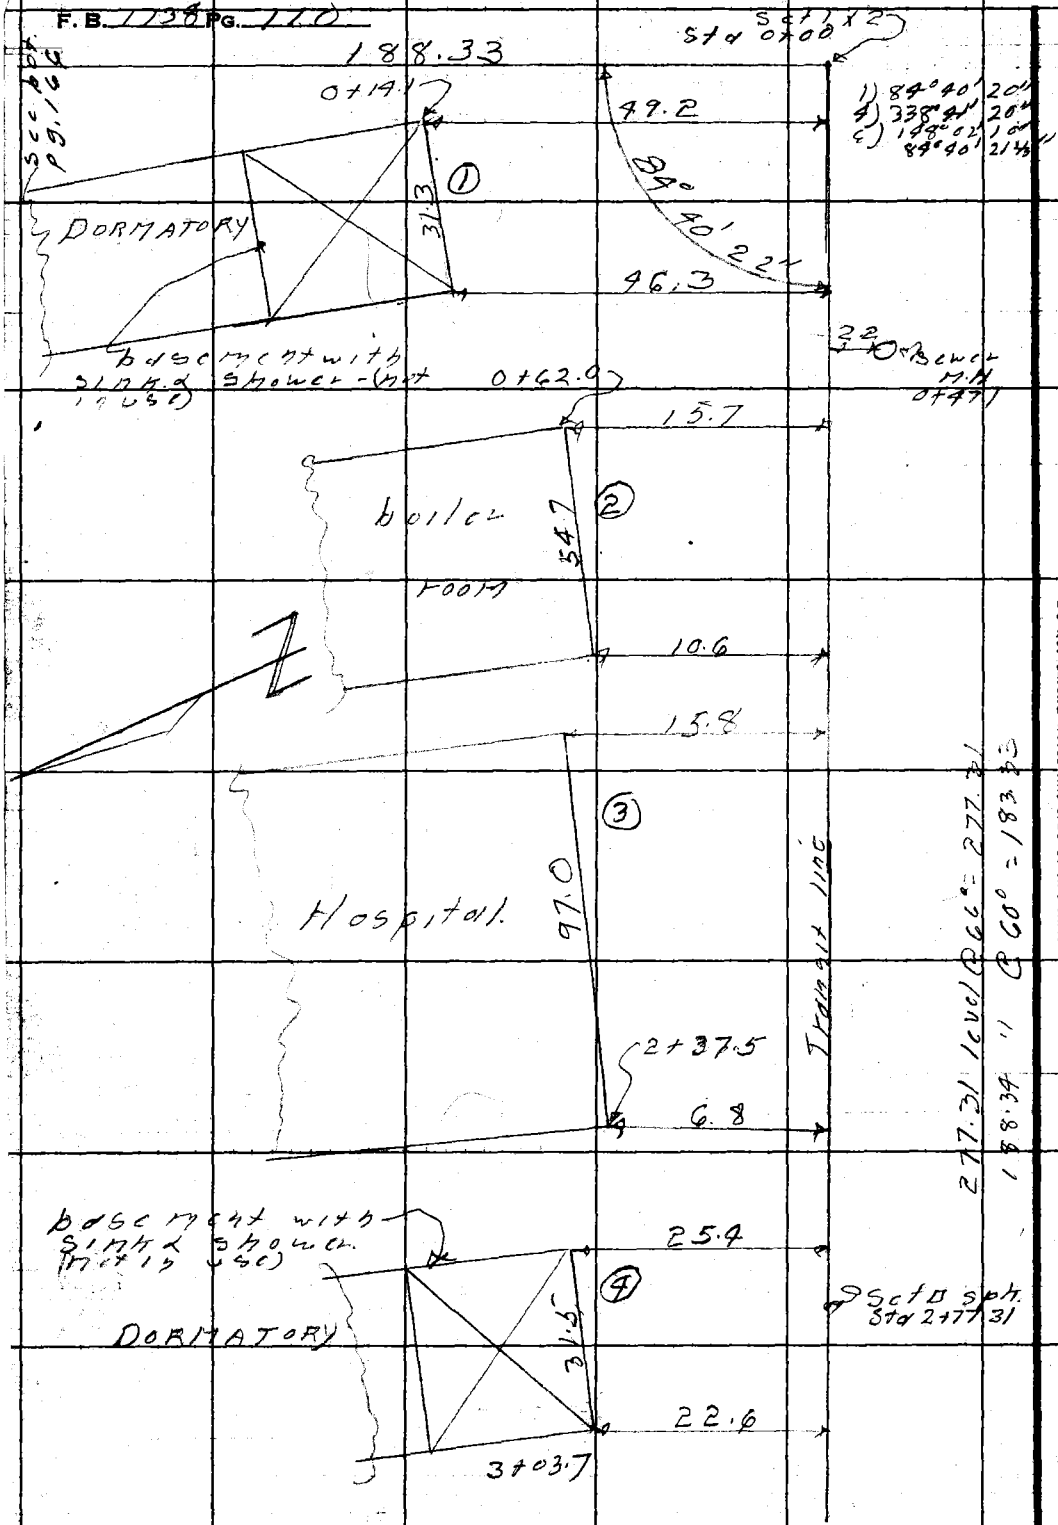

RETURN TO
LOS ANGELES COUNTY SURVEYOR
720 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No. ____ X-Sec. No. ____

Notes Red. ____ Date ____ Plotted ____ Date ____ Notes Chkd. ____ Date ____ Checked ____ Date ____

Job No 1462 Division No. ____

Survey of Castles Ave.

Survey by Lanigan Notes Lewis Date 5-15-

Map No. ____ Checked J. Johnson Date ____

F. B. 1738 Pg. 171

ELEVATIONS
OF
BUILDINGS AND SS MANHOLE

BOYS AND GIRLS AID SOCIETY
IN
TRACT 4702

C.I. 1462

V.J. Lanigan
C.H. Lewis
H.H. Raphael
H.C. Woodworth

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

761.298 307 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 1738 Pg. 172 | Job No. 1462 Division No. | Notes Red. | Plotted | Profile
Survey of Casitas Ave. | Date | No.
Survey by Lanigan Notes Lewis | Notes Chkd. | Checked | X-Sec.
Indexed C. Johnson Date | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.		
BM AE 521	11 14	1146 21		1135 07	AE 521 El 1135.066 FB 1568 P 153	
					El Sol Ave. (W. side) at Sacramento St.	
					Bt. spk. in curb 4' S. of ℄ prod of Sacramento St.	
			8 1/2	1133 1/2	basement floor of Bldg. #4	
			4 3/4	1141 1/4	ground at S.W. corner	" "
		(F)	1 0/2	1147 1/2	main floor	" "
			4 6/4	1141 1/4	ground at S.W. corner	Bldg #3
			2 3/4	1143 1/4	basement floor	" "
			4 5/4	1141 1/4	ground at S.W. cor.	Bldg #2
			3 7/4	1145 1/4	floor elev. of	" "
			6 8/4	1142 1/4	floor of sump in	" "
			3 4/4	1144 1/4	ground at S.W. cor.	Bldg #1
			9 9/4	1136 1/4	basement	" "
MH			9 86	1132 35	depth to flo line = 5.66 + 4.20 (rod to rim) = 9.86	
T. P.			4 15	1141 06	TP	
	5 56	1147 62				
T. P			2 78	1144 84	T. P	
	4 12	1148 96				
			4 44	1144 56	S. curb of Royce St at W. end.	
BM AE 519			3 49	1145 47	AE 519 El. 1145.459 FB 1568 P 152	
					Royce St. (N. side) 400'± W. of ℄ of Casitas Ave.	
					Bt. spk in curb in front of Ho. #733	

Profile No. | Notes Red. | Plotted | Job No 1462 | Division No.
Date | Date | Survey of Gaylord Avenue
X-Sec. No. | Notes Chkd. | Checked | Survey by Lanigan | Notes Lewis | Date 5-14-50
Date | Date | Map No. | Indexed C. Johnson

F. B. 1738 Pg. 173

PROFILE
of
TRANSIT LINE
IN
LOT 37 - M.R. 52-50

Mariposa St. North

C.I. 1462

V.J. Lanigan
C.H. Lewis
H.H. Raphael
H.C. Woodworth

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

96L298 307 4-50

76L298 307 4-50

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 1738 Pg. 174 | Job No. 1462 Division No. | Notes Red. | Plotted | Profile
Survey of Casitas Ave. | Date | No. | X-Sec.
Survey by Lanigan Notes Lewis | Notes Chkd. | Checked
Indexed C. Johnson Date | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	Transit	Lines
BM AE 501	7 32	1210 99		120.67	AE 501 El 1203.666 Crestford Dr. & Mariposa St. S.W. Cor. Bt. spk. in curb, 6' S of S end C.R.	FB 1568 P 135
0+00			2.44	1208 55	℄ of Mariposa St & ℄	
0+14			2 30	1209 69	edge of paving	
0+26			1 2/8	1209 8/8	b & k	
T. P.			1 18	1201 81	T. P	
	7 54	1217 35				
0+50			6 9/8	1210 5/8		
1+00			5 9/8	1211 5/8		
1+50			5 0/8	1212 4/8		
2+00			4 0/8	1212 4/8		
2+50			2 9/8	1214 5/8		
3+00			2 1/8	1215 5/8		
3+16			2 1/8	1215 3/8		
3+25			1 9/8	1215 5/8		
T. P.			9 17	1208 18	T. P.	
	2 62	1210 80				
BM AE 502			8 32	1202 48	AE 502 El 1202.466 Mariposa St. (S. Side) at W. end of St. end. Bt. spk. in W. end conc. catch basin	FB 1568 P. 136

RWFB 1823

1041

F. B. 1738 Pg. 175

Notes Ck'd by:
Map No.
Office Work
Checked
Date

Survey of Casitas Ave.
W. O. 8251 Tape No. 2131 Std. 66 °F
Surveyed by J. J. Lanigan
Notes J. J. L. Date 12-5-32
Indexed C. Johnson

M.S. 81-45

Note: Any Additions or Changes or This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Fd 1" I.P. 2.43' R.E. 2000' S.E. Cor. Tr. 12677 pcv. Tr. 12677

Cont. right of way

10.36'

131.25

Set 1X2

131.26' level @ 60° = 131.25'

89° 58' 10"

1) 89° 58' 10"
2) 359° 52' 40"
3) 179° 49' 00"
89° 58' 10"

SURVEY of Proposed Sewer Easement from a point 11.5 ft. Easterly of E. of El Nido Dr. on E. of Harriet St. to Southerly line of Tr. #12677 prod. and to Easterly line of Lot #8 Tr. #12677 and on Easterly line of Lot #8 Tr. #12677 to Cr. on East End Dr.

357.07'

357.09' level @ 60° = 357.07'

Transit line

1) 89° 58' 40"
2) 359° 55' 00"
3) 179° 52' 30"
89° 58' 45"

89° 58' 45"

Fd L.A. Co. Rd. Dept. Mon. Scc F.B. 1726-47

131.25'

Set 1X2

To S.W. ly @ Intsc of Casitas Ave per F.B. 1726-24

HARRIET ST.

EL NIDO DR.

(30)

131.25 level @ 64° = 131.25

78 FORM 247 2-51

F. B. 1726 PG. 176

PWFB 1823

1042

W.S. 88A-6

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

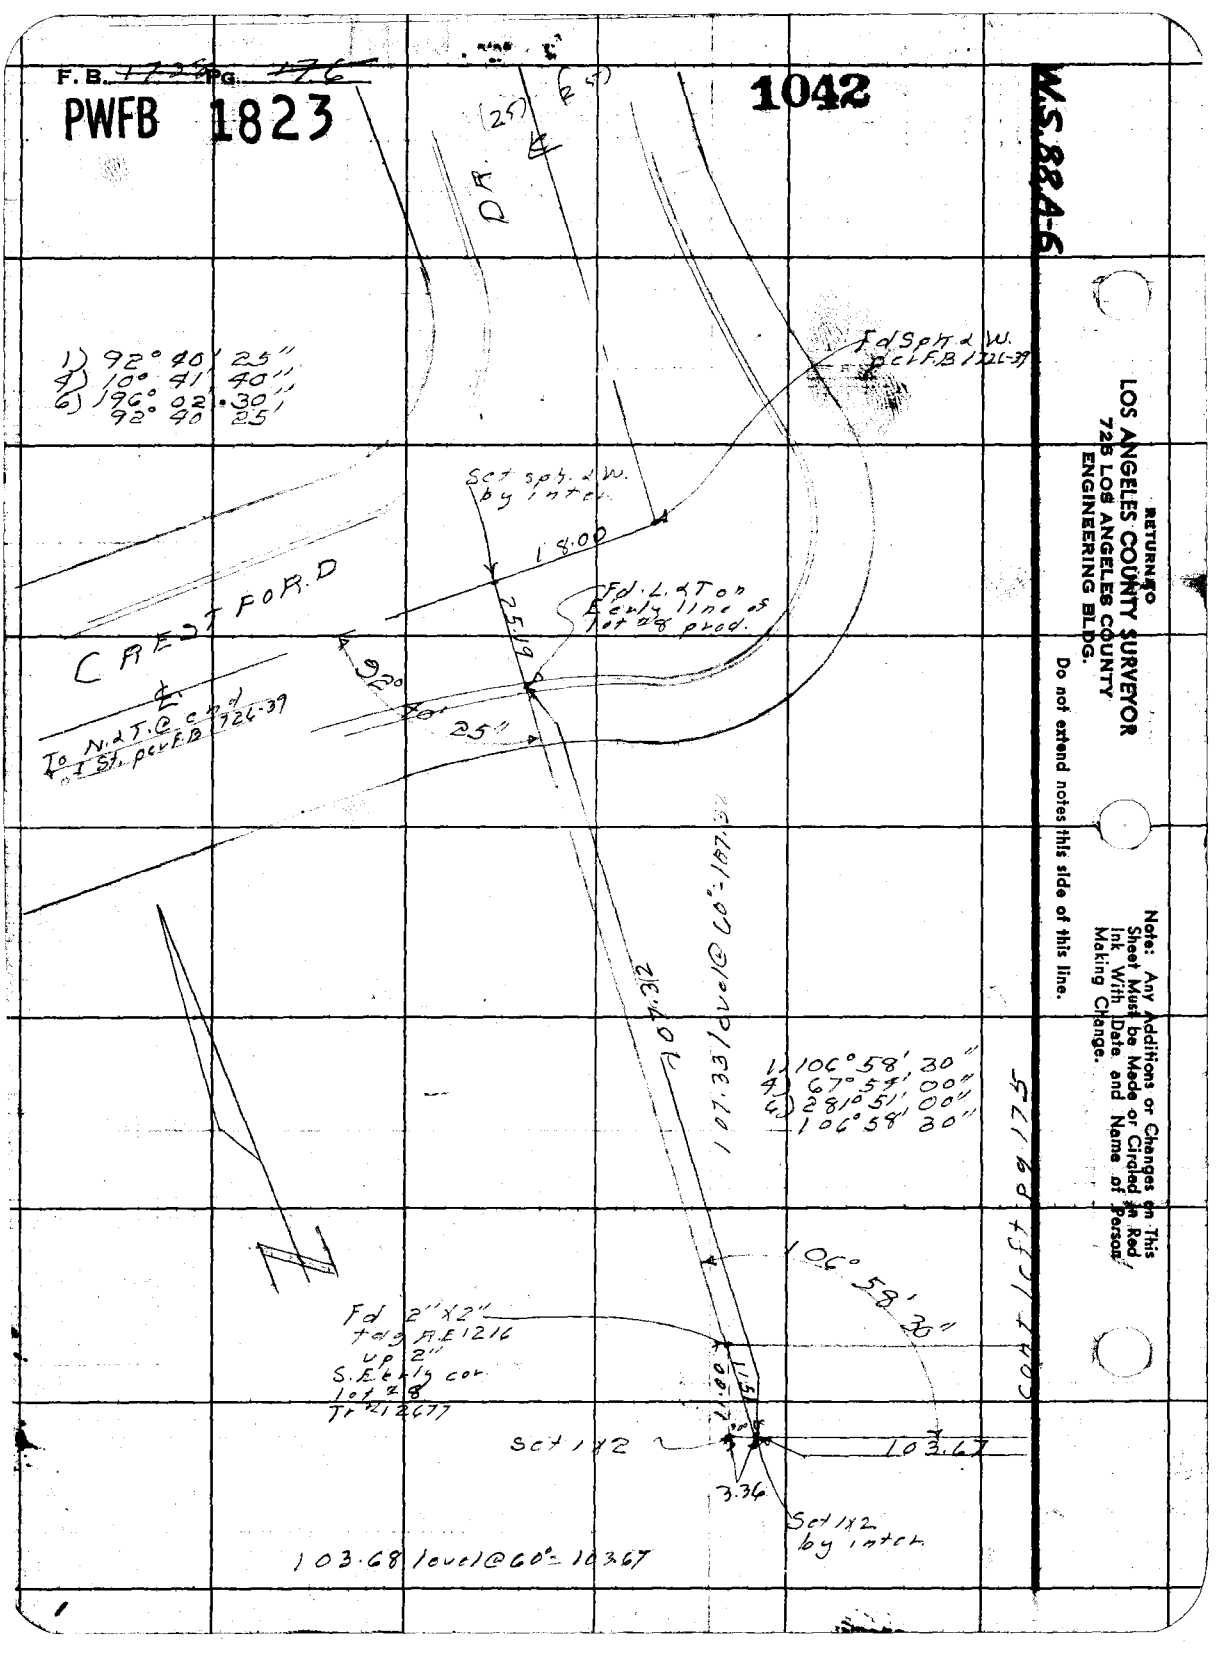

Notes C'k'd by:
Map No.
Office Work
Checked
Date

Survey of Castaic Area
W. O. 1462 Tape No. St'd. °F
Surveyed by J.J.L. Lonigan
Notes J.J.L. Date 12-5-52
Indexed C. Johnson

F. B. 1735 Pg. 177

Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
of
IMPROVEMENTS
on
PROPOSED EASEMENT
from
A POINT 115'± EASTERLY of E of EL NIDO DR.
on
E of HARRIET ST.
to
SOUTHERLY LINE of TR # 12677 PROD.
and to
EASTERLY LINE of LOT # 8 TR # 12677
and on
EASTERLY LINE of LOT # 8 TR # 12677
to
CRESTFORD DR.
C.I. 1462.

J.J. Lonigan
H. Nakaposki
J.C. Rife
A.P. Hoyr.

76F3095 247 2-51

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

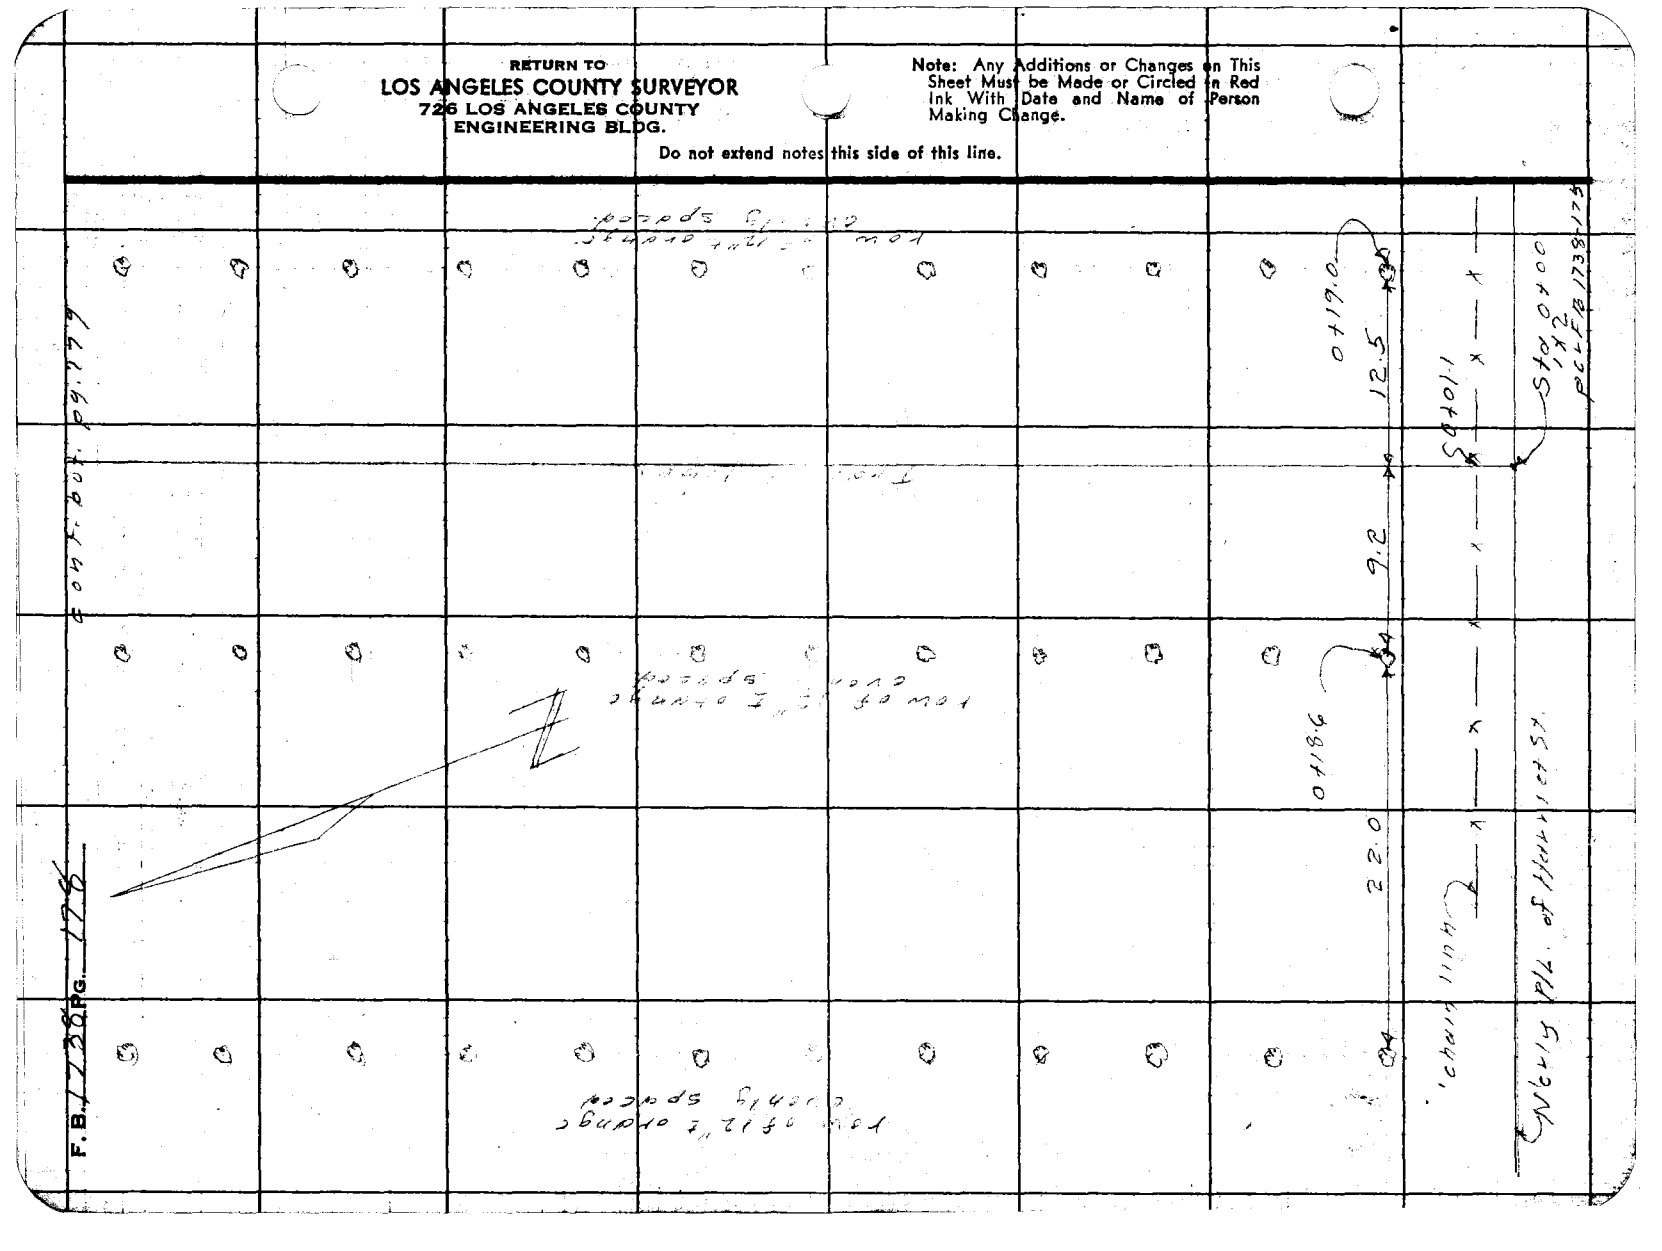

Notes C'k'd by:
Map No.
Office Work
Checked
Date

Survey of Casitas Ave.
W. O. 1462 Tape No. St'd. °F
Surveyed by J.J. Lanigan
Notes J. J. L. Date 12-5-57
Indexed C. Johnson

F. B. 733 PG. 170

Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note - all Trees 22' c to c to center.

2" water hydrant

9.8 12.4

22.0

Sta 3+57.07
1 x 2
pc of FB 1738-12

85 13.5

9.8 12.4

22.0

Bdy. Lot # 1.80

Row of 12" o maple

Row of 12" o maple

Row of 12" o maple

Missing tree

dead

cont. to p 17.8

76F3095 247 2-51

F.B. 1738 PG. 180

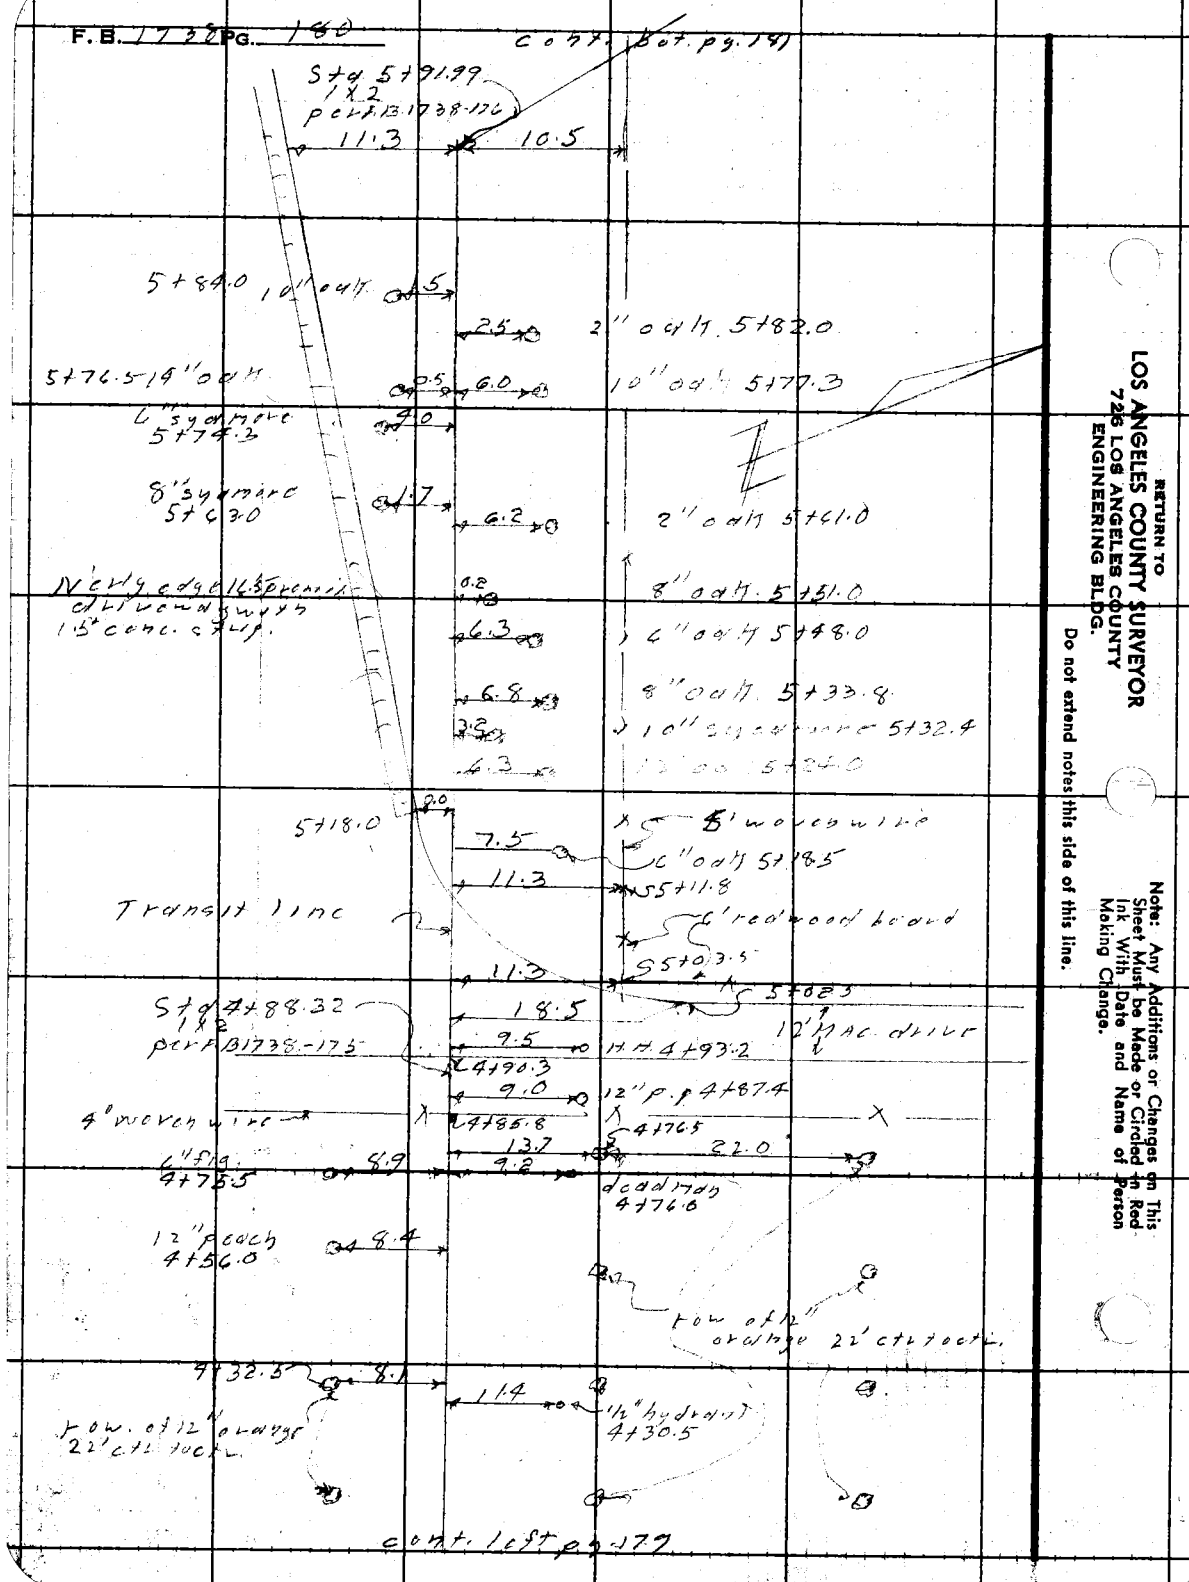

RETURN TO
LOS ANGELES COUNTY SURVEYOR
725 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Notes: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Plotted Ck'd by:
Map No.
Office Work
Checked
Date

Survey of: Crestford Ave
W. O. 1462 Tape No. St'd. °F
Surveyed by: J. J. Lamigan
Notes: J. J. L. Date 12-5-52
Indexed: A. C. Johnson

F. B. 1736 PG. 181

Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76F3095 247 2-51

5+00.7+24.50
P.C.C. B1738-17

℄

CRESTFORD DR.

Curb
7+01.0
1.0
13.6
conc. drive
6+94.8
1.7
6+93.8
1.3
0.7
6+88.7
edge 7.5' pvc-mix drive
4.1
35.5
6+60.5
0.9
1.5
1.0
35.1
1 story stucco House
20.2
Stucco garage
4.3
6+28.2
18.0
1.0
0.7
6+22.8
6+19.5
6+12.2
4' 4" clothes line post
1.2
5' redwood board
6+03.5
Sta 5+97.99
1 x 2
P.C.C. B1738-17
Switch wire

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

F.B. 1738 Pg. 152

Profile No. ____ X-Sec. No. ____

Notes Red. ____ Date ____ Plotted ____ Date ____
Notes Chkd. ____ Date ____ Checked ____ Date ____

Job No. 1462 Division No. ____
Survey of CASITAS AVE
Survey by J.J.L. Notes M.N. Date 12-5-62
Map No. ____ Inked C. Johnson Date ____

F.B. 1738 Pg. 183

PROFILE & X SECTIONS

on

PROPOSED SEWER EASEMENT

from

A POINT 115'± EASTERLY of ℄ of EL NIDO DR

on

℄ of HARRIET ST

to

SOUTHERLY LINE of TR.# 12677 PROD.

and to

EASTERLY LINE of Lot #8 TR# 12677

and on

EASTERLY LINE of LOT #8 TR# 12677

to

CRESTFORD DR

C.L. 1962

STATION	B.S.	H.I.	F.S.	ELEV.

J.J. LANIGAN
M. NATAPOFF
J.C. RIKE
A.P. HOAR

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76L298 307 10-51

76L298 307 10-51

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1738 Pg. 8 Job No. 1462 Division No. Notes Red. Plotted Profile
Survey of CASITAS AVE Date Date No. X-Sec.
Survey by J.J. LANIGAN Notes Chkd. Checked
Index C. Johnson Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.		
BM.AE524	8.96			1187.60	BM.AE524-EL.1187.600 per F.B.1568-156	
					EL NIDO DR. (W. side) @ HARRIET ST. BT.	
		1196.56			spk. in conc. walk to HO.# 2909.	
0-15			5.89	1190.67		tr/L - edge pav
0+00			5.2	1191.4		tr/L @ ℄ HARRIET ST.
0+01			4.9	1191.7		" 6'L
"			4.6	1192.0		9' R
"			5.9	1190.7	41' L	
1+00			2.6	1193.0		tr/L
"			2.4	1194.2		9' R
"			3.6	1193.0	41' L	
T.P.			2.09	1194.47		
	6.78	1201.25				
2+05			4.8	1196.5		tr/L
			4.7	1196.6		9' R
			5.9	1195.4	41' L	
3+00			3.7	1197.6		tr/L
			3.6	1197.7		9' R
			4.5	1196.8	21' L	
T.P.			3.65	1197.60		

76L298 307 10-51

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. 4462 Division No.____ F.B. 1738 Pg. 65
No.____ Date____ Date____ Survey of Cassitas Ave
X-Sec. ____ Notes Chkd____ Checked____ Survey by J.J.L. Notes J.J.L. Date 12-5-52
No.____ Date____ Date____ Map No.____ Indexed C. Jones Date

STATION	B. S.	H. I.	F. S.	ELEV.		
T.P.				119760		
	584	120344				
3+57.07			49	11985		tr/L - ⊥ pt.
"			48	11986		9'R - east
"			43	11991		36'R - north
4+00			57	11977		tr/L
"			64	11970		36'R
"			62	11972	12'L	
T. P.			561	11978		
	340	120123				
4+89.32			50	11962		tr/L @ Tr. cor.
			48	11964		11'R
			50	11962	4'L	
4+91			508	11961		tr/L - edge pave
			490	11963		11'R
			518	11960	4'L	
T.P.			595	11952		
	478	120006				
5+92.99			43	11958		tr/L - @ P/L
			44	11957	5.5'L - bk (Go.)	
			52	11949	12.5'L - bk to edge Pav	

76L298 307 10-51

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

B. 1738 Pg. 18 Job No. 1462 Division No. Notes Red. Plotted Profile
Survey of CASITAS AVE Date No. X-Sec.
Survey by J.J. LANGAN & C. TORRES-M. NATAROFF Notes Chkd. Checked
Indexed Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.		
		120006				
6+04			46	11955		Prop cor.
			46	11955		6'R
			45	11956	6'L	
T.P.			368	11963.8		
	475	1201.13				
6+69			47	11964		P/L
			43	11968		6R'
			472	11964.1	6'L	
7+00.32			480	11963.3		P/L - cb
"			525	11950.8		" - gut
7+25.51			475	11963.8		P/L - int. @ St. ℄
B.M. AE500			677	11943.6	B.M. AE500 - EL. 1194.363 per FB 1568-135 CRESTFORD DR. @ W. end of St. Bt. spk. in cb. 1' N. of ℄ prod.	

Notes Ck'd by	Survey of CASITAS AVE.
Map No.	W. O. 1462 Tape No. St'd. °F
Office Work	Surveyed by J. J. LANIGAN
Checked	Notes J. J. L. Date 5-19-53
Date	Indexed C. C. Johnson

F. B. 1756 Pg. 157

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
of
LOW HOUSES
and
SEWER OUTLETS
on
MOUNTAIN VIEW RD.
from
CASITAS AVE.
to
WINDSOR AVE
C.I. 1462.

J. J. LANIGAN.
M. NATAROFF.
J. C. RITE
W. N. WILLIAMS

76F309S 247 2-51

F. B. 1726 PG. 1-55

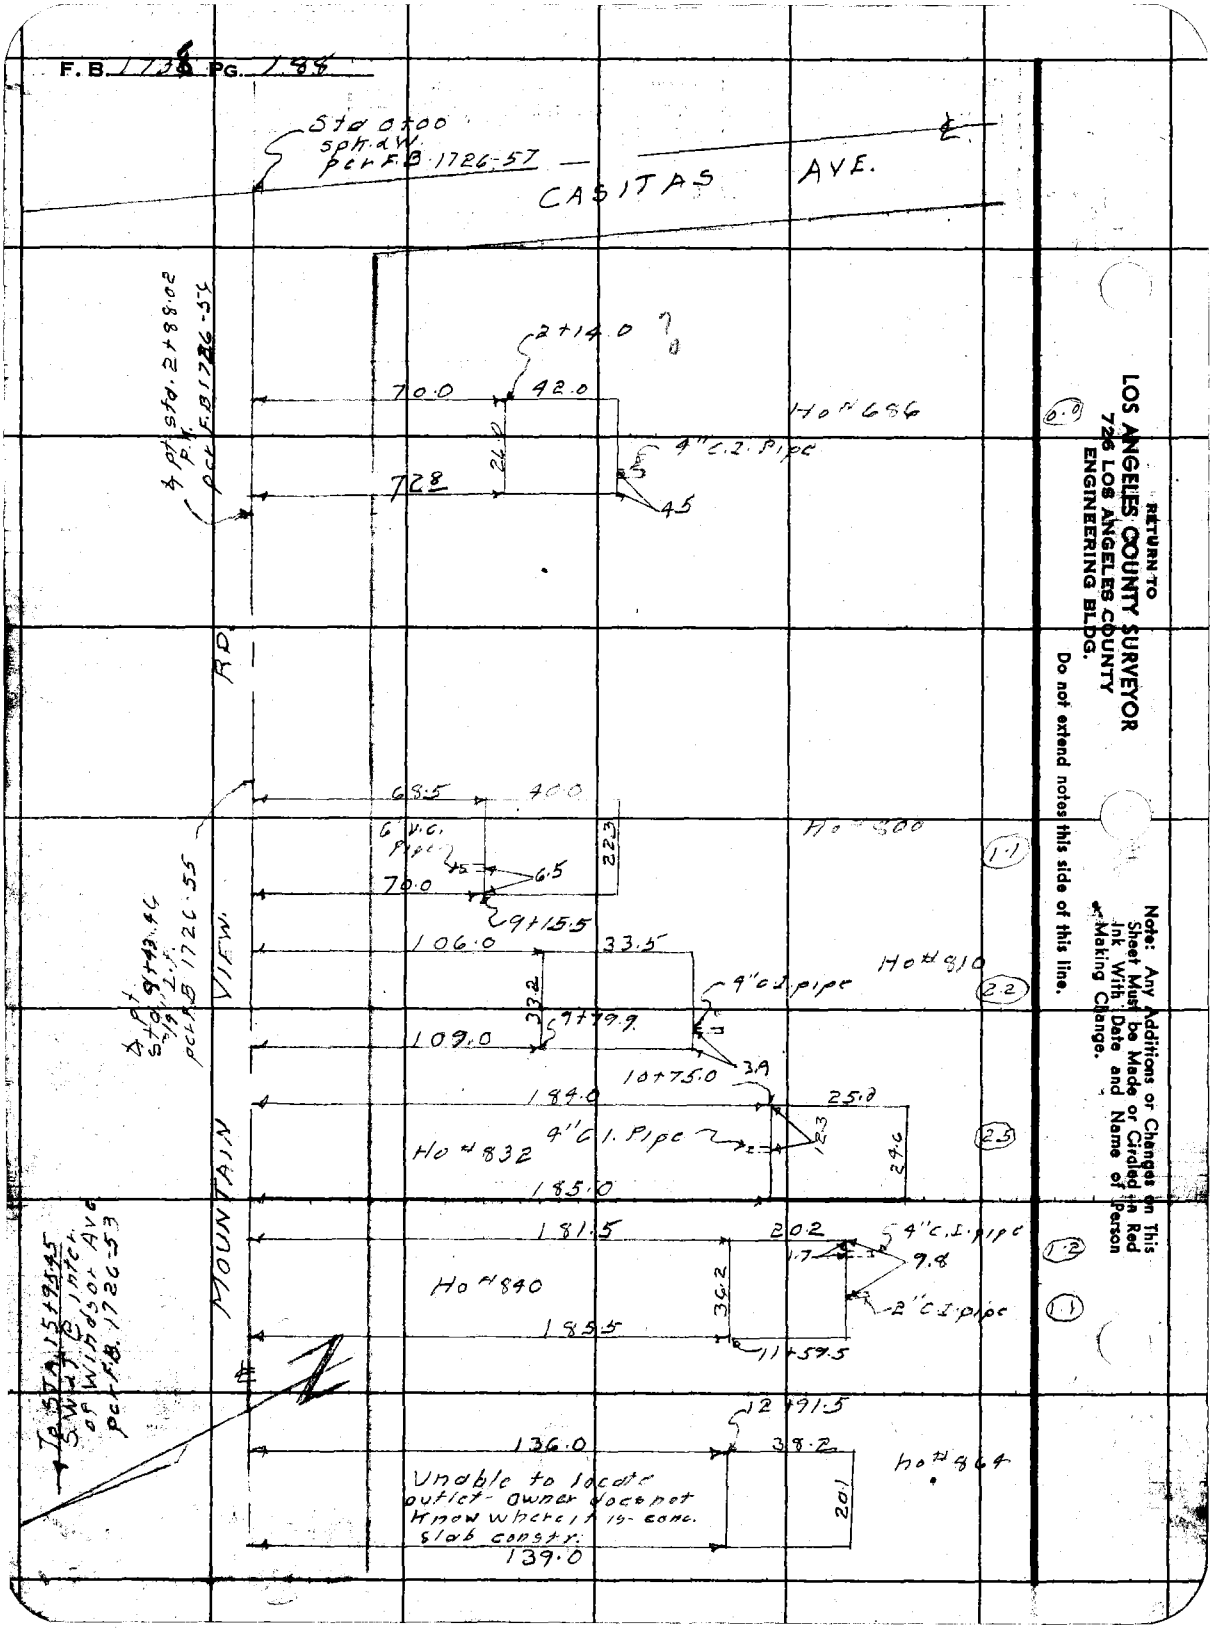

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No. | X-Sec. No. | Notes Red. | Date | Notes Chkd. | Date | Plotted | Date | Checked | Date | Job No. 1462 | Division No. V | Survey of CASITAS AVE | Survey by T.L.L. | Notes [illegible] | Map No. [illegible] | Indexed C. Johnson | Date | F.B. 1736 Pg. 189

ELEVATION
on
OUTLETS
of
HOUSES
on
MOUNTAIN VIEW RD.
from
CASITAS AVE.
to
WINDSOR AVE.

C.I. 1462

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.

J.T. LANIGAN
M. NATAPOFF
J.C. RIKE
W.N. WILLIAMS

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76L298 307 10-51

76L298 307 10-51

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1731 Pg. 190 Job No. 4462 Division No. V Notes Red Plotted
Survey of CAST. TAS AVE Date Profile
Survey by J. LANGAN Notes MANHATTAN BCH Notes Chkd Checked X-Sec.
Indexed C. JOHNSON Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	MOUNTAIN VIEW RD.
BM. AE-517				1158.82	BM. AE-517 - EL. 1158.823 per F.B. 1568-149
	351	116233			Mountain View Rd. & Casitas Ave. (N.W. cor.) Bk.
					spk. in cb. 5' W. of W. end of C.R.
3+35.5			74	1154.9	72.3 So. grd el. @ 4" C.I.P.
"			75	1154.8	" " el. tp. 4" C.I.P.
T.P.			530	1157.03	T.P.
	564	116267			
T.P.			603	1156.64	T.P.
	481	116145			
9+09			62	1155.3	70' So. - grd. el. @ 6" V.C.P.
"			73	1154.2	" " - el. tp 6" V.C.P.
9+76			72	1154.3	142' So. - grd. el. @ 4" C.I.P.
"			94	1152.1	" " - el. tp. 4" C.I.P.
T.P.			583	1155.62	T.P.
	525	116087			
10+87.5			81	1152.8	184.5' So. - grd. el. tp. 4" C.I.P.
"			106	1150.3	" " tp. 4" C.I.P.
11+25			82	1152.7	201.2 So. - grd. el. tp. 4" C.I.P.
"			94	1151.5	" " tp. 4" C.I.P.
11+33.1			80	1152.9	203.5 So. - grd. el. tp. 2" C.I.P.

76L298 307 10-51

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	MOUNTAIN VIEW RD.
		116087			
11+33			91	11518	203 E So. - tp. 2" C.I.P.
T.P.			537	15550	T.P.
	475	116025			
12+91 E			84	11519	174 E So. - grd. el. @ S.E. cor. Ho. 864
13+02			86	11517	177 E " " " " S.W. " " "
BM. AE496			421	11560	BM. AE-496 - EL. 1156.048 per F.B. 1568-33 WINDSOR AVE. & MOUNTAIN VIEW RD. (N.E. cor.) Bt. spk. in cb. 5' E. of W. end.

Profile
No. _____ Notes Red _____ Plotted _____ Job No. 496 Division No. 7
X-Sec. No. _____ Date _____ Date _____ Survey of CASITAS STATE
Notes Chkd. _____ Checked _____ Survey by T.T.L. Notes W.M. Date 5-14-53
Date _____ Date _____ Map No. _____ Indexed _____ C. J. Date _____

F.B. 1738 PG. 121

F.B. 1738 PG. 192 Job No. 4462 Division No. ✓ Notes Red. _____ Plotted _____ Profile

Survey of CASITAS AVE Date _____ Date _____ No. _____

Survey by J.J. LANIGAN Notes M. NAPOFF Notes Chkd. _____ Checked _____ X-Sec.

Indexed _____ Date _____ Date _____ Date _____ No. _____

STATION	B. S.	H. I.	F. S.	ELEV.
				MOUNTAIN VIEW RD

76L298 307 10-51

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR

726 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend notes this side of this line.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of CASITAS AVE
W. O. 1962 Tape No. St'd. °F
Surveyed by J.J. LANIGAN
Notes J.J.L. Date 5-14-53
Indexed A. C. Johnson

F. B. 1736 Pg. 173

Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
724 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
of
LOW HOUSES
and
SEWER OUTLETS
on
MOUNTAIN VIEW RD
from
CASITAS AVE.
to
LINCOLN AVE
C.I. 1462

J.J. LANIGAN
M. NATAPOFF
J.C. RITE
W.N. WILLIAMS

76F309S 247 2-51

F. B. 1726 PG. 194

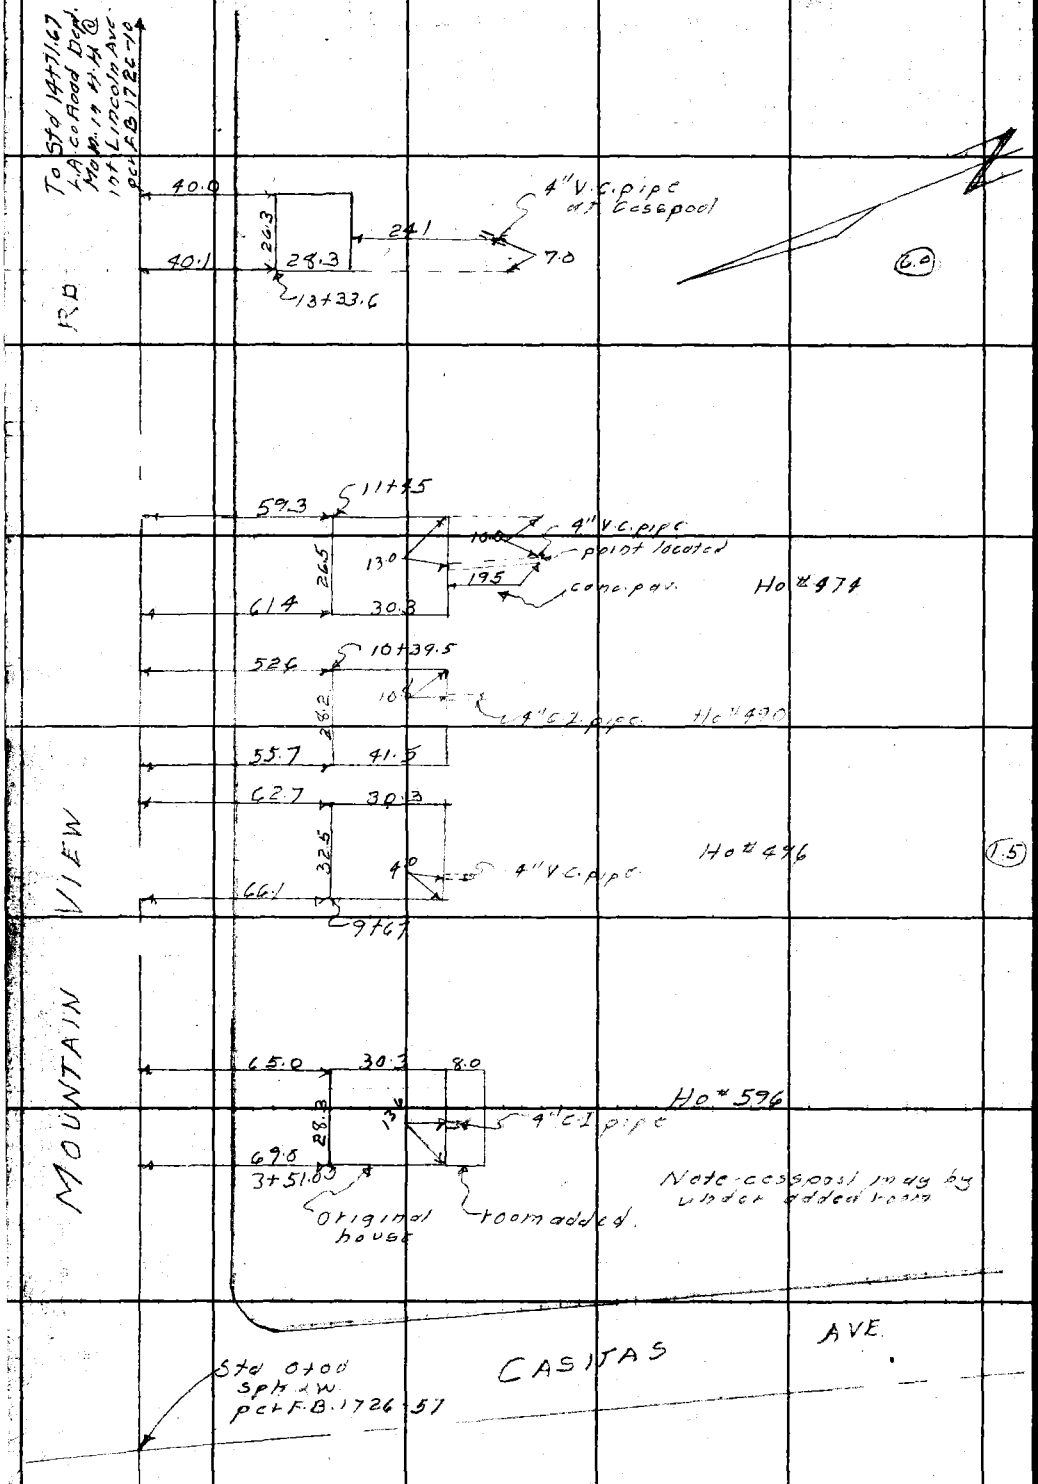

Profile No. | X-Sec. No. | Notes Red. | Date | Notes Chkd. | Date | Plotted | Date | Checked | Date | Job No. 1462 | Division No. V | Survey of CASITAS AVE. | Survey by J.J.L. | Map No. | Indexed | F.B. 1738 Pg. 195 | Notes M.A.L. Date 5-14-59 | C. Johnson Date

ELEVATIONS of HOUSE CONNECTIONS on MOUNTAIN VIEW RD. from CASITAS AVE. to LINCOLN AVE.

C.I. 1462

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

STATION	B.S.	H.I.	F.S.	ELEV.

J.J. LANIGAN
M. NATAPOFF
J.C. RIKE
W.N. WILLIAMS

76L298 307 10-51

76L298 307 10-51

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1736 PG. 196 Job No. 4462 Division No. V Notes Red. Plotted
Survey of CASITAS AVE Date Date
Survey by I. KANIGAN Notes Chkd Checked
Indexed by C. Johnson Date Date

Profile No. X-Sec. No.

STATION	B. S.	H. I.	F. S.	ELEV.	MOUNTAIN VIEW RD
BM AE-517				1158.82	BM. AE-517 - EL. 1158.823 per F.B. 1568-149
	358	1162.40			MOUNTAIN VIEW RD. & CASITAS AVE. (N.W. cor.) Bt.
T.P.			505	1157.35	spk. in ob. 5' W. of W. end of C.R.
	503	1162.38			
3+64.5			67	1155.7	97.3 So. - grd. el. @ 4" C.I.P. (inside Ho-hL.)
"			69	1155.5	" " - el. tp. 4" C.I.P. (" " h.L.)
T.P.			404	1158.34	T.P.
	764	1165.98			
T.P.			365	1162.33	T.P.
	598	1168.31			
9+71.0			79	1160.4	96.5 So. - grd. el. @ 4" V.C.P.
"			94	1158.9	" " - el. tp. 4" V.C.P.
10+29.5			77	1160.6	95.3 So. - grd. el. @ 4" C.I.P.
"			83	1160.0	" " - el. tp. 4" C.I.P.
T.P.			500	1163.31	T.P.
	508	1168.39			
11+35			82	1160.2	109.8 So. - grd. el. @ 4" V.C.P.
"			112	1157.2	" " - el. tp. 4" V.C.P.
11+32			74	1161.0	90.3 So. - grd. el. @ house
T.P.			569	1162.70	T.P.
	497	1167.67			

76L298 307 10-51

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red Plotted Job No. 4462 Division No. V F.B. 1738 Pg. 197
No. Date Survey of CASITAS AVE
X-Sec. Notes Chkd Date Checked Date Survey by J.T.E. Notes M.M. Date 5-7-51
No. Date Map No. Inked C. JENSEN

STATION	B. S.	H. I.	F. S.	ELEV.	MOUNTAIN VIEW RD.
		1167 67			
13+40 ±			76	11601 ·	92± So.-grd. el. @ 4" V.C.P.
"			136	11541 ·	" " - el. tp. 4" V.C.P.
B.M. AE-240			667	11600	B.M. AE-240 - EL. 1161.026 per F.B. [illegible] - R/W LINCOLN AVE. & MOUNTAIN VIEW RD. (E. cor.) Bl. spk. in cb. 15' S. of S. end C.R.

F.B. 1738 PG. 198 Job No. 1462 Division No. V Notes Red. Plotted Profile

Survey of CASITAS AVE Date Date No.

Survey by J.J. LANIGAN Notes M. NATAPOFF Notes Chkd Checked X-Sec.

Indexed Date Date Date No.

761.298 307 10-51

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR

726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.	
					MOUNTAIN VIEW RD

Notes Ck'd by	Survey of CASITAS AVE
Map No.	W. O. 1462 Tape No. St'd. °F
Office Work	Surveyed by J.J. LANIGAN
Checked	Notes J.J.L. Date 5-15-53
Date	Indexed A. C. Johnson

F. B. 1736 Pg. 196
199

Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
of
LOW HOUSES
and
SEWER OUTLETS
on
VENTURA ST
from
WINDSOR AVE.
to
LINCOLN AVE
C. I. 1462

J.J. Lanigan
M. NATAPOFF.
J.C. RITE.
W.N. WILLIAMS

76F3095 247 2-51

F. B. 173 Pg. 200

cont 6 of pg 201

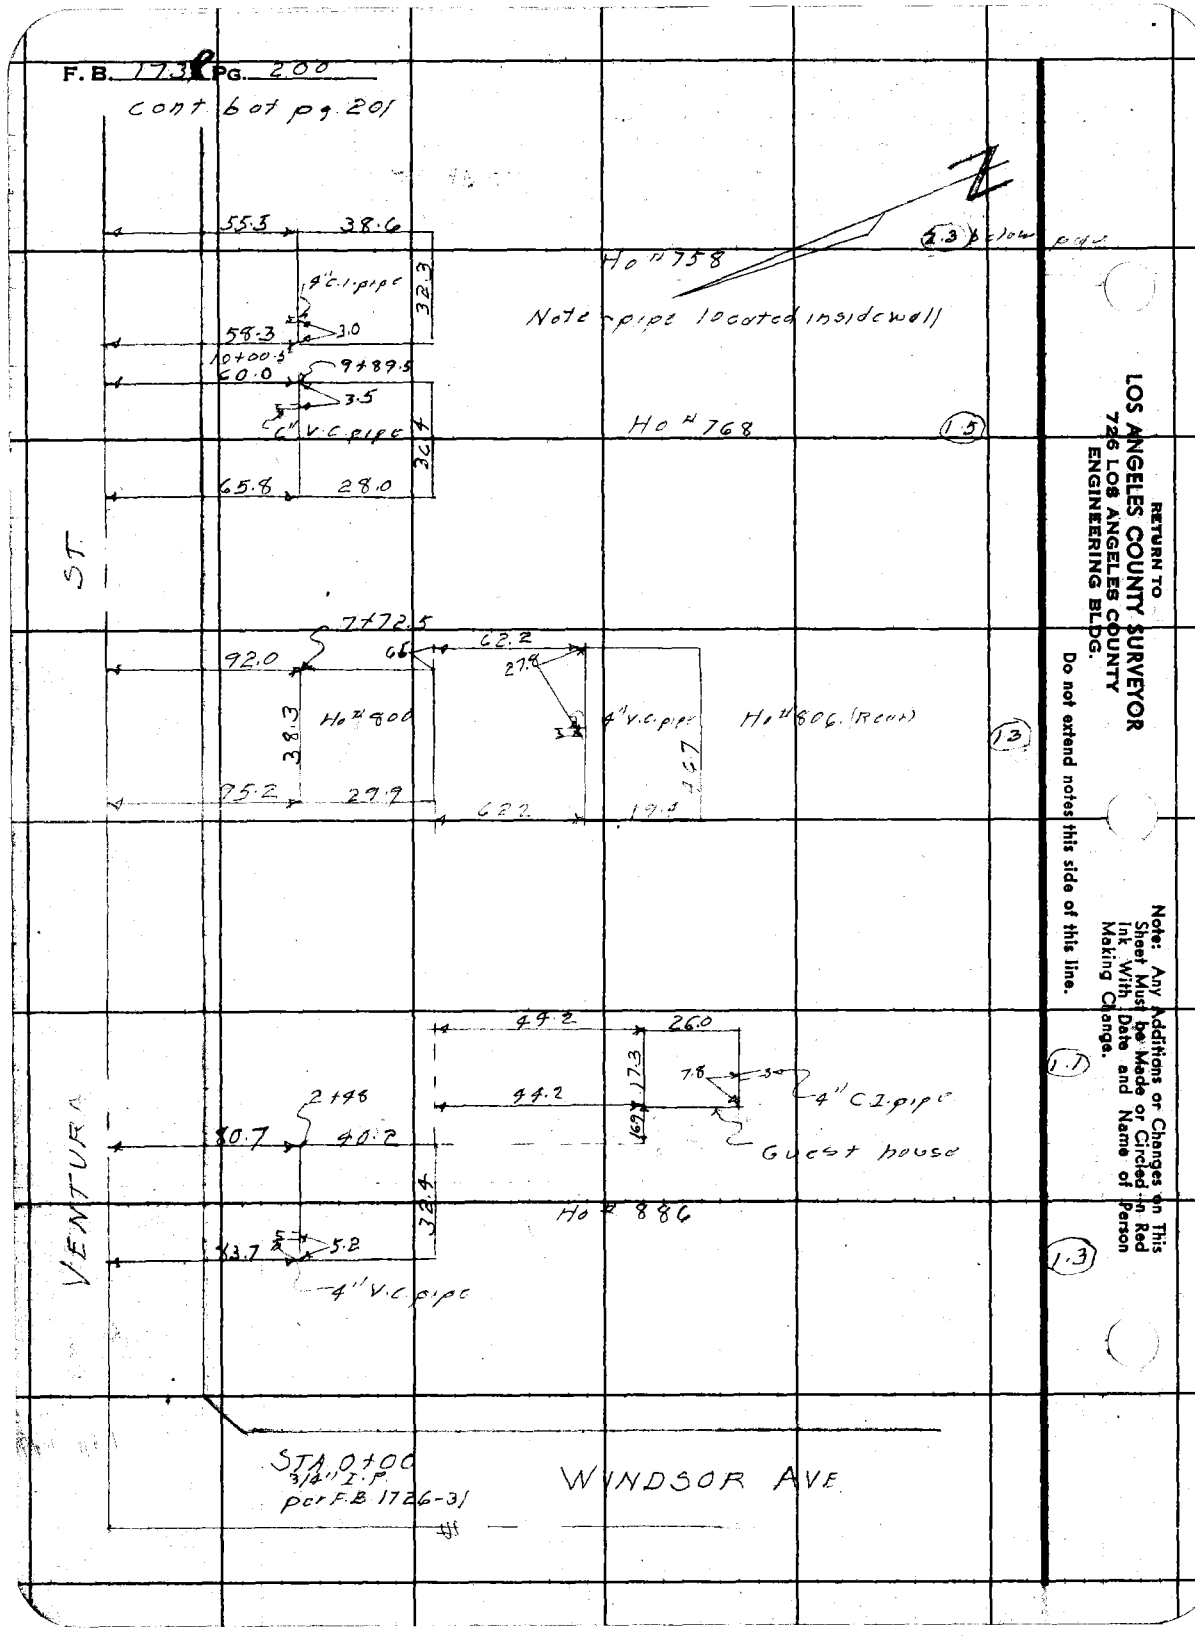

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of CASITAS AVE
W. O. 1462 Tape No. St'd. °F
Surveyed by J.S. LANIGAN
Notes J.L. Date 5-13-53
C. Johnson
Indexed

F. B. 1730 Pg. 201

Cont. from pg. 202.

Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
720 LOS ANGELES COUNTY
ENGINEERING BLDG.

76FS095 2.47 2.81

ST.

VENTURA

59.6 34.3 32.5 3.2 3.0

Ho # 680

(7.0)

Tub in b'sm't
Outlet 1½' above floor.

62.6

℄ 15+02.0

69.5 ℄ 13+69.2 30.0

7.0

4" C.I. pipe

Ho # 706

(6.1)

72.3 34.3

72.5 ℄ 12+68.0 14.5 40.3

4" C.I. pipe

Ho # 720

(2.2)

75.0 32.5

78.0 41.7 35.0 10.7 19.3 Wash room

Unable to locate outlet owner does not know where it is. May be under pav.

35.0 30.5 21.3

Ho # 730

80.5

℄ 11+82.5

30.6 40.4

℄ 11+56.0

67.0 39.0 Guest house 24.3

(2.0)

30.6 ℄ 13.0 34.0

4" C.I. pipe

71.0 52.0

Ho # 740

F. B. 1738 PG. 20

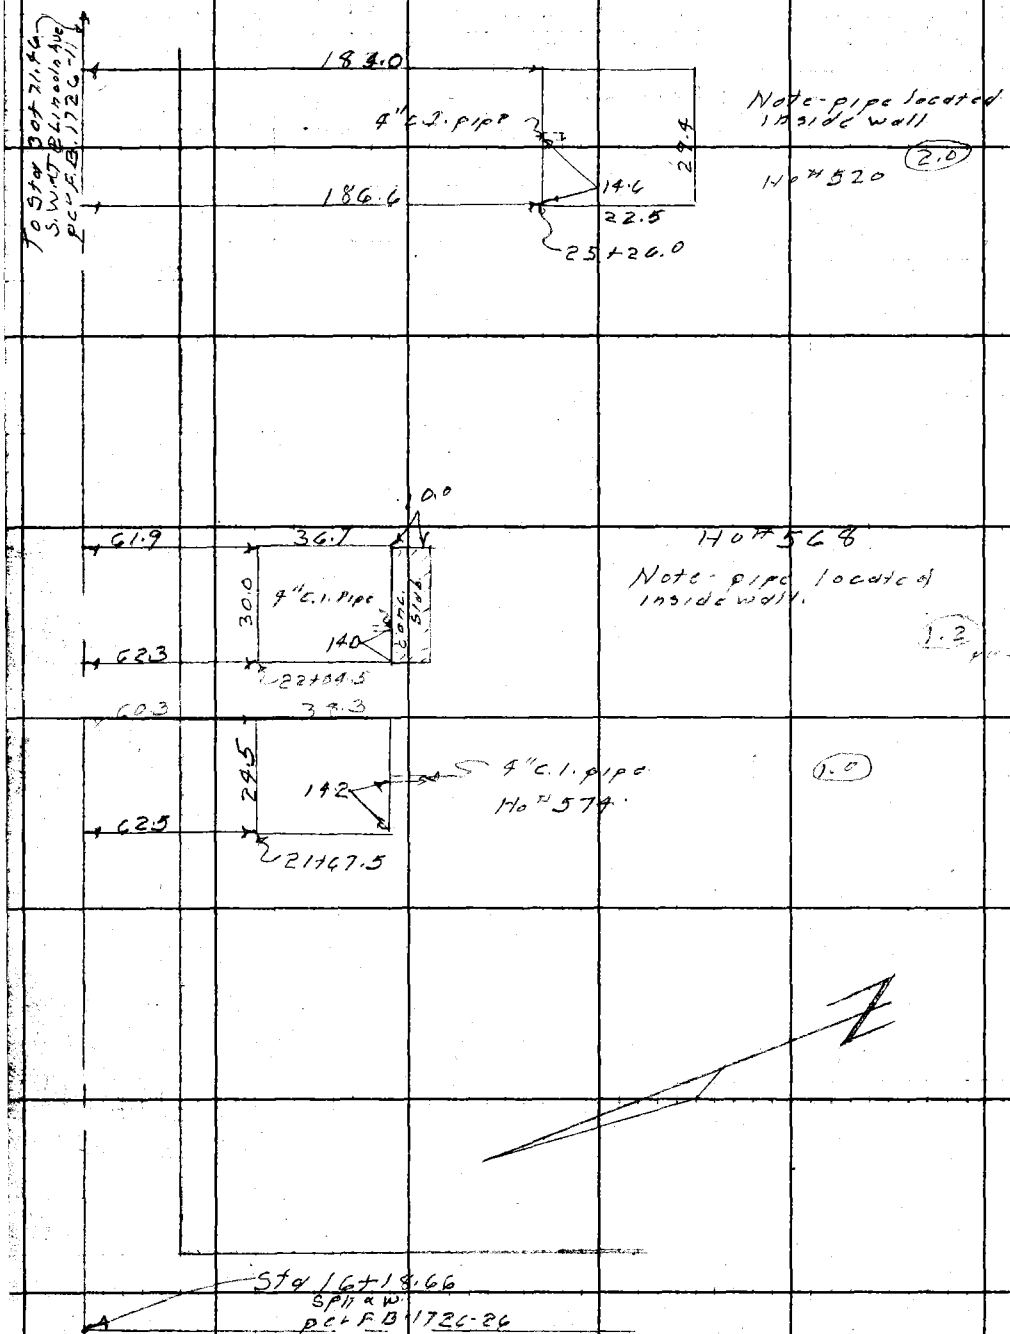

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No. ____ X-Sec. No. ____

Notes Red. ____ Date ____ Plotted ____ Date ____ Job No. 1462 Division No. V | F.B. 1738 Pg. 203

Notes Chkd. ____ Date ____ Checked ____ Date ____ Survey of CASITAS AVE

Survey by J.J.L. & C. Johnson Notes M.N. Date 5-15-33

Map No. ____ Indexed ____ Date ____

ELEVATIONS of HOUSE CONNECTIONS on VENTURA ST. from WINDSOR AVE. to CASITAS AVE.

C.I. 1462

STATION	B.S.	H.I.	F.S.	ELEV.
		J.C. RIKE W.N. WILLIAMS	J.J. LANIGAN M. NATAPOFF	

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76L298 307 10-51

F.B. 1738 Pg. 204 Job No. 1462 Division No. V Notes Red. Plotted
Survey of CASUELAS AVE Date Date No. X-Sec.
Survey by L.A. CO. SURVEYOR Notes L.A. CO. SURVEYOR Notes Chkd Checked
Indexed C. JOHNSON Date Date Date No.

76L298 307 10-51

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	VENTURA ST.
BM AE-497				1168.06	BM AE-497 - EL. 1168.061 per F.B. 1568-134
	371	1171.77			VENTURA ST. & STERLING PL. (N.E. cor.)
					Bt. spk. in cb. 6' N. of S. end.
2+20.8			62	1165.6	83.2 So. - grd. el. @ 4" V.C.P.
"			75	1164.3	" " - el. tp. 4" V.C.P.
2+62.2±			83	1163.5	82.2± So. - grd. el. @ 4" C.I.P.
"			94	1162.4	" " - el. tp. 4" C.I.P.
T.P.			506	1166.71	T.P.
	559	1172.30			
T.P.			473	1167.57	T.P.
	524	1172.81			
7+51.2			70	1165.8	184± So. - grd. el. @ 4" V.C.P.
"			83	1164.5	" " - el. tp. 4" V.C.P.
T.P.			441	1168.40	T.P.
	544	1173.84			
9+86			54	1168.4	61.2± So. - grd. el. @ 4" V.C.P.
"			69	1166.9	" " - el. tp. 4" V.C.P.
10+03.5			75	1166.3	58.3 So. - el. tp. 4" C.I.P. (inside house)
T.P.			309	1170.75	T.P.
	538	1176.13			

76L298 307 10-51

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ Notes Red ____ Plotted ____ Job No. 4462 Division No. V F.B. 1738 PG. 205
X-Sec. No. ____ Date ____ Date ____ Survey of VENTURA ST.
Notes Chkd ____ Checked ____ Survey by J.J.L. C. J. Notes Checked
No. ____ Date ____ Date ____ Map No. ____ Indexed ____ Date ____ Date 7-15-53

STATION	B. S.	H. I.	F. S.	ELEV.	VENTURA ST.
		1176 13			183.679.
11+43±			84	11677	182± 5o.-grd. el. @ 4" C.I.P.
"			104	11657	" " el. tp. 4" C.I.P.
BM AE 505			552	11706	BM AE 505 - El. 1170.612 per F.B. 1568 - 11
					VENTURA ST. (S. side) @ CASITAS AVE. BM tag
	567	1176 28			in cb. 10'± W. of ℄ prod. of CASITAS AVE.
12+03±			80	11683	164.7'± 5.- grd. el. @ S.W. cor. Washroom
"			74	11689	" " " - floor el. washroom
12+53±			35	11728	73.5'± 5.- grd. el. @ 4" C.I.P.
"			57	11706	" " " - el. tp. 4" C.I.P.
T.P.			281	11734.7	T.P.
	465	1178 12			
13+62±			68	11713	104'± 5.- grd. el. @ 4" C.I.P.
"			75	11701	" " " - el. tp. 4" C.I.P.
T.P.			472	11734.0	T.P.
	537	1178 77			
15+08±			32	11756	88.9'± 5 - floor level of Ho# 680
"			102	11686	" " - " " " basement

76L298 307 10-51

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

F.B. 1738 PG 206 Job No. 4462 Division No. V Profile No. X-Sec. No.
Survey of CASITAS AVE Notes Red Date Plotted
Survey by LV LANGSAN Notes Chkd Date Checked
Indexed C. Johnson Date Date

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	VENTURA	ST
		1178 77				
T.P.	653	1182 63	267	1176 10	T.P.	
21+81 I			78	1174 8	92'± S. - grd. el. @ 4" C.I.P.	
"			88	1173 8	" " " - el. tp. 4" C.I.P.	
T.P.	540	1182 45	558	1177 05	T.P.	
22+18 ±			65	1176 0	98 ± S. - grd. el. @ 4" C.I.P.	
"			77	1174 8	" " " - el. tp. 4" C.I.P.	
T.P.			307	1179 38	T.P.	
	542	1184 80				
25+406 ±			96	1175 2	185'± S. - grd. el. @ 4" C.I.P.	
"			116	1173 2	" " " - el. tp. 4" C.I.P.	
T.P.			553	1179 27	T.P.	
	456	1183 83				
BMAE 508			540	1178 43	BMAE 508 - EL. 1178.431 per F.B. 1568-140 VENTURA ST. (S. side) 880'± W. of ℄ of LINCOLN AVE. - Bk. spk. in conc. drive to Ho # 568	

Notes Ckd by:
Map No.
Office Mbrt.
Checked
Date

Survey of CASITAS AVE.
W. O. 1962 Tape No. St'd. °F
Surveyed by J.J. LANIGAN
Notes LANIGAN Date 6-3-53
Indexed C. Johnson

F. B. 173 & Pg. 207

Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION.
OF
LOW HOUSES
AND
SEWER OUTLETS
IN
LOT 15 TR ^ 13138
AND ON.
CASITAS AVE.
FROM.
CALAVERAS ST.
TO
MARIPOSA ST.
C.I. 1962.

J.J. LANIGAN.
M. NATAPOFF.
J.C. RITE

76F3095 247 2.51

F.B. 1738 PG. 208

Cont. to pg. 209



60.0

(1.6) Ho" #2851

4"V.C. pipe

7.0

9.0

37.3

26.3

60.0

5+22.5

AVE

4"G.I. pipe

51.1

5+07.8

(1.0)

1.0

20.2

31.0

65.3

84.3

51.1

Ho" #2843

42.3

30.8

65.3

Rear House

27.0

35.0

63.0

(1.0)

1.2

22.2

37.4

Ho" #2833

4"C.I. pipe

14.2

35.0

35.8

63.0

4+19.7

CASITAS

CALAVERAS ST

To STA 4+75.03
Nail and Tin.
pc L.F.B 1726-48

22.0

22.0

37.7

3+24.8

15

17.38

47.2

LOT TR.

STA 3+89.98
from S.
0.00 to E.
Sph. a W.
pc L.F.B 1726-25

CALAVERAS ST

Cont. 1 ft of pipe

Ho" #700

9" V.C. pipe

(1.4)

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Cahuenga Ave
W. O. 17462 Tape No. St'd °F
Surveyed by: J. J. Lanigan
Notes LANIGAN Date 6-3-53
Indexed A. C. Johnson

F. B. 1138 Pg. 207

cont bot pg. 210

Notice: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

20.1

AVE

159.2

Unable to locate outlet probably under pvt.

24.8

28.5 159.2

℄ 11+49.5

36.5 149.5

MENDOCINO

4" V.C pipe

(0.8)

27.6

6.8

199.5

11+01.8

ST

Sta 11+21.11
Sp ½" I.W.
P.C. F.B. 1726-23

65.0 188.0

26.3

12.37

188.0

(0.9)

9" C.I. pipe

℄ 7+74.5

CASITAS

Sta 7+83.24
6p ½" W.I.T.
P.C. F.B. 1726-29

Sta 7+79.24
Sp ¾" W.
P.C. F.B. 1726-29

HARRIET

ST

Cont'd on pg. 209

76F9095 247 2-51

F.B. 1138 PG. 210

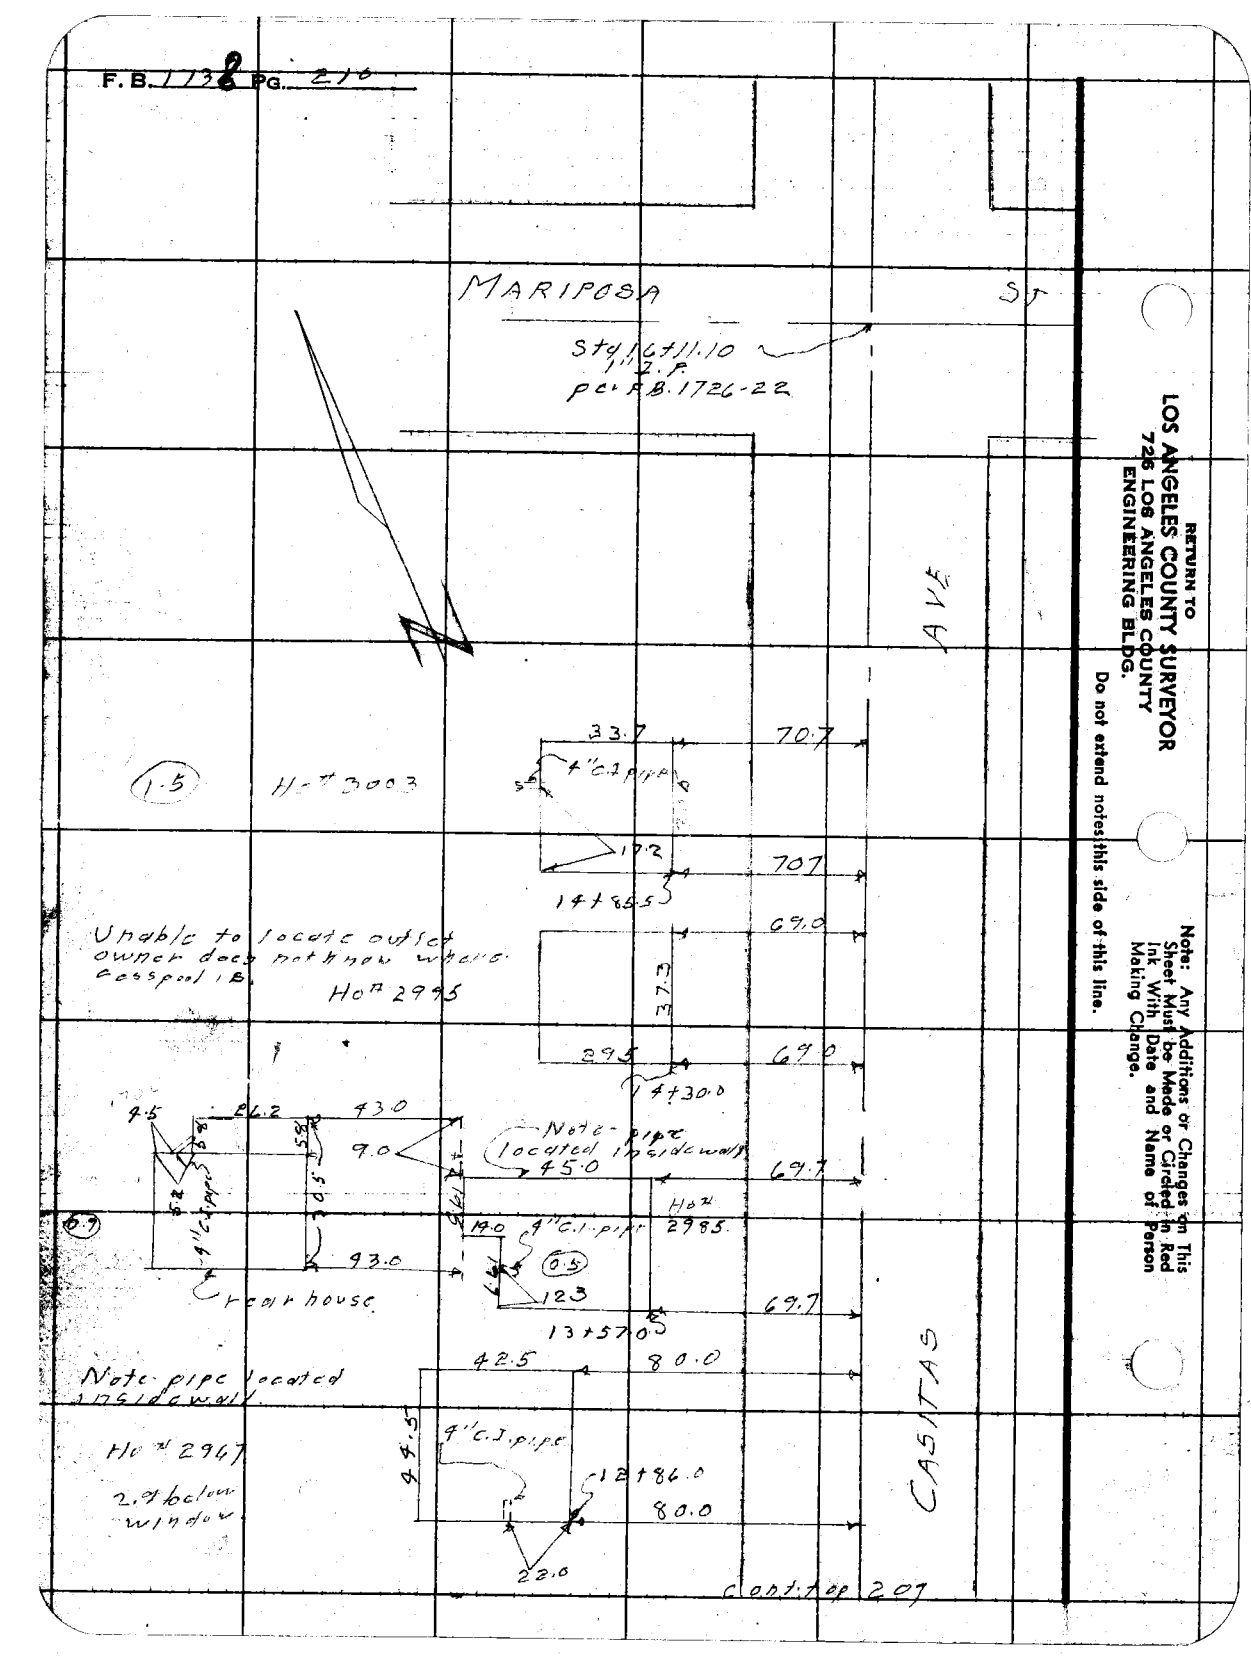

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No. | X-Sec. No. | Notes Red. | Date | Notes Chkd. | Date | Plotted | Date | Checked | Date | Job No. 1462 | Division No. V | Survey of CASITAS AVE | Survey by J.J.L. | Notes M.M. Date 6-5-53 | Map No. | Indexed C. Johnson Date | F.B. 1738 PG. 211

ELEVATIONS of HOUSE CONNECTIONS on CASITAS AVE. from VENTURA ST. to MARIPOSA ST. & 1 HOUSE on CALAVERAS ST.

C.I. 1462

J.J. LANIGAN
M. MATAPOFF
W.N. WILLIAMS

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76L298 307 10-51

76L298 307 10-51

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1738 Pg 212 Job No. 4462 Division No. V Profile No. X-Sec. No.
Survey of CASITAS AVE Notes Red Plotted
Survey by J. LANGAN Notes Chkd Checked
Indexed C. JOHNSON Date Date Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	CASITAS AVE
B.M. AE-514				1184.53	B.M. AE-514 - EL. 1184.526 per F.B. 1568-145 - Casitas Ave. & Calaveras St. (S.E. cor.) Bt. spk. in cb. 6' E. of E. end C.R.
	710	1191.63			
79+					
B.S. 19.8			67	1184.9	109.2 S. - grd. el. @ 4" V.C.P. } On Calaveras
"			81	1183.5	" " - el. tp. 4" V.C.P. } St.
T.P.			782	1183.81	T.P.
	490	1188.71			
4+33.9			45	1184.2	154.8 W. - grd. el. @ 4" C.I.P.
"			55	1183.2	" " - el. tp. 4" C.I.P.
T.P.			263	1186.08	T.P.
	668	1192.76			
5+10.8			71	1185.7	170.2 W. - grd. el. @ 4" C.I.P.
"			81	1184.7	" " - el. tp. 4" C.I.P.
5+41.5			49	1187.9	93.3 W. - grd. el. @ 4" V.C.P.
"			64	1186.4	" " - el. tp. 4" V.C.P.
T.P.			047	1192.29	T.P.
	1203	1204.32			

76L298 307 10-51

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR

726 LOS ANGELES COUNTY
ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red No. Date Plotted Date Job No. 4462 Division No. V
X-Sec. Notes Chkd Date Checked Date Survey of CASITAS AVE
No. Date Date Survey by J.J.L. Notes J.J.L. Date 5-3-63
Map No Indexed Date C. Jones

F.B. 1738 PG. 213

STATION	B. S.	H. I.	F. S.	ELEV.	CASITAS AVE
		1204.32			
8+74.5			75	1196.8	19.12' W. - grd. el. @ 4" C.I.P.
"			84	1195.9	" " - el. tp. 4" C.I.P.
T.P.			044	1203.88	T.P.
	8.12	1212.00			
11+08.6			87	1203.3	18.6' W. - grd. el. @ 4" V.C.P.
"			95	1202.5	" " - el. tp. 4" V.C.P.
T.P.			252	1209.48	T.P.
	6.17	1215.65			
12+86.0			63	1209.4	10.2' W. - grd. el. @ 4" C.I.P.
"			89	1206.8	" " - el. tp. 4" C.I.P.
T.P.			179	1213.86	T.P.
	5.79	1219.65			
13+76.2			68	1212.9	8.2' W. - grd. el. @ 4" C.I.P.
			73	1212.4	" " - el. tp. 4" C.I.P.
14+00.8			94	1210.3	18+09. 6.5' - grd. el. @ 4" C.I.P.
"			103	1209.4	" - el. tp. 4" C.I.P.

76L298 307 10-51

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1738 PG. 214 Job No. 1462 Division No. 1 Notes Red. Plotted
Survey of CASITAS AVE Date Date No.
Survey by LACKGAN Notes MANTARRE Notes Chkd. Checked X-Sec.
Indexed C. JOHNSON Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	CASITAS AVE
		1219 65			
14+30			63	1213 4	98± W. - S.W. cor. Ho #2995 - low corner
15+022			42	1215 5	104± - grd. el. @ 4" C.I.P.
"			57	1214 0	" - el. tp. 4" C.I.P.
T.P.	692	1224 04	253	1217 12	
B.M. AE-511			274	1221 30	B.M. AE-511 - EL. 1221.311 per F.B. 1568-146 CASITAS AVE & MARIPOSA ST. (N.E. cor.) Bh spk. in N. cb. of MARIPOSA ST. 24' E. of W. end.

38

Notes C'd by		Survey of CASITAS AVE.	F.B. 1702 Pg. 215
Map No.		W.O. 1462 Tape No.	St'd. °F
Office Work		Surveyed by V.J.L ANIGAN.	
Checked		Notes J.J.L Date 6-18-53	
Date		Indexed C. Johnson	

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
of
LOW HOUSES
and
SEWER OUTLETS
in
FOOTHILL BLVD
between
LINCOLN AVE
and
CITY of PASADENA BOUNDARY
C.I. 1462.

J.J. LANIGAN.
M. NATAPOFF.
J.C. RICE.
W.N. WILLIAMS

76F3095 247 2-51

38

F.B. 1756 PG. 214

To STA 19+16.70 S.W.ly @ Lincoln Ave. pcc F.B. 1726-14

65.7 24.3 4" V.C. pipe 39.5 65.7 11785.5

1.8 Ho # 712

CASITAS AVE

BLVD

Std 9194.64 Sph. W. pcc F.B. 1726-17

93.8 37.8 49.5 93.8 4" V.C. pipe

1.9

65.0 58+33.5 24.2 65.0 20.3 4" C.I. pipe

1.8 Ho # 770

47.7 27.7 19.0 52.3 74.7 14" C.I. pipe G 445.0

Note - pipe located inside wall

3.7 Ho # 796

65.0 55+68.5 14" C.I. pipe 52.0 2.0

3.2 Ho # 819

65.8 47.7

0+34.0 29.0 9.2

Z

60.2 27.3 60.2 51.0

Ho # 898 Washtub in basement outlet below floor

7.5

STA 0+00 I.L. pcc F.B. 1726-20

City of Pasadena Boundry

3.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No. X-Sec. No.

Notes Red. Plotted Job No. 1462 Division No. 1 F.B. 1738 Pg. 217
Date Date Survey of CASITAS AVE
Notes Chkd. Checked Survey by J.J.L. Notes M.N. Date 6-18-52
Date Date Map No. Indexed C. Johnson Date

ELEVATIONS

on

SEWER OUTLETS

of

HOUSES on FOOTHILL BLVD.

from

PASADENA CITY B'D'RY.

to

LINCOLN AVE.

C.I. 1462

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

STATION	B.S.	H.I.	F.S.	ELEV.
		W.N. WILLIAMS	M. NATAPOFF J.C. RIKE	J.J. LANIGAN

761-298 307 10-51

76L298 307 10-51

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ X-Sec. No. ____
Plotted ____ Date ____ Checked ____ Date ____
Notes Red ____ Date ____ Notes Chkd ____ Date ____
Division No. V
Job No 4446
Survey of CASITAS AVE
Survey by J. LEAVITT & GAY Notes MONTA PROJECT
Indexed C. JOHNSON Date ____
F.B. 1736 PG. 218

STATION	B. S.	H. I.	F. S.	ELEV.	FOOTHILL BLVD
B.M. AE-230				1226.86	B.M. AE-230 - EL. 1226.864 per F.B. 1447-223
	625	1233.11			FOOTHILL BLVD. & CRESTFORD DR. (N.W. cor.)
					Bt. spk. in cb., 2' N. of N. end C.R.
0+26±			118	1221.3	93± So. - base of floor of No # 898
T.P.			704	1226.07	T.P.
	517	1231.24			
4+98±			73	1223.9	65' So. - grd. el. @ 4" C.I.P.
"			105	1220.7	" " - el. tp. 4" C.I.P.
6+45			33	1227.9	87± So. - grd. el. @ 4" C.I.P.
"			70	1224.2	" " - el. tp. 4" C.I.P.
T.P.			262	1228.62	
	981	1238.43			
8+31±			62	1232.2	85± So. - grd. el. @ 4" C.I.P.
"			80	1230.4	" " - el. tp. 4" C.I.P.
8+94±			48	1233.6	81± So. - grd. el. @ 4" V.C.P.
"			58	1232.6	" " - el. tp. 4" V.C.P.
T.P.	676	1243.34	185	1236.58	T.P.
B.M. AE-232			382	1239.52	B.M. AE-232 - EL. 1239.503 per F.B. 1447 223
					FOOTHILL BLVD & CASITAS AVE (S.E. cor.)
					Bt. spk. in S. cb. FOOTHILL BLVD. 6' E. of W. end.

38

Notes Ck'd by		Survey of CRESTAS AVE.	F. B. 132 Pg. 219
Map No.		W. O. 1462 Tape No.	St'd. °F
Office Work		Surveyed by J. J. LANIGAN	
Checked		Notes J. J. L. Date 6-18-53	
Date		Indexed R. C. Johnson	

Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
of
LOW HOUSES
and
SEWER OUTLETS
on
CRESTFORD DR.
from
FOOTHILL BLVD.
to
NORTHERLY LINE OF TR # 14307
C.I. 1462

J. J. LANIGAN.
M. NATAPOFF.
J. C. RIKE.
W. N. WILLIAMS.

76FS095 247 2-51

F. B. 175 38 PG. 220

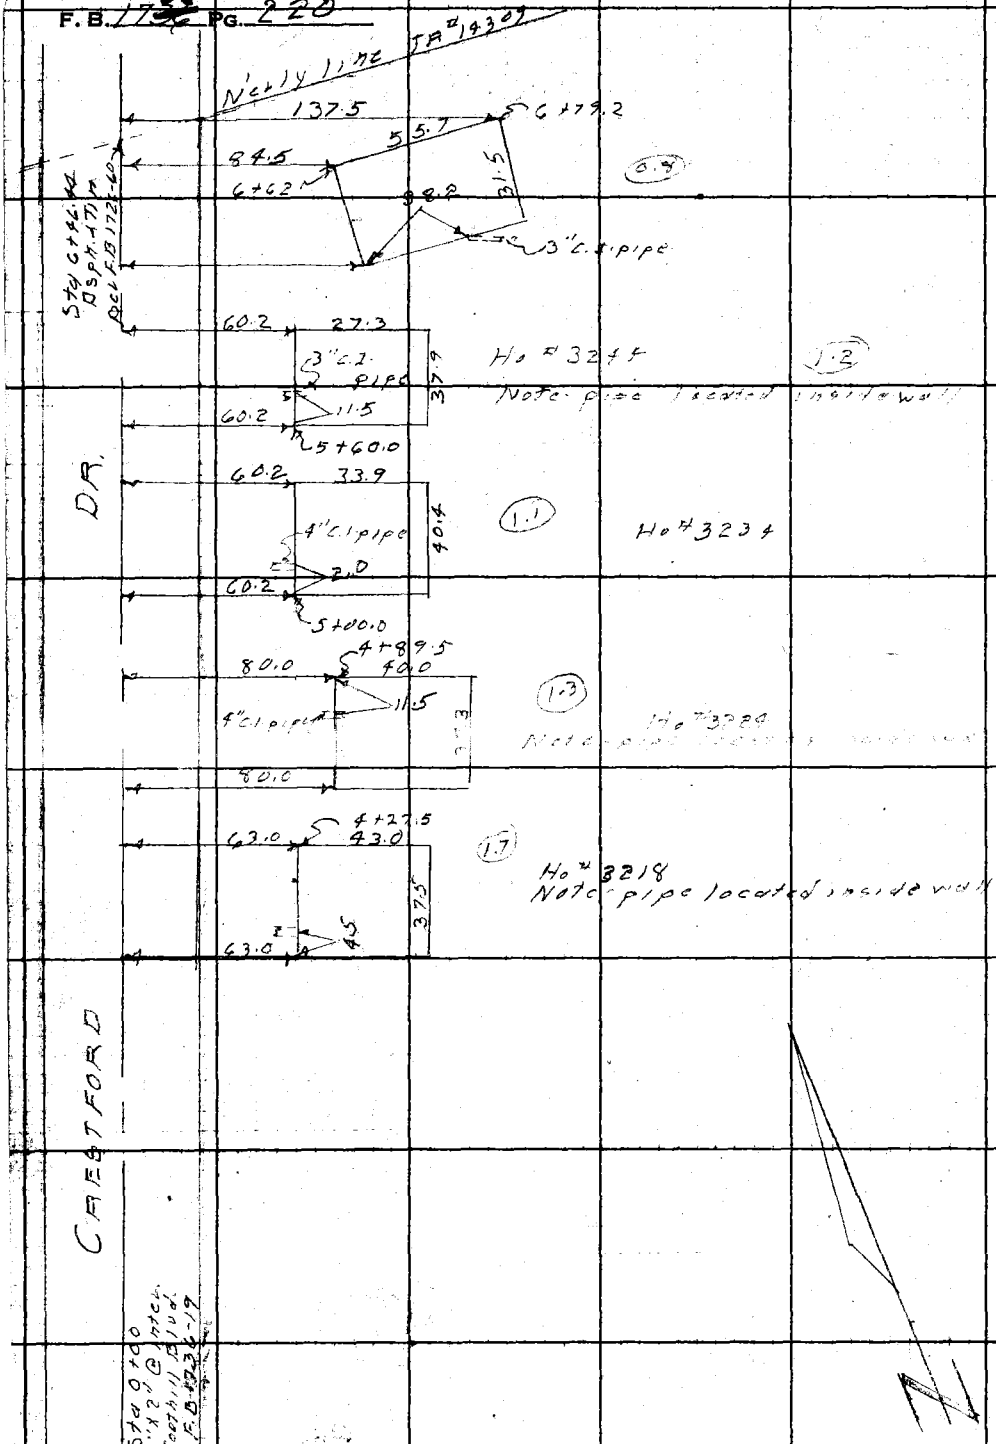

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No. ____ X-Sec. No. ____

Notes Red. ____ Plotted ____ Job No. 1462 Division No. V F.B. 1758 Pg. 221
Date ____ Date ____ Survey of LASITAS AVE.
Notes Chkd. ____ Checked ____ Survey by J.J.L. Notes M.N. Date 6-19-53
Date ____ Date ____ Map No. ____ Index C. Johnson Date ____

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

ELEVATIONS
of
SEWERAGE CONNECTIONS
of
LOW HOUSES
on
CRESTFORD DR.
from
FOOTHILL BLVD.
to
NORTHERLY LINE of TR. # 14309
C.I. 1462

STATION	B.S.	H.I.	F.S.	ELEV.

J.J. LANIGAN
M. NATAPOFF
J.C. RUKE
W.N. WILLIAMS

761-298 307 10-51

76L298 307 10-51

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1736 PG 222 Job No 4462 Division No. V Notes Red. Date Plotted Profile No.
Survey of CASITAS AVE Date X-Sec. No.
Survey by LANGAN Notes MI NATALOFF Notes Chkd. Checked
Indexed C. JORDAN Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	CRESTFORD	DR.
BM AF-532				124.63	BM AF-532-EL 1241.630	per F.B. 1568-16
	306	1244	69		CRESTFORD DR. & FLORECITA WAY (S.E. cor.) Bk. spk. in cb. 5'S. of S. end C.R.	
3+94±			97	12350	63°E. - grd. el. @ 4" C.I.P.	
"			114	12333	" " - el. tp. 4" C.I.P.	
4+78±			79	12368	80°E - grd. el. @ 4" C.I.P.	
"			92	12355	" " - el. tp. 4" C.I.P.	
5+02			75	12372	60°E grd. el. @ 4" C.I.P.	
"			86	12361	" - el. tp. 4" C.I.P.	
5+71±			57	12390	60°E. grd. el. @ 4" C.I.P.	
"			69	12378	" - el tp. 4" C.I.P.	
6+47±			60	12387	120'±E - grd. el. @ . 3" C.I.P.	
"			68	12379	" " " - el. tp. 3" C.I.P.	
T.P.			348	124.21	T.P.	
	353	1244	74			
BM AF-532			311	124.63	BM AF-532-EL. 1241.630 (For description see above)	

38

F.B. 173 Pg. 223

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of CASITAS AVE.
W. O. 1962 Tape No. St'd. °F
Surveyed by: J.J. LANIGAN
Notes J.J.L. Date 6-19-53
Indexed C. Johnson

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
of
LOW HOUSES
and
SEWER OUTLETS
on
DEVIRIAN PL.
from
CASITAS AVE.
to
LINCOLN AVE.
C.A. 1962

J.J. LANIGAN.
M. NATAPOFF.
J.C. FRITE.
W.N. WILLIAMS

76F3095 247 2-51

38

F. B. 179 Pg. 2-4

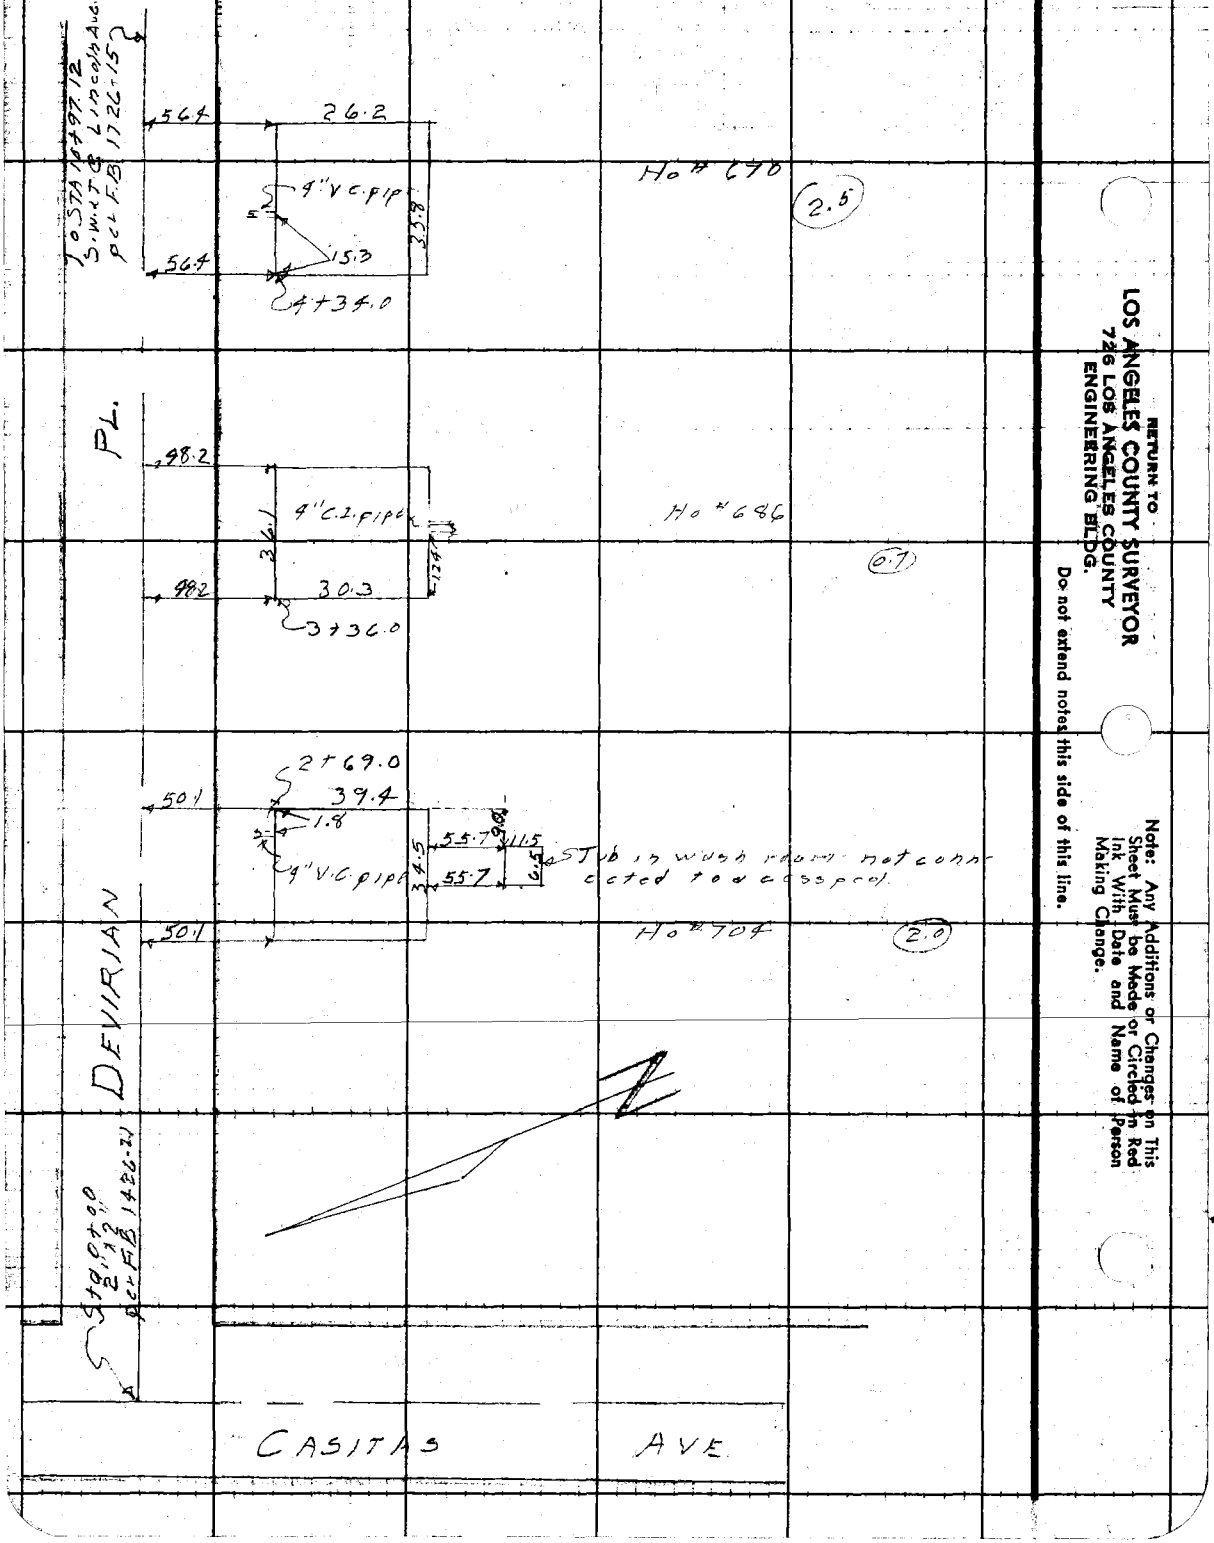

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink, With Date and Name of Person Making Change.

Profile No. | Notes Red. | Plotted | Job No. 1462 | Division No. V | F.B. 1738 Pg. 225

X-Sec. No. | Notes Chkd. | Checked | Survey by J.J.L. | Notes M.N. Date 6-19-53 | Map No. | Indexed C. Johnson Date

ELEVATIONS
of
SEWERAGE OUTLETS
of
LOW HOUSES
on
DEVIRIAN PL.
from
CASITAS AVE.
to
LINCOLN BLVD.

C.L. 1462

J.J. LANIGAN
M. HATAPOFF
J.C. RUKE
W.N. WILLIAMS

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

761_298 307 10-81

76L298 307 10-51

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1738 PG. 22 | Job No. 4462 Division No. V | Profile No. | Notes Red | Plotted | Date | X-Sec. No. | Notes Chkd | Checked | Date | Survey of CASITAS AVE. | Survey by L.A. COUNTY SURVEYOR | Indexed | Date

STATION	B. S.	H. I.	F. S.	ELEV.	DEVIRIAN	PL.
B.M.AE 510				1229.33	B.M. AE 510 - EL. 1229.332 per F.B. 1568-144 CASITAS AVE. & DEVIRIAN PL. (S.E. cor.) Bt. spk. in S. cb. of DEVIRIAN PL., 6' E. of W. end	
	12/14	12/24/47				
2+67 ±			61	12354	50 ± S. - grd. el. @ 4" V.C.P.	
"			81	12334	" " - el. tp. 4" "	
2+53 ±			82	12333	145 ± S. - floor el. of laundry	
"			86	12329	" " - grd. el. @ laundry	
T.P.			428	12379	T.P.	
	554/12+2.73					
3+48 ±			58	12369	78 ± S. - grd. el. @ 4" C.I.P.	
"			65	12362	" " - el. tp. 4" C.I.P.	
4+49 ±			42	12385	56 ± S. - grd. el. @ 4" V.C.P.	
"			67	12360	" " - el. tp. 4" V.C.P.	
B.M.AE 531			264	12400.9	B.M. AE 531 - EL. 1240.087 per F.B. 1568-158 DEVIRIAN PL. (N. side), 450' ± W. of ℄ of LINCOLN AVE. Bt. spk. in cb. in front of HO # 647.	

36

F. B. 1175 Pg. 227

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of CASITAS AVE.
W. O. 1462 Tape No. St'd. °F
Surveyed by J.V. LANIGAN
Notes J. J. L Date 6-19-53
Indexed

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
of
LOW HOUSES
and
SEWER OUTLETS
on
HARRIET ST
C.I. 1462

J.J. LANIGAN
M. NATAPOFF
J.C. FINE
W.N. WILLIAMS

76F309S 247 2-51

38

F. B. 1735 PG. 226

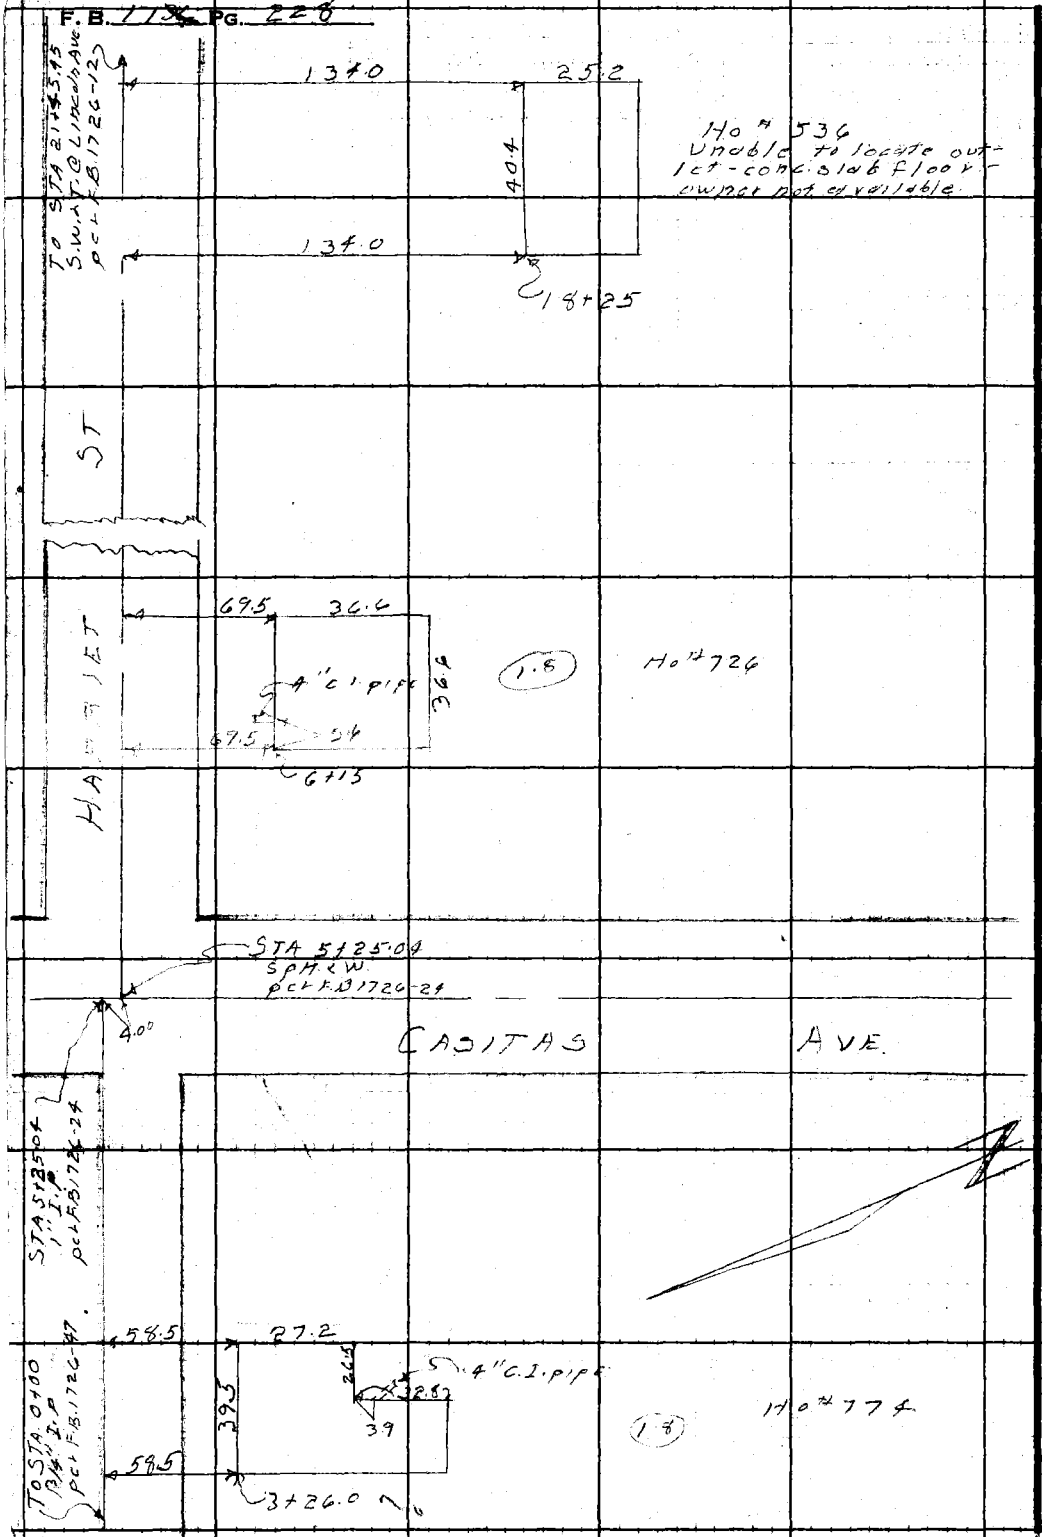

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Notice: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No. | Notes Red. | Plotted | Job No. 1462 | Division No. | F.B. 1736 | Pg. 229

X-Sec. No. | Notes Chkd. | Checked | Survey of CAPITAS AVE | Survey by J.J.L. | Notes M.N. | Date 6-19-53 | Map No. | Inked C. Johnson | Date

ELEVATIONS of SEWERAGE CONNECTIONS on HARRIET ST.

C.I. 1462

STATION	B.S.	H.I.	F.S.	ELEV.

J.J. LANIGAN
M. NATAPOFF
L.C. RIKE
W.N. WILLIAMS

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

761-228 307 10-51

76L298 307 10-51

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. X-Sec. No.

Job No 4662 Division No. V Notes Red. Plotted

Survey of CASITAS AVE Date Date

Survey by Lt. LANGDON Notes MAINTAPOLE Notes Chkd Checked

Indexed K. C. Johnson Date Date Date

F.B. 1568 Pg 38 Pg 239

STATION	B. S.	H. I.	F. S.	ELEV.	HARRIET ST.
BM AE 524				1187 60	BM AE 524 - EL. 1187.600 per FB. 1568-156
	1125	1198 85			EL NIDO DR (W. side) @ HARRIET ST. Bt. spk. in
					conc. walk to ho. # 2909
3+39			79	11910	89± S. - grd. el. @ 4" C.I.P.
"			97	11892	" " - el. tp. 4" C.I.P.
T.P.			073	119812	T.P.
	568	120380			
6+20±			65	11973	69± S - grd. el. @ 4" C.I.P.
"			73	11965	" " - el. tp. 4" C.I.P.
BM AE 513			182	120198	BM AE 513 - EL. 1201.964 per F.B. 1568-146
					HARRIET ST. (N. side) 115'± E of ℄ of CASITAS
					AVE - Bt. spk. in S'ly side of trans. pole # 834782
BM AE 527	435	121088		120653	BM AE 527 - EL. 1206.530 per FB. 1568-161 HARRIET ST. (N. side)
					81'± W. of ℄ TOLA AVE. Bt. spk. in conc. dr. to HO # 625
T.P.	546	121187	447	120641	T.P.
18+25			84	12035	159± S. - grd. el. @ S.W. cor. HO # 536
18+65±			85	12034	" " - " " " S.E. " " "
T.P.	695	121366	516	120671	T.P.
					BM AE 238 - EL. 1206.844 per FB. 1447-226
BM AE 238			683	120683	LINCOLN AVE. & HARRIET ST. (S.W. cor.) Bt.
					spk. in cb. 7' S. of S. end C.R.

COPIES TO

SAN GABRIEL VALLEY

(REGIONAL OFFICE)

pages 231 thru 232

PWFB 1823

1043

M.S. 8R 46

Notes Ck'd by:
Map No.
Office Work
Checked
Date

Survey of
W. O. 5251 Tape No. P/53 St'd. 68 °F
Surveyed by:
Notes Date 8-20-53
Indexed C. Johnson

F.B. 7738 Pg. 2-3

cont. bot. pg. 232.

Fd 2" I.P. S.E. cor. Tr. No. 12677

Set 1x2

From S.E. cor. TR. No. 12677

130.29

Fd 2" I.P. N.E. cor TR No 12677 Set F.B. 1726-37

Fd 2"x2" R.E. 1216 0.03' N.

90° 00' 00"

LOT No 5

1) 90° 00' 00"
2) 360° 00' 00"
3) 180° 00' 00"
4) 90° 00' 00"

126.79

126.77 /cv c/@ 80°

LOT No 6

1) 89° 59' 40"
2) 360° 00' 00"
3) 270° 00' 20"
4) 90° 00' 40"

LOT No 7

1) 90° 00' 15"
2) 360° 01' 00"
3) 180° 01' 50"
4) 90° 00' 18"

10703

Fd 2"x2" R.E. 1216

2.25

Set 1x2

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

S.S.E.F.B. 726-38

100° 30' 00"

Set N. & by inter.

10.26

Fd Sp. H.W. pcr F.B. 726-39

42° 00' 00"
293° 00' 00"
100° 30' 00"

LOT No 9

DA

CREST FORD

LOT No 8

1) 84° 00' 30"
2) 336° 02' 10"
3) 194° 03' 30"
4) 82° 00' 32"

183.85

183.83 /cv c/@ 82°

99° 00' 32"

279

Fd. 2"x2" R.E. 1216

Set 1x2

110° 17' 40"
80° 16' 00"
30° 56' 00"
110° 17' 40"

Fd N. & pcr F.B. 1726-37

83.32

83.31 /cv c/@ 86° : 83.32

LOT 10

TR. NO 12677

76FS095 247 2-51

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

1044

F.B. ~~1216~~ Pg. ~~236~~
PWFB 1823

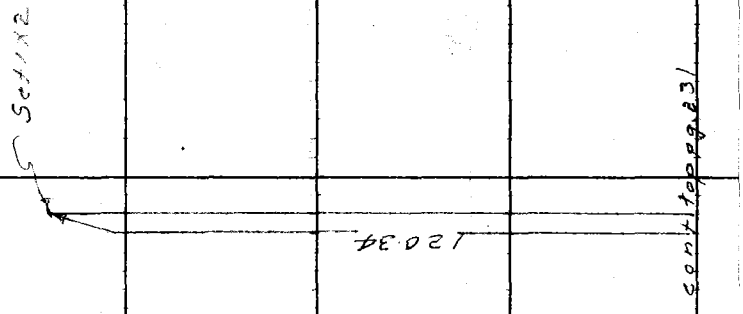

120.34 / Calc / @ 74° = 120.34

X

Notes Ck'd by	Survey of Cristina Ave
Map No.	W. O. 462 Tape No. St'd. °F
Office Work	Surveyed by J.J. Lanigan
Checked	Notes M. Natapoff Date 8-24-53
Date	Indexed A. C. Johnson

F. B. 1738 Pg. 233

LOCATION
of
IMPROVEMENTS
on
Southerly Line of Tract #12677
from
S.E. cor. of Lot #10
to
S.E. cor. of Tract #12677

C.I. 1462

J.J. LANIGAN
M. NATAPOFF
W.N. WILLIAMS
D.L. HOKANSON

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

76FS09S 247 2-51

F. B. 1738 PG. 234

(cont. pg. 235)

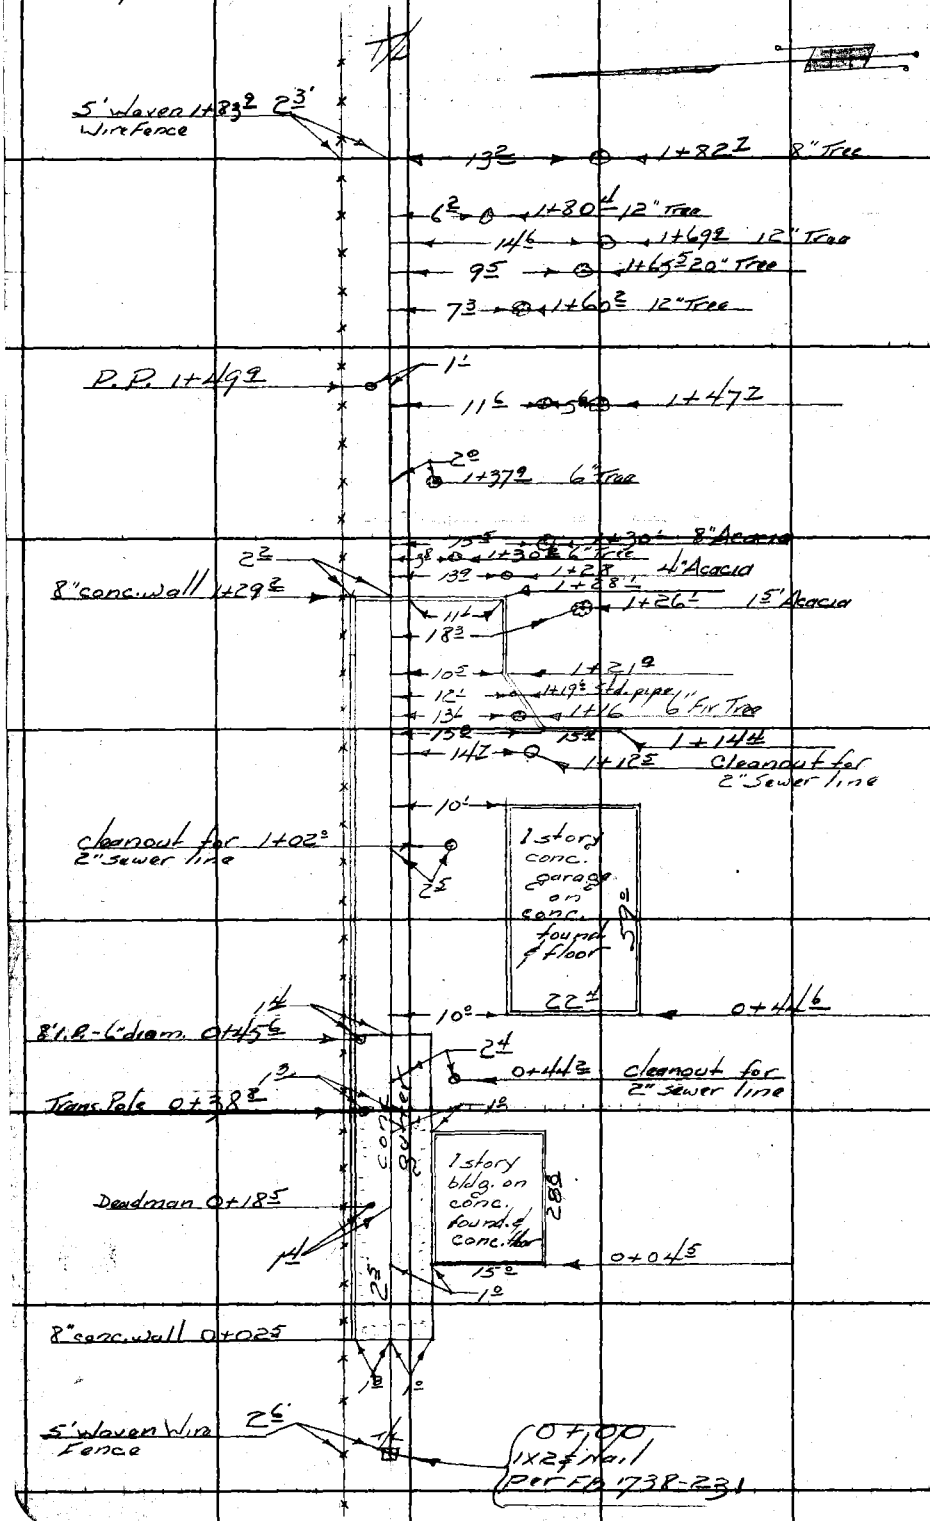

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

F.B. 1738 Pg. 235

Notes C'k'd by
Map No.
Office Work
Checked
Date

Survey of
W. O. Tape No. St'd. °F
Surveyed by
Notes Date 8-24-53
Indexed C. Johnson

Note: Any Additions or Changes or This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

T/L

2+90.88
per F.B. 1738-23

2+88.2 N. edge
5% driveway

3° 2+75.2

6' Clapboard

Swimming Pool 2+68.2

2+76

and 5' Woven Wire Fence 2+66.2

30'

2+65.2

25' 8" Tree

2+58.2 14" Tree

2+55

9' 2+57.2

6' 2+50 18" Sycamore

2' 2+45.5 24" Tree

4.5' 2+40.2 3" Tree

2' 2+31 12" Tree

12' 2+30.2 Std. pipe

8' 2+37.2 10" Tree

17' 2+19.2

15' ±

2' 2+17.2 6" Tree

9' 2+15.2 18" Sycamore

12° 10" Tree 2+08.2

9° 2+02.2 24" Tree

2° 2+02 24" Tree

5' 1+97.2 10" Tree

9' 1+94.2 20" Tree

T/L

1% Conc. Gutter & Roadway

(Cont. pg. 234)

76F3008 247 2-51

F.B. 1738 Pg. 536

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of CASITAS AVE.
W. O. 1962 Tape No. St'd. °F
Surveyed by J. J. LANIGAN
Notes J. J. L. Date 8-24-53
Indexed C. Johnson

F. B. 178 S Pg. 27

Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
of
IMPROVEMENTS
on
LINE - 29' N. of S.E. Cor. TR # 12677
from
E. LINE of TR # 12677
to
A POINT 120'± EAST.
C. I. 1962.

J. J. LANIGAN.
M. NATAPOFF.
W. N. WILLIAMS.
D. L. HOTANGON.

76F3095 247 2-51

F.B. 1736 PG. 238

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.



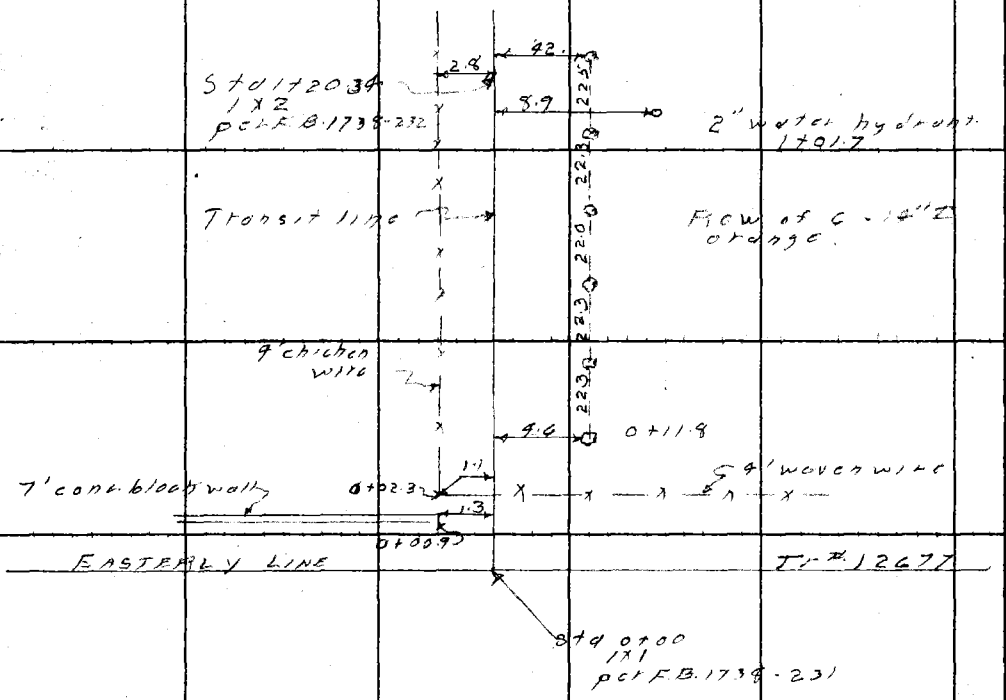

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Gardena Ave.
W. O. 1462 Tape No. St'd. °F
Surveyed by J. J. LANIGAN
Notes J.J.L. Date 8-24-52
Indexed A. C. Johnson

F. B. 173 & Pg. 237

Note: Any Additions or Changes of This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION of IMPROVEMENTS on 15' DRIVEWAY EASEMENT along EASTERLY SIDE of LOT #6 TRACT #12677 C.I. 1462

J. J. LANIGAN
M. NATAPOFF.
W. N. WILLIAMS
D. L. HOLMANSON

76F3095 247 2-51

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

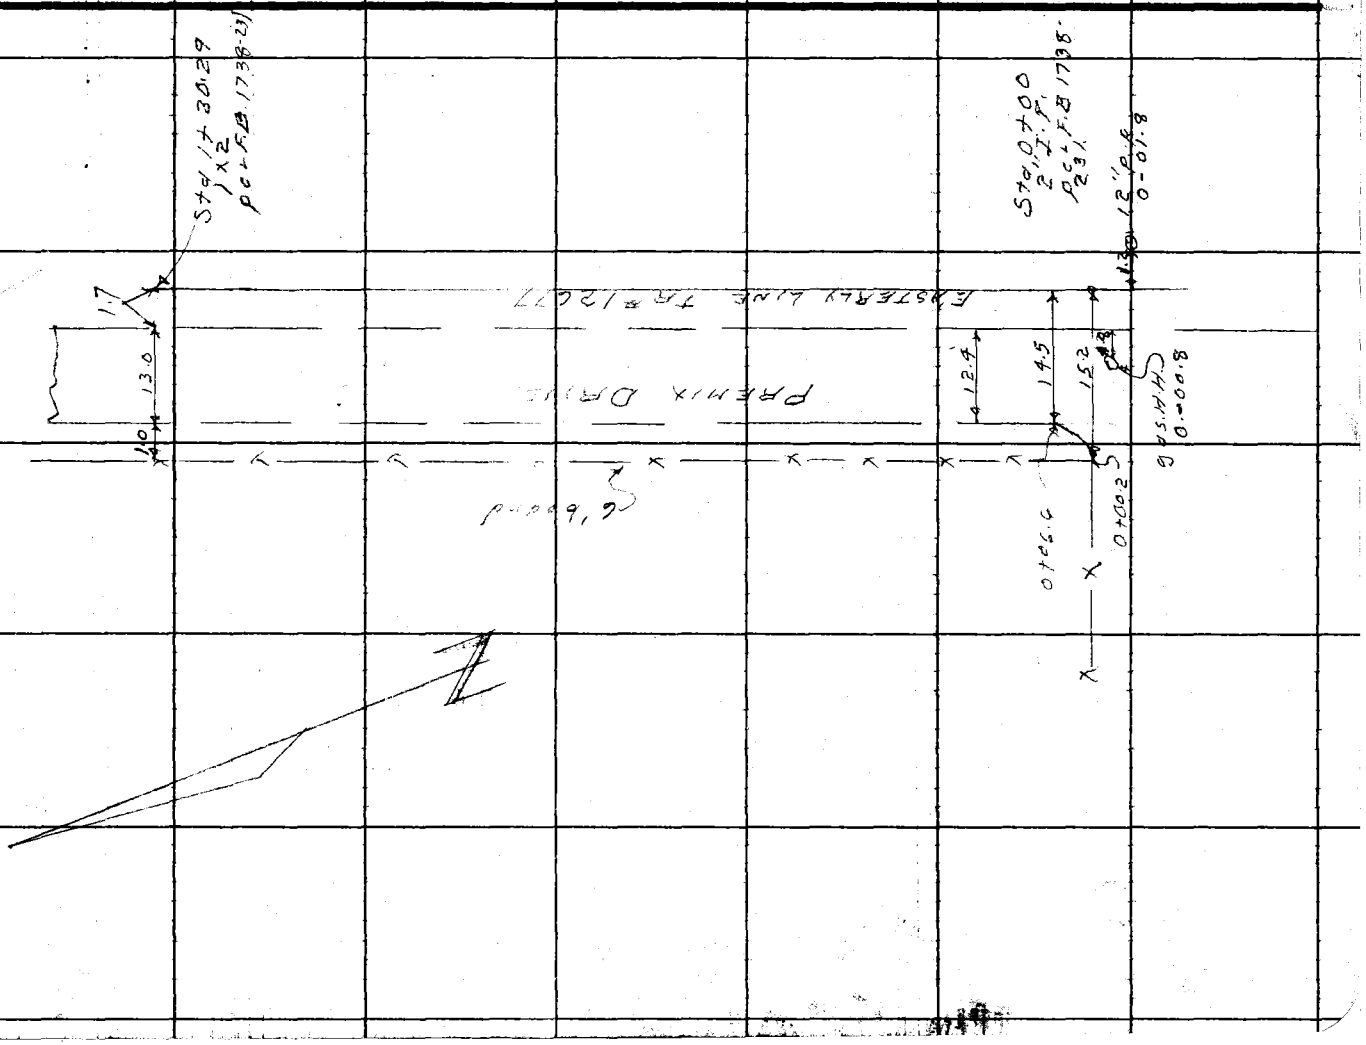

F.B. 1738 PG. 22-0

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Gas Tank Area
W. O. 1862 Tape No. St'd. °F
Surveyed by J. J. LANIGAN
Notes J. J. L. C. Jones Date 8-28-53
Indexed

F. B. 1238 Pg. 24

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

LOCATION
OF
IMPROVEMENTS
ON
SOUTHERLY LINE LOT #5
TRACT #12677
C. I. 1962

J. J. LANIGAN
M. NATAPOFF.
W. N. WILLIAMS.
D. L. HOHANSON.

76F3085 247 2-51

F.B. 1738 Pg. 242

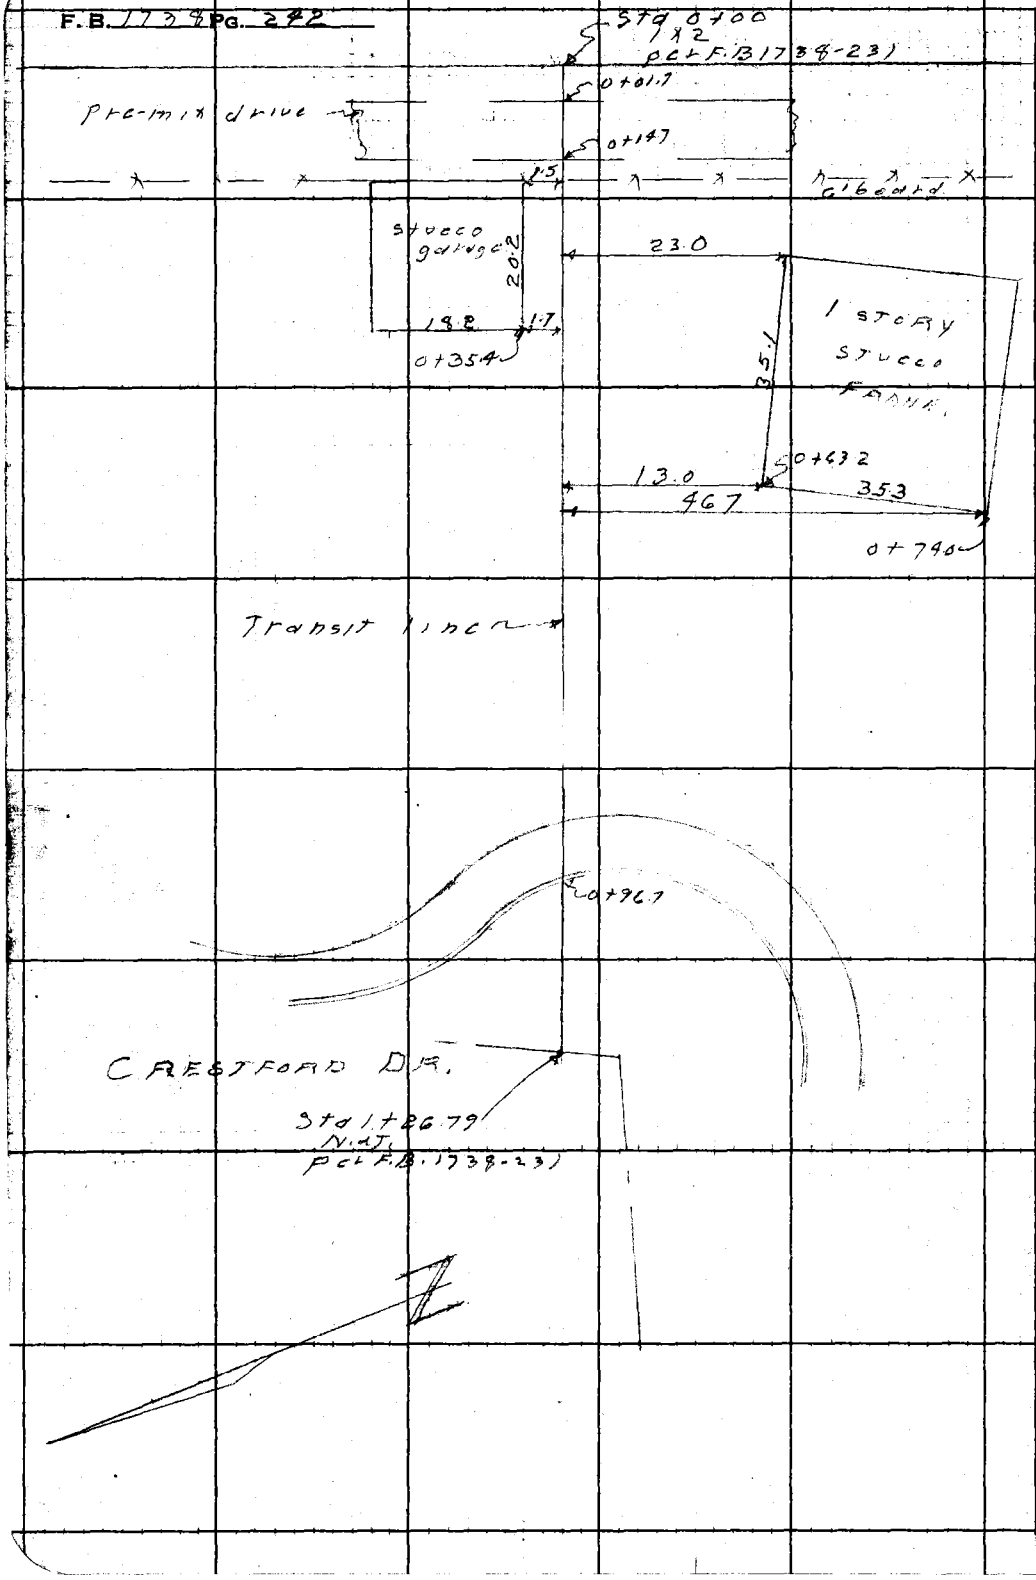

12679

RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

76L298 307 10-51

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR

726 LOS ANGELES COUNTY
ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red Plotted Job No. 4462 Division No. V
No. Date Date Survey of CASITAS AVE.
X-Sec. Notes Chkd Checked Survey by [illegible] Notes [illegible] Date 8-24-53
No. Date Date Map No. Inked C. Jones Date

F.B. 1738 Pg. 245

STATION	B. S.	H. I.	F. S.	ELEV.		
		1198 09 ✓				
1+14 ℄			480	1193 29		31 ± R or S - tp. wa
"			53	1192 8		15 ± R or S - bot. wa
"			347	1194 62		" " " " - tp.
1+21 ℄			50	1193 1		10 ± " " " - bot
"			291	1195 18		" " " " - top
1+28 ℄			48	1193 3		11 ± " " " - bot
"			258	1195 51		" " " " - tp
1+29 ℄			49	1193 2	2 ± L or N - bot. wall	
"			260	1195 49	" " " " - tp. "	
T.P.			132	1196 77		
	380	1200 57 ✓				
2+00			46	1196 0		T/L
"			47	1195 9		11 ± R or S - bk.
"			547	1195 10		18 ± " " " - edge pav bk
"			47	1195 9	3 L or N -	
2+19			45	1196 1		T/L
			46	1196 0		11 ± R or S - bk.
			52	1195 4		16 ± " " " - bk. edge conc.
			51	1195 5 ✓		17 ± " " " - edge pav.
T.P.			434	1196 23 ✓		

F.B. 1738 PG. 246 Job No. 1426 Division No. V Notes Red. Plotted Profile

Survey of CASITAS AVE Date Date No.

Survey by J.J. LANIGAN Notes M. NATAPOFF Notes Chkd. Checked X-Sec.

Indexed C. Johnson Date Date Date No.

STATION	B.S.	H.I.	F.S.	ELEV.

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR

726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

76L298 307 10-51

76L298 307 10-51

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No.____ Notes Red____ Plotted____ Job No. 4562 Division No. V
X-Sec. No.____ Date____ Date____ Survey of CAMILLA AVE
Notes Chkd.____ Checked____ Survey by J.L.L. Notes J.L.L. Date 8-25-53
No.____ Date____ Date____ Map No.____ Inked C. Johnson

F.B. 1738 PG. 247

STATION	B. S.	H. I.	F. S.	ELEV.		
T.P.				1196 23		
	529	1201 52				
2+60			130	1188 5	13'± L. or N. - bot. swimming pool	
2+75±			522	1196 30		T/L
"			544	1196 08		17' R. or S.
"			520	1196 32	3' L. or N.	
2+88±			522	1196 30		T/L - edge pav.
"			555	1195 97		17' R. or S.
"			49	1196 6	3' L. or N.	
On Line 29' N. of S.E. cor. Tr. # 12677 from E. line of Tr. # 12677 to point 120'± East.						
T.P.			479	1196 73		
	535	1202 08				
0+00			49	1197 2		T/L
"			52	1196 9		10' R. or S.
"			48	1197 3	2' L. or N.	
0+60			35	1198 6		T/L
"			42	1197 9		10' R. or S.
"			36	1198 5	2' L. or N.	
1+20			27	1199 4		T/L

76L298 307 10-51

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY
ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 1738 PG 24 Job No. 4462 Division No. V Notes Red. Plotted Profile
Survey of CASITAS AVE Date Date No.
Survey by J.J. LANGAN Notes P.I. DATA PAGE Notes Chkd. Checked X-Sec.
Indexed K. C. Johnson Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.		
		120208				
1+20			34	11987.		10' R. or S.
"			26	11995.	2' L. or N.	
		Easterly line of TR # 12677				
0+00			55	11966.		P/L
"			571	11963.7	2' L. or W. edge pav.	
"			576	11963.2	14' " " " - " "	
0+65			38	11983.		P/L
"			384	11982.4	2' L. or W. edge pav.	2'
"			386	11982.2	14' " " " - " "	
1+30.29			18	12003.		P/L
"			192	12001.6	2' L. or W. - edge pav	
"			232	11997.6	15' " " " - " "	
		Profile of Southerly line Lot # 5 - TR # 12677				
0+00			18	12003.		P/L
0+02			192	12001.6		
0+15			232	11997.6		

76L298 307 10-51

PLEASE RETURN TO

LOS ANGELES COUNTY SURVEYOR

726 LOS ANGELES COUNTY
ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red Platted Job No. 4462 Division No. X F.B. 1738 Pg. 249

X-Sec. Notes Chkd Checked Survey by [illegible] Notes [illegible] Date [illegible]

No. Date Date Map No. Ind. C. Johnson

STATION	B. S.	H. I.	F. S.	ELEV.	
		120208			
T.P.			347	119861	
	578	120439			
0+16			44	12000	P/L
0+35 4			47	11997	P/L
0+66			54	11990	P/L - bk
0+96 1			715	119724	P/L - tp. cb.
"			763	119676	P/L - out
1+26 79			767	119672	P/L - int. @ CRESTFORD DR
BM AE-509			625	119814	BM AE-509 - EL. 1198.132 per F.B. 1568-155 CRESTFORD DR (E. side) 295'± S. of ℄ of [illegible] St. Bk. spk. in cb. 3' N of N. end C.R.

F.B. 1738 Pg. 250 Job No. 462 Division No. ✓ Notes Red. Plotted

Survey of CASITAS AVE. Date Date

Survey by J.J. LANIGAN Notes M. NATAPOFF Notes Chkd. Checked

Indexed Date Date Date
