Notes Ck'd by	Survey of	F.B. 2920 Pg.
Map No.	JN Tape Std °F	
Office Work	Surveyed by	
Checked	Notes Date	
Date	Indexed	

Page	Job	Description
		HARBOR GENERAL HOSPITAL 7973.0
5-36	Grades	Grades for Parking Area on East side of Heating Plant-on W. side of Vermont Ave., & N. side of 220th St
[illegible]-38	Loc.Imp	Location of Drive along the west edge of New "Acute Unit Grounds.
3[illegible]-[illegible]4	X-Sec.	Cross-sections of existing drive along west side of New Acute Unit grounds.
45-51	Grades	Curb & planter grades.
53-134	Grades	Harbor General Hospital-Parking Lot grades.
35-136	Loc.Imp	Location of drains from parking area to ℄ of Sts. on 220th St. & Carson Ave.
137-138	Grades	For drains on 220th St. & Carson St.
13[illegible]-140	Loc.	Location of drains on Carson St.
141-142	Grades	For drains on Carson St.
143-144	Stak.	Acute Unit Bldg.-Constr. stakes for curb & drains outlets at west side of Vermont Ave. from 220th St. to Carson St.
145-147	Grades	For construction stakes for drains outlets at curbs west side of Vermont Ave. 120th St. North to Carson St.

Microfilmed June '85

(cont'd on next page)

Notes: Additions or Changes on this ... be Made or ... in Red ... Date and ... of Person ... King Change
Do not extend this side ... this ...
PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.
76P3095 CE #310 5-66

F.B. 2920 Pg.

Page	Job	Description
149-152	Loc.Imp	Location & elevations of S. Sewer MHs on 220th St. just east of Meyler St. J.N. 7973.01.
153-157	Cont.	Horiz. control survey for P.T. Sht's covering that area immediately E. of the conc. storm drain that runs between the new acute unit & the old hospital.
		PSYCHIATRIC SERVICES BLDG. HARBOR GENERAL HOSPITAL 0018.23
159-160	B.M.	Elevation on top of utility tunnel, S.E. of exist. Acute Unit.
161-162	Index	J.N. 0022.02
163-169	C.L.	Bdry. survey of proposed site of Acute Unit & Clinic Addition on Carson St. between Berendo Ave. & Vermont Ave.
171-172	B.M.	Temp. Bench levels for Acute Unit & Clinic Addt'
173-174	Index	
175-179	C.L.	Bdry. survey-bounded by Normandie Ave., Carson St., Vermont Ave. & 220th St.
181-182	Const.	New Psychiatric Service Bldg. Corners - J.N. 0018.23

405 LOS ANGELES COUNTY ENGINEER
PLEASE RETURN TO LOS ANGELES COUNTY ENGINEER
DO NOT REMOVE THIS SLIP FROM THIS BOOK

Profile No. | Notes Red. | Plotted | Job No. 7973.01 | Division No. 11 | F. B. 2920 Pg. 5.
Date | Date | Survey of HARBOR GEN. HOSP.
X-Sec. No. | Notes Chkd. | Checked | Survey by A.N.H. | Notes C. J. GALM. | Date 6-13-61
Date | Date | Map No. | Indexed | Date SEP 2 4 '62

J.N. 7973.01

HARBOR GENERAL HOSPITAL

GRADES FOR PARKING AREA ON EAST SIDE OF HEATING PLANT - ON W. SIDE OF VERMONT AVE., & N. SIDE OF 220TH ST.

SEE E.B. 1545 pgs 225-26-28-29 For Scheme of Stationing

A.N. Hellstrom
H.H. Spriggs
R.J. Rodriguez
L.W. Jones

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

76L298 S & E #307 9-54

76L298 S & E #307 9-54

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	
FD. Exist. Fin. Fl. - HEATING REF. & LAUND. BLDG				44 00	B.M. - Fin. Fl. Elev. 44.00 - EXIST. HEATING - REFRIG. & LAUNDRY BLDG.
SET T.B.M. - P.A. #1				41 54	T.B.M. # P.A.-1 - Elev. 41.54 Set Boat Spk. In Top Curbing At South End of C.R. At N. End of Island. On East Side Heating, Refrig. & Laundry Bldg.
SET T.B.M. - P.A. #2				42 00	T.B.M. - P.A. #2 - Elev. 42.00 Set Boat Spk. In P.P. #1334539 E (W. Sd.) - ON W. Sd. VERMONT AVE. 250'± N. & 30'± W. of ℄ INT. 220th ST. & VERMONT
SET T.B.M. - #P.A. #3				44 96	T.B.M. - P.A. #3 - Elev. 44.96 Set Boat Spk. In S.E. Cor of Window Well At S.E. Cor. OF OUTPATIENTS BLDG.
FD T.B.M.				39 50	T.B.M. - Elev. 39.50 Fd. 1" I.P. At S.W. Cor. Of Gen. CONTRACTS - FIELD OFFICE BLDG ON W. Sd VERMONT AVE 200'± E. of OUTPATIENTS BLDG. - No REF
Fd. BM # H-8				37 29	BM H-8 Elev. 37.29 - F.B. 1545-120 Bt Spk in No. Hdw. of Double 30" Dia. Conc Pipes - @ Roadwest new Steam Plant

F. B. 2920 Pg. 6 Job No. 7973.01 Division No. 11 Notes Red. Plotted Profile
*Survey of HARBOR GEN. HOSP. Date Date No.
Survey by A.N.H. Notes A.N.H. Notes Chkd. Checked X-Sec.
Indexed C. J. GANI Date Date No.

76L298 S & E #307 9-54

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. 7973 Division No. 11 F.B. 2920 Pg. 7
No. Date Date Survey of HEBER GEN. HOSP.
X-Sec. Notes Ckd. Checked Survey by A.N.H. Notes Date 6-13-61
No. Date Date Map No. Indexed by J. GALL Date

STATION	B. S.	H. I.	F. S.	ELEV.				
T.B.M.-P.A. "2"				42.00	T.B.M.-P.A. "2" - Elev. 42.00 P.F.B. 2920-6 Boat Spk in P.P. "1334539E			
					Sub	Finish	C/F	
"A"-46	From			40.62	40.17	40.75	C-0.45	40.76 Top Exist Paving
B-1	E-1171.59 To			40.44	40.40	40.98	C-0.04	
C	E-1426.00			40.30	40.56	41.14	F-0.26	
D	℄			40.54	40.76	41.34	F-0.22	
E	From			40.75	40.96	41.54	F-0.21	
F	N-1347.50 To			40.75	41.16	41.74	F-0.41	
G	N-1617.50			41.00	41.32	41.90	F-0.32	
H	pgs. 7 To 17 =			40.65	40.94	41.52	F-0.29	
J	Going E & S			40.33	40.56	41.14	F-0.23	
K	pgs. 17-18-19 =			39.86	40.17	40.75	F-0.31	
L	Going W'ly			40.82	39.67	40.25	C-1.15	
"A"-47	Exist Paving			40.66	40.04	40.62		OK
B-1				40.11	40.26	40.84	F-0.15	
C				40.27	40.42	41.00	F-0.15	
D				40.46	40.61	41.19	F-0.15	
E				40.70	40.80	41.38	F-0.10	
F				40.88	40.99	41.57	F-0.11	

76L298 S & E #307 9-54

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ X-Sec. No. ____

Job No. ____ Division No. ____ Notes Red. ____ Plotted ____

Survey of ____ Date ____ Notes Chkd. ____ Checked ____

Survey by C. J. GALLI Date ____ Notes ____ Date ____

Indexed ____ Date ____

F. B. 2920 Pg. 8

STATION	B. S.	H. I.	F. S.	ELEV.	Sub	Finish	C/F	
G - 47				41.00	41.17	41.75	F-0.17	
H -				40.71	40.94	41.52	F-0.23	
J -				40.41	40.56	41.14	F-0.15	
K -				39.83	40.17	40.75	F-0.34	
L -				40.88	39.74	40.32	C-1.14	
A-2 - 48	EXIST. PAVING			40.57	39.96	40.54		OK
B-1 -				40.12	40.13	40.71	GR.	
C -				40.11	40.27	40.85	F-0.16	
D -				40.26	40.44	41.02	F-0.18	
E -				40.52	40.61	41.19	F-0.09	
F -				40.78	40.78	41.36	GR.	
G -				40.81	40.95	41.53	F-0.14	
H -				40.68	40.94	41.52	F-0.26	
J -				40.56	40.56	41.14	GR	
K -				39.93	40.15	40.73	F-0.22	
L -				40.71	39.72	40.30	C-0.99	

76L298 S & E #307 9-54

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. 7973.01 Division No. 11 F. B. 2920 Pg. 9
No. Date Date Survey of HARBOR GEN. HOSP
X-Sec. Notes Chkd. Checked Survey by C.N.H. Notes Date 6-13-61
No. Date Date Map No. Indexed C. J. GALLI Date

STATION	B. S.	H. I.	F. S.	ELEV.	Sub Finish		C/F	
A-2 - 49		Top Curb		41.54	39.86	40.44		Mark Down 1.10
B -				39.96	40.00	40.58	F-0.04	
C -				40.08	40.12	40.70	F-0.05	
D -				40.24	40.28	40.86	F-0.04	
E -				40.32	40.43	41.01	F-0.11	
F -				40.58	40.58	41.16	Gr.	
G -				40.58	40.74	41.32	F-0.16	
H -				40.50	40.94	41.52	F-0.44	
J -				40.57	40.58	41.14	Gr.	
K -				40.07	40.23	40.81	F-0.16	
L -				4068	3967	40.25	C-1.01	
A-2 - 50		Top Curb		41.51	39.74	40.32		Mark down 1.19
B -				39.78	39.86	40.44	F-0.08	
C -				39.94	39.97	40.55	F-0.03	
D -				40.00	40.12	40.70	F-0.12	
E -				40.24	40.27	4085	F-0.03	
F -				40.40	40.42	41.00	F-0.02	
G -				40.52	40.57	4115	F 0.05	

76L298 S & E #307 9-54

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Sub	Finish	C/F	
H- 50				40.32	40.67	41.25	F-0.35	
J-				40.52	40.56	41.14	F-0.04	
K-				40.17	40.22	40.80	F-0.05	
L-				40.57	39.74	40.32	C-0.83	
A-2 — 51		Top Curb		41.52	39.65	40.23		Mark Down 1.29
B-1 —				39.49	39.75	40.33	F-0.26	
C —				40.00	39.85	40.43	C-0.15	
D —				39.96	39.98	40.56	F-0.02	
E —				40.15	40.12	40.70	C-0.03	
F —				40.27	40.26	40.84	Fr.	
G —				40.27	40.40	40.98	F-0.13	
H —				40.28	40.43	41.01	F-0.15	
J —				40.38	40.56	41.14	F-0.18	
K —				40.19	40.15	40.73	C-0.04	
L —				40.25	39.72	40.30	C-0.53	

F. B. 2920 PG. 10

Profile

Job No. ____ Division No. ____ Notes Red. ____ Plotted ____ No. ____

Survey of ____ Date ____ Date ____ X-Sec.

Survey by ____ Notes ____ Notes Chkd. ____ Checked ____ No. ____

Indexed C. J. GALLI Date ____ Date ____ Date ____

76L298 S & E #307 9-54

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 7973.01 Division No. ____ F. B. 2920 Pg. 11
No. ____ Date ____ Date ____ Survey of HARBOR GEN. HOSP
X-Sec. Notes Chkd. ____ Checked ____ Survey by A.N.H. Notes H.H.S. Date 6-13-61
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

STATION	B. S.	H. I.	F. S.	ELEV.	SUB	FINISH	C/F	
A-2 – 52		Top Curb		41.53	39.55	40.13		DOWN 1.40
B-1 –				39.70	39.61	40.19	C 0.09	
C –				39.54	39.71	40.29	F 0.17	
D –				39.90	39.83	40.41	C 0.07	
E –				40.11	39.96	40.54	C 0.15	
F –				40.21	40.08	40.66	C 0.13	
G –				40.24	40.21	40.79	C 0.03	
H –				40.14	40.33	40.91	F 0.19	
J –				40.37	40.42	41.00	F 0.05	
K –				40.22	40.15	40.73	C 0.07	
L –				40.10	39.62	40.20	C 0.48	
A-2 – 53		Top Curb		41.56	39.45	40.03		DOWN 1.37
B-1 –				40.61	39.47	40.05	C 1.14	
C –				40.16	39.56	40.14	C 0.60	
D –				39.90	39.68	40.26	C 0.22	
E –				40.17	39.80	40.38	C 0.37	
F –				40.29	39.92	40.50	C 0.37	
G –				40.28	41.004	41.62	C 0.24	

76L298 S & E #307 9-54

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Sub	Finish	C/F
H - 53				40.19	40.16	40.74	C-0.03
J -				40.30	40.28	40.86	C-0.02
K -				40.14	40.17	40.75	F-0.03
L -				39.90	39.67	40.25	C-0.23
A.2 - 54	Exist. Paving			39.95	39.33	39.91	
B.1 -				41.90	39.35	39.93	C-2.55
C -				41.55	39.52	40.10	C-2.03
D -				39.88	39.53	40.11	C-0.35
E -				40.24	39.64	40.22	C-0.80
F -				40.35	39.75	40.33	C-0.60
G -				40.26	39.86	40.44	C-0.40
H -				40.53	39.97	40.55	C-0.56
J -				40.35	40.09	40.67	C-0.26
K -				40.35	40.15	40.73	C-0.20
L -				39.96	39.72	40.30	C-0.24

F. B. 2920 Pg. 12

Job No. ____ Division No. ____ Notes Red. ____ Plotted ____ Profile ____

Survey of ____ Date ____ Date ____ No. ____

Survey by ____ Notes ____ Notes Chkd. ____ Checked ____ X-Sec. ____

Indexed C. J. GAUL Date ____ Date ____ Date ____ No. ____

76L298 S & E #307 9-54

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 2973.0 Division No. 11 F. B. 2920 Pg. 13
No. ____ Date ____ Date ____ Survey of HOREB OR GEN HOSP
X-Sec. Notes. Chkd ____ Checked ____ Survey by A.N.K. Notes ____ Date 6-13-61
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

STATION	B. S.	H. I.	F. S.	ELEV.	Sub	Finish	C/F	
A-1 -55		Exist. Paving		39.83	39.23	39.81		OK
B-1 -		NS			39.22	39.80		
C -		NS			39.29	39.87		
D -		NS			39.40	39.98		
E -				40.58	39.51	40.09	C-1.07	
F -				40.16	39.62	40.20	C-0.54	
[illegible] -				40.14	39.73	40.31	C-0.41	
[illegible] -				40.28	39.84	40.42	C-0.43	
[illegible] -				40.07	39.96	40.54	C 0.11	
[illegible] -				40.28	40.09	40.67	C 0.19	
-				40.16	39.77	40.35	C 0.39	
2 - 56		Exist. Paving		39.70	39.11	39.69		OK
[illegible] -		NS			39.07	39.65		
-		NS			39.12	39.70		
-		NS			39.23	39.81		
-		NS			39.34	39.92		
-				41.07	39.45	40.03	C 1.62	
[illegible]				40.30	39.56	40.14	C 0.74	

76L298 S & E #307 9-54

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 2920 Pg. 14

Job No. ____ Division No. ____ Notes Red. ____ Plotted ____ Profile
Survey of ____ Date ____ No. ____
Survey by C. J. GALLI Notes ____ Notes Chkd ____ Checked ____ X-Sec.
Indexed ____ Date ____ Date ____ Date ____ No. ____

STATION	B. S.	H. I.	F. S.	ELEV.	Sub	Finish	C/F	
H – 56				40.24	39.67	40.25	C 0.57	
J –				40.04	39.78	40.36	C 0.26	
K –				40.21	39.85	40.43	C 0.36	
L –				40.16	39.82	40.40	C 0.34	
A-2 – 57		Top Curb		40.17	38.98	39.56		Down .61
B-1 –		NS			38.92	39.50		
C –		NS			38.98	39.56		
D –		NS			39.08	39.66		
E –		NS			39.18	39.76		
F –		NS			39.28	39.86		
G –				40.16	39.38	39.96	C 0.78	
H –				40.22	39.48	40.06	C 0.74	
J –				40.07	39.60	40.18	C 0.47	
K –				40.24	39.72	40.30	C 0.52	
L –				40.11	39.75	40.33	C 0.36	

76L-298 S & E #807—1-56

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. 7973.04 Division No. 11 F. B. 2920 Pg. 15
No. Date Date Survey of HARBOR GEN. HOSP.
X-Sec. Notes Chkd. Checked Survey by A.N.H. Notes Date 6-13-61
No. Date Date Map No. Indexed C. J. GALLI Chkd. J.S.

STATION	B. S.	H. I.	F. S.	ELEV.	Sub Finish		C/F	
A-2 - 58		Exist Paving		39.47	38.81	39.39		OK
B-1 -		NS			38.71	39.29		
C -		NS			38.78	39.36		
D -		NS			38.87	39.45		
E -		NS			38.96	39.54		
F -		NS			39.05	39.63		
1				41.27	39.14	39.72	C-2.13	
4				40.32	39.22	39.80	C-1.10	
J				40.36	39.30	39.88	C-1.06	
L				40.48	39.40	39.98	C-1.08	
				40.18	39.57	40.15	C-0.61	

76L-298 S & E #307—1-56

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 2920 Pg. 16 | Job No 7973.01 | Division No. 11 | Notes Red. | Plotted | Profile
Survey of HARBOR GEN. HOSP. | Date | No. | X-Sec.
Survey by B.N.H. | Notes | Notes Ckd. | Checked
Indexed C.J. GALLI | Date | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.		Sub Grade	Finish Grade	C/F
SUB GRADES FOR PARKING AREA								
TBM-PA-2					T.B.M.-P.A.-2-Elev. 42.90-F.B. 2920-6. Bolt Spk in P.A. 1334539E			
B.1-45				40.52		40.53	41.11	ER
C-				40.43		40.71	41.29	F-0.28
D-				40.66		40.93	41.51	F-0.27
E-				40.92		41.15	41.73	F-0.23
F-				41.02		41.37	41.95	F-0.35
G-				41.00		41.32	41.90	F-0.32
H-				40.73		40.94	41.52	F-0.21
J-				40.39		40.56	41.14	F-0.17
K-				39.90		40.15	40.73	F-0.25
L- Face Crb		NS						
B.1-44				40.81		40.66	41.24	C-0.15
C-				40.77		40.65	41.23	C-0.12
D-				41.01		41.09	41.67	C-0.08
E-				41.19		41.33	41.91	F-0.14

76L-298 S & E #307—1-56

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. 7973.01 Division No. F. B. 2920 Pg. 17
No. Date Date Survey of HARBOR GEN HOSP
X-Sec. Notes Chkd. Checked Survey by A.N.H. Notes H.H.S. Date 6-23-61
No. Date Date Map No. Indexed C. J. GALL Date

STATION	B. S.	H. I.	F. S.	ELEV.	Sub Grade	Finish Grade	C/F
F-44				41.24	41.57	41.25	F-0.33
G-				41.21	41.32	41.90	F-0.11
H-				40.95	40.94	41.52	F.R.
J-				40.46	40.56	41.14	F-0.10
K-				40.07	40.22	40.80	F-0.15
L-		N.S.					
A-1-45			0.73	40.42	40.22	40.80	C+0.20
A-45			0.67	40.48	39.82	40.40	C-0.66
B-			0.59	40.20	39.72	40.30	C+0.48
C-			0.55	39.99	39.62	40.20	C-0.37
D-			0.44	39.95	39.52	40.10	C-0.43
E-			0.37	39.81	39.42	40.00	C-0.39
F-			0.31	39.95	39.32	39.95	C-0.63
G-			0.21	40.07	39.22	39.80	C-0.85
H-			0.11	40.38	39.12	39.70	C-1.26
J-			0.01	39.90	39.02	39.60	C-0.88

76L-298 S & E #307—1-56

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Sub Grade	Finish Grade	C/F
K- 45			992	39.18	3892	39.50	C-0.26
L-			978	3899	3932	39.90	F-0.33
N-			984	39.41	39.54	40.12	F-0.13
R-			964	39.04	39.16	39.74	F-0.12
T-		NS			3933	39.91	
U-		NS			39.05	39.63	
A1- 44				40.72	4022	4080	C-0.50
A-				40.56	4011	40.69	C-0.45
B-				40.40	4002	40.60	C-0.38
C-				40.42	39.95	40.53	C-0.47
D-				40.46	39.88	40.46	C-0.58
E-				40.46	39.81	40.39	C-0.65
F-				40.33	39.74	40.32	C-0.59
G-				40.48	39.67	40.25	C-0.81
H-				40.51	3960	40.18	C-0.91
J-				39.91	3953	40.11	C-0.38
K-				39.70	39.42	40.00	C-0.28
L-				39.62	39.42	40.00	C-0.20
N-				39.52	39.86	4044	F-0.34

F. B. 2920 Pg. 18 Job No. 797301 Division No. 11 Notes Red Plotted Profile
Survey of HARBOR GEN HOSP Date Date No.
Survey by A N H Notes Notes Chkd Checked X-Sec.
Indexed C. J. GAUI Date Date Date No.

76L-298 S & E #307—1-56

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. Notes Red. Plotted Job No. 2373.01 Division No. 11
X-Sec. No. Date Date Survey of HARBOR GEN. HOSP.
Notes Chkd. Checked Survey by E.N.H. Notes H.H.S. Date 6-23-61
Date Date Map No. Indexed C. J. GALLI Date

F. B. 2920 Pg. 19

STATION	B. S.	H. I.	F. S.	ELEV.	Sub Grade	Finish Grade	C/F
R - 44				39.23	39.27	39.85	F 0.04
T - 1			9.82	38.80	39.21	39.79	F 0.41
U - 1			9.80	39.13	38.91	39.49	C 0.21
B.M. H-8				37.29	B.M. - H-8 - Elev. 37.29 - F.B. 1545 - 120 - 24.5 pk. lo. N. Hdwl. of Double 30" Diam. Conc. Pipes.		

76L-298 S & E #307—1-56

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF [redacted] CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	
GRADES FOR ISLANDS & DRVWYS IN S.E. SECTION OF AREA N.W. COR. OF 220th ST. & VERMONT AVE. CURBING ON W. SIDE VERMONT & 74'± PARALLEL TO ℄ VERM. AVE. ALSO ISLANDS IN SAME AREA.					
		Cont. North On pg. 31			
T.B.M. "PA-2"				42.00	T.B.M. "PA-2" - Elev. 42.00 pr F.B. 2920-6 Boat Spk In PP #1334539E
				I. Russet @ Elev. Below	Elev. Top Curb
L-32	10' OFF (East) Fc Crb				—
L-33				40.81	40.81
34				40.81	40.81
35					—
36				40.82	40.82
37				40.75	40.75
38				40.82	40.82
39					—
40				40.75	40.75
41					—
42				40.80	40.80
43				40.75	40.75

F.B. 2920 PG. 20 #797301 Job No. Division No. 11 Notes Red. Plotted Profile
Survey of HARBOR GEN. HOSP Date Date No.
Survey by A.N.H. Notes H.H.S. Notes Chkd. Checked X-Sec.
Indexed C. J. GALLI Date Date No.

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.	
				I. Pin set @ Elev. Below	Elev Top Curb
L-44	10' off Fe Crb			40.82	40.82
45					40.82
46				40.75	40.75
47					40.82
48					
49				40.79	40.79
50				40.82	40.82
51					
52				40.70	40.70
53				40.75	40.75
54				40.80	40.80
55				40.85	40.85
56				40.90	40.90
57				40.85	40.85
58					
B.C. To W. - 15' Rad				40.52	40.52
E.C. To N. - 15' Rad				40.80	40.80

Profile No. ____ Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11 F.B. 2920 PG. 21
X-Sec. No. ____ Date ____ Date ____ Survey of HARBOR GEN. HOSP.
Notes Chkd. ____ Checked ____ Survey by A.N.H. Notes H.H.S. Date 6-27-61
Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 2920 Pg. 22

Job No. 2973.01 Division No. 11 Notes Red Plotted Profile
Survey of HARBOR GEN. HOSP. Date Date No.
Survey by D.N.H. Notes H.H.S. Notes Chkd. Checked X-Sec.
Indexed C. J. GAU Date Date Date No.

STATION	B.S.	H.I.	F.S.	ELEV.		
ISLAND "K-57				41.00		
ISLAND "K-54				41.00		
ISLAND "K-51				41.00		
ISLAND "K-48				41.00		
ISLAND "K-45				41.00		
ISLAND "K-42				41.00		
ISLAND "K-39				41.00		
ISLAND "K-36				41.00		
ISLAND "K-33				41.00		

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 2973.01 Division No. 11
No. ____ Date ____ Date ____ Survey of HARBOR GEN. HOSP.
X-Sec. Notes Chkd. ____ Checked ____ Survey by A.M.H. Notes H.H.S Date 6-27-61
No. ____ Date ____ Date ____ Map No. ____ Indexed C.J. GALLI Date ____

F.B. 2920 PG. 23

STATION	B. S.	H. I.	F. S.	ELEV.			
T.B.M.-P.A.-"3				44.96	T.B.M. "P.P.-3-Elev. 44.94-ITE 2920-L-Bolt Spk. in S.E. Cor. of Window Well At S.E. Cor. OUTPATIENTS BLDG.		
					Sub Gr.	Fin Grd. Top Pvmt.	C/F
K-43				39.97	40.25	40.83	F-0.28
L-				39.97	40.23	40.81	F-0.26
M-				39.65	40.05	40.63	F-0.40
N-				39.49	40.21	40.79	F-0.72
R-				39.73	39.63	40.21	C-0.10
S-				39.36	39.23	39.81	C-0.13
U-				39.52	38.73	39.31	C-0.79
K-42				40.45	40.58	41.16	F-0.13
L-				40.57	40.59	41.17	F-0.02
M-				40.56	40.37	40.95	C-0.19
N-				40.06	40.54	41.12	F-0.48
R-				40.11	40.02	40.60	C-0.09
S-				39.74	39.33	39.91	C-0.41
U-				39.54	38.59	39.17	C-0.95

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 29201 Pg. 24 | Job No. 7973.01 | Division No. 11 | Notes Red | Plotted | Profile
Survey of Harbor Gen. Hosp. | Date | Date | No. | X-Sec.
Survey by A.N.H. Notes H.H.S. | Notes Chkd. | Checked
Indexed C. J. GALLI | Date | Date | Date | No.

STATION	B.S.	H.I.	F.S.	ELEV.	7" Sub Sub Grd	Fin Gr Top Pvt.	C/F
K-41				40.57	40.75	41.33	F-0.18
L-				40.47	40.72	41.30	F-0.25
M-				40.27	40.67	41.25	F-0.40
N-				40.18	40.73	41.31	F-0.55
R-				39.78	40.02	40.60	F-0.24
S-				40.11	39.32	39.90	C-0.79
U-				39.44	38.42	39.00	C-1.02
K-40				41.00	41.04	41.62	F-0.04
L-				40.67	41.05	41.63	F-0.38
M-				40.60	41.09	41.67	F-0.49
N-		Not Set			40.72	41.30	—
R-				40.01	40.07	40.65	GR.
S-				40.07	39.23	39.81	C-0.84
U-				39.49	38.42	39.00	C-1.07
K-39				40.85	41.25	41.83	F-0.40
L- "				40.94	41.25	41.83	F-0.31

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red Plotted Job No. 3973 01 Division No. 11 F.B. 2920 Pg. 25
No. X.Sec. Date Date Survey of HARBOR GEN. HOSP
No. Notes Chkd. Checked Survey by A.N.H. Notes A.H.S Date 6-27-61
Date Date Map No. Indexed C. J. CAHU Date

STATION	B.S.	H.I.	F.S.	ELEV.	Fin. Sub Sub Grd	Fin. Grd Top Pvt	C/F
M-39				40.60	41.04	41.62	F-0.44
N-				40.34	40.65	41.23	F-0.31
R-				40.25	40.02	40.60	C-0.23
S-				39.94	39.33	39.91	C-0.61
U-				39.30	38.42	39.00	C-0.88
K-38				40.95	41.48	42.06	F-0.53
L-				40.90	41.48	42.06	F-0.58
M-				40.58	41.05	41.63	F-0.47
N-				40.05	40.57	41.15	F-0.52
R-				40.44	40.02	40.60	C-0.42
S-				40.00	39.21	39.79	C-0.79
U-				39.31	38.42	39.00	C-0.89
K-37				41.58	41.73	42.31	F-0.15
L-				41.27	41.52	42.10	F-0.25
M-				40.84	41.05	41.63	F 0.21
N-				40.46	40.62	41.20	F 0.16
R-				40.41	40.02	40.60	C-0.39
S-				39.85	39.21	39.79	C-0.64

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 2920 Pg. 26

Job No. ____ Division No. ____ Notes Red ____ Plotted ____ Profile
Survey of ____ Date ____ Date ____ No. ____ X-Sec.
Survey by C. J. GALLI Notes ____ Notes Chkd. ____ Checked ____ No.
Indexed ____ Date ____ Date ____ Date ____

STATION	B. S.	H. I.	F. S.	ELEV.	7"Sub Gr Sub Grd	Fin. Grd Top Pvt.	C/F
U- 37				3959	3842	39.00	C-1.17
K- 36				4210	4196	42.54	C-0.14
L-				41.59	41.42	42.00	C-0.17
M-				4092	41.05	4163	F-0.13
N-				4073	40.62	41.20	C-0.11
R-				4093	40.02	40.60	C-0.91
S-				4033	3933	39.91	C-1.00
U-				3947	3842	3900	C-1.05
K- 35				4190	4195	4253	F-0.05
L-				4151	41.42	4200	C-0.09
M-				4144	41.05	41.63	C-0.39
N-				4098	40.70	41.28	C-0.28
R-				4088	40.02	40.60	C-0.86
S-				4041	3927	3985	C-1.14
U-				3959	3842	3900	C-1.17
K- 34				4213	4229	42.87	F-0.16
L- 34				41.75	41.42	42.00	C-0.33

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11
No. X-Sec. Date ____ Date ____ Survey of HARBOR GEN. HOSP.
Notes Chkd. ____ Checked ____ Survey by A.W.H. Notes H.H.S. Date 6-27-61
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALLAHER Date ____

F.B. 2920 PG. 27

STATION	B.S.	H.I.	F.S.	ELEV.	7" Sub Sub Grd	Fin Grd Top Pvt.	C/F
M-34				41.34	41.05	41.63	C-0.29
N-				41.11	40.80	41.38	C-0.31
R-				40.69	40.02	40.60	C-0.67
S-				40.14	39.33	39.91	C-0.81
U-				39.62	38.42	39.00	C-1.20
K-33				41.96	42.23	42.81	F-0.27
L-		Not Set					
M-		Not Set					
N-		Top Curb @ End	West Wall	41.80			
R-				40.61	40.02	40.60	C-0.59
S-				40.25	39.27	39.85	C-0.98
U-				39.75	38.42	39.00	C-1.33
K-32				42.10	42.37	42.95	F-0.27
L-		Not Set					
M-		Not Set					
N-		Not Set					
R-				40.36	40.02	40.60	C-0.34

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 2920 Pg. 28

Job No. ____ Division No. ____ Notes Red ____ Plotted ____ Profile ____
Survey of ____ Date ____ Date ____ No. ____ X-Sec. ____
Survey by ____ Notes ____ Notes Chkd. ____ Checked ____ No. ____
Indexed C. J. GALLI Date ____ Date ____ Date ____

STATION	B. S.	H. I.	F. S.	ELEV.	Fin Sub Grd Sub Grd	Fin Grd Top Pvt	C/F
S-32				40.00	39.23	39.81	C-0.77
U-32				39.97	38.42	39.00	C-1.55
EAST SIDE RETAIN. WALL FOR RAMP 0+00 GOING S. FROM S. Rd. Wall							
A-0+12				43.77	44.25	44.83	F-0.48
0+37				43.64	43.80	44.38	F-0.16
0+62				43.38	43.42	44.00	F-0.04
0+87				43.04	43.22	43.80	F 0.18
B-0+12				43.77	43.92	44.50	F-0.15
0+37				43.60	43.52	44.10	C-0.08
0+62				42.87	43.21	43.79	F-0.34
0+87				42.85	42.99	43.57	F-0.14
C-0+12				43.75	43.62	44.20	C-0.13
0+37				43.56	43.23	43.81	C-0.33
0+62				43.23	42.93	43.51	C-0.30
0+87				42.73	42.74	43.32	F.

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.			
					7" Sub Sub Grd	Fin Grd Top Pvt	C/F
D-0+12		Not Set					
0+37		" "					
0+62		" "					
0+87		" "					
	Int. Walks @ N.W End Ramp			41 70			
	Cor Walks @ S.W. Cor Wall			40 28			
N-1852.50 = 0+00							
R-0+00							
R 0+06 5				40 06	40 02	40.60	C 0.04
+26 5				39 85	40 02	40.60	F-0.17
+46 5				39 69	40.02	40.60	F-0.33
+66 5				39 37	40.02	40.60	F-0.70
+86 5				40.10	40 02	40.60	C-0.08
+94 5							

Profile No. ____ Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11 F.B. 2920 Pg. 29
X-Sec. No. ____ Date ____ Date ____ Survey of HARBOR GEN. HOSP.
Notes Chkd. ____ Checked ____ Survey by A.N.H. Notes H.H.S. Date 6-27-61
Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 2920 Pg. 30

Job No. ____ Division No. ____ Notes Red ____ Plotted ____ Profile ____
Survey of ____ Date ____ Date ____ No. ____ X-Sec. ____
Survey by ____ Notes ____ Notes Chkd. ____ Checked ____ No. ____
Indexed C. J. CALL Date ____ Date ____ Date ____

STATION	B. S.	H. I.	F. S.	ELEV.	Fin Grd Sub Sub Geo	Fin Grd Top Pvt.	C/F
S-0+00							
- +06 S				39.60	39.28	39.86	C-0.32
- +26 S				39.70	39.28	39.86	C-0.42
- +46 S				39.60	39.28	39.86	C-0.32
- +66 S				39.64	39.28	39.86	C-0.36
- +86 S				40.18	39.28	39.86	C-0.90
- +94 S							
U-0+00							
- +06 U				39.96	38.42	39.00	C-1.54
- +26 U				40.00	38.42	39.00	C-1.58
- +46 U				39.78	38.42	39.00	C-1.36
- +66 U				39.55	38.42	39.00	C-1.13
- +86 U				39.60	38.42	39.00	C-1.18
- +94 U							

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.		
	Cont. From Pg. 20 – PERIMETER CURBING					
T.B.M.				39 50	T.B.M.	
					Fin. Grd Top. Curb	To T.C.
L-32 – 10' off Fc. Crb. 10' off Rad = E.C. – 20' Rad.				42 40	40.51	C-1.89
L-31 – 18' off Rad 2' " Fc Crb. – E.C. – 20' Rad.				40 75	40.48	C-0.27
L-30 – 2' N. on 2' off Fc Crb = N-1887.50 B.C. – 20' R.					✓ 40.75	
N-1918.50					✓ 40.68	
1928.50					✓ 40.66	
1953.50					✓ 40.61	
1978.50					40.56	
1996.50					40.53	

Profile No. ____ Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11
X-Sec. No. ____ Date ____ Date ____ Survey of HARBOR GEN. HOSP.
Notes Chkd. ____ Checked ____ Survey by A.N.H. Notes H.H.S. Date 6-27-61
Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

F.B. 2920 PG. 31

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.			
CURB GRDS. ALONG N Sd. 220th ST.							T.B.M. 41.54
					Fin. Grd. Tp Crb		
J-K. & H. N. Crb				40.86	40.81		
E.C. So. Crb	1.25 OFF						
J-57					✓ 40.68		
H-57					✓ 40.56		
G-57					✓ 40.46		
G-58	5.0 OFF				✓ 40.22		
H-58					✓ 40.30		
J-58					✓ 40.38		
K-58					40.48		
B.C.					40.52		

F.B. 2920 PG. 34 | Job No. 7973.01 | Division No. 11 | Notes Red | Plotted | Profile
Survey of HARBOR GEN HOSP. | Date | Date | No. | X-Sec.
Survey by A.N.H. | Notes H.H.S. | Notes Chkd. | Checked | No.
Indexed C. J. GALLI | Date | Date | Date

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. ____ Division No. ____ F.B. 2920 Pg. 35
No. ____ Date ____ Date ____ Survey of HARBOR GEN. HOSP
X-Sec. Notes Chkd. ____ Checked ____ Survey by A.N.A. Notes ANA Date 8-28-61
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALL Date ____

CURBING PARALLEL TO CARSON & SO. OF SA. P/L of CARSON
(For location See F.B. last page 210 & 211)

T.B.M. 3896 T.B.M.-Chis(x) in Conc. Slab Bldg. 2 At Gate House

STATION	B.S.	H.I.	F.S.	ELEV.	Grade Top Curb	Cut or Fill
Station				Elev.		
A = B.C.				.40 20	40.50	F-0 30
B = E.C.				.40 56	41.12	F-0 56
C				.40 65	41.14	F-0.49
D				.40 77	41.18	F-0 41
E				.40 77	41.21	F-0 44
F				.40 55	41.25	F-0 70
G				.40 34	41.25	F-0 91
H				.40 75 ~~.40 23~~	41.29	F-0 54 F-1 06
J				.40 23	41.32	F-1 09
K = B.C.				.40 33	41.35	F-1 02
L = E.C.				.40 04	40.78	F-0 74
M				.39 39	39.32	C-0 07

Notes Ck'd by	Survey of Harbor Gen. Hosp.
Map No.	JN 7973.01 Tape Std °F.
Office Work	Surveyed by Curtis
Checked	Notes Curtis Date Oct 6-61
Date	Indexed E. E. On NOV 9 '61

F.B. 2920 Pg. 37

Note: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY ENGINEER
900 LOS ANGELES COUNTY ENGINEERING BLDG.

J.N. 7973.01

Harbor Gen. Hospital

Location of Drive along the west edge of New "Acute Unit" Grounds.

"See pages 39 thru 44 for Grades"

Curtis
Burkholder
Vasui
Dover

76809S CE #247 7-58

F. B. 2920 PG. 38

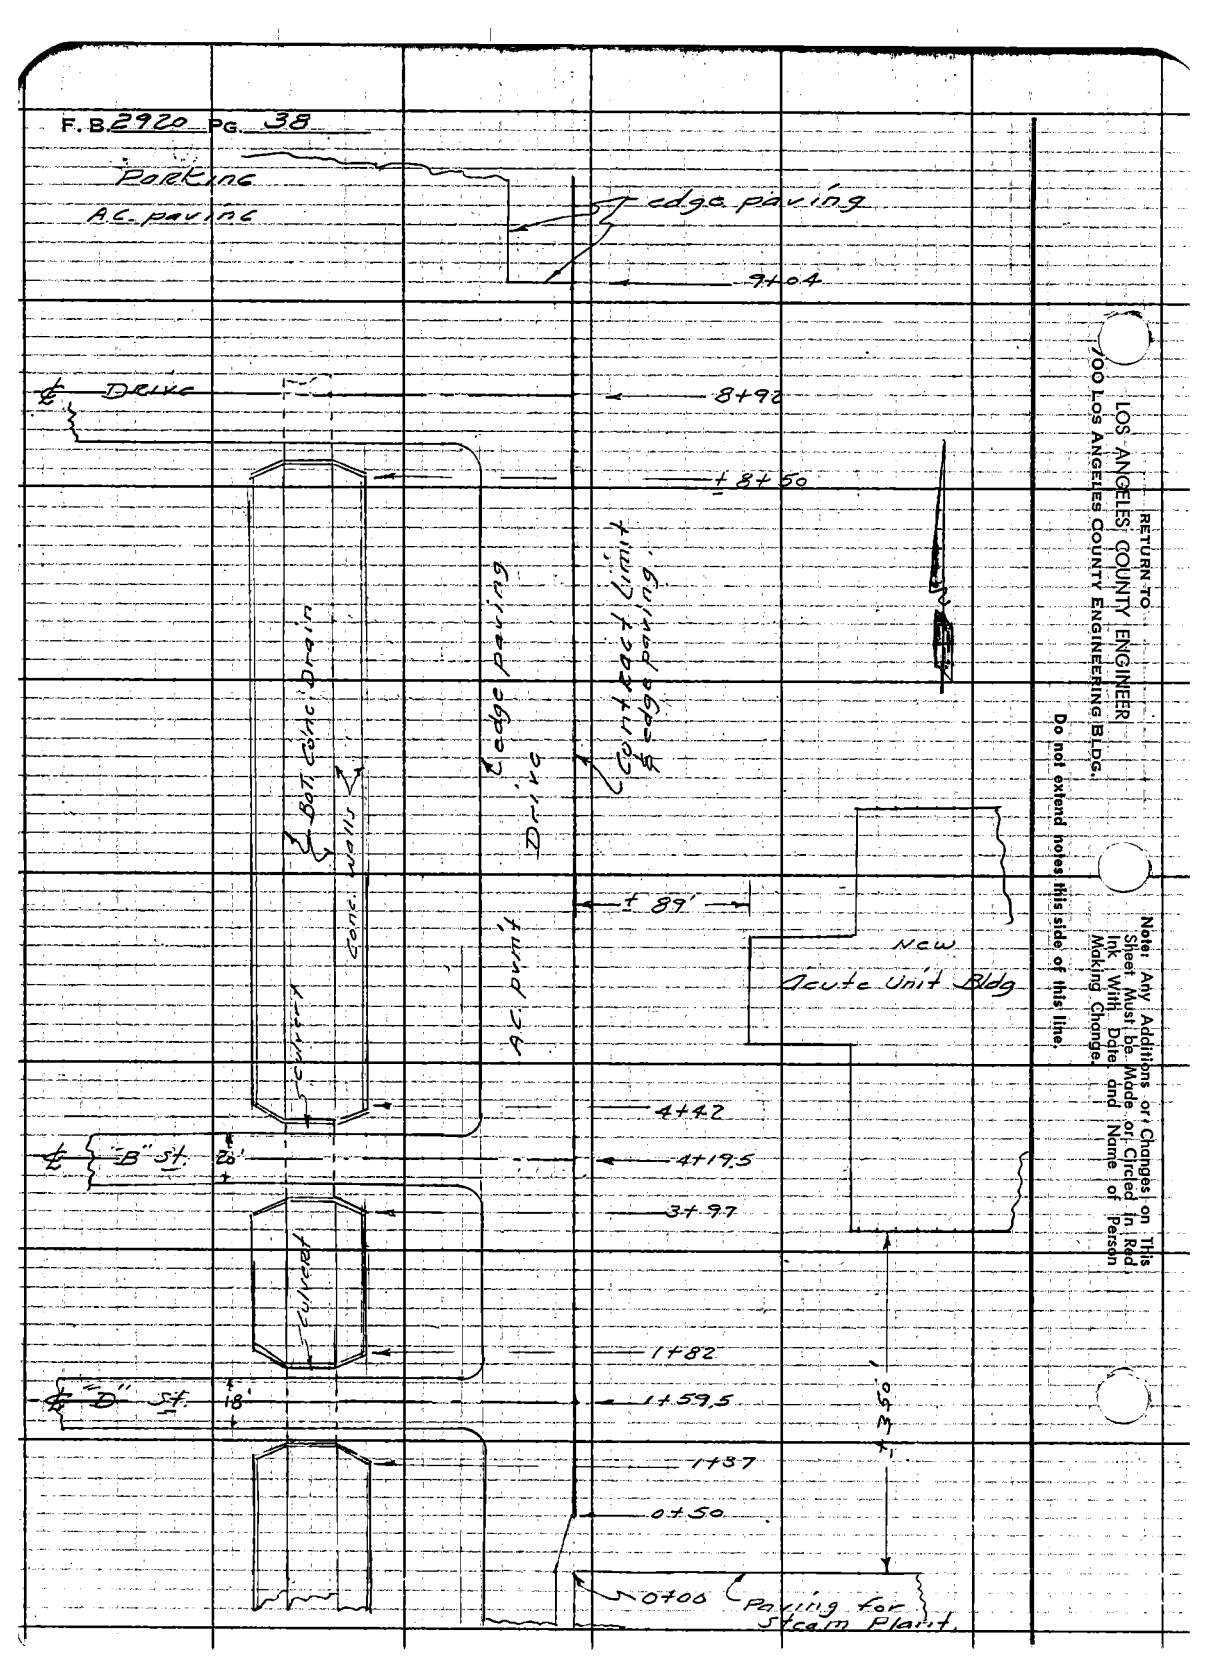

RETURN TO
LOS ANGELES COUNTY ENGINEER
700 Los Angeles County Engineering Bldg.
Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile	Notes Red	Plotted	Job No. 7973.01	Division No. 11	F.B. 2920	Pg. 39
No.	Date	Date	Survey of Harbor Gen. Hospital			
X-Sec.	Notes Chkd.	Checked	Survey by Curtis	Notes Curtis	Date Oct 6 - 1961	
No.	Date	Date	Map No.	Indexed 4 E. OTT	Date NOV 9 '61	

J.N. 7973.01

Harbor Gen. Hospital

Cross Sections of Exist.

Drive along west Side of

New Acute Unit Grounds.

(See page 38 for location)

Curtis
Burkholder
Yasui
Dover

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

76L-298 CE 307 11-58

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 2920 Pg. 40 Job No. 7923.01 Division No. 11 Notes Red Plotted Profile
Survey of Harbor Gen. Hospital Date Date No. X-Sec.
Survey by Curtis Notes Curtis Notes Chkd. Checked
Indexed H.E. Ott Date Date Date No.

STATION	B.S.	H.I.	F.S.	ELEV.	Left e West
					Elev. 37.97 FB. 154 - 120 & 166 - "D" Road - So. Sic
B.M. (Rd)				37.97	B.M. Bl. spk. in So. Hd. Wl. of 2-30" drain pipes.
					"Contract Limit"
0+00				39.77	Cob Pav. - Steam Plant
✓				39.07	3' Lt. edge pave - Drive
—				39.01	27' Lt ✓ ✓ ✓
—				38.7	43' Lt. Brk
—				36.09	51.5 Lt. Top Drain Ditch Wall
0+50				39.24	edge Pave - Drive & Contract limit
—				39.16	27' Lt edge Pave - Drive
—				38.6	43' Lt. Brk,
—				35.96	51.5 Lt. top Conc. Wall - Dr. Ditch
1+00				39.25	edge Pav. - Drive
—				39.18	27' Lt ✓ ✓ ✓
—				38.7	42.5 Lt. Brk.
—				35.85	51.5 Lt. Top Wall - Dr. Ditch
1+37 ✓				39.25	edge Pave - Drive
—				39.24	27' Lt ✓ ✓ ✓ ✓
—				39.0	43' Lt. Brk
—				35.79	51.5 Lt. Top Conc. Wall - Dr. Ditch

76L298 S & E #307 9-54

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. 7973.01 Division No. 11 F. B. 2720 Pg. 41
No.____ Date____ Date____ Survey of Lakeside Gen. Hospital
X-Sec. Notes Chkd____ Checked____ Survey by Curtis Notes Curtis Date Oct 6-1961
No.____ Date____ Date____ Map No.____ Indexed H. E. Ott Date____

STATION	B. S.	H. I.	F. S.	ELEV.	Left = West.
T.P.				39.47	T.P.
1+59.5 ℄ "D" St. (18' wide)				39.27	edge Pave & Contract Limit
✓				39.30	27' Lt. ℄ "D" St.
✓				39.58	52' Lt. ℄ "D" St.
1+82				39.39	edge Pave & Contract limit
✓				39.35	27' Lt. ✓ ✓
✓				38.7	42' Lt. Brk.
✓				35.6	51.3 Lt. Top Wall + Drain Ditch.
2+50				39.45	edge Pave-Drive & Contract limit
✓				39.42	27' Lt. ✓ ✓ ✓
✓				38.8	42' Lt. Brk.
✓				35.42	
3+00				39.48	edge pvmt-Drive & Contract Limit
✓				39.50	27' Lt. ✓ ✓ ✓
✓				38.8	42' Lt. Brk.
✓				35.34	51.0 Lt. Top Wall-Drain Ditch
3+50				39.55	edge pvmt.-Drive & Contract Limit
✓				39.62	27' Lt. edge Pvmt.
✓				39.0	42' Lt. Brk.
✓				35.16	50.8 Lt. Top Wall-Drain Ditch

76L298 S & E #307 9-54

PLEASE RETURN TO
LOS ANGELES COUNTY SURVEYOR
726 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 2920 Pg. 42 Job No. 7973.01 Division No. 11 Notes Red. Plotted
Survey of Harbor Gen. Hosp. Date Date No.
Survey by Curtis Notes Curtis Notes Chkd. Checked X-Sec.
Indexed H E OR Date Date Date No.
Profile

STATION	B. S.	H. I.	F. S.	ELEV.	Left = West.
(Fd.)					Elev. 37.36 F.B. 1545 - 120 & 166 - B. ST. - So. Side
B.M.				37.36	B.M. Bt. Spk. in Hd. Wall of 2-30" Drain Pipes
3+97				39.70	edge Pavmt. - Drive & Contract Limit
—				39.54	27' Lt. " " "
—				39.0	42' Lt. Brk.
✓				35.10	50.5 Lt. top conc. Wall - Drain Ditch
4+19.5	℄ "B" ST.	(20' wide)		39.88	edge pave. - Drive - Contract Limit "
✓				39.82	27' Lt. ℄ "B" ST.
✓				39.81	52' Lt. ℄ "B" ST.
T.P.				41.18	T.P. Spk in Lite pole @ Sta 4+50
4+42				39.58	edge pave. - Drive - ℄ Contract Limit "
—				39.24	31.5 Lt. " " "
—				39.0	40' Lt. Brk.
✓				35.00	50.2 Lt. top Wall - Drain Ditch
5+00				39.50	edge pave - Drive & Contract Limit "
—				39.27	31.5 Lt. " " "
—				38.9	39.5 Lt. Brk.
✓				34.85	50.1 Lt. top Wall - Drain Ditch
5+50				39.64	edge pave - Drive & Contract Limit
✓				39.41	31.5 Lt. " " "
✓				39.1	39' Lt. Brk.
✓				34.71	50' Lt. top Wall - Drain Ditch

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11 F.B. 2920 Pg. 43
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hospital
X-Sec. Notes Chkd. ____ Checked ____ Survey by Curtis Notes Curtis Date Oct.-4-1961
No. ____ Date ____ Date ____ Map No. ____ Indexed H.F.OM Date ____

STATION	B. S.	H. I.	F. S.	ELEV.	Left = West.
6+00				39.86	edge pave - Drive & Contract Limit
✓				39.56	31.5 Lt. edge pave - Drive
✓				39.5	38' Lt. Brk
✓				34.53	49.7 top Wall - Drain Ditch
6+50				40.04	edge pave - Drive & Contract Limit
✓				39.66	31.5 Lt. ✓ ✓ ✓
✓				39.9	37' Lt. Brk
✓				34.45	49.5 Lt. top Wall — Drain Ditch
7+00				40.14	edge pave - Drive & Contract Limit "
✓				39.69	31.5 Lt. ✓ ✓ ✓
✓				40.1	37' Lt. Brk.
✓				34.34	49.3 Lt. top Wall - Drain Ditch
7+50				40.09	edge pave - Drive & Contract Limit "
✓				39.73	31.5 Lt. ✓
✓				40.0	36' Lt. Brk
✓				34.33	49.3 Top Wall - Drain Ditch
8+00				40.20	edge pave - Drive & Contract Limit
✓				39.94	31.5 Lt. ✓ ✓ ✓
✓				40.2	36' Lt. Brk.
✓				34.11	49.1 Lt. top Wall - Drain Ditch

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 2920 Pg. 44 Job No. 7973.01 Division No. 11 Notes Red Plotted Profile
Survey of Harbor Gen. Hospital Date Date No. X-Sec.
Survey by Curtis Notes Curtis Notes Chkd. Checked
Indexed H.E.O.M. Date Date Date No.

STATION	B.S.	H.I.	F.S.	ELEV.	Left: West
84 50				40.27	edge pvmt. Drive & Contract limit
✓				39.99	31.5 Lt. ✓ ✓ — ✓
✓				40.0	35' Lt. Brk.
✓				34.00	49' Lt. top Wall — Drain Ditch.
8492 ℄ Drive				40.66	edge pave - Drive & Contract Limit
—				40.70	31.5 Lt. ℄
—				40.81	50' Lt. ℄
9404				40.21	edge & end pvmt. Drive & Contract Limit
✓				40.23	13' Lt. end pave North & begin pave - West
✓				40.24	31' Lt paving.
				40.32	50' Lt ✓
T.P.				39.93	T.P.
BM				37.36	Elev. 3736 - per page 42 - BM. "B" 57. Spk in Conc. Hd. Wall

Profile No. ____ X-Sec. No. ____

Notes Red ____ Date ____ Notes Chkd. ____ Date ____

Plotted ____ Date ____ Checked ____ Date ____

7973.01

Job No. ____ Division No. 11

Survey of Harbor Gen. Hosp

Survey by Curtis Notes ASC. Date Oct 11-1961

Map No. ____ Indexed C. J. Gmehl Date SEP 2 4 '62

F. B. 2920 PG. 45

J.N. 7973.01

Harbor Gen. Hospital

Curb & Planter Grades

Curtis
Burkholder
Yasui
Dover

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 Los Angeles County Engineering Bldg.

761-298 CE 307 11-58

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.	
		Curb Grade	Elev.	C or F	Stk & Tin 3' off.
(1) B.C.		42.57 ~~42.16~~	41.23	F 1.34 ~~F 0.93~~	
(2) E.C.		42.52 ~~42.12~~	41.38	F 1.14 ~~F 0.74~~	
(3) B.C.		42.37 42.07	41.26	F 1.11 ~~F 0.81~~	
(4) E.C.		42.00	41.18	F 0.82	
(5) 4 Pt.		42.00	41.17	F 0.83	
C-6		41.98	41.02	F 0.96	1.25 off.
D-6		41.95	40.87	F 1.08	
D-7		42.00	40.87	F 1.13	
E-6		41.92	40.61	F 1.31	
E-7		42.00	40.61	F 1.39	
F-6		41.89	40.23	F 1.66	
F-7		42.00	40.23	F 1.77	
G-6		41.37	39.85	F 1.52	
G-7		41.50	39.85	F 1.65	
H-6		40.85	39.60	F 1.25	
H-7		40.94	39.60	F 1.34	
J-6		40.33	39.24	F 1.04	
J-7		40.40	39.29	F 1.11	

Island #2
F.B. 1545 - 211 & 212

F.B. 2920 PG. 46
Job No. 797301 Division No. 11 Notes Red Plotted Profile
Survey of Harbor Gen. Hospital Date Date No.
Survey by Curtis Notes Burk Notes Chkd. Checked X-Sec.
Indexed C. J. Gabel Date Date No.

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11 F.B. 2920 Pg. 47
X-Sec. No. ____ Date ____ Date ____ Survey of Harbor Gen. Hospital
Notes Chkd. ____ Checked ____ Survey by Curtis Notes Curtis Date 10-11-6
Date ____ Date ____ Map No. ____ Indexed E. J. GALLI Date ____

STATION	B.S.	H.I.	F.S.	ELEV.				
		Curb Grade		Elev	(Island #2) (Cont.) C-F	(For location See F.B. 1545-211 & 212)		
6 No BC		40.00		38.94	F-1.06	Stks & Tins	1.25	off
6 So ± PT		40.10		38.94	F-1.16	—	—	—
7 E.C.		40.14		39.13	F-1.01	—	3°	off
8 B.C		40.16		39.12	F-1.04	✓	—	—
9 E.C.		40.20		39.09	F-1.11	—	—	—
		(Island #1)		F.B. 1545-211 & 212				
(1) BC	X	40.62		39.94	F0.68	Stks & Tins	3°	off
(2) E.C.		40.43		40.26	F0.17	—	—	—
(3) BC.		40.75		40.23	F0.52	—	—	—
(4) EC.		40.80		40.05	F0.75	—	—	—
(5) BC.		40.85		40.21	F0.64	—	—	—
(6) ± PT.	X	41.00		40.30	F0.70	—	—	—
(7) E.C.		40.99		40.24	F0.75	—	—	—
C-4	X	40.92		40.23	F0.73	Stks & Tins	1.25	off
C-5		40.92		40.23	F0.69			
D-4		40.93		40.02	F0.91			
D-5		40.92		40.02	F0.90			
E-4		40.90		39.79	F1.11			
E 5		40.92		39.79	F1.13			

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 2920 Pg. 48 | Job No. 797301 Division No. 11 | Notes Red ____ Plotted ____ | Profile ____

Survey of Harbor Gen. Hospital | Date ____ | No. ____

Survey by Curtis Notes Buck. | Notes Chkd. ____ Checked ____ | X-Sec. ____

Indexed C. J. GALL Date ____ | Date ____ Date ____ | No. ____

STATION	B. S.	H. I.	F. S.	ELEV.	
		Curb Grade			Cut F
F-4		40.87		39.48	F1.39
F-5		40.92		39.48	F1.44
G-4		40.85		39.29	F1.56
G-5		40.92		39.29	F1.63
H-4		40.82		39.03	F1.79
H-5		40.92		39.03	F1.89
J-5		40.20		38.97	F1.23
8 ℄ Pt.		40.12		39.00	F1.12
9 BC.		39.92		38.67	F1.25
10 EC.		39.80		38.43	F1.22
11 BC.		39.80		38.67	F1.13
12 EC.		39.70		38.49	F1.21
13 BC.		39.17		38.55	F1.15
14 EC		39.88		38.73	F1.15

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.		
		(Planter or Island #1 per 1545 - pg 214)				
		Curb Grade			cut or Fill	
1 B.C. - 5' R		42.88		41.93	F - 0.95	Stk's & Tins 3° off face Curb
2 P.C.C.		43.14		41.57	F - 1.57	— — —
3 E.C. 2.50 R		43.26		41.60	F - 1.66	— — —
4 ∡ Pt		43.52		41.92	F - 1.60	— — —
5 ∡ Pt		43.56		42.22	F - 1.34	— — —
6 B.C. 4' R.		43.60		42.62	F - 0.98	— — —
7 P.C.C.		43.68		42.62	F - 1.06	— — —
8 E.C. 10' R.		43.80		42.27	F - 1.53	— — —
		Planter or Island #2 per F.B. 1545 pg - 214				
1 P.C.C.		43.95		43.01	F 0.94	Stk's & Tins 3° off face Curb
2 E.C.		44.00		43.24	F 0.76	
3		44.10		42.83	F 1.27	
4 B.C.		43.97		42.77	F 1.20	
5 P.C.C.		43.72		42.65	F 1.07	
6 E.C.		43.76		42.64	F 1.12	
7 ∡ Pt.		43.82		42.73	F 1.09	
8 ∡ Pt.		43.69		42.60	F 1.09	
9 B.C.		43.90		42.77	F 1.13	

Profile No. ____ Notes Red ____ Plotted ____ Job No. 797301 Division No. 11 F.B. 2920 PG. 49
X-Sec. No. ____ Date ____ Date ____ Survey of Harbor Gen. Hosp.
Notes Chkd. ____ Checked ____ Survey by Curtis Notes ____ Date 10-11-61
Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.		
		Planter or Island #4 - For location See F.B. 1545-213				
	Act. Curb.	Curb Grade			Fill	
1 PCC. 4'R	41.05	41.00	39.70		F 1.30	Stk's & Tins 3° off face Curb
2 E.C. 4'R	41.10	41.08	39.71		F 1.37	— — —
3 ∡PT.	41.28	41.29	40.00		F 1.29	— — —
4 ∡PT.	41.49	41.42	39.63		F 1.79	— — —
5 B.C. 4'R.	41.22	41.21	39.74		F 1.47	— — —
6 E.C. 4'R	41.08	41.06	39.73		F 1.33	— — —
7 B.C. 10'R	41.01	41.00	39.66		F 1.34	— — —
8 E.C. 10'R	40.90	40.86	39.50		F 1.36	— — —
9	40.89	40.89	39.51		F 1.38	— — —
10 B.C. 10'R.	40.87	40.87	39.55		F 1.32	— — —

F.B. 2920 PG. 50
Job No. 7973ab Division No. 11 Notes Red Plotted Profile
Survey of Harbor Gen. Hosp. Date Date No.
Survey by Curtis Notes ASC Notes Chkd. Checked X-Sec.
Indexed C. J. GALLI Date Date Date No.

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 7423-M Division No. 11 F.B. 2920 Pg. 5-1
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hosp.
X-Sec. Notes Chkd. ____ Checked ____ Survey by Curtis Notes Newman Date 10-23-61
No. ____ Date ____ Date ____ Map No. ____ Indexed R. J. CALL Date ____

STATION	B. S.	H. I.	F. S.	ELEV.		
					T.B.M. El. 42.00	
	Planter or Island			#5 - For location see F.B. 1545-213		
	Act. Curbs	Curb Grade	Elev.		Fill	
1 E.C. 10'R	41.00	41.00	39.56	Exist. 41.01	F - 1.44	
2. B.C.4'R.	41.12	41.04	39.76	41.04	F - 1.28	
3. E.C.4'R.	41.19	41.16	39.71	41.16	F - 1.45	
4 ℄ Pt.	41.25	40.75	39.52	40.75	F - 1.23	
5 ℄ Pt.	41.22	40.57	39.75	40.57	F - 0.82	
6. B.C.4'R.	40.43	40.31	39.33	40.41	F - 0.98	
7 P.C.C.	40.64	40.36	39.28	40.36	F - 0.98	
8 E.C.10'R	40.58	40.57	39.29	Exist. 40.57	F - 1.21	
9	40.57	40.67	39.29		F - 1.38	
10 B.C. 10'R	40.63	40.77	39.32		F - 1.45	
T.P.						
T.B.M.				39.50	T.B.M. Elev. 39.50	
					1" I.P. cor. const. Bldg.	

NOTE
May 8-1962
Found this Island built Wrong - Not to stakes. stakes, still in. Told Inspt'r & Contractor. Old stk's still O.K.

Note: Grades in red pencil reset 5-25-62

F. B. 2920 PG. 52 Job No. Division No. Notes Red Plotted Profile

Survey of Date Date No.

Survey by Notes Notes Chkd. Checked X-Sec.

Indexed C. J. GALLI Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend notes this side of this line.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

76-L298 CE 307 3-61

Profile No. ____ X-Sec. No. ____ | Notes Red ____ Date ____ | Plotted ____ Date ____ | Job No. 7973.01 Division No. 11 | Survey of Harbor Gen. Hospital | Survey by A.S.Curtis Notes A.S.C Date 4-9-62 | Map No. ____ Indexed C. J. GALLI Date SEP 24 '62

F.B. 2920 PG. 53

J.N. 7973.01
Harbor Gen. Hospital
Parking Lot.
Grades.

STATION	B.S.	H.I.	F.S.	ELEV.
			Note ÷ ✓ Red Check marks after Sub Grades are pts set for Final Sub. 5-21-62 W.E.N.	

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

76-L298 CE 307 3-61

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.	Parking Lot S.E. Cor. Bldg.
(fd) TBM.				39.50	TBM. Elev. 39.50 F.B. 2920-6 - 1" I.P. @ S Cor. Field office Bldg. on W. Side of Vermont Ave. - 200' E. of Outpatients Bla
		(7" Sub. Grade)			
(set) BM.				40.99	± 100' W. of Vermont & ± 100' No. of BM. 220th ST. - most So. Estly Planter Isle of parking Lot. Set Bt. spk in East. Curb.

	Elev.	Fin. pav. Grade	C or F		Sta.	Elev	Sub Grade	C or F	remarks. Rock Gr.
B'-44		41.24			—	40.66	40.66	Gr.	40.99
C'-44		41.23			—	40.65	40.65	"	40.98
D'-44		41.67			—	41.09	41.09	"	41.42
E'-44		41.91			—	41.33	41.33	"	41.86
F'-44		42.15			—	41.57	41.57	"	41.90
F'+04-44		42.20			—	41.62	41.62	"	41.95
G'-44		41.90			—	41.32	41.32	"	41.65
H'-44		41.52			—	40.94	40.94	"	41.27
J'-44		41.14			—	40.56	40.56	"	40.89
K'-44		40.73			—	40.15	40.15	Gr.	40.48
L'-44 Act Curb.	40.90								
Prm't	40.40	40.40							

1x2 red heads

F.B. 2920 Pg. 54
Job No. 79730 Division No. 11 Notes Red Plotted Profile
Survey of Harbor Gen. Hospital Date Date No.
Survey by A.S. Curtis Notes Newman Notes Chkd. Checked X-Sec.
Indexed C. J. GALLI Date Date No.

76-L 298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 7273.01 Division No. 11 F.B. 2920 Pg. 53
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hospital
X-Sec. ____ Notes Chkd. ____ Checked ____ Survey by A.S. Curtis Notes/Kenmen Date 4-9-62
No. ____ Date ____ Date ____ Map No. ____ Indexed ____ Date SEP 2 4 '62

STATION	B.S.	H.I.	F.S.	ELEV.	Parking lot S.E. Cor Bldg.				
	Elev.	Fin. Pvmt. Grade	C or F		Sta.	Elev.	Sub. Grade	C or F	Rock Gr.
B'-45	41.11	41.11	Gr.	Mark on curb	—				
C'-45		41.29			—	40.71	40.71	"	
D'-45		41.51			—	40.93	40.93	"	
E'-45		41.73			—	41.15	41.15	"	
F'-45		41.95			—	41.37	41.37	"	
F+13-45		42.08			—	41.50	41.50	"	
G'-45		41.90			—	41.32	41.32	"	
H'-45		41.52			—	40.94	40.94	Gr.	
J'-45		41.14			—	41.66	40.56	C-12	
K'-45		40.73			—		40.15		
L'-45 Act cb.	40.91				—		39.74		
" Rm 4	40.45	40.42							✓
12-46		40.75					40.17		
B'-46		40.98			—	40.40	40.40	Gr. ✓	40.73
C'-46		41.14			—	40.56	40.56	"	✓ 40.89 ✓
D'-46		41.34			—	40.76	40.76	" ✓	40.09 ✓
E'-46		41.54			—	40.96	40.96	"	✓ 41.29 ✓
F'-46		41.74			—	41.16	41.16	" ✓	41.49 ✓
22-46		41.92			—	41.34	41.34	"	✓ 41.87 ✓
G'-46		41.90			—	41.32	41.32	"	41.65 ✓

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 2920 Pg. 56 | Job No. 2923.01 Division No. 11 Notes Red ____ Plotted ____ Profile ____
Survey of Harbor Gen. Hospital Date ____ No. ____ X-Sec. ____
Survey by A.S. Curtis Notes Neuman Notes Chkd. ____ Checked ____ No. ____
Indexed C.J. GALLI Date ____ Date ____ Date ____

STATION	B.S.	H.I.	F.S.	ELEV.	Parking Lot. S.E. Cor. Bldg.				
	Elev	Fin. Pav. Grade	Cor F		Sta.	Elev.	Sub Grade	Cor F.	Rock Gr.
H'-46		41.52			—	40.94	40.94	Gr.	41.27
J'-46		41.14			—	40.56	40.56	"	40.89
K'-46		40.73			—	40.15	40.15	"	40.48
L'-46 Acl Cb.	40.88	~~40.20~~			—	40.40	Exist. F.L. in Curb.		
Drain	40.~~40~~	40.40							
A²-47	40.62	40.62	Exist. Prm't.		—				
B'-47		40.84			—	40.26	40.26	"	40.59
C'-47		41.00			—	40.52	40.52	"	40.75
D'-47		41.19			—	40.61	40.61	"	40.94
E'-47		41.38			—	40.80	40.80	"	41.13
F'-47		41.57			—	40.98	40.99	"	41.32
G'-47		41.75			—	41.17	41.17	"	41.50
G+7-47		41.77			—	41.19	41.19	"	41.52
H'-47		41.52			—	40.94	40.94	"	41.27
J'-47		41.14			—	40.56	40.56	"	40.89
K'-47		40.73			—	40.15	40.15	Gr.	40.58
L'-47 Acl Tie	40.93	~~40.20~~							
Prm't.	40.43	40.43							

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red Plotted Job No. 7473.01 Division No. 11 F.B. 2920 Pg. 57
No. Date Date Survey of Harbor Gen. Hospital
X-Sec. Notes Chkd. Checked Survey by A.S. Curtis Notes Kaiman Date 4-9-62
No. Date Date Map No. Indexed C. J. GALLI Date

STATION	B. S.	H. I.	F. S.	ELEV.	Parking Lot S.E. Cor. Bldg.				
	Elev.	Fin. Pav. Grade	Cor F.		Sta	Elev	Sub Grade	Cor F.	Rock Gr.
1² - 48	40.34	40.50	Exist.	prm't.					
3' - 48	40.71	40.71	mark	on curb.					
?' - 48		40.85			—	40.27	40.27	Gr.	
D' - 48		41.02			—	40.54	40.54	" ✓	
E' - 48		41.19			—	40.61	40.61	"	
F' - 48		41.36			—	40.78	40.78	" ✓	
G' - 48		41.53			—	40.95	40.95	" ✓	
?' - 48		41.63			—	41.05	41.05	"	
H' - 48		41.52			—	40.94	40.94	"	
J' - 48		41.14			—	40.56	40.56	"	
K' - 48	40.73	40.73	Mark	on curb.					
L' - 48 Adj. T.B.	40.86	~~40.81~~							
12 Rm't	40.~~48~~	40.41							✓
A² - 49	40.44	40.44	Mark	on conc.					
B' - 49		40.58			—		40.00	Gr. ✓	40.33
C' - 49		40.70			—	40.12	40.12	"	✓ 40.45 ✓
D' - 49		40.86			—	40.28	40.28	"	✓ 40.61 ✓
E' - 49		41.01			—	40.43	40.43	"	✓ 40.76 ✓
F' - 49		41.16			—	40.58	40.58	"	✓ 40.91 ✓
G' - 49		41.32			—	40.74	40.74	Gr.	✓ 41.07 ✓

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 2980 Pg. 58 Job No. 7973.0 Division No. 11 Notes Red Plotted Profile
Survey of Harbor Gen. Hospital Date Date No. X-Sec.
Survey by A.S. Curtis Notes Newman Notes Chkd. Checked No.
Indexed C.J. GALLI Date Date Date

Parking lot S.E. Cor. Bldg.

STATION	B.S.	H.I.	F.S.	ELEV.	Sta	Elev.	Sub Grade	Cor F.	Rock Gr.
	Elev.	Fin. Pav. Grade	Cor F						
H'-49		41.52			—	40.94	40.94	Gr.	41.27
J'-49		41.14			—	40.56	40.56	"	40.89
K'-49		40.73			—	40.15	40.15	Gr.	
L'-49 Act. cb.	40.83	40.25		(40.38 Exist F.h.)					
" Drain	40.38								
A²-50	40.32	40.32	Mark on conc.						
B'-50		40.44			—	39.86	39.86	Gr.	
C'-50		40.55			—	39.97	39.97	"	
D'-50		40.70			—	40.12	40.12	"	
E'-50		40.85			—	40.27	40.27	"	40.60
F'-50		41.00			—	40.42	40.42	"	40.75
G'-50		41.15			—	40.57	40.57	"	
H'-50		41.25			—	40.67	40.67	"	41.00
H'+10-50		41.37			—	40.79	40.79	"	41.12
J'-50		41.14			—	40.56	40.56	"	40.89
K'-50		40.73			—	40.15	40.15	"	
L'-50 Act. T.C.	40.90	40.31							
Prm'k.	40.45	(40.90 T.C. 40.45)	Mark on curb.						

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 7673.01 Division No. 11 F.B. 2920 Pg. 59
No. ____ Date ____ Date ____ Survey of Harbor Gtwy, Hospital
X-Sec. Notes Chkd. ____ Checked ____ Survey by A.S. Curtis Notes Newman Date 4-5-62
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

Parking lot S.E. Cor. Bldg.

STATION	B. S.	H.I.	F. S.	ELEV.	Sta	Elev.	sub Grade	C or F	Rock Gr.
	Elev.	Fin. Pav. Grade	C or F						
A²-51	40.23	40.23	Mark on Cond.						
B'-51	40.33	40.33	Mark on Curb.		—				
C'-51		40.42			—	39.84	39.84	Gr.	
D'-51		40.56			—	39.98	39.98	"	
E'-51		40.70			—	40.12	40.12	"	
F'-51		40.84			—	40.26	40.26	"	
G'-51		40.98			—	40.40	40.40	"	
H'-51		41.07			—	40.49	40.49	"	
H+19-51		41.17			—	40.59	40.59	"	
J'-51		41.14			—	40.56	40.56	Gr.	
K'-51	40.73	40.73	Mark on curb						
L'-51	40.90 40.48	40.30	(40.90 T.C. 40.48 T.P.) Mark on Curb.					✓	
A²-52	40.13	40.13	Mark on Conc.						
B'-52		40.19			—	39.61	39.61	Gr. ✓	
C'-52		40.29			—	39.71	39.71	"	✓ 40.04 ✓
D'-52		40.41			—	39.83	39.83	" ✓	✓ 40.16 ✓
E'-52		40.54			—	39.96	39.96	"	✓ 40.29 ✓
F'-52		40.66			—	40.08	40.08	" ✓	✓
G'-52		40.79			—	40.21	40.21	"	✓

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.	Parking Lot. S.E. Cor. Bldg.					
Sta.	Elev.	Fin. Pav. Grade	C or F		Sta.	Elev.	Sub. Grade	C or F.		Rock Gr.
H'-52		40.91			—	40.33	40.33	Gr.	✓	40.66 ✓
S'-52		41.06			—	40.58	40.58	"	✓	
S'+03-52		41.06			—	40.58	40.58	"		40.81 ✓
K'-52		40.73			—	40.15	40.58	Gr.		
L'-52		~~40.20~~		T.C. 40.82 Drain 40.36 } Exist.					✓	
A²-53	40.03	40.03	Mark on conc.							
B'-53		40.05			—	39.47	39.47	Gr.		39.80
C'-53		40.14			—	39.56	39.56	"	✓	39.89 ✓
D'-53		40.26			—	39.68	39.68	"	✓	40.01 ✓
E'-53		40.38			—	39.80	39.80	"	✓	40.13 ✓
F'-53		40.50			—	39.92	39.92	"	✓	40.25 ✓
G'-53		40.62			—	40.04	40.04	"	✓	40.37 ✓
H'-53		40.74			—	40.16	40.16	"	✓	40.49 ✓
S'-53		40.86			—	40.28	40.28	"	✓	40.61 ✓
S'+12-53		40.91			—	40.33	40.33	"	✓	40.66 ✓
K'-53		40.73			—	40.15	40.15	Gr.		40.48
L'-53		40.25		T.C. 40.82 - Exist. T.P. 40.40 - Mark on curb.					✓	

F.B. 2920 PG. 60 Job No. 7973.01 Division No. 11 Notes Red Plotted Profile
Survey of Harbor Gen. Hospital Date Date No.
Survey by A.S. Curtis Notes Newman Notes Chkd. Checked X-Sec.
Indexed C. J. GALLI Date Date Date No.

76-L298 CE 307 8-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Parking Lot S.E. Cor. Bldg.				
Sta	Elev	Fin. Pav. Grade	C or F		Sta	Elev.	Sub. Grade	C or F	Rock Gr.
A² -54	39.92	39.91	Existing Pvm't						
B' -54		39.93	(T.C. 40.55) Mark on Curb.						
C' -54		40.10			—	39.52	39.52	Gr.	
D' -54		40.11			—	39.53	39.53	"	
E' -54		40.22			—	39.64	39.64	"	
F' -54		40.33			—	39.75	39.75	"	
G' -54		40.44			—	39.86	39.86	"	
H' -54		40.55			—	39.97	39.97	"	
J' -54		40.67			—	40.08	40.08	"	
K' -54		40.73	(T.C. 41.18) Mark on Curb						
L' -54	(40.45) x	40.45	(T.C. 40.91) Mark on Curb.						
A² -55	39.79	39.81	Existing Pvm't.						
B' -55		39.80			—	~~40.22~~ 39.22	39.22	~~C 1.00~~ Gr.	39.55
C' -55		39.87			—	39.~~79~~ 29	39.29	~~C 0.50~~	39.62
D' -55		39.98			—	39.~~40~~ 40	39.40	~~C 0.50~~	39.73
E' -55		40.09			—	39.51	39.51	Gr.	39.84
F' -55		40.20			—	39.62	39.62	"	39.95
G' -55		40.31			—	39.73	39.73	"	40.06
H' -55		40.42			—	39.84	39.84	Gr.	40.17

Profile Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11 F.B. 2920 PG. 61
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hospital
X-Sec. Notes Chkd. ____ Checked ____ Survey by A.S. Curtis Notes Newman Date 4-4-62
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.	Parking Lot. S.E. Cor. Bldg.				
Sta	Elev	Fin. Pav. Grade	Cor F.		Sta.	Elev.	Sub. Grade	Cor F.	Rock Gr.
J'-55		40.54			—	39.96	39.96	Gr.	40.29
K'-55		40.62			—	40.04	40.04	Gr.	40.37
L'-55		~~40.25~~	T.C. 41.91 40.49	Exist. Drain					
A²-56	39.65	39.69	Exist.	Prm't.					
A²+15-56		39.62			—	39.04	39.04	Gr.	
B'-56		39.65			—	39.07	39.07	"	39.40
C'-56		39.72 ~~39.70~~			—	39.14 ~~40.14~~	39.14	C-1.00	39.47
D'-56		39.86 ~~39.81~~			—	39.28	39.28	Gr.	39.61
E'-56		39.98 ~~39.92~~			—	39.40 ~~39.50~~	39.40	~~C-0.50~~	39.73
F'-56		40.10 ~~40.03~~			—	39.52 ~~40.02~~	Gr 39.52	~~C-0.50~~	39.85
G'-56		40.21 ~~40.14~~			—	39.63	39.63	Gr.	39.96
H'-56		40.30 ~~40.25~~			—	39.72	39.72	"	40.05
J'-56		40.40 ~~40.36~~			—	39.82	39.82	"	40.15
K'-56		40.50			—	39.92	39.92	"	40.25
K'+15-56		40.55			—	39.97	39.97	"	
L'-56		40.46	T.C. 40.92 40.46	Exist. Marking on Curb.					

F.B. 2920 PG. 62
Job No. 7973.01 Division No. 11 Notes Red Plotted Profile
Survey of Harbor Gen. Hospital Date No.
Survey by A.S. Curtis Notes Newman Notes Chkd. Checked X-Sec.
Indexed C. J. GALLI Date Date No.

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red Plotted Job No. 7773.01 Division No. 11 F.B. 2220 Pg. 43
No. X-Sec. Date Date Survey of Harbor Gen. Hospital
No. Notes Chkd. Checked Survey by A.S. Curtis Notes Kaufman Date 4-9-62
Date Date Map No. Indexed C. J. GALL Date

STATION	B. S.	H. I.	F. S.	ELEV.	Parking Lot S.E. Cor. Bldg.			
Sta	Elev.	Fin. Pvmt. Grade	C or F.		Sta	Elev.	Sub Grade	C or F
ing 57 North side								
A²-57.	39.56	39.56	Mark on Curb.					
A²+15-57		39.48			—	38.90	38.90	Gr.
B'-57		39.52			—	38.94	38.94	Gr.
C'-57	39.60	↑ 39.60	Mark on Curb.			↑	39.02	
D'-57	39.80	(39.80) 39.78	"				39.22	
E'-57	39.90	39.90	"			Set Top Pvmt	39.32	
F'-57	39.95	Existing Drains 39.95	"				39.37	
G'-57	40.13	40.13	"				39.55	
H'-57	40.15	(40.15) 40.11	"				39.57	
J'-57	40.29	↓ 40.29	Mark on Curb.			↓	39.71	
K'-57		40.30			—	39.72	39.72	Gr.
L'-57	40.45	(40.45) 40.38	40.45	Existing Drain				✓
ing 57 South side								
J²-57		Not Set						
A²+15-57		"						
B'-57		"						
C'-57		↑ (39.56)×					38.98	
D'-57		(39.80) 39.44 ×					39.08	
E'-57		(39.60) 39.76 ×					39.18	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.	Parking Lot. S. E. Cor. Bldg.				
Sta.	Elev.	Fin. Pav. Grade	C or F.		Sta.	Elev.	Sub. Grade	C or F.	
F'-57		(39.90) x 39.86					39.32		
G'-57		(40.05) x 39.96					39.47		
H'-57		(40.11) x 40.06					39.53		
J'-57		(40.28) x 40.18					39.70		
K'-57		Not Set							
L'-57		"							
A²-58									
A²+15-58									
B'-58									
C'-58									
D'-58									
E'-58									
F'-58									
G'-58									
H'-58									
J'-58									
K'-58									
L'-58									

F.B. 2920 Pg. 64 Job No. 7973.01 Division No. 11 Notes Red ___ Plotted ___ Profile ___
Survey of Harbor Gen. Hospital Date ___ Date ___ No. ___
Survey by A.S. Curtis Notes Newman Notes Chkd. ___ Checked ___ X-Sec. ___
Indexed C. J. GALLI Date ___ Date ___ No. ___

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Parking Lot, S.E. Cor. Bldg.				
Sta	Elev.	Fin. Pav. Grade	C or F		Sta	Elev.	Sub. Grade	C or F	Rock Gr.
B1 - 43		41.37			—	40.79	40.79	Gr.	
C - 43		41.59			—	41.01	41.01	"	✓
D - 43		41.87			—	41.29	41.29	" ✓	✓
E - 43		42.15			—	41.57	41.57	" ✓	✓ 41.90 ✓
(E+19) - 43		42.35			—	41.77	41.77	"	✓ 42.10 ✓
F - 43		42.29			—	41.71	41.71	" ✓	✓ 42.04 ✓
G - 43		41.90			—	41.32	41.32	" ✓	✓
H - 43		41.52			—	40.94	40.94	" ✓	✓
J - 43		41.14			—	40.56	40.56	"	✓
K - 43		40.73			—	40.15	40.15	" ✓	
L - 43 Act Cb	40.86	40.86							
L - 43 Act Dr	40.36	40.36							✓
B1 - 42 Act Curb	42.05	42.05							
B1 - 42 Pav. Grd.	41.50	41.50	Mark	on Curb.					
C - 42		41.75			—	41.17	41.17	"	
D - 42		42.05			—	41.47	41.47	"	
E - 42		42.38			—	41.80	41.80	" ✓	
(E+11) - 42		42.51			—	41.93	41.93	"	

Profile Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11 F.B. 2920 Pg. 65
No. ____ Date ____ Date ____ Survey of Harbor Gen Hosp.
X-Sec. Notes Chkd. ____ Checked ____ Survey by Curtis Notes Newman Date 4-10-62
No. ____ Date ____ Date ____ Map No. ____ Indexed C. I. GAHM Date ____

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

STATION		B.S.	H.I.	F.S.	ELEV.*	Parking Lot S.E. Cor. Bldg.				
Sta.		Elev	Fin Pav Grd	C or F		Sta.	Elev.	Sub Grade	C or F	Rock Gr.
F-42			42.29			—	41.71	41.71	Gr.	
G-42			41.90			—	41.32	41.32	"	
H-42			41.52			—	40.94	40.94	"	
J-42			41.14			—	40.56	40.56	"	✓
K-42	Act. Curb	41.24	(41.24)							
K-42	Pav Grd	40.73	40.73	Gr.						
L-42	Act Curb	40.91	40.91							
L-42-	Pav Grd	40.39	40.39	Mark on Curb.						✓
B1-41			41.73			—	41.15	41.15	Gr.	
C-41			41.92			—	41.34	41.34	"	✓
D-41			42.31			—	41.73	41.73	" ✓	✓ 42.06 ✓
E-41			42.56			—	41.98	41.98	"	✓ 42.31 ✓
F-41			42.29			—	41.71	41.71	" ✓	✓ 42.04 ✓
G-41			41.90			—	41.32	41.32	"	✓
H-41			41.52			—	40.94	40.94	" ✓	✓
J-41			41.14			—	40.56	40.56	"	✓
K-41			40.73			—	40.15	40.15	" ✓	
L-41	Act Curb	40 89	40.89							
L-41	Pav. Grade	40 42	40 42	Mark on curb						✓

F.B. 2920 Pg. 66 Job No. 7973.01 Division No. 11 Notes Red Plotted Profile
Survey of Harbor Gen. Hosp. Date Date No.
Survey by Curtis Notes Newman Notes Chkd. Checked X-Sec.
Indexed C. J. GALL Date Date No.

76-L 298 CE 307 3-61

PLEASE RETURN TO:
LOS ANGELES COUNTY ENGINEER
408 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 7773.01 Division No. 11 F.B. 2920 Pg. 67
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hosp
X-Sec. Notes Chkd. ____ Checked ____ Survey by Curtis Notes Harvey Date 4-10-62
No. ____ Date ____ Date ____ Map No. ____ Indexed C.J. GALL Date ____

Parking Lot S.E. Cor. Bldg

STATION	B. S.	H. I.	F. S.	ELEV.	Sta.	Fin Fin. Grade	Sub. Grade	C or F	Rock Gr.
	Elev.	Fin. Fin Grd	C or F						
B,-40		42.13			—	41.55	41.55	Gr.	
C-40		42.28			—	41.70	41.70	"	✓
D-40		42.58			—	42.00	42.00	"	✓ 42.33 ✓
D+16)-40		42.79			—	42.21	42.21	"	✓ 42.54 ✓
E-40		42.67			—	42.09	42.09	" ✓	✓ 42.42 ✓
F -40		42.28			—	41.70	41.70	" ✓	✓ 42.03 ✓
G- 40		41.90			—	41.32	41.32	"	✓
H- 40		41.52			—	40.94	40.94	"	✓
J - 40		41.14			—	40.56	40.56	"	✓
K — 40		40.73			—	40.15	40.15	" ✓	
L-40 Act Curb	40 90	40 90							
M-40 Act DR	40 41	40 41							✓
N-39 Act Curb	42.75	42.75							
O,-39 Par Grd	42.23	42.23	Mark on curb						
C-39		42 58			—	42.00	42.00	Gr.	
D-39		42 85			—	42.27	42.27	"	
D+07)-39		42 93			—	42.35	42.35	"	
E -39		42 68			—	42.10	42.10	"	
F - 39		42 29			—	41.71	41.71	"	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 292 Pg. 68 | Job No. 7973.01 | Division No. 11 | Notes Red | Plotted | Profile
Survey of Hawthorne Gen Hosp. | Date | Date | No. | X-Sec.
Survey by Curtis Notes Newman | Notes Chkd. | Checked | No.
Indexed C. J. Galli Date | Date | Date

STATION	B. S.	H. I.	F. S.	ELEV.	Parking lot S.E. Cor. Bldg.				
	Elev.	Fin. Pav. Grade	C or F		Sta	Elev	Sub Grade	C or F	Rock Gr.
G - 39		41.90			—	41.32	41.32	Gr.	
H - 39		41.52			—	40.94	40.94	"	
J - 39		41.14			—	40.56	40.56	"	
K - 39 Prm't.	40.74	40 74	Mark on curb						
K - 39 Act. Curb	41.27								
L - 39 Prm't.	40 ~~82~~		Mark on curb.						
L - 39 Act. Curb.	40 88								
B' - 38		42.42			—	41.84	41.84	Gr.	
C' - 38		42.70			—	42.12	42.12	"	42.45
D' - 38		43.07			—	42.49	42.49	"	42.82
E' - 38		42.68			—	42.10	42.10	"	42.43
F' - 38		42.29			~~Mkd~~ Sta.	41.71	41.71		
G' - 38		41.90			—	41.32	41.32	"	
H' - 38		41.52			—	40.94	40.94	"	
J' - 38		41.14			—	40.56	40.56	"	
K' - 38		40.74			—	40.16	40.16	Gr.	
L' - 38 Act. Curb	40.95								
L' - 38 Prm't.	40.45								

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 7973.0' Division No. 11 F.B. 2920 Pg. 67
No. X-Sec. ____ Date ____ Date ____ Survey of Hawthorne Gen. Hospital
No. ____ Notes Chkd. ____ Checked ____ Survey by Curtis Notes Kaufman Date 4-11-62
Date ____ Date ____ Map No. ____ Indexed C. J. GAU Date ____

Parking Lot. S.E. Cor. Bldg.

STATION	B. S.	H. I.	F. S.	ELEV.	Sta	Elev	Sub Grade	C or F	Rock Gr.
	Elev	Fin. pav. Grade	C or F						
B'-37		42.70			—	42.12	42.12	Gr. ✓	
C'-37		42.98			—	42.40	42.40	" ✓	✓ 42.73 ✓
C'+13-37		43.22			—	42.62	42.62	" ✓	✓ 42.93 ✓
D'-37		43.05			—	42.47	42.47	" ✓	✓ 42.80 ✓
E'-37		42.68			—	42.10	42.10	" ✓	✓
F'-37		42.29			—	41.71	41.71	" ✓	✓
G'-37		41.90			—	41.32	41.32	" ✓	✓
H'-37		41.52			—	40.94	40.94	" ✓	✓
J'-37		41.14			—	40.56	40.56	" ✓	✓
K'-37		40.74			—	40.16	40.16	" ✓	
L'-37 Act. Curb	40.93								
L'-37 Act. Drain	40.43								✓
B'-36 Act Curb	43.46								
B'-36 prm't.	42.94	42.94	Mark on curb.						
C'-36		43.32			—	42.74	42.74	GR.	
C'+04-36		43.37			—	42.79	42.79	"	✓
D'-36		43.05			—	42.47	42.47	" ✓	
E'-36		42.68			—	42.10	42.10	"	
F'-36		42.29			—	41.71	41.71	Gr. ✓	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 2920 Pg. 70 | Job No. 7973.01 | Division No. 11 | Notes Red | Plotted | Profile
Survey of Harbor Gen Hosp. | Date | Date | No. | X-Sec.
Survey by Curtis Notes Newman | Notes Chkd. | Checked | No.
Indexed C. J. GALLI Date | Date | Date

Parking lot. S.E. Cor. Bldg.

STATION	B. S.	H. I.	F. S.	ELEV.	Sta.	Elev.	Sub Grade	C or F	Rock Gr.
	Elev.	Fin. Pav. Grade	C or F						
G-36		41.90			—	41.32	41.32	Gr.	
H-36		41.52			—	40.94	40.94	"	
J-36		41.14			—	40.56	40.56	"	
K'-36 Act. Curb									
K'-36 prm't.	40.74	40.74	Mark on curb						
L'-36 Act. Curb.	40.96								
L'-36 prm't	40.46	40.46	Mark on curb.						
B'-35		43.30			—	42.72	42.72	Gr.	
B'+14-35		43.50			—	42.92	42.92	"	43.25
C'-35		43.37			—	42.79	42.79	"	43.12
D'-35		43.05			—	42.47	42.47	"	
E'-35		42.68			—	42.10	42.10	"	
F'-35		42.29			—	41.71	41.71	"	
G-35		41.90			—	41.32	41.32	"	
H-35		41.52			—	40.94	40.94	"	
J-35		41.14			—	40.56	40.54	"	
K-35		40.74			—	40.16	40.16	"	
L'-35 Act Curb	40.95								
L'-35 prm't.	40.45	40.45	Mark on Curb.						

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Parking Lot S.E. Cor. Bldg.				
	Elev.	Fin. Pav Grade	C or F		Sta.	Elev.	Sub Grade	C or F	
B1-34		43.65			—	43.07	43.07	Gr. ✓	
C-34		43.44			—	42.86	42.86	"	✓
D		43.05			—	42.47	42.47	" ✓	✓
E		42.68			—	42.10	42.10	"	✓
F		42.29			—	41.71	41.71	" ✓	✓
G		41.90			—	41.32	41.32	"	✓
H		41.52			—	40.94	40.94	" ✓	✓
J		41.14			—	40.56	40.56	"	✓
K		40.74			—	40.16	40.16	" ✓	
L-34 Act Curb	40.92								
L-34 Act Drain	40.41								✓
B'-33 Act. Curb	44.15								
B'-33 prmt	43.73	43.73	Mark on Curb				43.15		
C'-33		43.43			—	42.85	42.85	Gr.	
D'-33		43.05			—	42.47	42.47	"	
E-33		42.68			—	42.10	42.10	"	
F'-33		42.29			—	41.71	41.71	"	
G-33		41.90			—	41.32	41.32	"	
H-33		41.52			—	40.94	40.94	"	
J-33		41.14			—	40.56	40.56	"	

Profile Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11 F.B. 2920 PG. 71
No. ____ Date ____ Date ____ Survey of Harbor Gen Hosp.
X-Sec. Notes Chkd. ____ Checked ____ Survey by Curtis Notes Newman Date 4-11-62
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 2920 Pg. 72 Job No. 7973.01 Division No. 11 Notes Red Plotted Profile
Survey of Hazeboe Gen. Hosp. Date Date No. X-Sec.
Survey by Curry's Notes Newman Notes Chkd. Checked No.
Indexed C. J. GALLI Date Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	Parking lot S.E. Cor. Bldg.			
	Elev	Fin Pav. Grade	C or F		Sta.	Elev.	Sub Grade	C or E
K'-33 Act. Curb.	41.25							
K'-33 prm't.	40.74	40.74	Mark on Curb					
L: at Curb Rot. Act. Curb.	40.90							
" prm't.	40.43	40.43	Mark on Curb.					✓
B'-32		43.70			—	43.12	43.12	Gr. ✓
C'-32		43.43			—	42.85	42.85	" ✓
D'-32		43.05			—	42.47	42.47	" ✓ ✓
E'-32		42.68			—	42.10	42.10	" ✓
F'-32		42.29			—	41.71	41.71	" ✓ ✓
G'-32		41.90			—	41.32	41.32	" ✓
H'-32		41.52			—	40.94	40.94	" ✓ ✓
J'-32		41.14			—	40.56	40.56	" ✓
K'-32		40.74			—	40.16	40.16	" ✓
L'-32		40.25			—	39.67	39.67	"

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11 F.B. 2920 Pg. 73
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hospital
X-Sec. Notes Chkd. ____ Checked ____ Survey by A.S. Curtis Notes Newman Date 4-12-62
No. ____ Date ____ Date ____ Map No. ____ Indexed C.J. GALLI Date ____

Parking Lot S.E. Cor. Bldg.

STATION	B.S. Elev.	H.I. Fin. Pavmt Grade	F.S. C or F	ELEV.	Sta	Elev.	Sub. Grade	C or F	
B'-31		43.68			—	43.10	43.10	Gr. ✓	
C'-31		43.42			—	42.84	42.84	"	✓
D'-31		43.05			—	42.47	42.47	" ✓	✓
E'-31		42.65			—	42.07	42.07	"	✓
F-31		42.29			—	41.71	41.71	" ✓	✓
G-31		41.90			—	41.32	41.32	"	✓
H-31		41.52			—	40.94	40.94	" ✓	✓
J-31		41.14			—	40.56	40.56	"	✓
K-31		40.74			—	40.16	40.16	" ✓	
L-31		40.20			—	39.62	39.62	"	
B'-30 Act. Curb	44.16								
B'-30 Pavm't	43.96	43.96	Mark	on curb					
C-30		43.43			—	42.85	42.85	Gr.	
D-30		43.05			—	42.47	42.47	"	
E-30		42.68			—	42.10	42.10	"	
F-30		42.29			—	41.71	41.71	" ✓	
G-30		41.90			—	41.32	41.32	"	
H-30		41.52			—	40.94	40.94	" ✓	
J-30		41.14			—	40.56	40.56	"	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.	Parking Lot S.E. Cor. Bldg.				
	Elev.	Fin. Prm't. Grade	C. or F.		Sta.	Elev.	Sub. Grade	C. or F.	
K-30 Act. Curb	41.27								
K-30 prm't.	40.75	40.75	Mark on Curb.						
L-30 Act Curb	40.85								
L-30 prm't.	40.35	40.35	Mark on curb.						
B'-29		43.71			—	43.13	43.13	Gr. ✓	
C-29		43.43			—	42.85	42.85	"	✓
D-29		43.05			—	42.47	42.47	"	✓
E-29		42.68			—	42.10	42.10	"	✓
F-29		42.29			—	41.71	41.71	"	✓
G-29		41.90			—	41.32	41.32	"	✓
H-29		41.52			—	40.94	40.94	"	✓
J-29		41.14			—	40.56	40.56	"	✓
K-29		40.75			—	40.17	40.17	"	
L-29 Act. Curb	40.76								
L-29 prm't.	40.26	40.26	Mark on Curb.						

F.B. 2920 Pg. 74 Job No. 7973.01 Division No. 11 Notes Red Plotted Profile
Survey of Harbor Gen. Hospital Date Date No.
Survey by A.S. Curtis Notes Newman Notes Chkd. Checked X-Sec.
Indexed C. J. GALLT Date Date Date No.

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Parking Lot S.E. Cor. Bldg.				
	Elev	Fin. Pav. Grade	C or F		Sta.	Elev	Sub Grade	C or F	
B'-28		43.70			—	43.12	43.12	Gr.	
C-28		43.43			—	42.85	42.85	"	✓
D-28		43.05			—	42.47	42.47	"	✓
E-28		42.68			—	42.10	42.10	"	✓
F-28		42.29			—	41.71	41.71	"	✓
G-28		41.90			—	41.32	41.32	"	✓
H-28		41.52			—	40.94	40.94	"	✓
J-28		41.14			—	40.56	40.56	"	✓
K-28		40.72			—	40.14	40.14	"	
L-28 Act. Curb	40.71								
[illegible]-28 Act. Drain	40.21								
B'-27 Act. Curb	44.17								
B'-27 prm't.	43.96	43.96	Mark on Curb						
C-27		43.43			—	42.85	42.85	Gr.	
D-27		43.05			—	42.47	42.47	"	
E-27		42.68			—	42.10	42.10	"	
F-27		42.29			—	41.71	41.71	"	
G-27		41.90			—	41.32	41.32	"	

Profile Notes Red ____ Plotted ____ Job No. 797301 Division No. 11 F.B. 2920 Pg. 75
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hospital
X-Sec. Notes Chkd. ____ Checked ____ Survey by Curtis Notes Newman Date 4-12-62
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALL Date SEP 24 '62

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.	Parking Lot. S.E. Cor. Bldg			
	Elev	Fin Pav. Grade	C or F		Sta.	Elev.	Sub Grade	C or F
H-27		41.52			—	40.94	40.94	Gr.
J-27		41.14			—	40.56	40.56	"
K-27 Act. Curb.	41 20							
K-27 prm't.	40.70	40.70	Mark on Curb.					
L-27 Act. Curb.	40 61							
L-27 Prm't.	40.18		Mark on curb					
B'-26		43.70			—	43-12	43.12	Gr.
C-26		43.43			—	42.85	42.85	"
D-26		43.05			—	42.47	42.47	"
E-26		42.68			—	42.10	42.10	"
F-26		42.29			—	41.71	41.71	"
G-26		41.90			—	41.32	41.32	"
H-26		41.52			—	40.94	40.94	"
J-26		41.14			—	40.56	40.56	"
K-26		40.69			—	40.11	40.11	"
L-26 Act. Curb.	40.57							
L-26 prm't.	40.16	40.16	Mark on curb					

F.B. 2920 Pg. 76 Job No. 7973.01 Division No. 11 Notes Red Plotted Profile
Survey of Harbor Gen. Hosp. Date Date No.
Survey by Curtis Notes Newman Notes Chkd. Checked X-Sec.
Indexed C. J. GALLI Date Date No.

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 7613.01 Division No. 11
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hospital
X-Sec. ____ Notes Chkd. ____ Checked ____ Survey by A.S. Curtis Notes Newman Date 4-16-62
No. ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

F.B. 2920 Pg. 77

STATION	B. S.	H. I.	F. S.	ELEV.	Parking Lot S.E. Cor. Bldg				
	Elev	Fin. Pavm't. Grade	Cor F.		Sta	Elev.	Sub. Grade	Cor F	
B'-25		43.73			—	43.15	43.15	Gr.	
C'-25		43.43			—	42.85	42.85	"	✓
D'-25		43.04			—	42.46	42.46	"	✓
E-25		42.68			—	42.10	42.10	"	✓
F-25		42.29			—	41.71	41.71	"	✓
G-25		41.90			—	41.32	41.32	"	✓
H-25		41.52			—	40.94	40.94	"	✓
J-25		41.14			—	40.56	40.56	"	✓
K-25		40.68			—	40.10	40.10	"	
L-25 Act. Curb	40.66								
L-25 Act. Drain	40.14								
B'-24 Act. Curb	44.27								
B'-24	43.96	43.96	Mark on Curb		(13'-24 5' West)	43.32	43.32	Gr.	
C-24		43.43			—	42.85	42.85	"	
D-24		43.04			—	42.46	42.46		
E-24		42.68			—	42.10	42.10	"	
F-24		42.29			—	41.71	41.71	"	
G-24		41.90			—	41.32	41.32	"	
H-24		41.52			—	40.94	40.94	"	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 2920 Pg. 78 Job No. 79730 Division No. 11 Notes Red Plotted Profile
Survey of Harbor Gen. Hosp. Tr. Date Date No. X-Sec.
Survey by A.S. Curtis Notes Newman Notes Chkd. Checked
Indexed C.J. GALLI Date Date Date No.

STATION	B.S.	H.I.	F.S.	ELEV.	Parking Lot. S.E. Cor. Bldg.			
	Elev.	Fin. Pvmt Grade	C. or F.		Sta	Elev.	Sub Grade	C. or F.
J-24		41.14			—	40.56	40.56	GF
K-24 Act. Curb	41.26							
K-24	40.68	40.68	Mark	on curb				
L-24 Act. Curb	40.55							
L-24	40.05		Mark	on curb				
B'-23		43.71			—	43.13	43.13	GF
C-23		43.43			—	42.85	42.85	"
D-23		43.04			—	42.46	42.46	"
E-23		42.68			—	42.10	42.10	"
F-23		42.29			—	41.71	41.71	"
G-23		41.90			—	41.32	41.32	"
H-23		41.52			—	40.94	40.94	"
J-23		41.14			—	40.56	40.56	"
K-23		40.67			—	40.09	40.09	"
L-23		40.00			—	39.42	39.42	"

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red Plotted Job No. 7573.01 Division No. 11 F.B. 2920 Pg. 79
No. X-Sec. Date Date Survey of Harbor Gen. Hospital
No. Notes Chkd. Checked Survey by A.S. Curtis Notes Newman Date 4-14-62
Date Date Map No. Indexed C. J. GALLI Date

STATION	B. S.	H. I.	F. S.	ELEV.	Parking Lot S.E. Cor Bldg.				
	Elev.	Fin. Prop. Grade	Cor E		Sta	Elev.	sub. Grade	C. or E.	
B^2-22		43.54			—	42.96	42.96	Gr.	
D-22		43.04			—	42.46	42.46	"	✓
E-22		42.68			—	42.10	42.10	"	✓
F-22		42.29			—	41.71	41.71	"	✓
G-22		41.90			—	41.32	41.32	"	✓
H-22		41.52			—	40.94	40.94	"	✓
J-22		41.14			—	40.56	40.56	"	✓
K-22		40.65			—	40.07	40.07	"	
L-22		39.95			—	39.37	39.37	"	
B^2-21 Act. Curb	44.02								
B^2-21	43.90	43.90	Mark on Curb.		(B^2-21 5' West)	43.22	43.22	Gr.	
D-21		43.04			—	42.46	42.46	"	
E-21		42.68			—	42.10	42.10	"	
F-21		42.29			—	41.71	41.71	"	
G-21		41.90			—	41.32	41.32	"	
H-21		41.52			—	40.94	40.94	"	
J-21		41.14			—	40.56	40.56	"	
K-21 Act. Curb	41.20								
K-21	40.63	40.63	Mark on Curb.						

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.	Parking Lot. S.E. Cor. Bldg				
	Elev.	Fin. Prm't Grade	C or F.		Sta	Elev.	Sub. Grade	C. or F.	
L-21		39.92			—	39.34	39.34	Gr.	
B2-20		43.50			—	42.92	42.92	Gr.	
D-20		43.04			—	42.46	42.46	"	✓
E-20		42.68			—	42.10	42.10	"	✓
F-20		42.29			—	41.71	41.71	"	✓
G-20		41.90			—	41.32	41.32	"	✓
H-20		41.52			—	40.94	40.94	"	✓
J-20		41.14			—	40.56	40.56	"	✓
K-20		40.61			—	40.03	40.03	"	
L-20		39.89			—	39.31	39.31	"	
T.B.M.#				39.50	T.B.M.#	Elev. 39.50 F.B.			
T.B.M.#				40.87	T.B.M.#	Elev.		F.B. 2920-80	

N. end of N. Curb Ret. at pt. L-30 Parking Lot.
Bench. nail in Ledge.

F.B. 2920 PG. 80
Job No. 7973.01 Division No. 11 Notes Red Plotted Profile
Survey of Harbor Gen. Hospital Date Date No.
Survey by A.S. Curtis Notes Newman Notes Chkd. Checked X-Sec.
Indexed C. J. GALLI Date Date Date No.

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red Plotted Job No. 7473.9 Division No. 11 F.B. 2920 Pg. 81
No. Date Date Survey of Harbor Gen. Hospital
X-Sec. Notes Chkd. Checked Survey by A.S. Curtis Notes Kremen Date 4-16-62
No. Date Date Map No. Indexed C. J. GAHL Date

STATION	B. S.	H. I.	F. S.	ELEV.	Parking Lot. S.E. Cor. Bldg.
	Elev.	Fin. Prm't Grade	C or E		
C-19 B.C. Act. Curb	44.61				
C-19 Prm't.	43.50	43.50	Mark on	Curb.	
D-19 Act. Curb	43.59				
D-19 Prm't	43.04	43.04	"		
E-19 Act. Curb	43.20				
E-19 Prm't	42.67	42.67	"		
G-19 Act. Curb	42.43				
G-19 Prm't	41.90	41.90	"		
H-19 Act. Curb.	42.07				
H-19 Prm't	41.50	41.50	"		
J-19 Act. Curb	41.69				
J-19 Prm't	41.13	41.13	"		
(J+15)-19 B.C. Act. Curb	41.36				
(J+15)-19 B.C. Prm't	40.82	40.82 Sub. Grade	"		
K-19	39.97	39.97	1x1 set to	Grade.	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 2920 Pg. 82 Job No. 7773.01 Division No. 11 Notes Red Plotted Profile
Survey of Date Date No. X-Sec.
Survey by Notes Notes Chkd. Checked
Indexed C. J. GARI Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	S.E. Parking Lot (east side of Bldg.)
Exist Curb & Drains on "L" Line					
	Elev.				
L - 23 T.C.	40.55				
Prm 4.	40.02				
L - 22 T.C.	40 48				
Prm 4.	40 00				
L - 21 T.C.	40 44				
Drain	39 95				
L - 20 T.C.	40 38				
Prm 4	39.91				
L - 19 T.C.	40.29				
Prm 4	39.82				
" No. 11' T.C.	40.24				
" Drain	39.76				
" No. 36' T.C.	40.26				
" Prm 4	39.79				
" No. 61' T.C.	40.27				
" Prm 4	39.74				
" No. 86' T.C.	40.21				
" Drain	39.71				
B.C. " No. 114' T.C.	40.13				
Prm 4	39.63				

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Parking Lot So. of Bldg.				
	Elev.	Fin. Prm't. Grade	C or F		Sta	Elev.	Sub Grade	C or F	
1+2.83 - 30 Act. Curb	44.54								
" Prm't.	44.05	44.05							
B - 30 Act. Curb	44.53								
" Prm't	44.05	44.05							
C - 30 Act. Curb	44.55								
" Prm't	44.05	44.05							
D - 30 Act. Curb									
" Prm't		44.05							
E - 30 Act. Curb									
" Prm't		44.05							
F - 30 Act. Curb									
" Prm't.		44.05							
G - 30 Act. Curb									
" Prm't		44.05							
(+20) - 30 Act. Curb									
" Prm't.		44.05							
22) - 30 Act. Curb									
" Prm't		44.05							
-30 N-C.R. Act. Curb									
" Prm't		43.44							

Profile Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11 F.B. 2920 PG. 83
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hospital
X-Sec. Notes Chkd. ____ Checked ____ Survey by A.S. Curtis Notes Newman Date 4-17-62
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 2420 Pg. 84 | Job No. 7973.01 | Division No. 11 | Profile No. | X-Sec. No.
Survey of Harbor Gen. Hospital | Notes Red | Plotted
Survey by A.S. Curtis | Notes Chkd. | Checked
Indexed C. J. GALLI | Date | Date | Date

STATION	B. S.	H. I.	F. S.	ELEV.	Parking Lot So. of Bldg.				
	Elev.	Fin. Pvm't. Grade	C. or F.		Sta	Elev.	Sub Grade	C or F.	
K+ -30 So. C.R. Act. curb									
" Pvm't		40.40							
A,-31 Act curb									
A,-31 Pav.		44.00							
A-31		43.81				43.23	43.23	Grd	✓
B-31		43.81				43.23	43.23	Grd,	✓
C-31		43.81				43.23	43.23	Grd,	✓
D-31		43.81				43.23	43.23	Grd	✓
F-31		43.80				43.22	43.22	Grd	✓
F-31		4380				43.22	43.22	Grd	✓
G-31		4380				43.22	43.22	Grd	✓
H-31		4380				43.22	43.22	Grd	✓
J-31 ℄ B.C.	Act. cl. 44.10	43.64							
K-31 ℄ B.C.	Act. cl. 43.73	43.32							
A,-32		43.44				42.86	42.86	Grd	
A-32		43.44				42.86	42.86	Grd.	✓
B-32		43.44				42.86	42.86	Grd.	✓
C-32		43.45				42.85	42.85	Grd	✓

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11 F.B. 2920 Pg. 85
No. X-Sec. Date ____ Date ____ Survey of Hartbeat Gen. Hosp
No. ____ Date ____ Notes Chkd. ____ Checked ____ Survey by Curtis Notes ____ Date 4-17-62
Date ____ Map No. ____ Indexed C. J. GALLI Date ____

STATION	B. S.	H. I.	F. S.	ELEV.	Park Lot So. of Bldg.			
	Elev.	Fin Pav Grade	C or F		Sta.	Elev.	Sub Grade	C or F
D-32		43.43				42.85	42.85	Grd. ✓
E-32		43.43				42.85	42.85	Grd. ✓
F-32		43.42				42.84	42.84	Grd. ✓
G-32		43.42				42.84	42.84	Grd. ✓
H-32		43.41				42.83	42.83	Grd. ✓
(H+12)-32		43.44					42.86	✓
J-32		42.33				42.75	42.75	Grd. ✓
K-32		42.90					42.32	
A1-33 Act Curb	43.57							
A1-33 Pav Grd.	43.20	43.20						
A-33		43.21				42.63	42.63	Grd.
B-33		43.21				42.63	42.63	Grd.
C-33		43.21				42.63	42.63	Grd.
D-33		43.21				42.63	42.63	Grd.
E-33		43.21				42.63	42.63	Grd.
F-33		43.21				42.63	42.63	Grd.
G-33		43.20				42.62	42.62	Grd.
H-33		43.20				42.62	42.62	Grd.

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 2920 Pg. 86 Job No. 7973.01 Division No. 11 Notes Red Plotted Profile
Survey of Alameda Gen Hosp. Date Date No. X-Sec.
Survey by Curtis Notes C. J. GALLI Notes Chkd. Checked No.
Indexed Date Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	Park Lot So. of Bldg.			
	Elev.	Fin. Pav. Grd.			Sta.	Elev.	Sub. Grd	C or F
J-33 Act Cb.		43.20				42.62	42.62	Grd.
K-33 Fin Pav.	42.81	42.81						
A,-34		43.00				42.42	42.42	Grd
A-34		42.99				42.41	42.41	Grd
B-34		42.99				42.41	42.41	Grd,
C-34		42.99				42.41	42.41	Grd,
D-34		42.99				42.41	42.41	Grd
E-34		42.99				42.41	42.41	Grd,
F-34		42.99				42.41	42.41	Grd
G-34		42.99				42.41	42.41	Grd
H-34		42.99				42.41	42.41	Grd,
J-34		43.00				42.42	42.42	Grd.
K-34		42.80				42.22	42.22	Grd
L		42.00				41.42	41.42	Grd
M 16'		41.63				41.05	41.05	Grd
A-35		42.66				42.08	42.08	GRD
A-35		42.76				42.18	42.18	GRD.
B-35		42.76				42.18	42.18	Grd

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Park Lot So. of Bldg.				
	Elev	Fin Pav. Grd	C or F			Elev.	Sub Grade		
-35		42.76				42.18	42.18	Grd.	✓
-35		42.76				42.18	42.18	Grd.	✓
-35		42.76				42.18	42.18	Grd	✓
-35		42.76				42.18	42.18	Grd.	✓
-35		42.76				42.18	42.18	Grd.	✓
-35		42.76				42.18	42.18	Grd.	✓
35		42.76				42.18	42.18	Grd.	✓
-35		42.76				42.18	42.18	Grd	✓
-35		42.53				41.95	41.95	Grd	✓
-35		42.08				41.50	41.50	Grd.	
-36 Act Cb.		42.93			M-35	41.05	41.05	"	✓
-36 Pav		42.52	42.52						
-36		42.45				41.87	41.87	Grd ✓	
-36		42.54				41.96	41.96	Grd.	
-36		42.54				41.96	41.96	Grd ✓	
-36		42.54				41.96	41.96	Grd.	
-36		42.54				41.96	41.96	Grd ✓	
-36		42.54				41.96	41.96	Grd.	
-36		42.54				41.96	41.96	Grd. ✓	

Profile Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11 F.B. 2920 Pg. 87
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hosp.
X-Sec. Notes Chkd. ____ Checked ____ Survey by Curtis Notes ____ Date 4-18-62
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date SEP 2 4 62

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 2920 Pg. 88 | Job No. 7973.01 | Division No. 11 | Notes Red | Plotted | Profile
Survey of Harbor Gen. Hosp | Date | Date | No.
Survey by Curtis | Notes | Notes Chkd. | Checked | X-Sec.
Indexed C. J. GALLI | Date | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	Park. Lot. So. Bldg.		
	Elev.	Fin Pav Grd.			Elev	Sub Grd.	
H-36		42.54			41.96	41.96	Grd.
J-36		42.45			41.87	41.87	Grd. ✓
K-36		42.54			41.96	41.96	Grd.
L-36 Act Curb	42.53						
L-36 Pav Grd	42.00	42.00					
M-36 ℄ 16		41.63			41.05	41.05	Grd
N-36 Act Curb	41.83						
N-36 Pav Grd		41.20					
A1-37		42.35			41.77	41.77	Grd
A-37		42.31			41.73	41.73	Grd ✓
B-37		42.31			41.73	41.73	Grd ✓
C-37					41.73	41.73	Grd. ✓
D-37					41.73	41.73	Grd. ✓
E-37					41.73	41.73	Grd. ✓
F-37					41.73	41.73	Grd. ✓
G-37					42.73	41.73	Cle ✓
H-37						41.73	✓
J-37		42.31			41.73	41.73	Grd.

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Park. Lot So. of Bldg.				
	Elev	Fin Pav Grade	C or F		Sta	Elev	Sub Grade		
K-37		42.31				41.73	41.73	Grd.	✓
(K+8)-37		42.31				41.73	41.73	Grd.	✓
L-37		42.08				41.50	41.50	Grd.	
M-37 16' ℄		41.63				41.05	41.05	Grd	✓
N-37		41.13				40.55	40.55	Grd	
P-37		40.60				40.02	40.02	Grd	
R-37		39.79				39.21	39.21	Grd.	
A1-38		42.03				41.45	41.45	Grd,	
A-38		42.06				41.48	41.48	Grd ✓	✓
B-38		42.06				41.48	41.48	✓	✓
C-38		42.06				41.48	41.48	Gr. ✓	✓
D-38		42.06				41.48	41.48	✓	✓
E-38		42.06				41.48	41.48	Gr ✓	✓
F-38		42.06				~~42.48~~	41.48	~~Gr~~	✓
G-38		42.06				41.48 ~~42.98~~	41.48	Gr. ✓ ~~Gr~~	✓
H-38		42.06				~~42.48~~	41.48	~~Gr~~	✓
I-38		42.06				41.48	41.48	Gr. ✓	✓
K-38		42.06				41.48	41.48	Grd.	✓
[illegible]-38		42.06				41.48	41.48	Grd	

Profile No. ____ Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11 F.B. 2920 Pg. 89
Date ____ Date ____ Survey of Harbor Gen. Hosp.
X-Sec. No. ____ Notes Chkd. ____ Checked ____ Survey by Curtis Notes ____ Date 4-18-62
Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 2920 Pg. 90 | Job No. 7973.01 Division No. 11 | Profile No. | X-Sec. No.
Survey of Harbor Gen. Hosp | Plotted | Date | Notes Red | Date | Checked | Date
Survey by Curtis | Notes Chkd. | Date
Indexed C. J. GALLI | Date

STATION	B.S.	H.I.	F.S.	ELEV.	Park. Lot So. of Bldg			
	Elev.	Fin. Pav Grade	C or F		Sta.	Elev	Sub Grd	C or F
M-38		41.63				41.05	41.05	Grd. ✓
N-38		41.17				40.49	40.49	Grd.
R-38		40.60				40.02	40.02	Grd.
T-38		39.79				39.21	39.21	Grd.
A1-39 Act cb		42.30						
A1-39-Pav	41.84	41.84						
A-39		41.83					41.25	
B-39		41.83				41.25	41.25	Grd.
C-39		41.83					41.25	
D-39		41.83				41.25	41.25	Grd.
E-39		41.83					41.25	
F-39		41.83				42.75	41.25	C 1.50
G-39		41.83				43.25	41.25	C 2.0
H-39		41.83				42.25	41.25	C 1.0
J-39		41.83					41.25	C
K-39 Act		41.83				41.25	41.25	Grd
L-39 Curb		42.29						
L-39 Pav	41.83	41.83						
L+07)-39		41.86				41.28	41.28	Grd ✓
M-39		41.62				41.04	41.04	Grd. ✓

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Parking Lot So. of Bldg.				
	Elev.	Fin. Pav. Grade	C or F		Sta	Elev.	Sub Grade	C or F	
A_1 - 40		41.66				41.08	41.08	Grd.	
A - 40		41.62					41.04		✓
B		41.62				41.04	41.04	Grd	✓
C		41.62			–	41.04	41.04	Gr ✓	✓
D		41.62				~~42.04~~ 41.04	41.04	~~Gr~~	✓
E		41.62			–	41.04	41.04	Gr. ✓	✓
F		41.62					41.04		✓
G		41.62			–	41.04	41.04	Grd. ✓	✓
H		41.62				~~42.04~~ 41.04	41.04	~~Gr~~	✓
J		41.62			–	~~42.04~~ 41.04	41.04	~~Gr~~ Gr. ✓	✓
K		41.62				41.04	41.04	Grd	✓
L		41.62				41.04	41.04	Grd	
M		41.67				41.09	41.09	Grd	✓
N-40 Act Cb									
N-40 DR		41.30							
A_1 - 41		41.30				40.72	40.72	Grd	
A - 41		41.37				40.79	40.79	Grd	✓
B - 41		41.39				41.79	40.79	Cl°	✓

Profile Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11 F.B. 2920 PG. 91
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hosp.
X-Sec. Notes Chkd. ____ Checked ____ Survey by Curtis Notes ____ Date 4-18-62
No. ____ Date ____ Date ____ Map No. ____ Indexed G. J. GALLI Date ____

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 2920 Pg. 92 | Job No. 7973.01 | Division No. 11 | Notes Red | Plotted | Profile
Survey of Hazard Gen. Hosp | Date | Date | No. | X-Sec.
Survey by Curtis Notes C. J. GALLI | Notes Chkd. | Checked | No.
Indexed | Date | Date | Date

Parking Lot So. of Bldg.

STATION	B.S. Elev.	H.I. Fin. Pav. Grade	F.S. Cut or Fill	ELEV.	Sta.	Elev.	Sub. Grade	Cut	
C-41		41.36				40.78			✓
D-41		41.36				~~41.78~~ 40.78	40.78	~~Cut~~	✓
E-41		41.35				40.77	40.77	Grd.	✓
F-41		41.35				~~41.77~~ 40.77	40.77	~~Cut~~	✓
G-41		41.34				~~41.76~~ 40.76	40.76	~~Cut~~	✓
H-41		41.34				~~41.76~~ 40.76	40.76	~~Cut~~ Gr.	✓
J-41		41.33				40.75	40.75	Grd.	✓
K-41		41.33				40.75	40.75	Grd.	✓
L-41		41.30				40.72	40.72	Grd	
M-41 & 16'		41.20				40.62	40.62	Grd.	✓
N-41 Act Cb	41.78								
N-41 Pav	41.31	41.31							
A1-42 Act Curb	41.51								
A1-42 pav	41.13	41.13							
A-42		41.16				40.58	40.58	Grd	
B-42		41.16				41.08	40.58	C0.5	
C-42		41.16					40.58		
D-42		41.16				41.58	40.58	C1.0	
E-42		41.16					40.58		

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11
X-Sec. No. ____ Date ____ Date ____ Survey of Harbor Gen. Hosp.
Notes Chkd. ____ Date ____ Checked ____ Survey by Cerny Notes ____ Date 4-18-62
Map No. ____ Date ____ Indexed C. J. GAU Date ____
F.B. 2920 Pg. 93

Parking Lot So. of Bldg.

STATION	B. S.	H. I.	F. S.	ELEV.	Sta.	Elev.	Sub. Grade	C or F
	Elev.	Fin. Pav. Grade	C or F					
F-42		41.16				42.08	40.58	C 1.5
G-42		41.16				41.58	40.58	C 1.0
H-42		41.16				42.08	40.58	C 1.5
J-42		41.16					40.58	
K-42		41.16				40.58	40.58	Grd.
L-42 ac't, Curb	41.62							
L-42 Fav. Grd.	41.16	41.16						
M-42 ac't		40.95				40.39	40.37	Grd.
N-42 CB	41.69							
N-42 Pav.		41.12						
4,-43		40.98				40.80	40.40	C 0.5
4-43		40.91				40.37	40.33	Grd. ✓
3-43		40.90				40.83 (32)	40.32	~~C 0.5~~ ✓
-43		40.89				40.81 (31)	40.31	~~C 0.5~~ ✓
D-43		40.88				40.30	40.30	Grd. ✓
E-43		40.87				40.29	40.29	Grd. ✓
F-43		40.86				40.28	40.28	Grd. ✓
G-43		40.85				40.27	40.27	Grd. ✓
H-43		40.84				40.76 (26)	40.26	~~C 0.5~~ ✓

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 2920 Pg. 94 Job No. 7773.01 Division No. 11 Profile
Survey of Harbor Gen. Hosp. Date No. X-Sec.
Survey by Curtis Notes Notes Chkd. Checked No.
Indexed C. J. Gallo Date Date Date

STATION	B.S.	H.I.	F.S.	ELEV.	Parking Lot So. of Bldg.				
	Elev.	Fin. Pav. Grade	C or F		Sta.	Elev.	Sub. Grade	C or F	
J-43		40.83				40.25	40.25	~~Co.5~~	✓
K-43		40.82				40.24	40.24	Grd.	✓
L-43		40.78				40.20	40.20	Grd.	
M-43 & 16'		40.63				40.05	40.05	Grd	✓
N-43 Act Cb.	41.31								
N-43 pav.	40.79	40.79							
A1-44		40.80				40.72	40.22	Co.5	
A-44		40.69				40.61	40.11	~~Co.5~~	✓
B-44		40.60				40.02	40.02	Grd	✓
C-44		40.53				39.95	39.95	Grd.	✓
D-44		40.46				39.88	39.88	Grd.	✓
E-44		40.39				39.81	39.81	Grd.	✓
F-44		40.32				39.74	39.74	Grd.	✓
G-44		40.25				39.67	39.67	Grd.	✓
H-44		40.18				39.60	39.60	Grd.	✓
J-44		40.11				39.53	39.53	Grd.	✓
K-44		40.04				39.46	39.46	Grd.	✓
L-44		40.06				40.48	39.48	C1.0	
M-44 & 16'		40.27				39.69	39.69	Grd.	✓

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11 F.B. 2920 Pg. 95
No. ____ Date ____ Date ____ Survey of Lakeboe Gen Hospital
X-Sec. Notes Chkd. ____ Checked ____ Survey by Curtis Notes ____ Date 4-18-62
No. ____ Date ____ Date ____ Map No. ____ Indexed C. A. GALL Date ____

Parking Lot So. of Hospital

STATION	B. S.	H. I.	F. S.	ELEV.	Sta	Elev.	Sub. Grade	C or F	
	Elev	Fin. Pav. Grade	C or F						
V-44 Act cb.	40.95								
V-44 Pav	40.44	40.44							
1, -45 Act. cb	41.25								
1, -45 Pav	40.80	40.80							
1 -45		40.40				39.82	39.82	Grd.	✓
5 - 45		40.30				39.72	39.72	Grd.	✓
2 - 45		40.20				39.62	39.62	Grd.	✓
3 - 45		40.10				39.52	39.52	Grd	✓
4 - 45		40.00				39.42	39.42	Grd.	✓
5 - 45		39.90				39.32	39.32	Grd	✓
6 - 45		39.80				39.22	39.22	Grd	✓
7 - 45		39.70				39.12	39.12	Grd	✓
8 - 45		39.60				39.02 (39.40)	39.02	~~Grd~~	✓
9 - 45		39.50				38.92	38.92	Grd.	✓
Sp Catch Basin	39.50	39.50							
45 Act cb	40.44								
45 Pav.		39.88							
V+ 45		39.94				3936	3936	Grd	✓
45 Act cb	40.65								
V-45 Pav	40.12	40.12							

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 2920 Pg. 96 | Job No. 7973.01 | Division No. 11 | Notes Red | Plotted | Profile
Survey of Harbor Gen. Hosp. | Date | Date | No. | X-Sec.
Survey by Curtis | Notes | Notes Chkd. | Checked | No.
Indexed C.J. GALLI | Date | Date | Date

STATION	B.S.	H.I.	F.S.	ELEV.	Park Lot South of the Bldg.			
	Elev. As built	Fin. Pav. Grade	Cor F		Sta.	Elev	Sub. Grade	C. F
A1-46	40.73	40.73						
A-46	40.67	40.65						
B-46	40.56	40.56						
C-46	40.51	40.47						
D-46	40.40	40.38						
E-46	40.35	40.29						
F-46	40.26	40.20						
G-46	40.15	40.11						
H-46	40.03	39.98						
J-46	40.00	39.84						
K-46	39.91	39.68						
L-46	39.76	39.79						
M-46	39.64	39.62						
N-46 Act. Curb	40.39							
N-46 Act. Pav.	39.79	39.59						
Top K-45 Catch Basin	39.50	39.50						

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B.S. Elev	H.I. Finish Pav. Grd	F.S. C or F	ELEV.	Parking Lot S.W. of Hospital Sta.	Elev	Sub Grade	C or F	
P-28	41.29	41.29	mark on curb						✓
P-28 Act Cb	41.72								
R-28	48.40	40.60		"		40.02	40.02	Grd	✓
S-28	39.88	39.88		"					✓
U-28	39.72	39.72	Join						
P-29 Pav	41.29	41.29	mark on curb						✓
P-29 Act Cb	41.77								
R-29		40.60				40.02	40.02	Grd.	✓
S-29 FL	Act 39.85	39.82							
S-29 Act Curb	40.41			"					✓
T-29 Pav.	Act. DR 39.74	39.79		"					✓
T-29 Act Cb	40.30								
U-29	39.64		Join						
P-30 Pav	41.29	41.29	mark on curb						✓
P-30 Act Cb	41.77								
R-30		40.60				40.02	40.02	Grd.	✓
S-30 FL Pav	39.82	39.82		"					✓
S-30 Act Cb.	40.36								
T-30 Pav	ACT DR 39.67	39.79		"					✓
T-30 Act. Cb.	40.22								

Profile No. ____ Date ____ Notes Red ____ Date ____ Plotted ____ Date ____ Job No. 7973.01 Division No. 11 Survey of Harbor Gen. Hosp Survey by Curtis Notes ____ Date Apr 25-61 Map No. ____ Indexed C. J. GALLI Date ____

F.B. 2920 Pg. 97

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.	Park Lot S.W. of Hospital			
	Elev	Finish Pav Grd	C or F		Sta	Elev.	Sub Grade	C or F
P-31 Pav	41.29	41.29						
P-31 Act. Curb	41.80							
R-31		40.60			—	40.02	40.02	Grd
S-31 Act Curb	40.46							
S-31 Pav. F.L.	Act 39.84	39.81	"					
T-31 Pav.	39.79	39.79	"					
T 31 Act Curb	40.28							
U-31	39.51		Join					
P-32 Pav	41.29	41.29	mark on curb.					
P-32 Act. Cb	41.81							
R-32		40.60			—	40.02	40.02	Grd
S-32 Pav. FL	39.81	39.81	"					
S-32 Act. Curb.	40.37							
T-32 Pave	Act Dr 39.70	39.79	"					
T-32 Act. Curb.	40.27							
U-32	39.51		Join					
P-33 Pav.	41.29	41.29	mark on curb.					
P-33 Act Curb	41.81							
R-33		40.60			—	40.02	40.02	Grd.

F.B. 2920 Pg. 98 Job No. 7973.01 Division No. 11 Notes Red Plotted Profile
Survey of Harbor Gen Hospital Date Date No. X-Sec.
Survey by Curtis Notes Notes Chkd. Checked
Indexed C. J. GALLI Date Date No.

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 7913.01 Division No. 11 F.B. 2920 Pg. 79
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hospital
X-Sec. Notes Chkd. ____ Checked ____ Survey by Curtis Notes ____ Date Oct. 25-62
No. ____ Date ____ Date ____ Map No. ____ Indexed G. J. GALLI Date ____

Park Lot - SW. of Hospital

STATION	B. S.	H. I.	F. S.	ELEV.	Sta	Elev	Sub Grade	Cor E	
	Elev.	Finish Pav. Grd.	Cor F						
5-33 Pav.	39.86	39.86	mark on curb						⌐
-33 Act cb.	40.47								
-33 Pav.	39.79	39.79	"						⌐
-33 Act cb	40.32								
1-33	39.52		Join						
0-34 Pav.	41.29	41.29	mark on curb						⌐
-34 Act cb	41.81								
-34		40.60				4002	40.02	Grd	⌐ ⌐
-34 Pav.	39.91	39.91	"						⌐
-34 Act cb.	40.43								
-34 Pav	39.79	39.79	"						⌐
-34 Act cb.	40.30								
1-34	39.45		Join						
-35 Pav	41.29	41.29	mark on curb						⌐
-35 Act cb	41.79								
-35 Pav		40.60			—	40.02	40.02	Grd	⌐ ⌐
-35 Pav	39.91	39.91	"						⌐
-35 Act cb	40.46								
-35 Pav	39.79	39.79	"						⌐
-35 Act cb	40.32								

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 2920 Pg. 100 Job No. 7923.01 Division No. 11 Notes Red Plotted Profile
Survey of Harbor Gen Hosp. Date Date No. X-Sec.
Survey by Curtis Notes Checked
Indexed C. J. GALL Date Notes Chkd. Date No.
Date

STATION	B. S.	H. I.	F. S.	ELEV.	Parking Lot S.W. Cor. Hosp. Bldg.				
	Elev.	Fin. Grade	℄ or F.		Sta.	Elev.	sub Grade	℄ or F.	
H-28		44.83			—	44.28	44.28	Gr	✓
J-28		44.50			—	43.97	43.92	"	✓
K-28		44.20			—	43.62	43.62	"	✓
L-28	43.85	43.85	mark	on wall	—				✓
H-29		44.38			—	43.80	43.80	"	✓
J-29		44.10			—	43.52	43.52	"	✓
K-29		43.81			—	43.23	43.23	"	✓
L-29	43.49	43.49	mark	on wall	—				✓
H-30(605)	44.00	44.00	mark	on curb	—				✓
J-30(605)	43.79	43.79		"	—				
K-30(605)	43.49	43.49		"	—				✓
L-30	43.14	43.14	mark	on wall	—				✓
L-31	42.79	42.79	mark	on wall	—				✓

76-1.298 GE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 773.01 Division No. 11 F.B. 2920 Pg. 101
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hospital
X-Sec. Notes Chkd. ____ Checked ____ Survey by A.S. Curtis Notes Neiman Date 5-2-62
No. ____ Date ____ Date ____ Map No. ____ Indexed R.J. GAHL Date ____

Parking Lot (Northeast of Hospital Bldg.)

STATION	B. S.	H. I.	F. S.	ELEV.	
T.B.M.				39 50	T.B.M. Elev. 39.50 F.B. 2920-6. 1" I.P. e S.W. Cor. Field office Bldg. on W. Side of Vermont Ave. 200' E. of Out Patients Bldg.
T.B.M.				42.00	T.B.M. Elev. 42.00 F.B. 2920-101. Large Br. Sq. K. in Trans. pole 100'± East of main Bldg.
	Elev.	Fin. Pvm't Grade	C or F		
T.C. 20' Rad. T.C.	40.50	40.50	Gr.		
" Pvm't	40.00	40.00	"		
B.C. 15' Rad. T.C.		40.30			
" Pvm't.		39 80			
T.C. 15' Rad. T.C.		39.90			
" Pvm't.		39 40			
T.C. 4' Rad. T.C.		39.85			
" Pvm't.		39.35			
T.C. 4' Rad. T.C.		39.80			
" Pvm't		39.30			
P.P.T. curb T.C.	39. 32				
" Pvm't.		38.75			
C-1 T.C.	39. 47				
" Pvm't	38.85	38.85	"		
D-1 T.C.	39. 39				
" Pvm't	38.87	38.~~70~~ 87	Gr.		

Sta.	Elev.	Sub Grade	C or F

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 2920 Pg. 102 Job No. 7473.01 Division No. // Notes Red ____ Plotted ____ Profile ____
Survey of Harbor Gen. Hospital Date ____ No. ____ X-Sec. ____
Survey by A.S. Curtis Notes Newman Notes Chkd. ____ Checked ____ No. ____
Indexed C.J. GALLI Date ____ Date ____ Date ____

STATION	B.S.	H.I.	F.S.	ELEV.	Parking lot (Northeast of Hospital Bldg.)			
	Elev.	Fin. Grade	< or F		Sta	Elev.	Sub Grade	C. or F.
E-1 T.C.	39.32							
" Prm'l	38.85	38.~~80~~ 85	Gr.					
F-1 T.C.	39.30							
" Prm'l	38.83	38.~~78~~ 83	"					
G.B. G-1 T.C.	39.21							
" Prm'l	38.70	38.70	"					
H-1 T.C.	39.13							
" Prm'l	38.66	38.66	"					
~~X~~ pt. curb T.C.	39.13							
" Drain Prm'l	38.65	38.~~50~~ 65	"					
B.C. 10' Rad. T.C.	39.39							
" Prm'l	38.80	38.80	"					
E.C. 10' Rad. T.C.	39.60							
" Prm'l	39.00	39.00	"					
B.C. 15' Rad. T.C.	39.36							
" Prm'l	38.82	38.82	"					
E.C. 15' Rad. T.C.	39.21							
" Drain Prm'l	38.70	38.79 ~~38.54~~	Gr					

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Parking lot (Northeast of Hospital Bldg.)				
	Elev.	Fin. Grade	C or F	Rock Grade	Sta	Elev.	Sub. Grade	C or F	
C - 2		39.~~27~~ 37		39.02	—	38.69	38.69	Gr.	4 Reset 6-7-62
D - 2		39.~~23~~ 25		39.~~48~~ 83	—	38.~~15~~ 65	38.65	~~C-0.5~~	4
E - 2		39.19		38.94	—	38.61	38.61	Gr.	4
F - 2		39.15		38.90	—	38.57	38.57	Gr.	4
G - 2		39.11			—	38.53	38.53	Gr.	4
H - 2		39.07			—	38.49	38.49	Gr.	4
J - 2		39.03			—	38.45	38.45	Gr.	4
C - 3		40.03 ~~39.93~~		39.~~7~~8	—	39.~~3~~45	39.~~3~~45	Gr.	4
D - 3		39.88		39.63	—	39.~~30~~ 30	39.30	~~C-0.5~~	4
E - 3		39.83		39.58	—	39.25	39.25	Gr.	4
F - 3		39.78		39.53	—	39.~~70~~ 20	39.20	C-~~0.5~~	4
G - 3		39.73			—	39.15	39.15	Gr.	4
H - 3		39.68			—	39.10	39.10	Gr.	4
J - 3		39.63			—	39.05	39.05	Gr.	4
3 T.C.	39.21								
Prm'T.	38.76	38.76							
T.B.M.				42.00	T.B.M.	Elev.	42.00	F.B. 2920-103	

Large Bt. Spk. in P.P. CTR. Island ±125' N. & ±60' E. of main Bldg.

Cont. pg. 105

Profile Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11 F.B. 2920 PG. 103
No. ____ Date ____ Date ____ Survey of Harbor Gen Hospital
X-Sec. Notes Chkd. ____ Checked ____ Survey by A.S. Curtis Notes Newman Date 5-2-60
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

STATION		B.S.	H.I.	F.S.	ELEV.	Parking Lot. (Southeast of Hospital Bldg.)				
Cont. from pg. 99		Elev.	Fin. Grade	C or F.		Sta.	Elev.	Sub. Grade	C or F.	
P-36	Act. Curb	41.78								
P-36	Prm't	41.29	41.29	mark on curb						✓
R-36			40.60			—	40.02	40.02	Gr.	✓ ✓
S-36	Act. curb	40.45								
S-36	Prm't	39.91	39.~~99~~ 91		"					
T-36	Act. curb	40.31								
T-36	Prm't	39.79	39.79		"					
U-36		39.36		Soin						
R-37			40.60			—	40.02	40.02	Gr.	✓ ✓
T-37			39.79			—	39.21	39.21	"	✓
U-37		39.42	39.42	Soin						
R-38			40.60			—	40.02	40.02	Gr.	✓ ✓
T-38			39.79			—	39.21	39.21	"	✓
U-38		39.28	39.28	Soin						

Cont. pg. 131

F.B. 2920 PG. 104
Job No. 797301 Division No. 11 Notes Red Plotted Profile
Survey of Harbor Gen. Hospital Date Date No.
Survey by A.S. Curtis Notes Newman Notes Chkd. Checked X-Sec.
Indexed C. J. GALLI Date Date No.

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red Plotted Job No. 7773.1 Division No. 11 F.B. 2920 PG. 105
No. Date Date Survey of Harbor Gen. Hospital
X-Sec. Notes Chkd. Checked Survey by A.S. Curtis Notes Neuman Date 8-2-62
No. Date Date Map No. Indexed C. J. GALLI Date SEP 24 62

STATION	B. S.	H. I.	F. S.	ELEV.	Parking Lot (Northeast of Hospital Bldg.) Sta	Elev.	Sub Grade	C or F	
Cont. Pg. 103	Elev.	Fin. Grade	C or F						
C-4 T.C.	41.03								
" Prm 4	40.56	40.56	Gr.						
D-4 T.C.	40.00								
" Prm 4	40.43	40.43	Gr.						
E-4 T.C. Drain	40.97								
" Prm 4	40.48	40.48	Gr.						
F-4 T.C.	40.93								
" Prm 4	40.37	40.37	Gr.						
G-4 T.C.	40.88								
" Drain Prm 4	40.40	40.38	Gr.						
H-4 T.C.	40.83								
" Prm 4	40.32	40.32	Gr.						
J-4 T.C.	40.30								
" Prm 4	39.65	39.65	Gr.						
B-5 Prm 4		40.50					39.92		
?-5 T.C.	40.98								
" Prm 4	40.57	40.57	Gr.						
D-5 T.C.	41.00								
" Prm 4	40.52	40.52	Gr.						

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 2920 Pg. 106 Job No. 7973.00 Division No. 11 Notes Red. Plotted Profile
Survey of Harbor Gen. Hospital Date Date No.
Survey by A.S.Curtis Notes Newman Notes Chkd. Checked X-Sec.
Indexed C.J. GALLI Date Date Date No.

STATION	B.S.	H.I.	F.S.	ELEV.	STA.	ELEV.	Sub Grade	C or F.
	Elev.	Fin. grade	C or F.					
E-5 T.C.	41.00							
" Prm't.	40.50	40.42	Gr.					
F-5 T.C.	40.95							
" Prm't.	40.46	40.46	Gr.					
G-5 T.C.	40.96							
" Drain Prm't.	40.50	40.34	Gr.					
H-5 T.C.	40.90							
" Prm't.	40.42	40.42	Gr.					
J-5 T.C.	40.27							
" Prm't.	39.70	39.70	Gr.					
L-5 T.C.	39.25							
" Prm't.	38.78	38.78						

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Parking Lot. (Northeast of Hospital Bldg.)				
	Elev.	Fin. Grade	C or F.		Sta	Elev.	Sub Grade	C. or F.	
B-6 prm't		41.51			—	40.93	40.93	Gr.	
C-6 T.C.	42.06								
" Prm't.	41.62	41.62	Gr.						
D-6 T.C.	41.96								
" Prm't.	41.45	41.45							
E-6 T.C.	41.95								
" Act. Prai. Prm't.	41.49	41.49	Gr.						
F-6 T.C.	41.93								
" Prm't	41.39	41.39	Gr.						
G-6 T.C.	41.42								
" Prm't	40.87	40.87	Gr.						
H-6 - T.C.	40.90								
" Prm't	40.35	40.35	Gr.						
J-6 - T.C.	40.42								
" Prm't	49.83	39.83							
K-6 Prm't		39.33							
L-6 T.C.									
" Prm't									

Profile Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11 F.B. 2920 PG. 107
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hosp
X-Sec. Notes Chkd. ____ Checked ____ Survey by Curtis Notes Newman Date 5-2-62
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 2920 Pg. 108 | Job No. 7923.01 | Division No. " | Notes Red | Plotted | Profile
Survey of Harbor Gen. Hospital | Date | No. | X-Sec.
Survey by Curtis Notes New Main | Notes Chkd. | Checked
Indexed C. J. GALLI | Date | Date | No.

STATION		B. S.	H. I.	F. S.	ELEV.	Parking Lot (Northeast of Hospital Bldg.)			
		Elev.	Fin. Grade	℄ or E		Sta	Elev.	Sub Grade	℄ or E
C-7	T.C.	42.00							
"	Act. Drain Prm't	41.45	41.45	Gr.					
D-7	T.C.	42.04							
"	Prm't	41.60	41.60	"					
E-7	T.C.	42.02							
"	Act. Drain Prm't	41.58	~~41.58~~ 41.45	"					
F-7	T.C.	42.01							
"	Prm't	41.55	41.55	"					
G-7	T.C.	41.52							
"	Prm't.	41.00	41.00	"					
H-7	T.C.	41.00							
"	Prm't	40.44	40.44	"					
S-7	T.C.	40.50							
"	Prm't.	39.90	89.90	"					
St-7	Act. Drain	39.82							

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11 F.B. 2920 PG. 109
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hospital
X-Sec. ____ Notes Chkd. ____ Checked ____ Survey by Curtis Notes Newman Date 5-2-62
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALL Date ____

STATION	B. S.	H. I.	F. S.	ELEV.	Parking Lot @ NE Side Bldg.				
T.B.M.				42.00	T.B.M.				
	Elev.	Finish Rev. Grad	C or E		Sta.	Elev.	Sub. Grade	Cut or Fill	
A-8 T.C.									
" Prm't		42.19							
B-8		42.07					41.44		
C-8		42.00 ?			—	41.42	41.42	Gr.	✓
D-8		42.01			—	41.43	41.43	Gr.	✓
E-8		42.03			—	41.45	41.45	Gr.	✓
F-8		41.58			—	41.00	41.00	Gr.	✓
G-8		41.03			—	40.45	40.45	Gr.	✓
H-8		40.48			—	39.90	39.90	Gr.	✓
J-8		39.94			—	39.36	39.36	Gr.	✓
K-8		39.39			—	38.81	38.81	Gr.	✓
L-8 T.C.	39.43								
" Prm't	39.00	~~38.83~~ 39.00	Gr.						
A-9 T.C.									
" Prm't		42.85							
B-9		42.83					42.25		
C-9		42.56					41.98		✓
D-9		42.50			—	41.92	41.92	Gr.	✓
E-9		42.07					41.49		✓

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.	Parking Lot @ N.E.			Side of Bldg.	
	Elev	Fin. Pav. Grade	C or F		Sta	Elev.	Sub. Grade	C or F	
F-9		41.61			—	41.03	41.03	Gr.	✓
G-9		41.07					40.49		✓
H-9		40.53			—	39.95	39.95	Gr.	✓
J-9		39.99			—	39.41	39.41	Gr.	✓
K-9		39.46					38.88		✓
L-9 T.C.									
" Prm't.		38.88							
A-10 T.C.									
" Prm't		43.45							
B-10 T.C.									
" Prm't									
C-10		42.97					42.39		
D-10		42.55			—	41.97	41.97	Gr.	
E-10		42.10					41.52		
F-10		41.64			—	41.06	41.06	Gr.	
G-10		41.10					40.52		
H-10		40.57			—	39.99	39.99	Gr.	
J-10		40.03			—	39.45	39.45	Gr.	

F.B. 2920 PG. 110 Job No. 7973.01 Division No. 11 Notes Red Plotted Profile
Survey of Harbor Gen. Hospital Date Date No.
Survey by Curtis Notes Newman Notes Chkd. Checked X-Sec.
Indexed C. J. GAHI Date Date No.

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11 F.B. 2920 Pg. 111
No. ____ Date ____ Date ____ Survey of Hare Lee Gen. Hospital
X-Sec. Notes Chkd. ____ Checked ____ Survey by Curtis Notes Newman Date 5-2-62
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

STATION	B. S.	H. I.	F. S.	ELEV.	Parking Lot @ NE. Side Bldg.				
	Elev	Fin Pav Grade	C or F		Sta	Elev.	Sub Grade	C or F	
Act K-10 Curb.									
K-10 Pav.		39.50							
-10 Act Cb									
-10 Pav.		38.95							
-11 Act Curb									
-11 Pav.		44.00							
-11		43.35					42.77		
-11		43.03					42.45		✓
-11		42.60			—	42.02	42.02	GX	✓
-11		42.13					41.55		✓
11		41.67			—	41.09	41.09	"	✓
-11		41.13					40.55		✓
-11		40.61			—	40.03	40.03	"	✓
-11		40.07			—	39.49	39.49	GX	✓
-11		39.55					38.97		✓
Act -11 Cb.									
-11 Pav.		39.02							

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 29 20 Pg. 112 | Job No. 7973.01 | Division No. 11 | Notes Red | Plotted | Profile
Survey of Harbor Gen. Hospital | Date | Date | No.
Survey by Watts | Notes Newman | Notes Chkd. | Checked | X-Sec.
Indexed C. J. GALLI | Date | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	Parking Lot @ N.E. Side Bldg.			
	Elev.	Fin Pav. Grade	C or F		Sta.	Elev.	Sub. Grade	C or F
A-12 Act. Curb								
A-12 Pav.		44.07						
B-12		43.41					42.83	
C-12		43.09					42.51	✓
D-12		42.67			–	42.09	42.09	Gr. ✓
E-12		42.17					41.59	✓
F-12		41.70					41.12	✓
G-12		41.17					40.59	✓
H-12		40.66			–	40.08	40.08	Gr. ✓
J-12		40.13			–	39.55	39.53	✓
K-12		39.60					39.02	✓
L-12 Act Curb								
L-12 Pav.		39.04						
A-13 Act Curb								
A-13 Pav		44.14						
B-13 Act Cb								
B-13 Pav.		43.40 ?						
C-13		43.14					42.54	
D-13		42.69			–	42.11	42.11	Gr.
E-13		42.20					41.52	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Parking Lot @ N.E. Side of Bldg.				
	Elev.	Fin. Pav. Grade	C or F		Sta	Elev.	Sub. Grade	C or F	
F-13		41.73			—	41.15	41.15	Gr.	
G-13		41.20					40.62		
H-13		40.70			—	40.12	40.12	Gr.	
J-13 FL		40.18			—	40.10	39.60	CO5	39.93 ✓
K-13 Act. Cb.									
K-13 Pav.		40.17							
L-13 Act. Cb.									
L-13 pav.		39.05							
A-14 Act Cb	44.81								
A-14 Pav.	44.22	44.22	Gr.						
B-14		43.51			—	42.93	42.93	Gr.	
[illegible]-14		43.20			—	42.62	42.62	" ✓	
D-14		42.73			—	42.15	42.15	Gr. ✓	
E-14		42.23			—	41.65	41.65	" ✓	
F-14		41.76			—	41.18	41.18	" ✓	
[illegible]-14		41.24			—	40.66	40.66	" ✓	
[illegible]-14+7		41.26				40.68	40.68	✓	41.01 ✓
1-14-05		40.78			—	40.15	40.15	" ✓	40.48 ✓
[illegible]-14 R-		40.89			—	40.31	40.31	" ✓	40.64 ✓
[illegible]-14		40.20					39.62	✓	

Profile Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11 F.B. 2920 Pg. 113
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hospital
X-Sec. Notes Chkd. ____ Checked ____ Survey by Curtis Notes Newman Date 5-2-62
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 2928 Pg. 114 | Job No. 7973.01 | Division No. 11 | Notes Red | Plotted | Profile
Survey of Harbor Gen. Hospital | Date | Date | No.
Surveyed by Letts Notes Newman | Notes Chkd. | Checked | X-Sec.
Indexed C. J. GALLI | Date | Date | No.

STATION	B.S.	H.I.	F.S.	ELEV.	Parking Lot @ NE. Side Bldg.			
	Elev.	Fin. Pave Grade	C or F		Sta.	Elev.	Sub. Grade	C or F
K-14 Act.		40.20					39.62	
L-14 Curb.								
L-14 Pav.		39.21						
A-15 Act. Curb.	44.83							
" Prm't	44.22	44.22	Gr.					
B-15		43.57			—	42.99	42.94	Gr.
C-15		43.26					42.68	"
D-15		42.78					42.20	"
E-15		42.27			—	41.69	41.69	"
F-15 P.L.		41.79			—	41.21	41.21	" 41.54
G-15		41.70			—	41.12	41.12	"
H-15 -R-		41.61			—	41.03	41.03	" 41.36
S-15		40.93			—	40.35	40.35	"
K-15		40.24			—	39.66	39.66	"
L-15 Act. curb	39.86							
" Prm't								

76-1.298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 76780 Division No. 11 F.B. 2920 Pg. 115
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hospital
X-Sec. Notes Chkd. ____ Checked ____ Survey by A.S. Curtis Notes Newman Date 5-3-62
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GAMM Date ____

STATION	B. S.	H. I.	F. S.	ELEV.	Parking Lot (Northeast of Hospital Bldg.)				
	Elev.	Fin. Grade	C. or F.		Sta.	Elev.	Sub. Grade	C. or F.	Rock Gr.
A-16 Act. Curb.		44.72							
" Prm't.		44.22							
B-16 Act. Curb		44.06							
" Prm't		43.56							
D-16		42.83			—	42.25	42.25	Gr.	
D-16+06	F.L.	42.65				42.27	42.27	"	42.40
E-16		42.53					41.93	"	
E-16+06 F.L.		42.32			—	41.74	41.74	"	42.07
F-16		42.44			—	41.86	41.86	"	
G-16 R=		42.33			—	41.75	41.75	"	42.08
H-16		41.65			—	41.07	41.07	"	
J-16		40.97			—	40.39	40.39	"	
K-16 Act. Curb.	40.87								
K-16 Prm't	40.27	40.27	Gr.						
L-16 Act. Curb	39.93								
" Prm't.	39.33	39.33	Gr.						
1-17 Act. Curb.									
" Prm't		44.22							
C-17 Act. Curb.									
" Prm't.		43.35							

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 2920 Pg. 116 Job No. 7973.01 Division No. 11 Notes Red Plotted Profile
Survey of Harbor Gen. Hospital Date Date No. X-Sec.
Survey by A.S. Curtis Notes Neuman Notes Chkd. Checked No.
Indexed C.F. GALL Date Date Date

Parking Lot (Northeast of Hospital Bldg.)

STATION		B.S.	H.I.	F.S.	ELEV.	Sta	Subgrade	Subgrade	C or F	Rock Grt.
		Elev.	Fin. Grade	C or F						
D-17			43.22			—	42.64	42.64	Gr.	
E-17			43.17			—		42.59	"	
~~E-17.49~~			43.79					43.21		43.54
F-17	R =		43.07			—		42.49	"	42.82
G-17			42.40			—		41.82	"	
H-17			41.70			—		41.12	"	
J-17			41.00			—		40.42	"	
K-17			40.30			—		39.72	"	
L-17			?							
E.C. 20'-17										
C-18	Act. Curb	44.72	44.72							
"	Prm't.	44.22	44.22	Gr.						
D-18	Act. Curb	~~44.71~~								
D-18	Prm't.	44.22	44.22	"						
D+10-18	Prm't	44.22	44.22	"						
E-18	Act. Curb.	44.43								
"	Prm't.	43.83	43.83	"						
F-18	Act. Curb	43.60								
"	Prm't.	43.12	43.12	"						
G-18	Act. Curb.									
"	Prm't.		42.43							

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.		
	Elev.	Fin Grade	C or F.		Parking Lot (Westside of Bldg.)	
T-25 Act. Curb	41.43					
" Prm't	41.00	41.00	Gr.			
U-25						
T-26 Act. Curb	40.99					
" Prm't	40.56	40.56	Gr.			
U-26						
T-27 Act. Curb	40.46					
" Prm't	40.06	40.06	Gr.			
U-27	39.63	39.63	Soin			

F.B. 2920 PG. 118

Job No. 797301 Division No. 11 Notes Red Plotted Profile

Survey of Harbor Gen. Hospital Date Date No.

Survey by A.S. Curtis Notes Newman Notes Chkd. Checked X-Sec.

Indexed C. J. GALLI Date Date Date No.

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 7973.20 Division No. 11 F. B. 2920 Pg. 119
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hospital
X-Sec. Notes Chkd. ____ Checked ____ Survey by A.S. Curtis Notes Returned Date 5-4-62
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

STATION	B.S.	H.I.	F.S.	ELEV.	Parking Lot. (West side of Bldg.)			
	Elev.	Fin. Grade	C or F.		Sta.	Elev.	Sub Grade	C. or F.
T-24 Act. Curb	41.87							
" Prm't.	41.42	41.42	Gr.					
U-24		39.62						
T-23 Act. Curb	42.22							
" Prm't	41.82	41.82	Gr.					
U-23		39.80						
K-23A Act. Curb								
" Prm't								
L-23A Act. Curb								
" Prm't								
M-23A Act. Curb	43.98							
" Prm't	43.51	43.51	Gr.					
N-23A Act. Curb	43.57							
" Prm't	43.12	43.12	Gr.					
P-23A Act. Curb	43.21							
" Prm't	42.75	42.75	Gr.					
(23A+17) F.L.		42.75			—	43.17	42.17	C.L.
R-23A Act. Curb	42.84							
" Prm't	42.36	42.36	Gr.					
23A+07 F.L.		42.35			—	41.77	41.77	Gr.

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 2920 Pg. 120 Job No. 7923.0 Division No. IV Notes Red Plotted Profile
Survey of Harbor Gen. Hospital Date Date No. X-Sec.
Survey by A.S. Curtis Notes Newman Notes Chkd. Checked
Indexed C. J. GALLI Date Date Date No.

STATION	B.S.	H.I.	F.S.	ELEV	Parking Lot (West side of Bldg.) Sta.	Elev.	Sub Grade	C. or F.
	Elev.	Fin. Grade	C. or F.					
T-23A Act. Curb	42.43							
" Prm'l	42.00	42.00	Gr.					
U-23A Act. Prm'l.	40.20	40.20	"					
M-22		44.415			—	43.87	43.87	Gr.
L-22		43.76			—	43.18	43.18	"
(L-(22-16) F.L		43.76			—	"	"	"
M-22		43.51			—	42.93	42.93	C of F
(M-(22-7) F.L		43.51			—	43.93	42.93	C of F
N-22 F.L.		43.88			—	42.75	42.75	C of F
P-22		43.14			—	42.56	42.56	C of F
(P-(22-17) R.	Not Set	43.86						
(P+19-22) R.		43.09						
R-22		42.86			—	42.28	42.28	Gr.
T-22		41.34			—	40.78	40.78	C of F
U-22 Act. Prm'l	39.69		Join					
K-21 Act. Curb	44.72							
" Prm'l	44.22	44.22	Gr.					
L-21 Act. Curb	44.72							
" Prm'l	44.22	44.22	Gr.					

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. 7273.01 Division No. 11 F.B. 2920 Pg. 121
No.____ Date____ Date____ Survey of Harbor Gen. Hospital
X-Sec. Notes Chkd.____ Checked____ Survey by A.S. Curtis Notes Newman Date 3-4-62
No.____ Date____ Date____ Map No.____ Indexed C. J. GALLI Date____

STATION	B.S.	H.I.	F.S.	ELEV.	Parking Lot (Westside of Bldg.)				
	Elev.	Fin. Grade	C. or F.		Sta.	Elev.	Sub. Grade	C. or F.	
M-21 Act. Curb	44.72								
" Prm't	44.22	44.22	Gr.						
N-21 Act. Curb	44.72								
" Prm't	44.22	44.22	Gr.						
P-21		43.88			—	43.30	43.30	Gr.	✓ ✓
T-21		41.47			—	40.89	40.89	Gr.	✓ ✓
U-21 Act. Prm't	39.73	39.73	Join						
P-20		44.02			—	43.44	43.44	Gr.	✓
R-20 Act. Curb	43.31								
" Prm't	42.78	42.78	Gr.						
S-20 Act. Curb	43.16								
" Prm't	42.63	42.63	Gr.						
T-20		41.57			—	40.99	40.99	Gr.	✓
U-20 Act. Prm't	39.79	39.79	Join						
P-19		44.04			—	43.46	43.46	Gr.	✓
R-19 Act. Curb	43.32				—				
" Prm't	42.78	42.78	Gr.						

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 2920 PG. 122
Survey of Harbor Gen. Hospital Job No. 7973.01 Division No. 11 Notes Red Plotted Profile
Survey by A.S. Curtis Notes Measured Date No. X-Sec.
Indexed C.J. GALLI Date Notes Chkd. Checked No.
Date Date

STATION		B.S.	H.I.	F.S.	ELEV	Parking Lot (Westside of Bldg.)				
		Elev.	Fin. Grade	C. or F.		Sta.	Elev.	Sub Grade	Fin. F.	
S-19	Act. Curb	43.15								
"	Prm'T	42.62	42.62	Gr.						
T-19			41.65			—	41.07	41.07	Gr.	—
U-19	Act. Prm'T	39.97		Soln						
P-18			43.85			—	43.27	43.27	Gr.	—
R-18	Act. Curb	43.31								
"	Prm'T	42.78	42.78	Gr.						
S-18	Act. Curb	43.19								
"	Prm'T	42.63	42.63	Gr.						
T-18			41.78			—	41.20	41.20	Gr.	—
U-18	Act. Prm'T	40.09		Soln						

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Parking Lot - West side Bldg.				
	Elev.	Fin. Pav. Grade	C or F		Sta.	Elev.	Sub. Grade	C or F	
H-17 Act cb									
H-17 Pav.		44.22							
J-17		43.62					43.04		
K-17		43.00					42.42		✓
L-17 Act cb									
L-17 pav.		43.18		✓					
M-17 pav		43.12		✓					
N- 17		43.03		✓			42.45		
P- 17		43.06					42.48		✓
T- 17		42.00					41.42		✓
U- 17 Act.									
H- 16		44.22			—	43.64	43.64	Gr.	✓
J- 16		43.62			—	43.04	43.04	"	✓
K- 16		43.00			—	42.42	42.42	"	✓
L-16 Act cb.	43.10								
L-16 Pav	42.65	42.65	Gr.						
M-16 Act cb	43.03								
M-16 Pav.	42.49	42.49	Gr.						
N- 16		42.34			—	41.76	41.76	Gr. ✓	✓

Profile Notes Red ____ Plotted ____ Job No. 797301 Division No. 11 F.B. 2920 PG. 123
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hospital
X-Sec. Notes Chkd. ____ Checked ____ Survey by Curtis Notes Newman Date 5-4-62
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

STATION		B. S.	H. I.	F. S.	ELEV.					
		Elev	Fin. Pav. Grade	C or F		Sta.	Elev	Sub Grade	C or F	
P-16			42.34			–	41.76	41.76	Gr.	✓
R-16	Act cb.	42.82								
R-16	Pav.	42.29	42.25	Gr.						
S-16	Act. cb	42.80								
S-16	Act. Drain Pav	42.24	42.24	Gr.						
T-16			41.45			–	40.87	40.87	Gr. ✓	✓
U-16	Act. Prmit.	40.20		Join						
H-15			44.22			–	43.64	43.64	Gr.	✓
J-15			43.62				43.04	43.04		✓
K-15			43.00				42.42	42.42		✓
L-15	Act cb	43.09								
L-15	Pav.		42.~~25~~ 48		✓					
M-15	Act cb.	~~43~~.01 42.47	42.47	Gr.	✓					
N-15			42.14					41.56		
P-15			41.55 ~~41.42~~					40.97		✓
R-15	Act cb									
R-15	Pav.		41.~~64~~ 49 ~~41.40~~							✓
T-15			40.90					40.32		✓
U-15	Act. Prmit	40.31		Join						

F.B. 2920 PG. 124 Job No. 7973.01 Division No. 11 Notes Red Plotted Profile
Survey of Harbor Gen Hosp. Date Date No.
Survey by Curtis Notes Newman Notes Chkd. Checked X-Sec.
Indexed C. J. GALLY Date Date No.

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.					
	Elev.	Fin. Pav. Grade	C or F		Sta	Elev	Sub. Grade	C or F	
H-14		44.22			–	43.64	43.64	Gr.	✓
J-14		43.62			–	43.04	43.04	Gr.	✓
K-14		43.00			–	42.48	42.48	Gr.	✓
L-14 Act. Curb	43.11								
" Prm't	42.60	42.60	Gr.						
M-14 Act. Curb	43.03								
" Prm't.	42.45	42.45	Gr						
N-14		41.90			–	41.32	41.32	Gr ✓	✓
P-14		41.40 ~~41.25~~			–	40.82	40.82	Gr. ✓	✓
R-14 Act. Curb	41.67								
" Act Drain		41.12 ~~40.70~~							
S-14 Act. Prm't	41.58								
" Act. Drain Prm't.	41.02	41.02 40.68							
T-14		40.35			–	39.77 ~~40.27~~	39.77	Gr. ~~CDE~~ ✓	✓
V-14 Act. Prm't.	40.29		Soln						

Profile Notes Red ____ Plotted ____ Job No. 7923.01 Division No. 11 F.B. 2920 PG. 125
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hospital
X-Sec. Notes Chkd. ____ Checked ____ Survey by Curtis Notes Newman Date 5-4-62
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

STATION		B. S.	H. I.	F. S.	ELEV.				
		Elev.	Fin. Pav. Grade	C or F		Sta.	Elev.	Sub. Grade	C or F
H-13	Act. Curb								
"	Prm't.		44.20						
J-13			43.62				3.04	43.04	✓
K-13	Act. Curb								
"	Prm't		43.0~~4~~9		✓				
M-13	Act. Curb	42.88							
"	Prm't.		42.35		✓				
N-13			41.84				1.26	41.26	✓
P-13			41.30 ~~41.22~~			–	0.72	40.72	✓
R-13	Act. Curb								
"	Act. Drain	40.80	~~40.70~~ 80		✓				
S-13	Act. Curb								
"	Prm't.		40.6~~8~~4		✓				
T-13			40.35			–	9.77	9.77	
U-13	Act. Prm't.	40.29							

F.B. 2920 PG. 126 Job No. 7973.01 Division No. 11 Notes Red Plotted Profile
Survey of Harbor Gen. Hospital Date No. X-Sec.
Survey by Curtis Notes Newman Notes Chkd. Checked
Indexed C. J. GALLI Date Date No.

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.					
	Elev.	Fin Pav. Grade	C or F			Elev.	Sub Grade	C or F	
H-12 Act. Curb	44.12								
" Prm't	43.54	43.54	Gr.						
J-12		43.34			—	42.76	42.76	Gr.	✓
K-12 Act. Curb	43.69								
" Prm't	43.15	43.15	Gr.						
M-12 Act Curb	42.78								
" Prm't	42.24	42.24	Gr.						
N-12		41.75			—	~~41.67~~ 41.17	41.17	~~Co~~ Gr. ✓	✓
P-12		~~41.18~~ 41.23			—	40.65	40.65	Gr. ✓	✓
R-12 Act. Curb	41.34								
" Act. Drain	40.76	40.~~70~~ 76	Gr.	✓					
S-12 Act. Curb	41.21								
" Act. Drain Prm't	40.64	40.~~68~~ 64	Gr.	✓					
T-12		40.35			—	39.77	39.77	Gr. ✓	✓
U-12 Act Prm't	40.26		Soin						

Profile Notes Red ____ Plotted ____ Job No. 7973.01 Division No. 11 F.B. 2920 Pg. 127
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hospital
X-Sec. Notes Chkd. ____ Checked ____ Survey by Curtis Notes Newman Date 5-4-62
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GAUL Date ____

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F.B. 2920 Pg. 128 | Job No. 7973.01 | Division No. 11 | Notes Red | Plotted | Profile
Survey of Harbor Gen. Hospital | Date | Date | No.
Survey by Curtis Notes Newman | Notes Chkd. | Checked | X-Sec.
Indexed C. J. GALLI Date | Date | Date | No.

STATION	B.S.	H.I.	F.S.	ELEV	Sta.	Elev.	Sub Grade	Cut or Fill
	Elev.	Fin. Fau. Grade	Cut or Fill					
H-11 Act. Curb	43.47							
" Prm't	42.91	42.91	Gr.					
J-11		42.82			—	42.24	42.24	Gr. ✓
K-11 Act. Curb	43.24							
" Prm't	42.72	42.72	Gr.	✓				
M-11 Act. Curb	42.65							
" Prm't	42.13	42.13	Gr.	✓				
N-11		41.68			—	41.10	41.10	Gr. ✓
P-11		~~41.15~~ 41.20			—	40.62	40.62	Gr. ✓ ✓
R-11 Act. Curb	41.35							
" Act. Drain Prm't	40.77	~~40.73~~ 40.77	Gr.	✓				
S-11 Act. Curb	41.22							
" Act. Drain Prm't	40.43	~~40.68~~ 40.43	Gr.	✓				
T-11		40.35			—	39.77	39.77	Gr. ✓ ✓
U-11	40.33		Join					

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.	Parking Lot (N.W. Cor. Bldg.)				
	Elev.	Fin Grade	C or F		Sta	Elev.	Sub Grade	C or F	
H-10		42.36			–	41.78	41.78	Gr.	
S-10		42.30			–	41.72	41.72	"	✓
K-10 Act. Curb	42.87								
" Pavm't		42.25							
M-10 Act. Curb	42.52								
" Pavm't	42.02	42.02	Gr.						
N-10		41.47			–	41.09	41.09	Gr.	✓
P-10 Act. Curb	41.71								
" Pavm't	41.27	41.27	Gr.						
~~T-10~~ Act. Curb	40.78								
" Pavm't	40.35	40.35	Gr.						
U-10 Act. Pvm't	40.30		Join						
H-9		41.96			–	41.38	41.38	Gr.	
J-9		41.96			–	41.38	41.38	Gr.	
K-9		41.96			–	41.38	41.38	Gr.	
M-9 Act. Curb	42.47								
" Pvm't	41.98	41.98	Gr.						
N-9		41.62			–	41.04	41.04	Gr.	
P-9		41.22			–	40.64	40.64	Gr.	

Profile Notes Red ____ Plotted ____ Job No. 79730 Division No. 11 F.B. 2920 Pg. 129
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hospital
X-Sec. Notes Chkd. ____ Checked ____ Survey by A.S. Curtis Notes Newman Date 5-8-62
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV	Parking Lot (N.W. Cor. Bldg.)			
	Elev.	Fin. Grade	C. or F.		Sta.	Elev.	Sub. Grade	C. or F.
T-9		40.35			–		39.77	
U-9 Act. Prm't	40.34	40.34	Join					
H-8		40.85			–	40.27	40.27	Gr.
J-8		40.85			–	40.27	40.27	"
K-8		40.85			–	40.27	40.27	"
M-8		41.02			–	40.44	40.44	"
B.C. R=15' Act. Curb.	41.57							
" Prm't.	41.07	41.07	Gr.					
P+10-8 Act. Curb	41.35							
" Prm't	40.85	40.85	Gr.					
T-8 Act. Curb	40.87							
" Prm't	40.35	40.35	Gr.					
U-8 Act. Prm't	40.46	40.46	Join					

F.B. 2920 PG. 130 Job No. 7973.01 Division No. 11 Notes Red ____ Plotted ____ Profile ____
Survey of Harbor Gen. Hospital Date ____ Date ____ No. ____
Survey by A.S. Curtis Notes Newman Notes Chkd. ____ Checked ____ X-Sec. ____
Indexed C. J. GALLI Date ____ Date ____ No. ____

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.					
Cont. From Pg. 104	Elev.	Fin. Grade	C or F.		Sta	Elev.	Sub Grade	C or F.	
Q - 39 Act. Cb.	41.72								
Q - 39 Prm't.	41.28	41.28	Mark	on. curb					
R - 39		40.60					40.02		✓
S - 39 Act. Cb.									
S - 39 Prm't	39.90	39.90		"					✓
T - 39 Act. Cb.									
T - 39 Prm't.	39.79	39.79	Mark	on curb.					✓
U - 39	39.30	39.30	Join						
P - 40 Act. Cb.	41.72								
P - 40 Prm't	41.16	41.16	mark	on. curb.					✓
R - 40		40.60			—	40.02	40.02	Gr.	✓✓
S - 40 Act. Cb.									
S - 40 Prm't	39.91	39.81	"						
T - 40 Act. Cb.									
T - 40 Prm't.	39.79	39.79	mark	on. Curb.					✓
U - 40	39.16	39.16	Join.						

Profile Notes Red ____ Plotted ____ Job No. 79T301 Division No. 11 F.B. 2920 Pg. 131
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hospital
X-Sec. Notes Chkd. ____ Checked ____ Survey by A.S. Curtis Notes Newman Date 5-28-62.
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 2920 PG. 132 Job No. 7973.01 Division No. 11 Notes Red Plotted Profile
Survey of Harbor Gen. Hospital Date Date No. X-Sec.
Survey by A.S. Curtis Notes Newman Notes Chkd. Checked No.
Indexed C. J. GALLI Date Date Date

STATION	B. S.	H. I.	F. S.	ELEV.				
	Elev.	Fin. Grade	C or F.		Sta.	Elev.	Sub Grade	C or F.
P-42 Act. Cb.								
P-42 Prm't								
R-42		40.60			—	40.02	40.02	Gr.
S-42 Act. Cb.								
S-42 Prm't		39.91						
T-42 Act. Cb.								
T-42 Prm't.		39.79						
U-42								
P-41 Act. Cb.	41.65							
P-41 Prm't	41.06	41.06	mark on curb					
R-41		40.60			—	40.02	40.02	Gr.
S-41 Act. Cb.	40.44							
S-41 Prm't	39.91	39.91	"					
T-41 Act. Cb.	40.34							
T-41 Prm't.	39.79	39.79	"					
U-41	39.24		Join					

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.					
	Elev.	Fin. Grade	C or F.		Sta.	Elev.	Sub. Grade	C or F.	
P-43 Act. Cb.	41.20								
P-43 Prm't.	40.70	40.70	mark on curb		—				
R-43		39.95			—	39.37	39.37	Gr.	✓
S-43 Act. Cb.	40.59								
S-43 Prm't	39.91	39.91		"					
T-43 Act. Cb.	40.33								
T-43 Prm't.	39.79	39.79		"					
U-43	39.28		Join						
P-44 Act. Cb.	40.83								
P-44 Prm't	40.34	40.34	Mark on Curb						
R-44		39.85			—	39.27	39.27	Gr.	✓
S-44 Act. Cb.	40.43								
S-44 Prm't	39.91	39.91		"					
T-44 Act. Cb.	40.32								
T-44 Prm't.	39.75	39.75		"					
T+06 Ridge.		39.79			—	39.21	39.21	Gr.	✓
U-44	39.22		Join						

Profile Notes Red ____ Plotted ____ Job No. 7473.01 Division No. 11 F.B. 2920 PG. 133
No. ____ Date ____ Date ____ Survey of Harbor Gen. Hospital
X-Sec. Notes Chkd. ____ Checked ____ Survey by A.S. Curtis Notes Newman Date 5-28-62.
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.					
	Elev.	Fin. Grade	C or F		Sta	Elev.	Sub Grade	C or F.	
P-45 Act. Cb.	40.56								
P-45 Prm't	40.06	40.06	mark on curb						
R-45		39.78			—	39.20	39.20	Gr.	✓
S-45 Act. Cb.	40.41								
S-45 Prm't	39.91	39.91		"					
T-45 Act. Cb.	40.35								
T-45 Prm't	39.80	39.80		"					
T+08-45 F.L.		39.70			—	39.12	39.12	Gr.	✓
T+16-45 Ridge.		39.79			—	39.21	39.21	"	✓
U-45	39.21		Join						

F.B. 2920 PG. 134
Job No. 7973.01 Division No. 11 Notes Red ____ Plotted ____ Profile
Survey of Harbor Gen. Hospital Date ____ Date ____ No. ____
Survey by A.S. Curtis Notes Newman Notes Chkd. ____ Checked ____ X-Sec.
Indexed C. J. GALLI Date ____ Date ____ No. ____

(A)

Notes Ck'd by	Survey of HARBOR GEN. HOSP.
Map No.	JN 7973.01 Tape Std. °F
Office Work	Surveyed by A.N. Hellstrom
Checked	Notes D.L.B. Date 4-27-62
Date	Indexed C. J. GALLI SEP 24 '62

F.B. 2920 Pg. 135

J.N. 7973.01

L.A. HARBOR GEN. HOSP

LOCATION OF DRAINS FROM PARKING AREA TO E OF STS. ON 220TH ST. E CARSON AVE.

SEE PAGE "D" FOR GRADES

	PAGE
DRAINS ON 220TH ST.	"B"
DRAINS ON CARSON ST.	"E"
GRADES FOR DRAINS ON 220TH ST.	"D"
GRADES FOR DRAINS ON CARSON ST.	"G"

A.N. Hellstrom
D.L. Burkholder
L.W. Jones
C.R. Yasui
G.P. Alwin

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY ENGINEER
900 Los Angeles County Engineering Bldg.

765098 CE #247—7-59

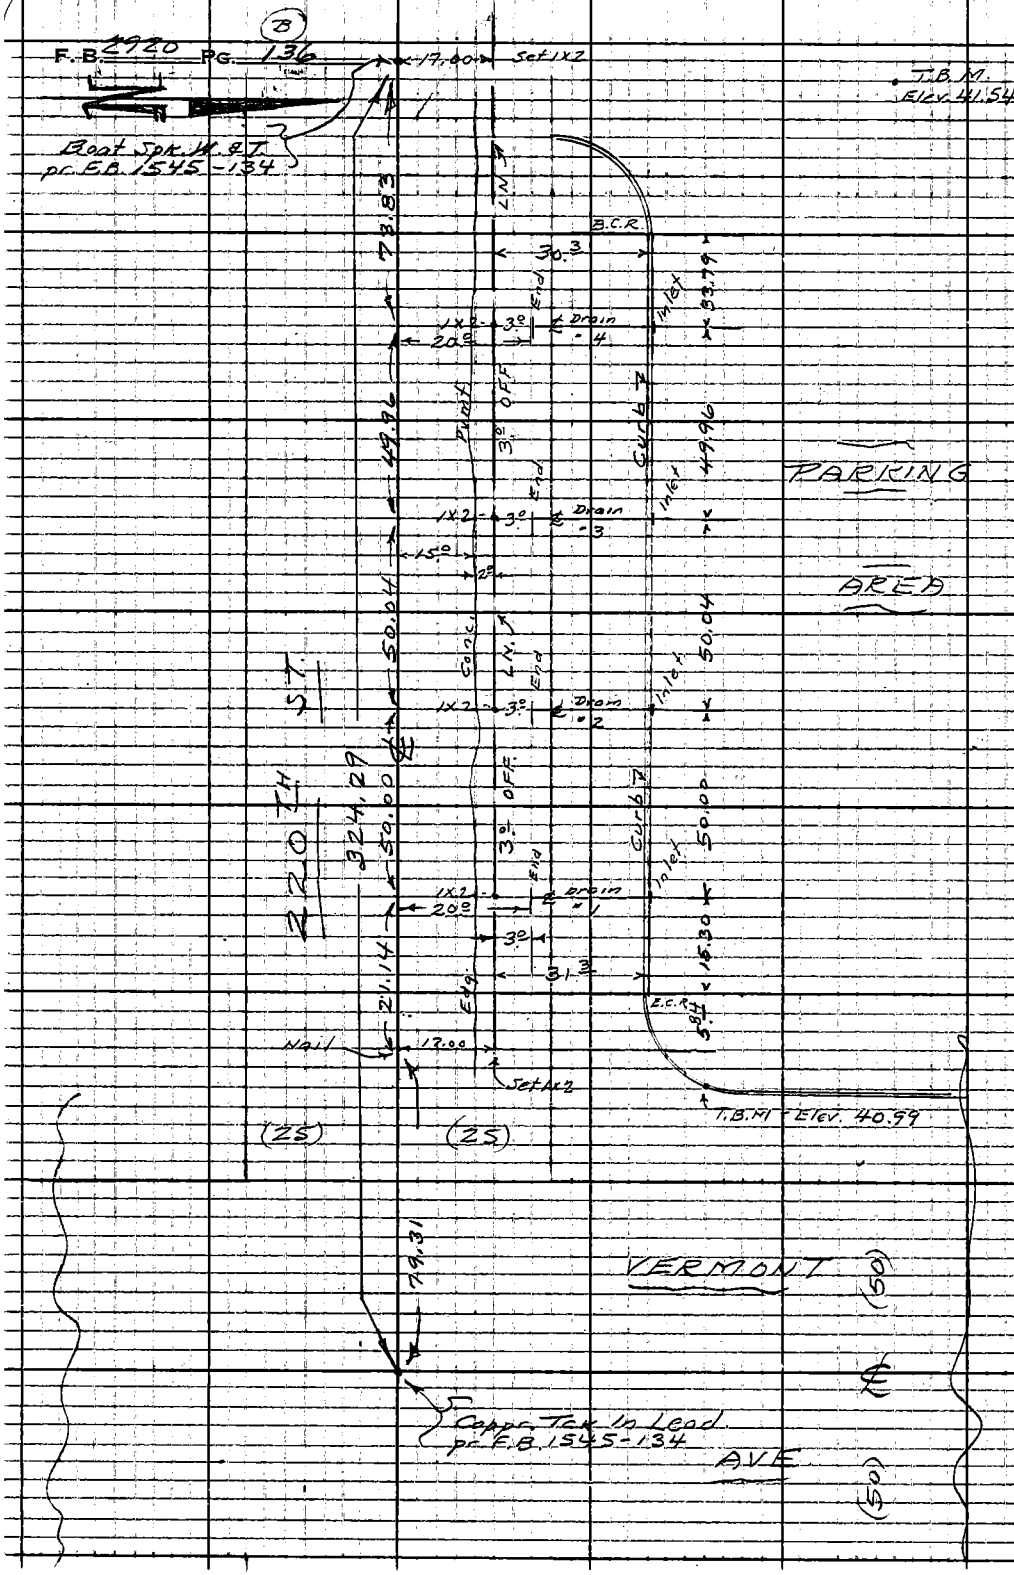

RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend notes this side of this line

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Profile No.	Notes Red	Date	Plotted	Date	Job No. 7973.01	Division No. 11	F.B. 2920 Pg. 13
X-Sec. No.	Notes Chkd.	Date	Checked	Date	Survey of Harbor General Hosp.		
					Survey by A.N.H.	Notes D.L.B. Date 4-27-62	
					Map No.	Indexed C. J. GALLI Date SEP 2 4 '62	

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.

J.N. 7973.01

HARBOR GENERAL HOSPITAL

Grades for Drains on 220th st. & Carson St.

SEE PAGE (3) FOR PLAN OF DRAINS

Hellstrom
Burkholder
Jones
Yasui
Alwin

76L-298 CE 307 11-58

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 2920 Pg. 38 Job No. 7973.01 Division No. 11 Notes Red Plotted Profile
Survey of Harbor General Hosp. Date 4-27-62 Date No. X-Sec.
Survey by A.N.H Notes D.L.B. Notes Chkd. Checked
Indexed C. J. GALLI Date Date Date No.

STATION	B.S.	H.I.	F.S.	ELEV			
	F.L.	Grades for drains on 220th st.					
T.B.M.				40 99	T.B.M. as Mkd. F.L. Grade @ Outlet	Cut or Fill	
Drain #1	(inlet)	In Prkng. Area		Exist 40.09			
"		End Dr. @ Strt.		39.56	39.27	C-0.29	(39.77 Edge of Exist Conc. Pvmt
Drain #2	(inlet)	In Prk. Area		Exist. 39.91			
"		End Dr. @ Strt.		39.44	39.05	C-0.39	(39.60 " " " ")
Drain #3	(inlet)	In Prk. Area		Exist. 39.72			
"		End Dr. @ Strt		39.29	38.86	C-0.43	(39.47 " " " ")
Drain #4	(inlet)	In Prk. Area.		Exist. 39.54			
"		End Dr. @ Strt.		39.01	38.67	C-0.34	(39.33 " " " ")
T.B.M				41 54	T.B.M. as Mkd.		

Notes Ck'd by	Survey of HARBOR GEN. HOSP.
Map No.	JN 7973.01 Tape Std °F
Office Work	Surveyed by A.N. Hellstrom
Checked	Notes D.L.B. Date 4-27-62
Date	Indexed E. J. GAMI SEP 2 4 '62

F.B. 2920 PG. 139

E

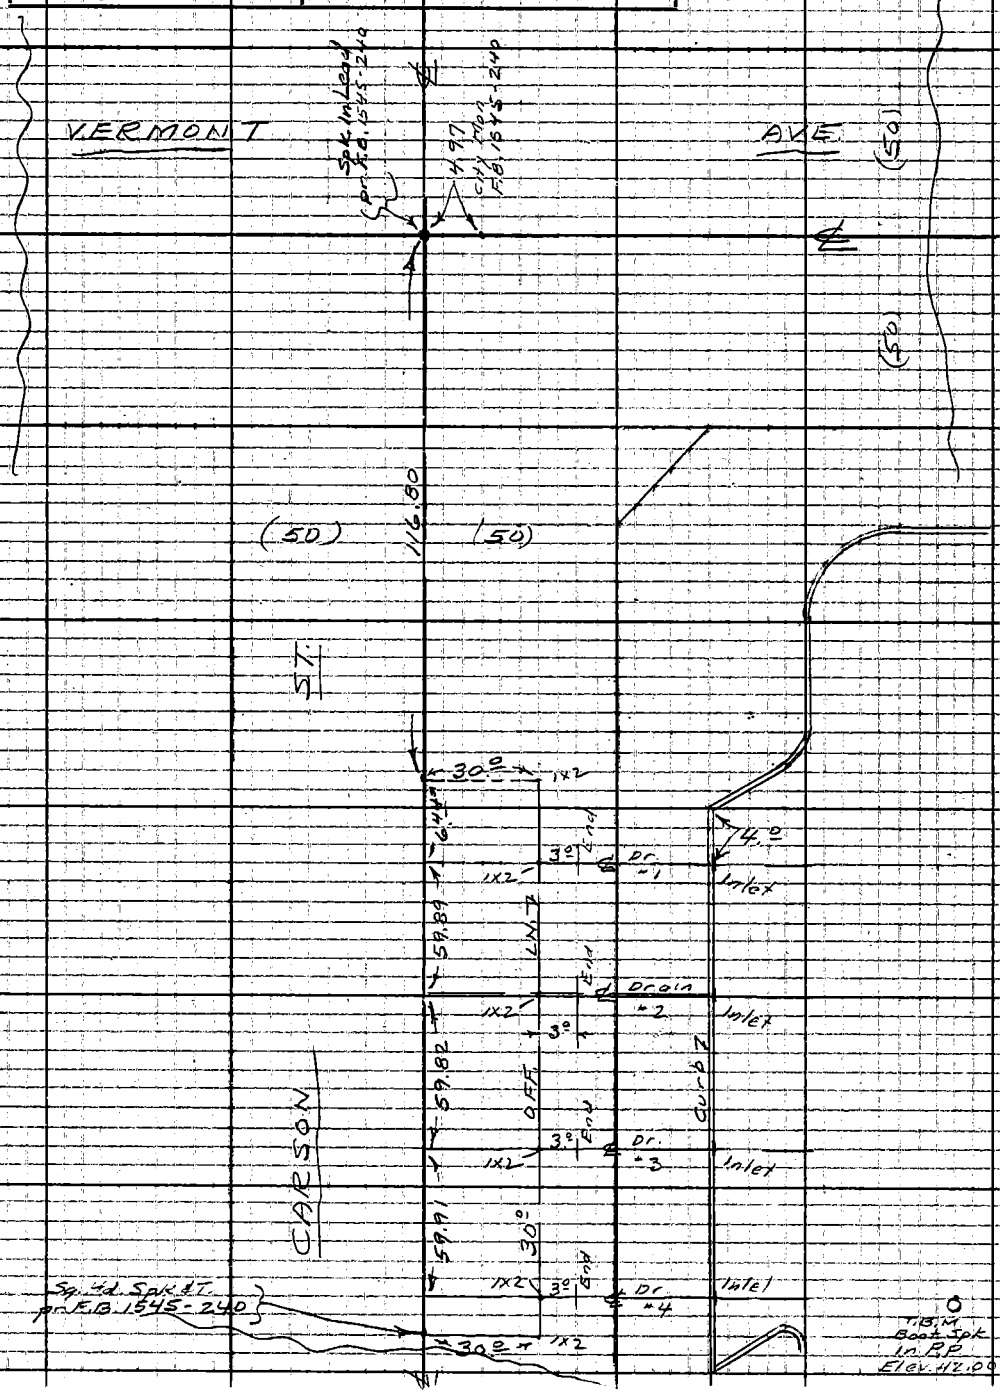

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY ENGINEER
1100 LOS ANGELES COUNTY ENGINEERING BLDG.

763095 CE #247—7-58

F.B. 2760 PG. (F) 140

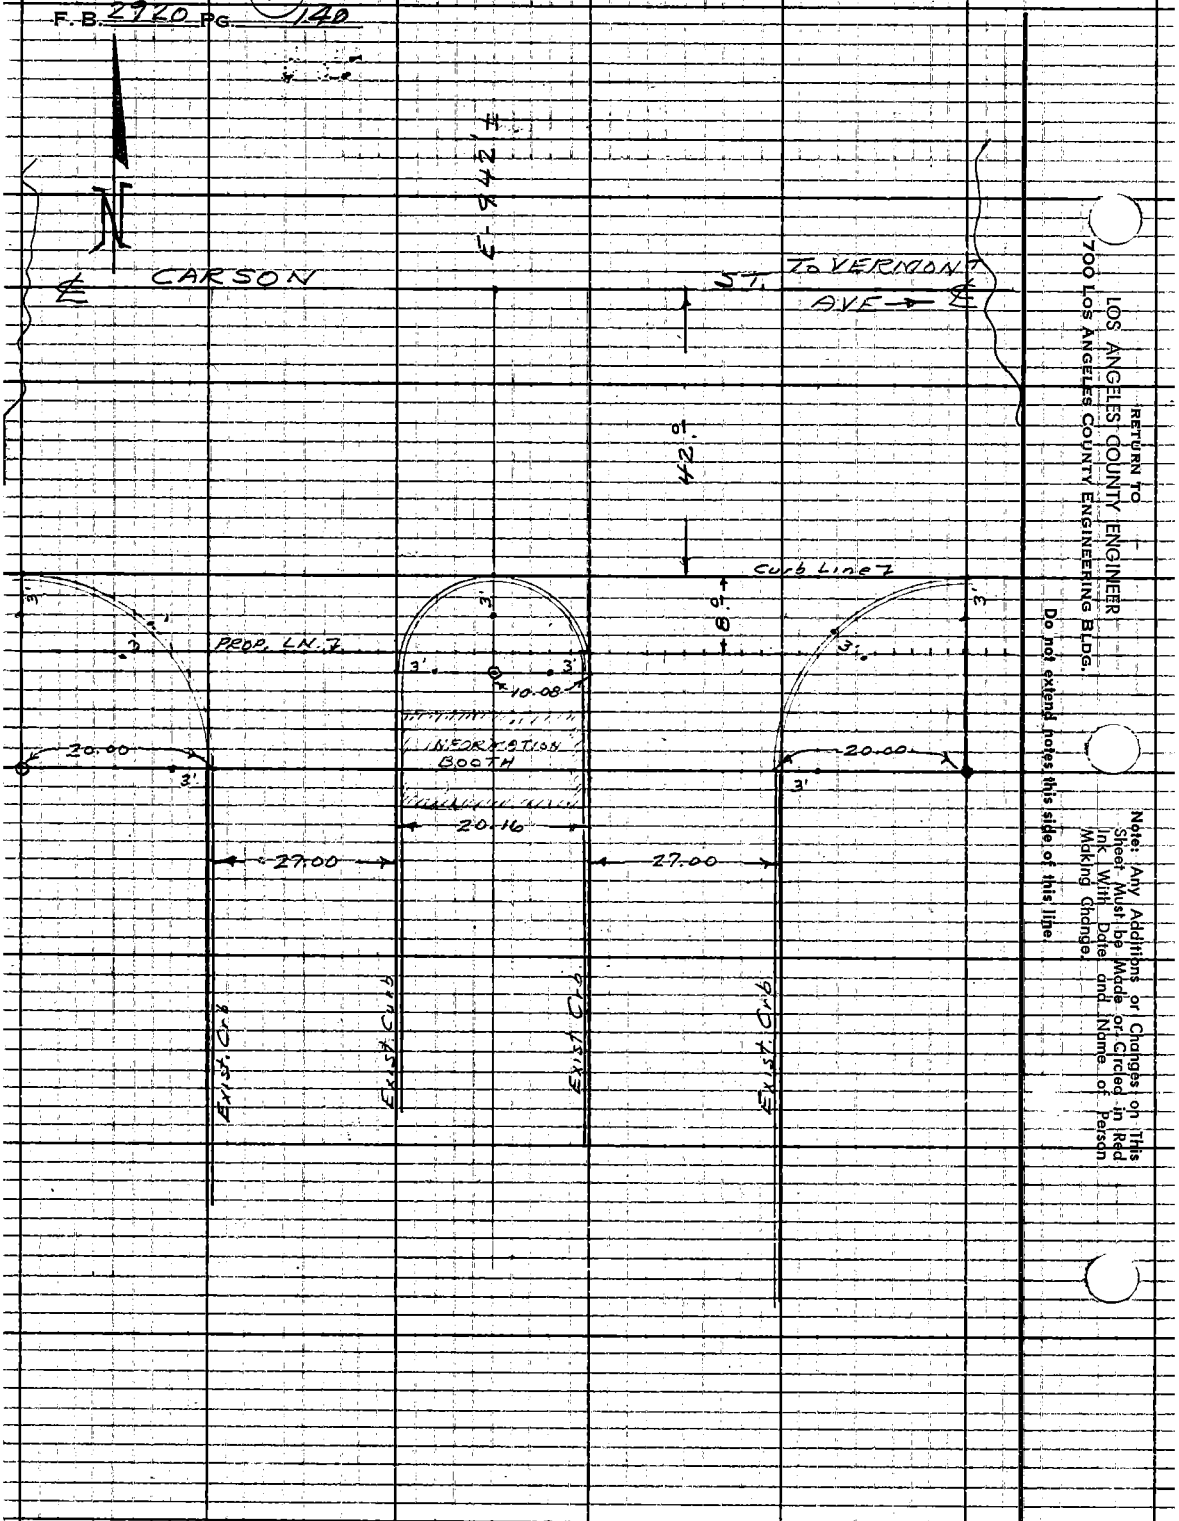

RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend notes this side of this line

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red Plotted Job No. 7973.01 Division No. 11 F.B. 2920 PG. 19(6)
No. X-Sec. Date Date Survey of Herbar General Hosp.
No. Notes Chkd. Checked Survey by AMH Notes D.L.B. Date 4-27-62
Date Date Map No. Indexed C. L. GAU Date SEP 24 62

F.L. Grades for drains on Carson St.

STATION	B.S.	H.I.	F.S.	ELEV.	T.B.M. F.L. Grade @ outlet	Cut or Fill	June 6-1962 Invert Grd. @ outlet
T.B.M.				42 00			
				Exist.			
Drain # 1	(Inlet @ Parking Area)			38.60			
	(outlet @ street)			37.82 Exist.	~~37.95~~	~~F-0.13~~	35.84
Drain # 2	(Inlet @ Parking Area)			38.81			
	(outlet @ St.)			38.15 Exist.	~~38.03~~	~~C-0.12~~	35.98
Drain # 3	(Inlet @ Parking Area)			38.88			
	(outlet @ St.)			37.99 Exist.	~~38.13~~	~~F-0.14~~	36.12
Drain # 4	(Inlet @ Parking Area)			38.82			
	(outlet @ St.)			38.13	~~38.20~~	~~F-0.07~~	36.24
T.B.M.				45 00	Fin. Floor In MAIN BLDG.		

76L-298 CE 507 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 2920 Pg. (H) 142 | Job No. 7973.01 | Division No. 11 | Notes Red | Plotted | Profile
Survey of HARBOR GEN. HOSP | Date | No. | X-Sec.
Survey by Heistrom | Notes D.L.B. | Notes Chkd. | Checked | No.
Indexed C. J. GALLI | Date | Date | Date

STATION	B.S.	H.I.	F.S.	ELEV		
B.M. "A"				38.48	B.M. "A" - Elev. 38.48 - L.B. 439-5 = 2" B.M. in W. End Gas Island ± 119' S. & Carson St. & 62'± E. & Vermont	
					Invert Grades for Parking Lot drains along Carson St. (Per Rd. Dept.) See Pg. "E" for Location	
				Elev.	Invert Gr. @ outlet	cut or Fill
Drain #1	Invert @ Street			37.52	35.84	C-1.68
" #2	"			37.86	35.98	C-1.88
" #3	"			37.69	36.12	C-1.57
" #4	"			37.85	36.24	C-1.61
					Grades for Curbs @ Information Booth (See Pg. "F" for Location)	
				Elev.	Fin. Cb Grades	cut or Fill
E. end of E. 20' Radius				37.97	37.25	C-0.72
Midpoint of E. 20' Radius				38.06	38.04	C-0.02
S. end of E. 20' Radius				38.43	38.83	F-0.40
E. Side of 10' Radius				37.86	38.85	F-0.99
Midpoint of 10' Radius				38.35	37.37	C-0.98
W. Side of 10' Radius				38.05	38.87	F-0.82
S. end of W. 20' Radius				38.07	39.10	F-1.03
Midpoint of W. 20' Radius				37.77	38.30	F-0.53
W. end of W. 20' Radius				37.66	37.50	C-0.16
B.M. "A"				38.48	B.M. "A" Elev. 38.48 (See Above)	

Notes Ck'd by	Survey of Harbor Gen. Hosp
Map No.	JN 1973.01 Tape Std
Office Work	Surveyed by Carrasco
Checked	Notes A.L Date 4-27-72
Date	Indexed C. J. GALLI SEP 2-4-68

F. B. 2920 Pg. 43

C.L. 1973.01

Harbor General Hospital

Acute Unit Bldg

Construction Stakes for

Curb & Drain Outlets

(Per Sheets No. 2 to No. 5)

At West side of Vermont Ave.

From

220th Street To Carson Street

Set 1½" ⌀ Tins 3' E. of W. Curb of Vermont Ave

Carrasco
Spriggs
Adams
Rodriguez

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY ENGINEER
900 LOS ANGELES COUNTY ENGINEERING BLDG.

763095 CE #247—7-59

RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend notes this side of this line

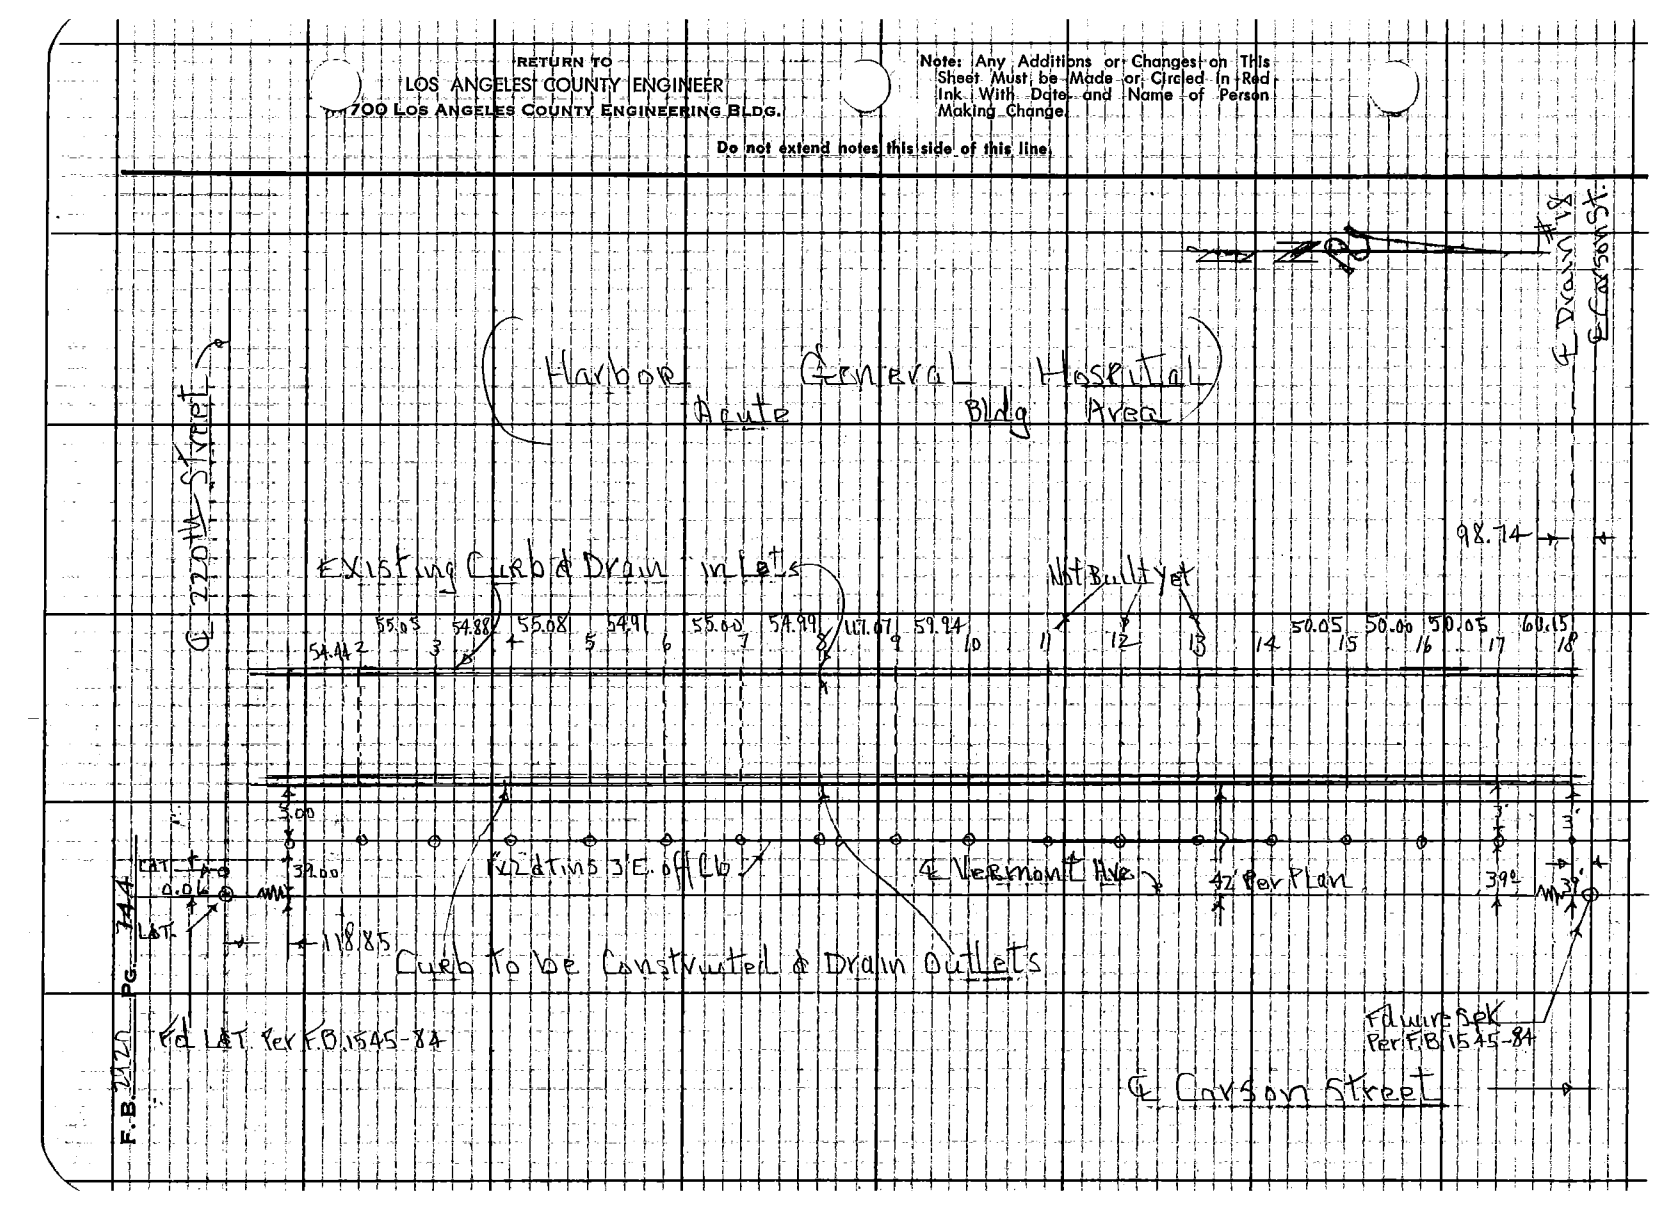

Profile No. | Notes Red. | Plotted | Job No. 79 73 01 | Division No. 11 | F. B. 2920 | PG. 145
Date | Date | Survey of Harbor Gen. Hosp
X-Sec. No. | Notes Chkd. | Checked | Survey by A. Carrasco | Notes A.C. | Date 4-27-62
Date | Date | Map No. | Indexed C. J. GALLI | Date SEP 2 4 '62

C.I. 79 73-01

Harbor General Hospital

Construction Stakes For Drains Outlets

At Curbs West Side of Vermont Ave

From

120th Street North to Carson Street

Per Sheets No. 7 to No. 5

Carrasco
Spriggs
Rodriguez
Adams

STATION | B. S. | H. I. | F. S. | ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

76L-298 S & E #307—1-56

76L-298 S & E #307—1-56

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.				
T.B.M.				40.99	T.B.M. Fd. Bt. SP.K. 100'± W. of ℄ Vermont Ave & 91'± N. of ℄ 220th St. Set & Used By Al. Curtis F.B. 2920-			
					Grade	Cut	Fill	
1				40.37	39.27	1.10		Set st'K & T. 3' E. of Cb Face
2				40.57	39.21	1.36		
3	⊙			40.39	39.15	1.24		
4				40.22	39.09	1.13		
5				40.09	39.03	1.06		
6				40.27	38.98	1.29		
7				40.45	38.92	1.53		
8				40.56	38.85	1.71		
9	⊙			39.74	38.72	1.02		
10				39.74	38.66	1.08		
11	⊙	Not Built			38.38			
12		"			38.12			
13		"			37.84			
14	⊙			38.53	37.22	1.31		14'
15				38.60	37.00	1.60		3'

F. B. 2920 PG. 146

Survey of Harbor General Hospital Job No. 7973.01 Division No. 11 Notes Red Plotted Profile

Survey by A.C. Notes A. Carrasco Date Date No.

Indexed C. J. GALLI Date Notes Chkd. Checked X-Sec.

Date Date No.

76L-298 S & E #307—1-56

90
64
154

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	Grade	Cut	Fill	
TP.				37.41				
6				38.23	36.73	1.50		Set St'K & T. 3' E. of Cb. Face
17				37.11	36.54	0.57		" 14' "
18				36.90	36.36	0.54		" 3' "
T.B.M.				41.98				T.B.M. Fd Large spk So. Side P. Pole with Lath Mark Elev. 42.00 Set Al Curtis ± 155' S. of ℄ Carson St & 43' ± W. of E. Acute Bldg Line Prod.

Profile Notes Red ____ Plotted ____ Job No. 7973-01 Division No. 11 F. B. 2920 PG. 147
No. ____ Date ____ Date ____ Survey of Harbor General Hospital
X-Sec. Notes Chkd. ____ Checked ____ Survey by A. Carrasco Notes A.C. Date 4-27-62
No. ____ Date ____ Date ____ Map No. ____ Indexed C. J. GALLI Date ____

Notes Ck'd by
Map No. B-2345-4
Office Work
Checked
Date

Survey of Harbor Gen. Hospital F.B. 2920 PG. 179
JN Tape Std °F
Surveyed by A.S. Curtis
Notes Curtis Date 3-14-62
Indexed H. E. OTT MAR 16 62

J.N. 797301

Location of S. Sewer MH's
on 220th ST. just East of
Meyler ST.

(For Fl. Elevs. see page 104)

Curtis
Newman
Yasui
Dover

Note: Any Additions or Changes on This Sheet Must be Made in Red Ink With Date and Name of Person Making Change.
Do not extend notes this side of this line.

RETURN TO
LOS ANGELES COUNTY ENGINEER
900 Los Angeles County Engineering Bldg.

76S09S CE #247—7-55

F.B. 2920 PG. 150

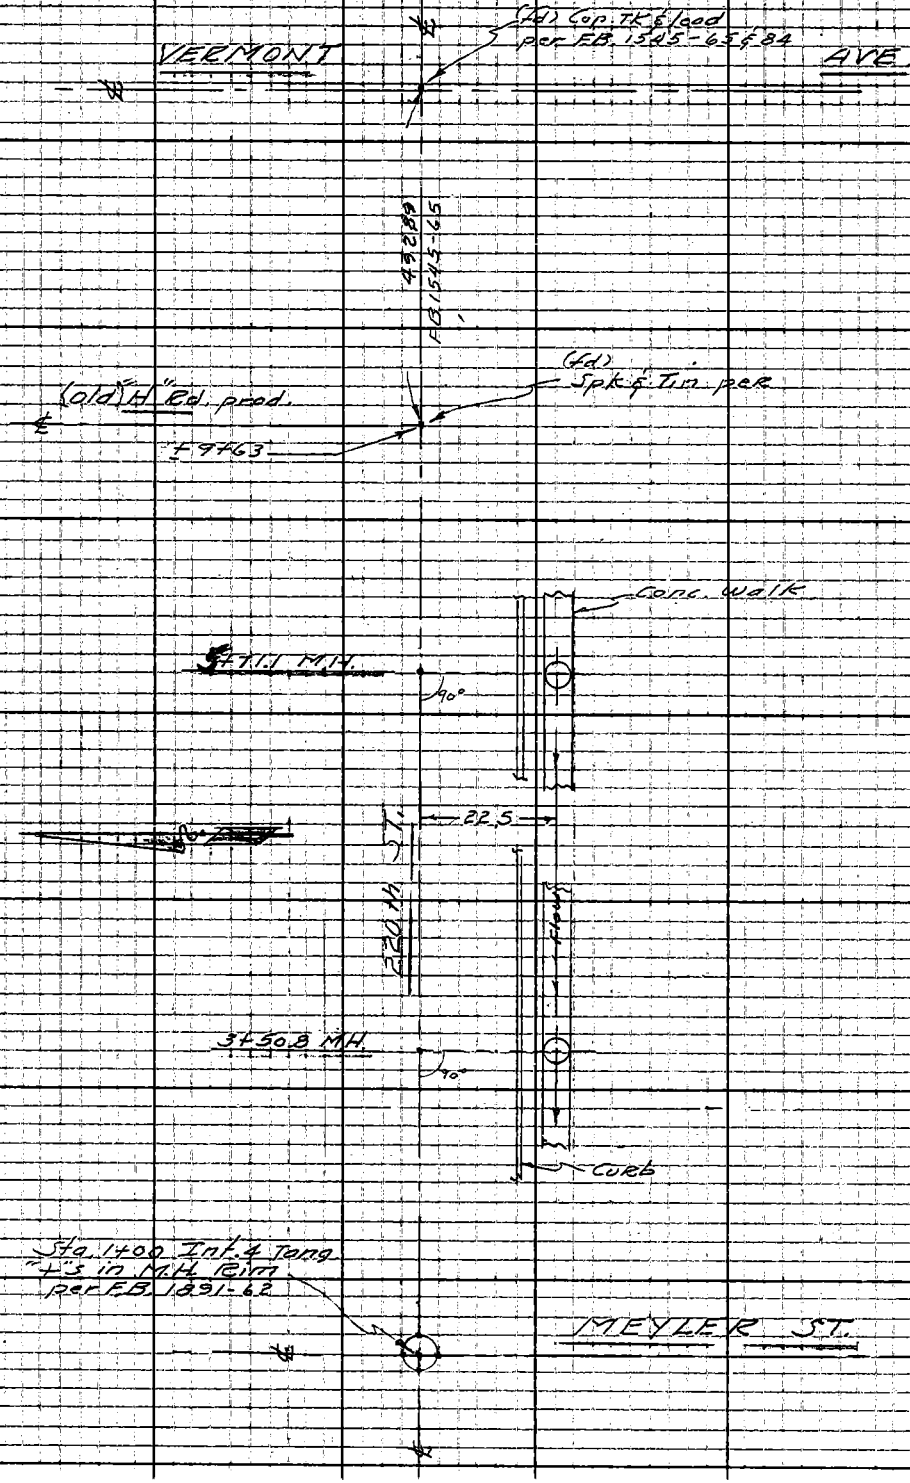

RETURN TO
LOS ANGELES COUNTY ENGINEER
700 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

Note: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

F.B. 2920 PG. 151

Profile No. | Notes Red | Plotted | Job No. | Division No. 11
Date | Date | Survey of Harbor General Hospital
X-Sec. No. | Notes Chkd. | Checked | Survey by Curtis | Notes Curtis | Date 3-14-62
Date | Date | Map No. | Indexed H. E. OTT | Date MAR 1 6 '62

J.N.

Grades for S. Sewer MH's on

220th ST. Just east of Meyler ST.

(See page 102 for location)

Curtis
Newman
Yasui
Dover

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 Los Angeles County Engineering Bldg.

761-296 CE 307 11-58

76L-298 CE 307 11-58

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
700 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.	
(fd)					Elev. 37.97 FB 1545-120 Road D 50 Side
BM.				37.97	BM. Bt. Spk in Conc. Hd. Wall for 2-30" Conc dra. pipes (East of Bldg F-9).
(fd)					El. 37.29 FB 1545-68 & 120 ± 35 E & ± 35
BM# H-8				37.29	BM# H-8 of Bldg F-9 (South St No Side) Bt Spk in Conc. Hd Wall
TP				39.18	T.P.
T.P.				37.92	TP
M.H. @ Sta 3+50.8					
Rim Elev.				38.38	
			Rod	11.19	
				27.19	F.L. Elev. 8" Inlet from East
Rim Elev.				38.38	
			Rod	11.27	
				27.11	F.L. Elev 8" outlet to west.
M.H. @ Sta. 5+71.1					
Rim Elev.				38.31	
			Rod	9.98	
				28.33	F.L. Elev. 8" Inlet from East.
Rim Elev.				38.31	
			Rod.	10.08	
				28.23	F.L. Elev. 8" Outlet to West.
BM# H-8				37.29	BM# H-8 (above)

FIB. 2920 PG. 152

Job No. ____ Division No. 11 Notes Red ____ Plotted B-2345-4 Profile

Survey of ____ Date ____ Date ____ No. ____

Survey by Curtis Notes Curtis Notes Chkd. ____ Checked ____ X-Sec.

Indexed H. E. OTT Date ____ Date ____ No. ____

Notes Ck'd by	Survey of HARBOR GEN. HOSPITAL
Map No.	J.N. 0022.02 Tape 131 Std 84 °F
Office Work	Surveyed by R.B. HOBSON
Checked	Notes R.B.H. Date 1-17-64
Date	Indexed C. J. DALLI JAN 29 '64

F.B. 2920 Pg. 153

HARBOR GENERAL HOSP.
J.N. 0022.02

HORIZONTAL CONTROL SURVEY FOR

P.T. SHEETS COVERING THAT AREA IMMEDIATELY EAST OF THE CONC. STORM DRAIN THAT RUNS BETWEEN THE NEW ACUTE UNIT & THE OLD HOSP.

REF: E.B. 1645

JAN 17TH, 1964

HOBSON
FRONK
SONNENSCHEIN
CROWDER

SEE PG. 154 FOR INDEX

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

76F3095 CE # 310 3-61

F. B. 2920 Pg. 154

INDEX MAP
OF
A PORTION OF THE HARBOR GENERAL HOSP.

(No Scale)

CIRCLED FIGURES = PAGE No.

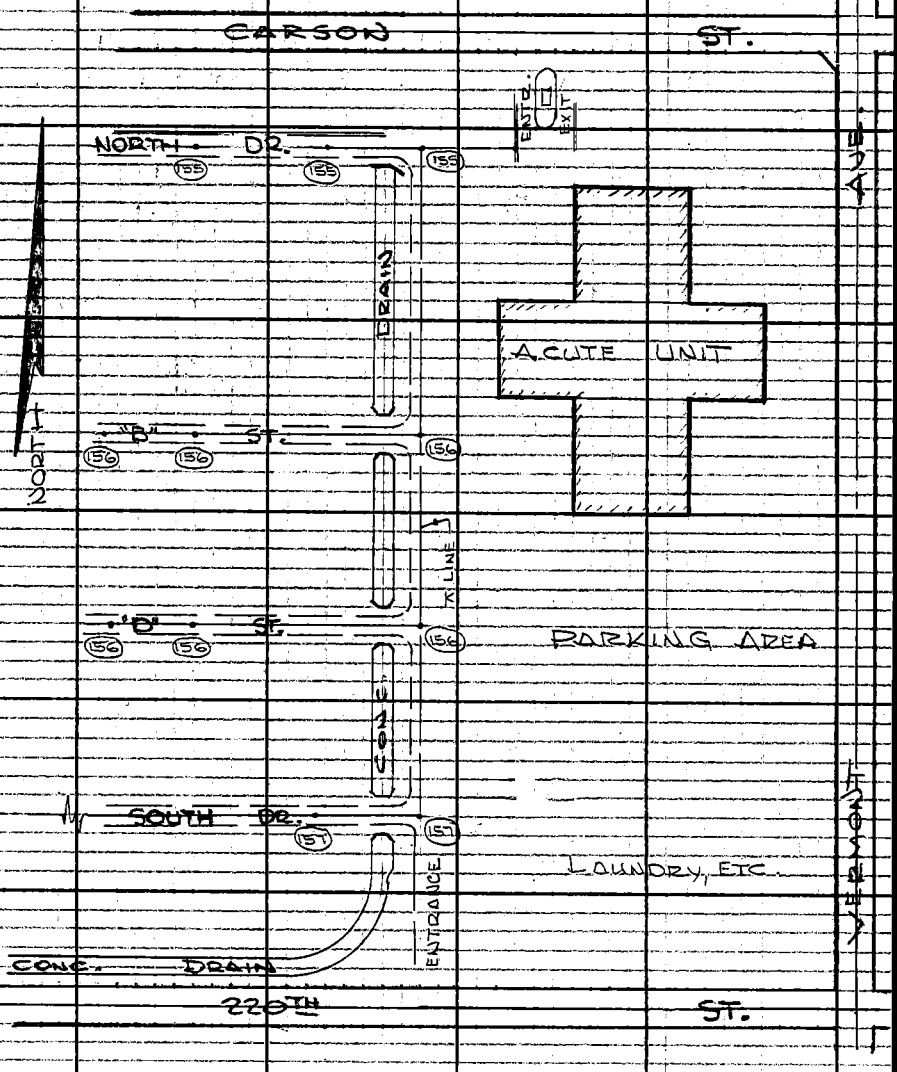

LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

PLEASE RETURN TO

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by	Survey of HARBOR GEN. HOSPITAL
Map No.	JN0022.02 Tape 131 Std 84 °F
Office Work	Surveyed by R.B. HOBSON
Checked	Notes R.B.H. Date 1-17-64
Date	Indexed C. J. GALLI

F. B. 2920 PG. 155

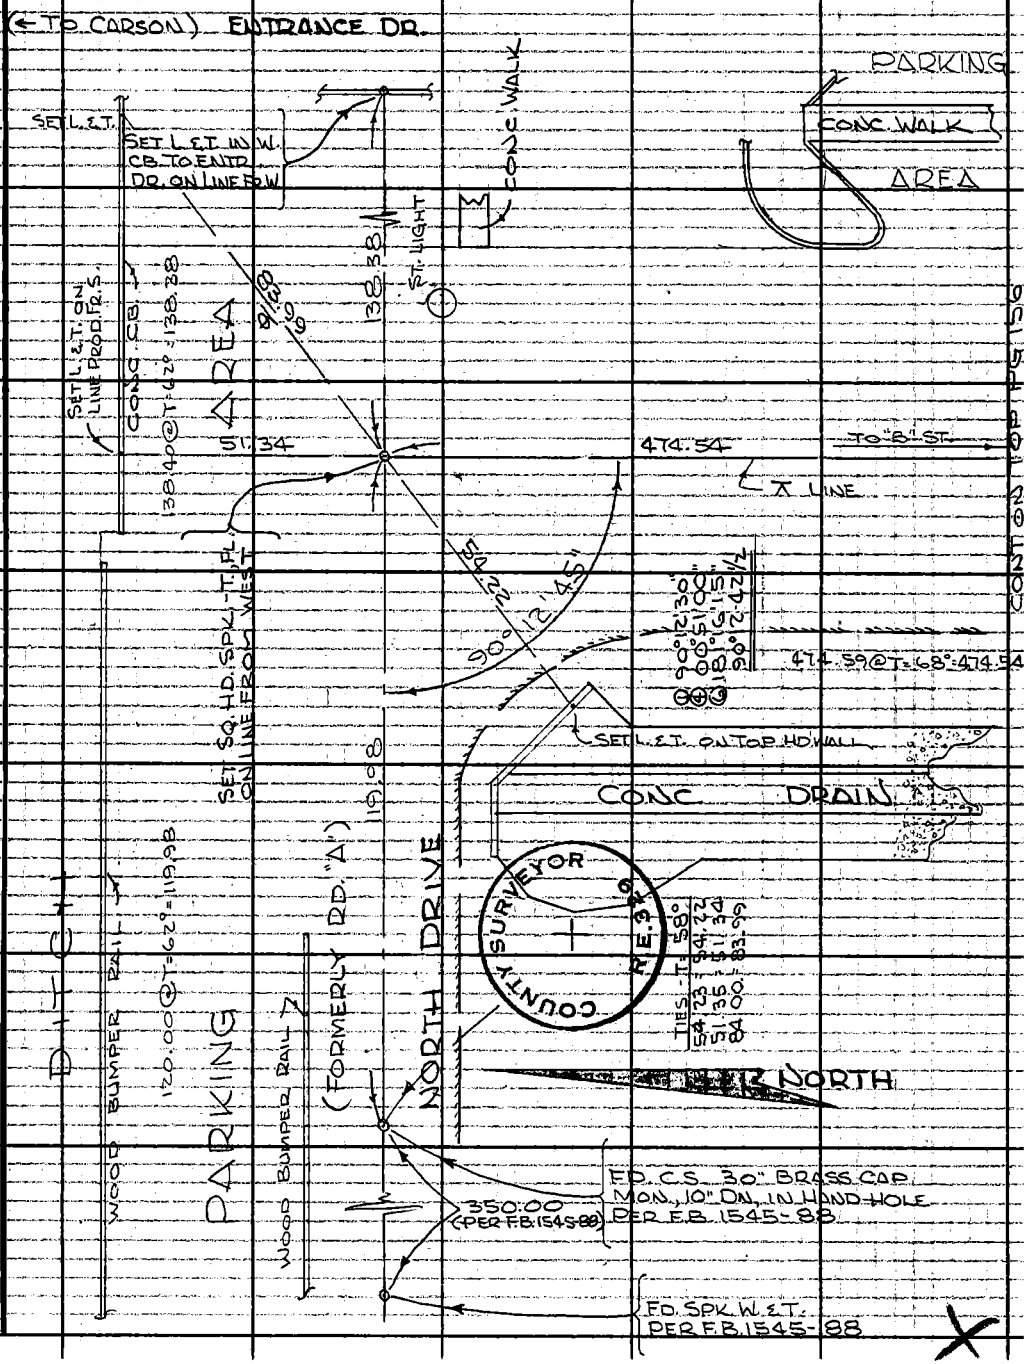

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

76F3095 CE # 310 3-61

F. B. 2920 PG. 156

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.
Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by	Survey of HARBOR GEN. HOSPITAL
Map No.	JN 0022.02 Tape 131 Std 84 °F
Office Work	Surveyed by R.B. HOBSON
Checked	Notes R.B.H. Date 1-17-64
Date	Indexed [illegible]

F. B. 2920 PG. 157

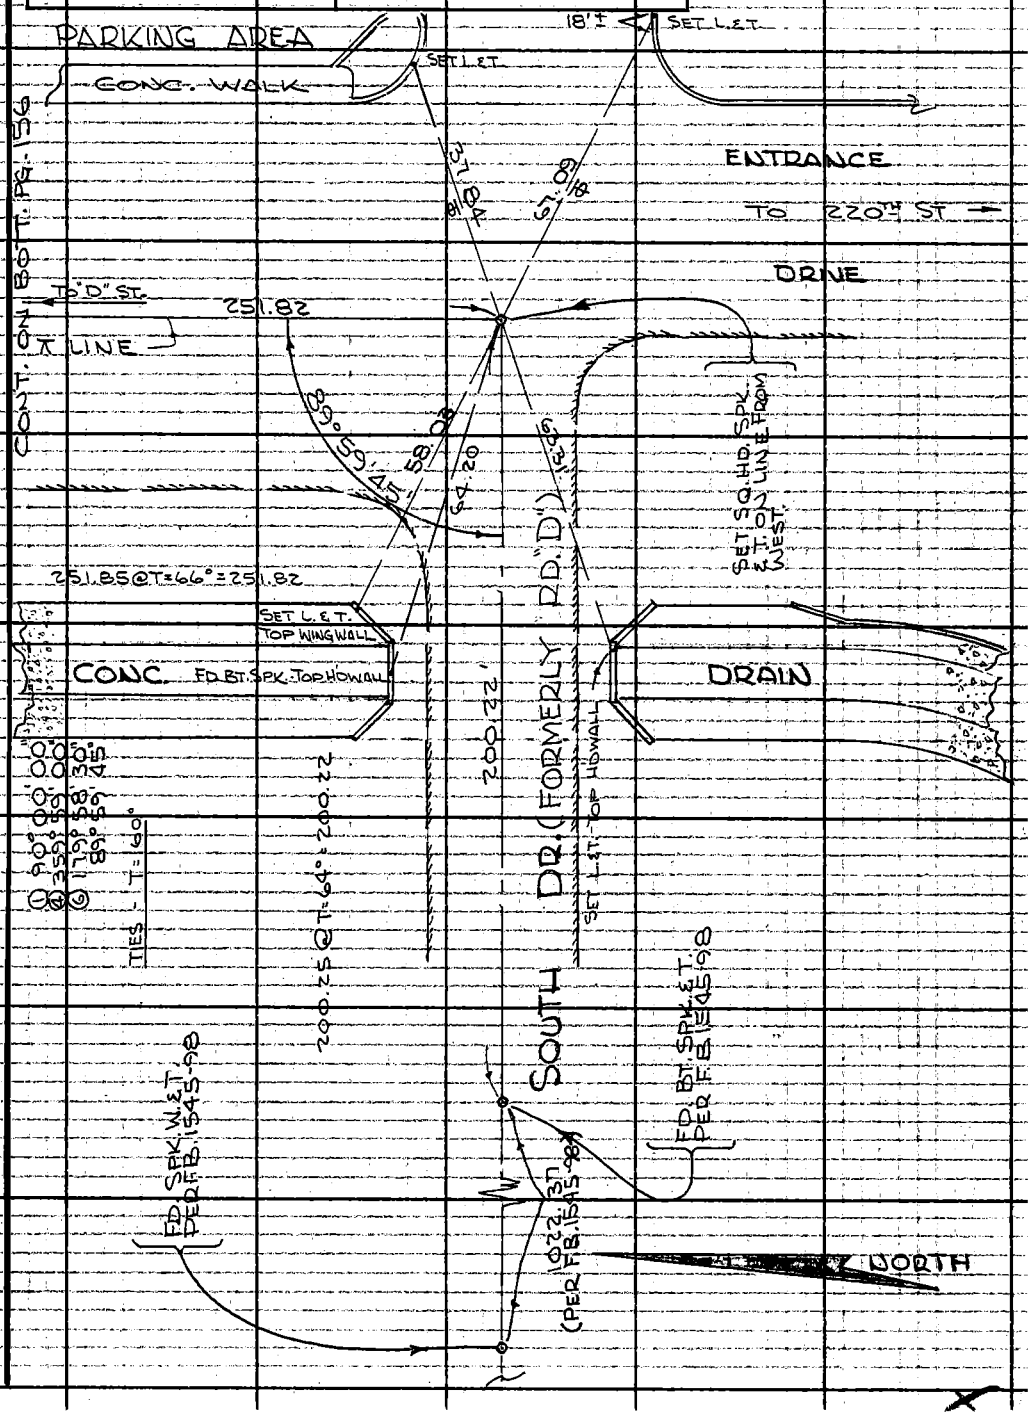

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

76F3095 CE # 310 3-61

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of HARBOR GEN. HOSP F. B. 2920 Pg. 159
J.N. 0018.23 Tape — Std. — °F.
Surveyed by KEN MYERS
Notes KEN MYERS Date 8/4/70
Indexed D.L. GAULT AUG 6 '70

PSYCHIATRIC SERVICES BUILDING
HARBOR GEN HOSP.
J.N. 0018.23

ELEVATION TOP OF UTILITY TONNEL, S.E. OF EXIST. ACUTE UNIT

REF. F.B. 1545-68

PARTY 8/4/70
K. MYERS
D. LEGAULT
D. PRIEBE

Note: Any Additions or Changes on This Sheet Must be Made in Red Ink With Date and Name of Person Making Change.

PLEASE RETURN TO
COUNTY OF LOS ANGELES
DEPARTMENT OF COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.
Do not extend this side of this line.

16F309S CE#310 3-68

F. B. 2920 PG. 160

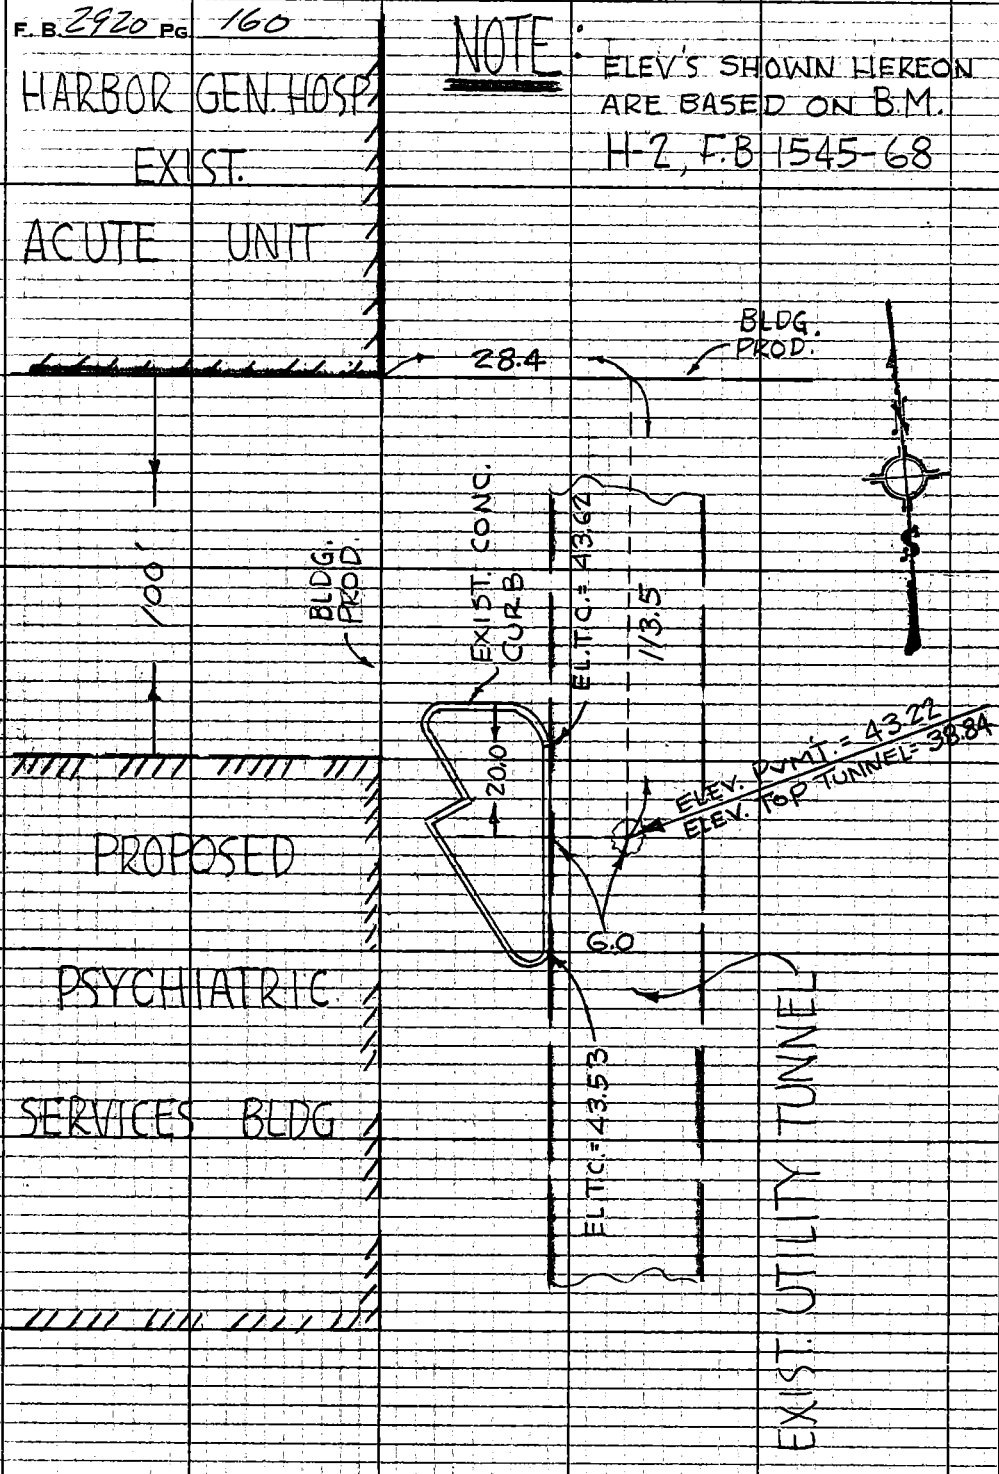

PLEASE RETURN TO
COUNTY OF LOS ANGELES
DEPARTMENT OF COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.
Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by R. HILARIO	Survey of Harbor Gen. Hosp.
Map No.	JN 002202 Tape 0137 Std. 68 °F
Office Work	Surveyed by English
Checked	Notes Ed. Date 12-70
Date	Indexed G.I. GALT BC 177

F. B. 2920 PG. 161

HARBOR GENERAL HOSPITAL

ACUTE UNIT AND CLINIC ADDITION.

J.N. 002202

Parcel
Boundary
Survey.

Nov. 10, 1970.
English
Shoemaker
Clifford
Goodwin.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
COUNTY OF LOS ANGELES
DEPARTMENT OF COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

76F309S CE#310 3-68

F. B. 2920 PG. 162

INDEX MAP

PLEASE RETURN TO
COUNTY OF LOS ANGELES
DEPARTMENT OF COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

Notes Ck'd by R. HILARIO	Survey of Harbor Gen. Hos.	F. B. 2920 PG. 163
Map No.	JN 002202 Tape 0137 Std 68 °F	
Office Work	Surveyed by English	
Checked	Notes Ed. Date 12-70	
Date	Indexed [illegible] 16 17 [illegible]	

Con't. Pg. 164

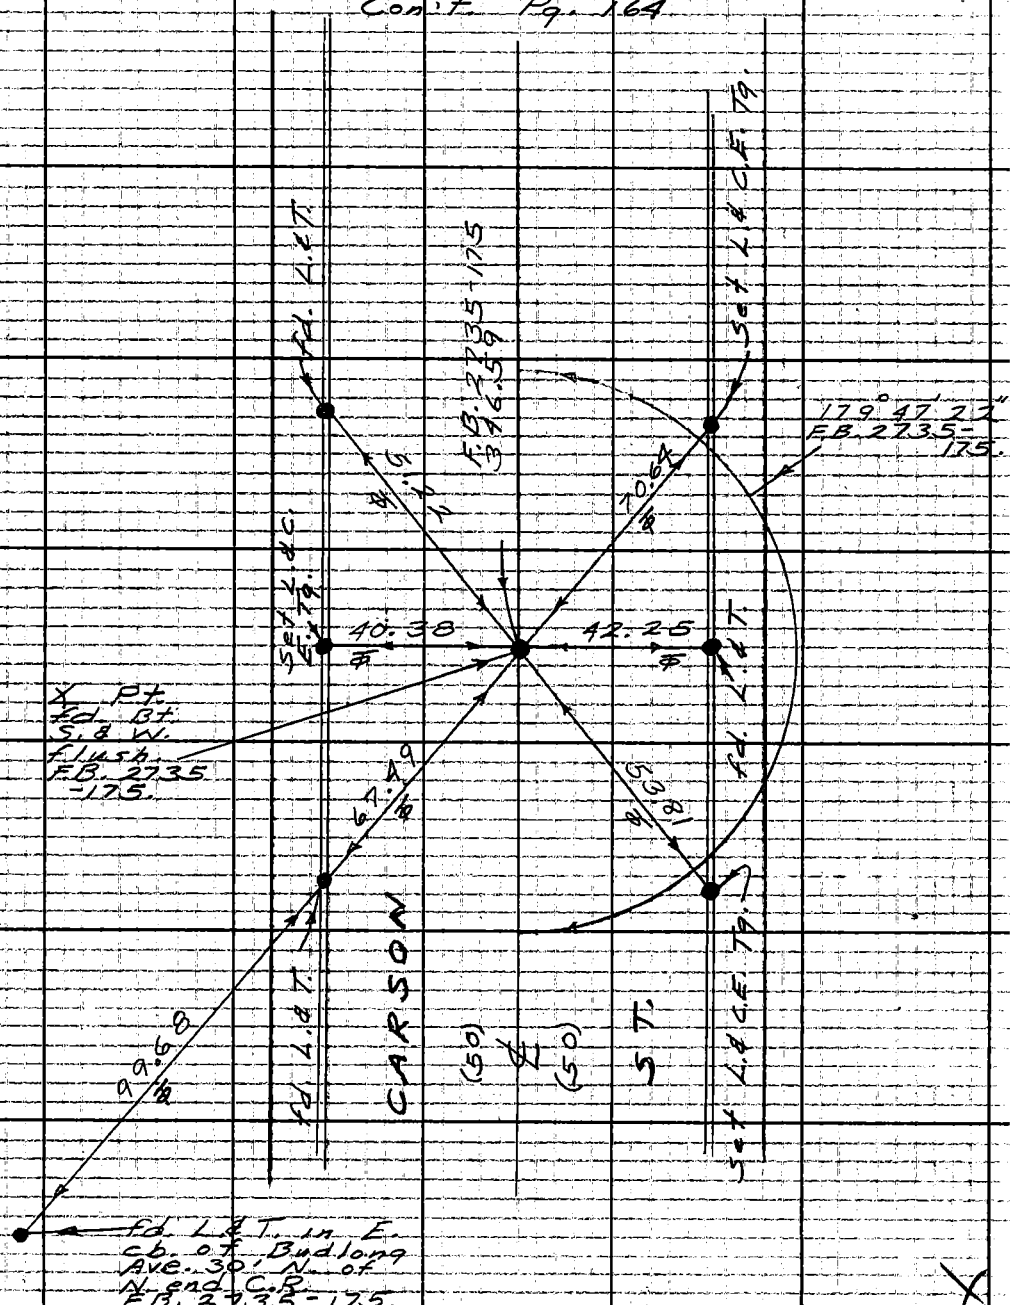

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
COUNTY OF LOS ANGELES
DEPARTMENT OF COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

76F309S CE#310 3-68

F.B. 2920 PG 164

PLEASE RETURN TO
COUNTY OF LOS ANGELES
DEPARTMENT OF COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by R. HILARIO	Survey of Harbor Gen. Hosp.
Map No.	JN 0022.02 Tape 0137 Std 68 °F
Office Work	Surveyed by English
Checked	Notes Ed. Date 12-70
Date	Indexed G. J. GALLI DEC 17 '70

F.B. 2920 PG. 165

W528 B-1

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
COUNTY OF LOS ANGELES
DEPARTMENT OF COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

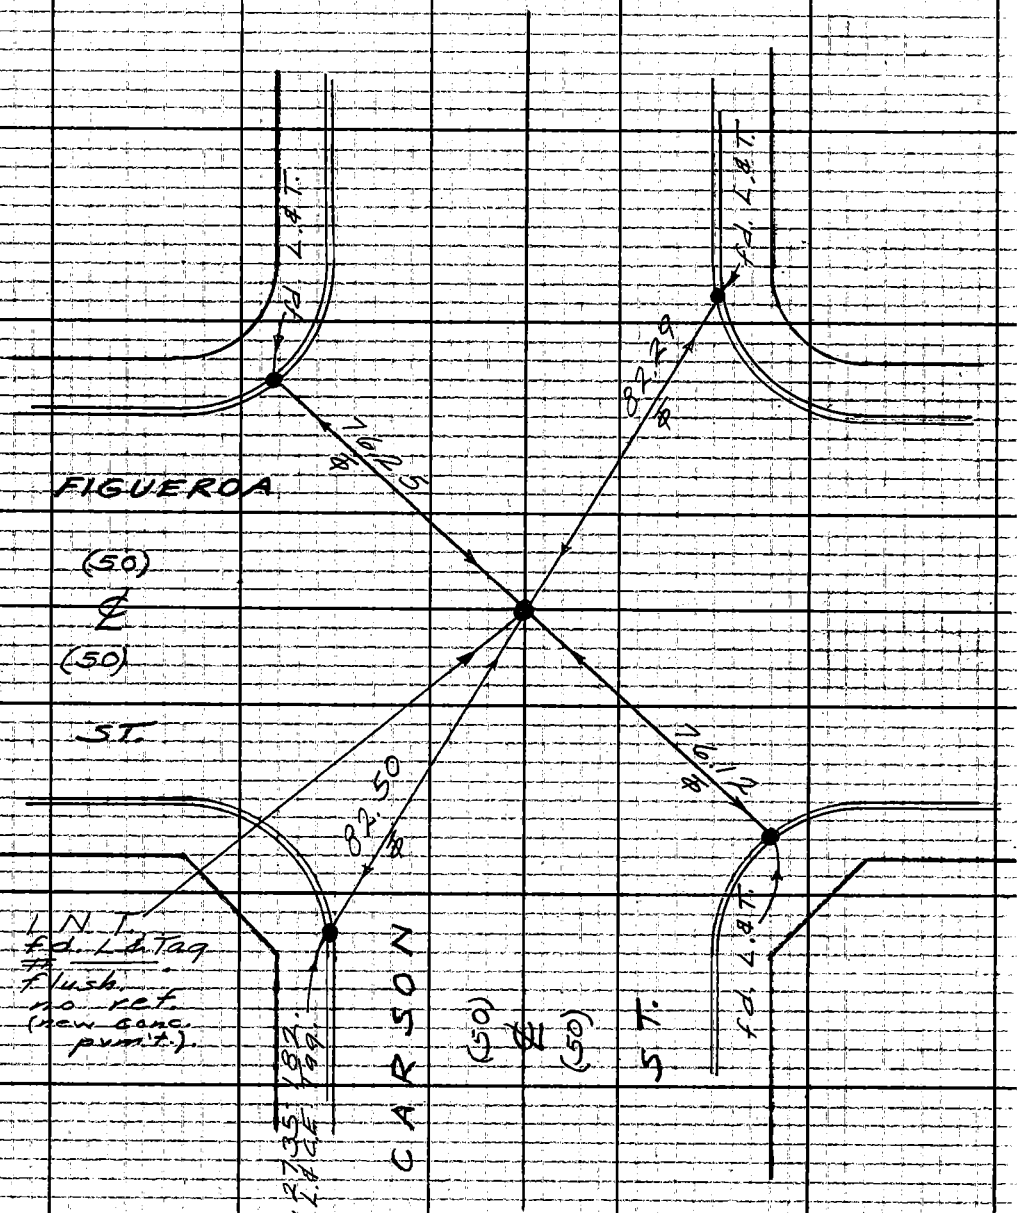

Con't. Pg. 167

76F309S CE#310 3-68

F. B. 2920 PG. 166

Con't. Pg. 167

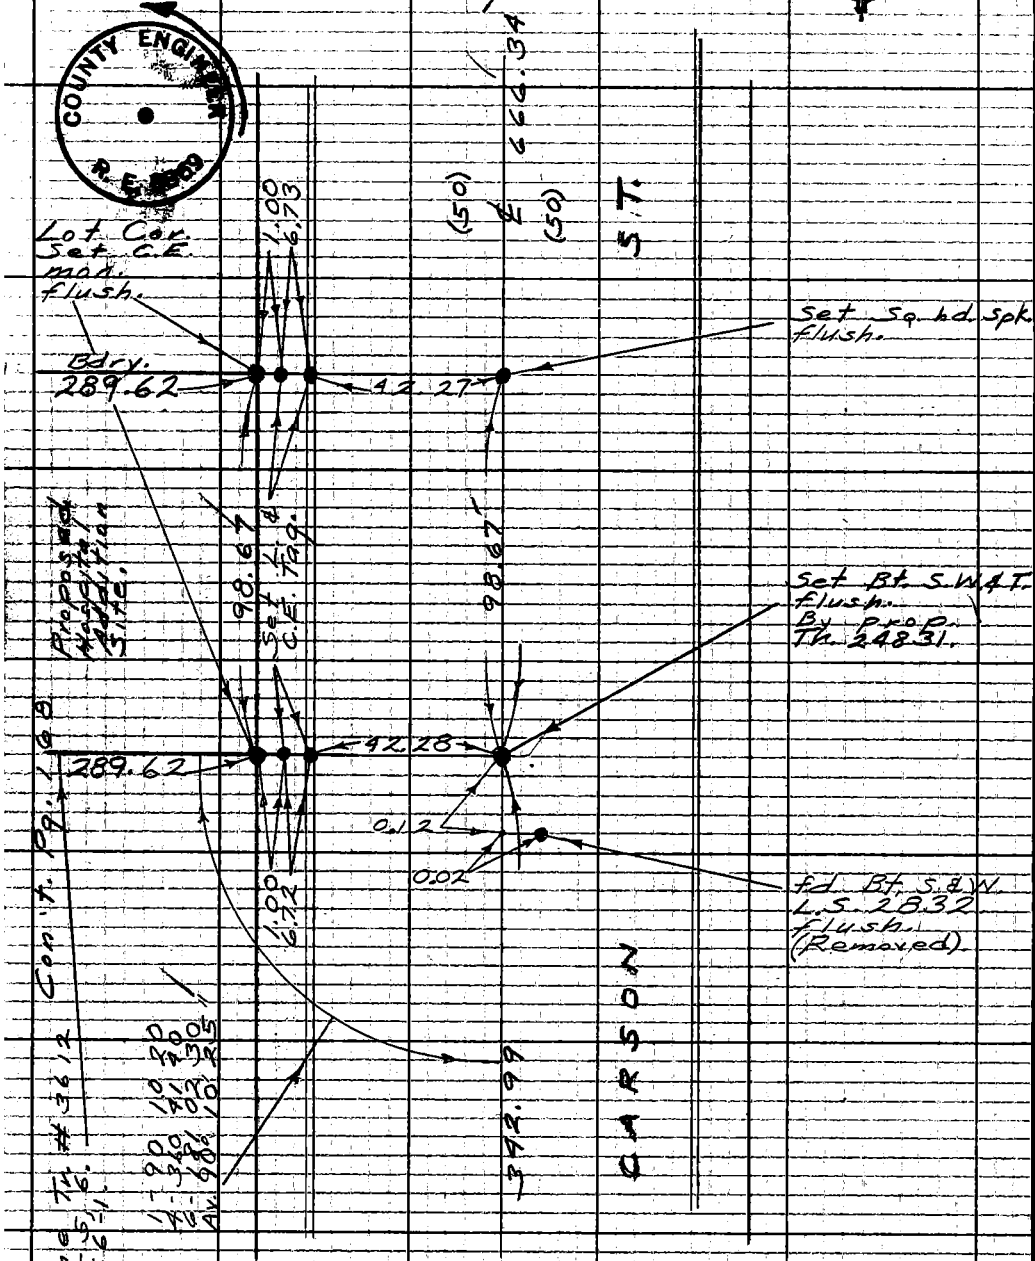

Con't. Pg. 164

T-68°
342.99 Lev. = 342.99
666.34 " = 666.34
98.67 " = 98.67

PLEASE RETURN TO
COUNTY OF LOS ANGELES
DEPARTMENT OF COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by R. HILARIO	Survey of Harbor Gen. Hosp.
Map No.	JN 0022.02 Tape 0137 Std. 68 °F
Office Work	Surveyed by English
Checked	Notes Ed. Date 12-70
Date	Indexed [illegible] GALLI DEC 17 [illegible]

F.B. 2920 PG. 167

W.S. 28 B-1

Con't. Pg. 165

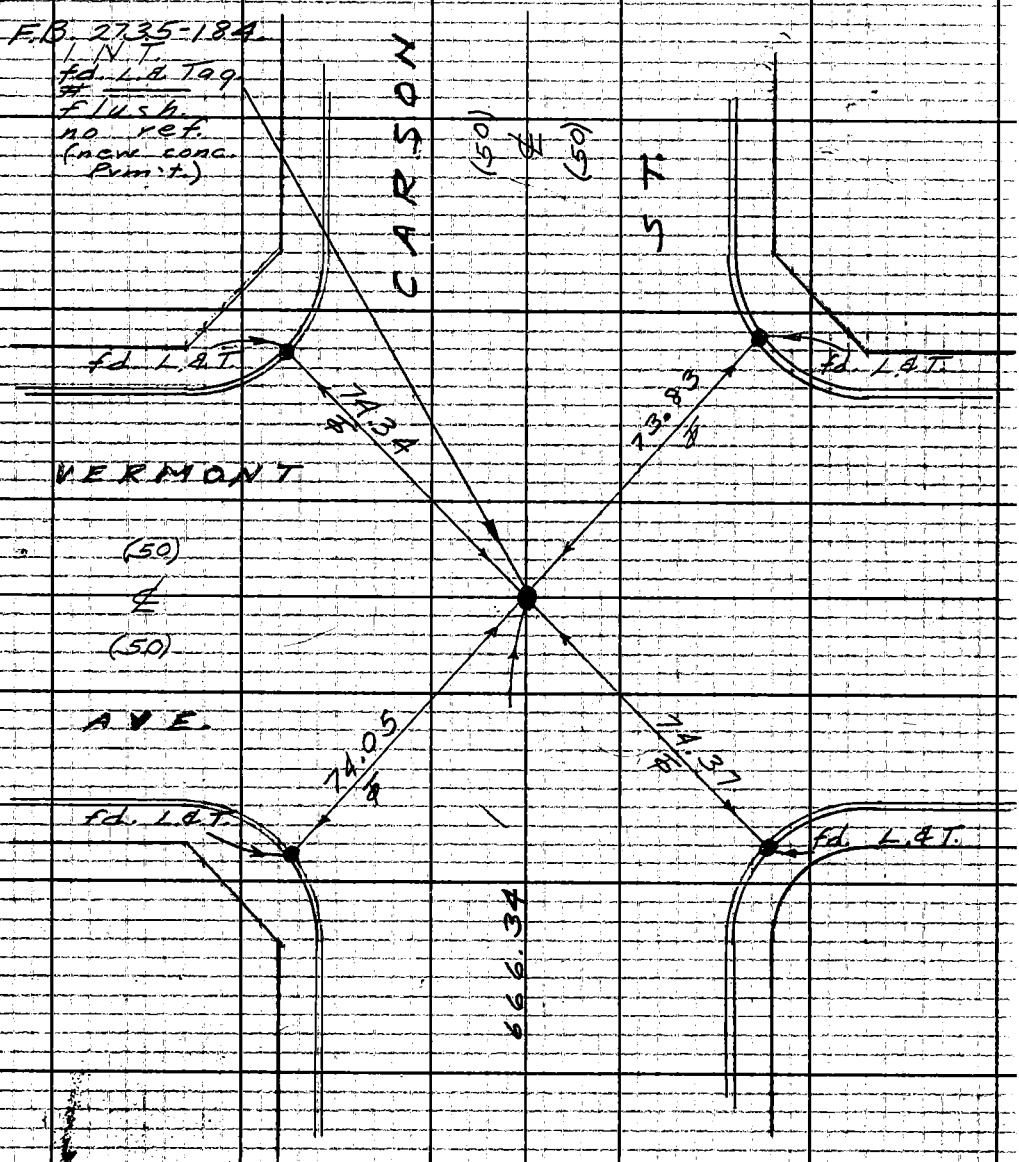

Con't. Pg. 166

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
COUNTY OF LOS ANGELES
DEPARTMENT OF COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

76F309S CE#310 3-68

F. B. 2920 Pg. 168

289.62 T-68°
98.67 Lev. = 289.62
" = 98.67

R.P.
Lot Cor.
Set C.E.
mon.
flush.

COUNTY ENGINEER
R.E. 5869

10.00

Lot Cor.
Set Nothing.
(8" of water).

Bdry.
289.62

E'ly. P.L. est.
parallel with &
98.67 at rt. angle
from W. line of
Tr. 3612 M.B. 40-5,6.
Per E. 68-187.

N'ly. P.L. est.
parallel with &
339.62 at rt. angle
from S. Carson
Per E. 68-187

1 - 90 10 20
4 - 360 41 40
6 - 181 02 30
Av. 90 10' 25"

289.62

COUNTY ENGINEER
R.E. 5869

Lot Cor.
Set C.E.
mon.
flush.

(Cor. Falls in water)

483.01

West line
Tr. # 3612
M.B. 40-5,6.
C.S.B. 766-1.

PLEASE RETURN TO
COUNTY OF LOS ANGELES
DEPARTMENT OF COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by R HILARIO	Survey of Harbor Gen. Hosp.
Map No.	JN 0022.02 Tape 0137 Std 68 °F
Office Work	Surveyed by English
Checked	Notes Ed Date 12-70
Date	Indexed G. S. GALLI DEC 17 70

F.B. 2920 PG. 169

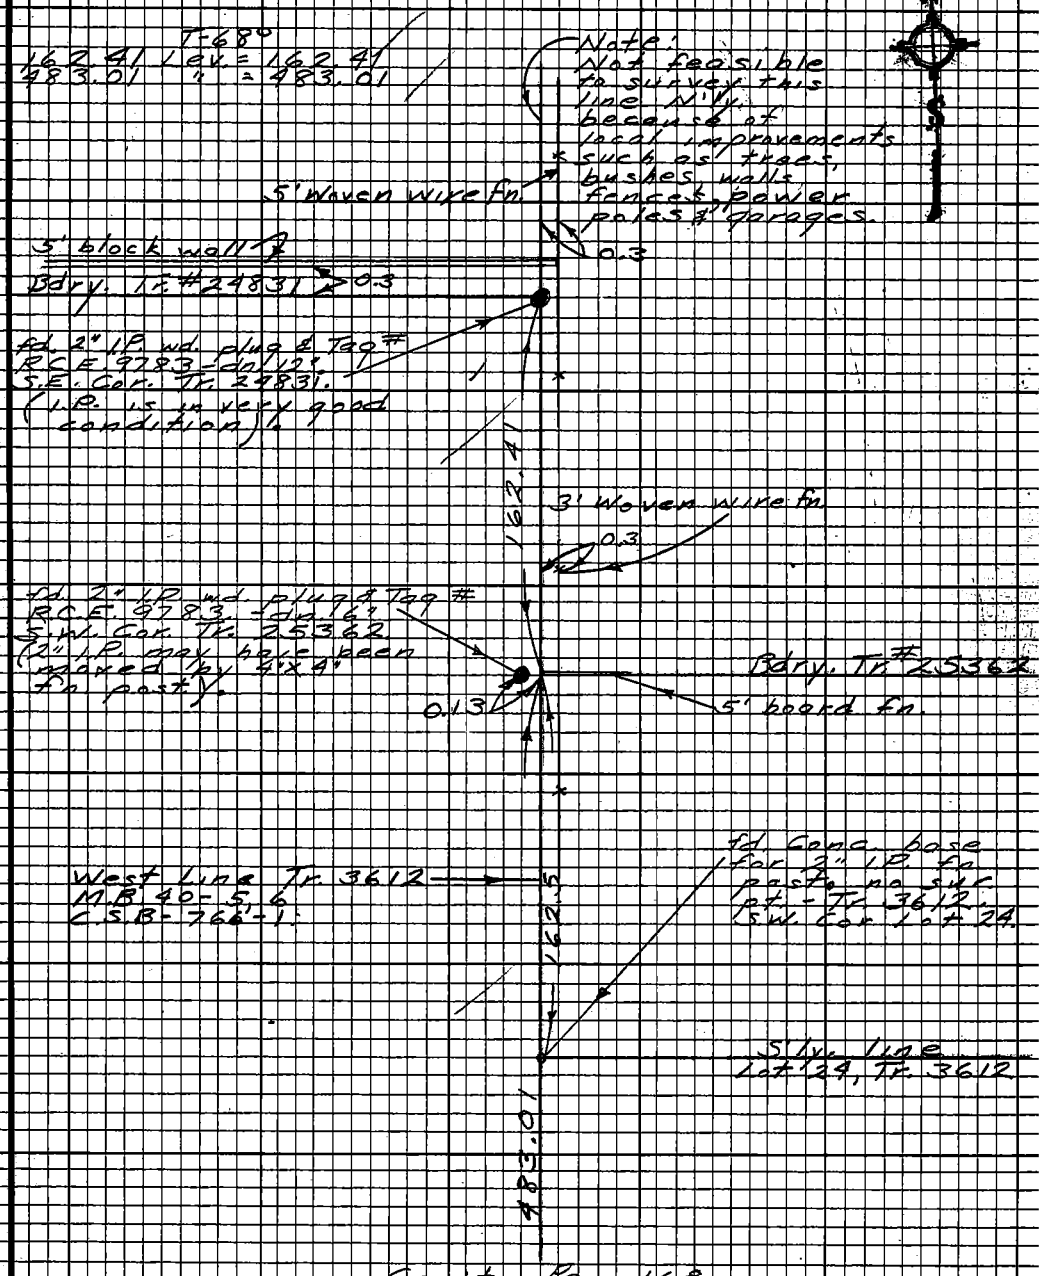

Con't Pg. 168.

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this side of this line.

75F3098 CE# 310 9-67

Profile No. ____ Notes Red ____ Date ____ Plotted ____ Date ____ Job No. 0022.02 Division No. 11 F. B. 2920 Pg. 171

X-Sec. No. ____ Date FEB 5 1971 Notes C'k'd R. MANOR Date ____ Checked ____ Date ____ Survey of HARBOR GEN. HOSP. Survey by J.J. BAZEN Notes KAPP Date 2-4-71 Map No. ____ Indexed C.L. GALLI Date FEB 5 71

J.N. 0022.02

HARBOR GENERAL HOSPITAL

ACUTE UNIT & CLINIC ADDITION

(TEMP.) BENCH LEVELS

REF. = F.B. 1545-68

STATION	B.S.	H.I.	F.S.	ELEV.
	STROUD	TULLIER	2-4-71	
		KAPP		
		BAZEN		

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	
BM H-2				41 827	BM H-2 El.= 41.827 F.B. 1545-68
	2 794	44 621	5 248	39 373	Fd. Bt. Spk. in conc. walk 5' W. of
	4 549	43 922	5 283	38 639	Flag Pole in front of Adm. Bldg.
TBM #1	4 928	43 567	5 616	37 951	TBM #1
					L. & C.E. Tag in Cb. 7.72 S. of S.N. COR.
					OF PROP. PER F.B. 2920-166.
TBM #2	5 189	43 140	5 326	37 814	TBM #2
					L. & C.E. Tag in Cb. 7.73 S. of
					S.E. COR. OF PROP. PER F.B. 2920-166
BM	5 822	43 636	1 183	42 453	BM El.= 42.45, L.A. Dept. of
					Public Works 4" Br. Cap, 1.3 N. of
					Flag Pole, 100'± S.E. OF MAIN ENTR.
					To HAR. GEN. HOSP. ON CARSON ST.
	0 962	43 415	5 067	38 348	T.P.
	5 301	43 649	4 818	38 831	T.P.
	5 364	44 195	4 705	39 490	T.P.
BM H-2	5 173	44 663	2 828	41 835	BM H-2 El.= 41.827 F.B. 1545-68

F. B. 2920 PG. 172 Job No. 0022-02 Division No. 11 Notes Red Plotted Profile
Survey of HARBOR GEN. HOSP. Date Date No.
Survey by J. J. Bazen Notes K.M.K. Notes Chk'd R. MANOR Checked X-Sec.
Indexed C. J. GALLI Date Date FEB 5 1971 Date No.

Notes Ck'd by H. HOLLMAN
Map No.
Office Work
Checked
Date

Survey of Har. Gen. Hosp.
JN 002202 Tape 0137 Std. 68 °F
Surveyed by English
Notes Ed. Date 3-71
Indexed S. S. BALL APR 2 '71

F. B. 2920 PG. 173

HARBOR GENERAL HOSPITAL

J.N. 002202

Property Corners.

March 25, 1971
English
Shoemaker
Goodwin
Clifford

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
COUNTY OF LOS ANGELES
DEPARTMENT OF COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

76F309S CE#310 3-68

F.B 2920 Pg. 174

INDEX MAP

PLEASE RETURN TO
COUNTY OF LOS ANGELES
DEPARTMENT OF COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

Notes Ck'd by H. HOLMAN	Survey of Har. Gen. Hosp.	F. B. 2920 PG. 175
Map No.	JN 002202 Tape 137 Std 68 °F	
Office Work	Surveyed by English	
Checked	Notes Ed. Date 3-71	
Date	Indexed G. O. GALLI APR 2 71	

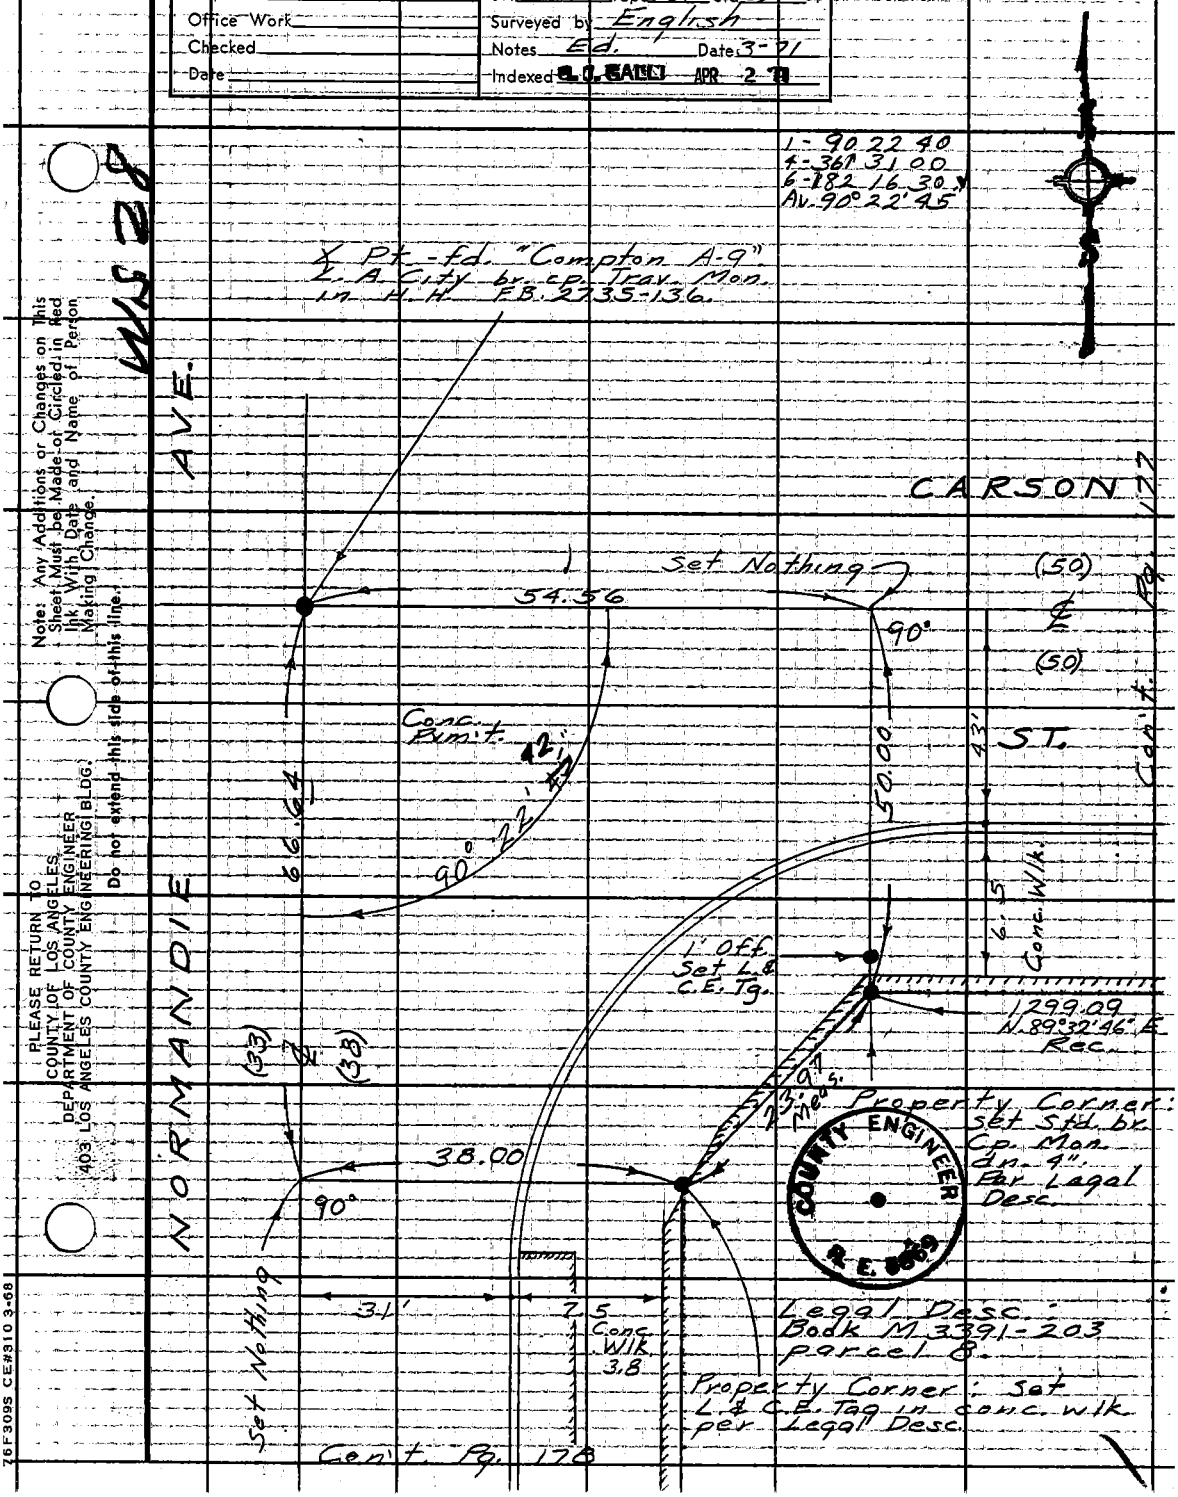

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
COUNTY OF LOS ANGELES
DEPARTMENT OF COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

76F309S CE#310 3-68

F.B. 2920 PG 176

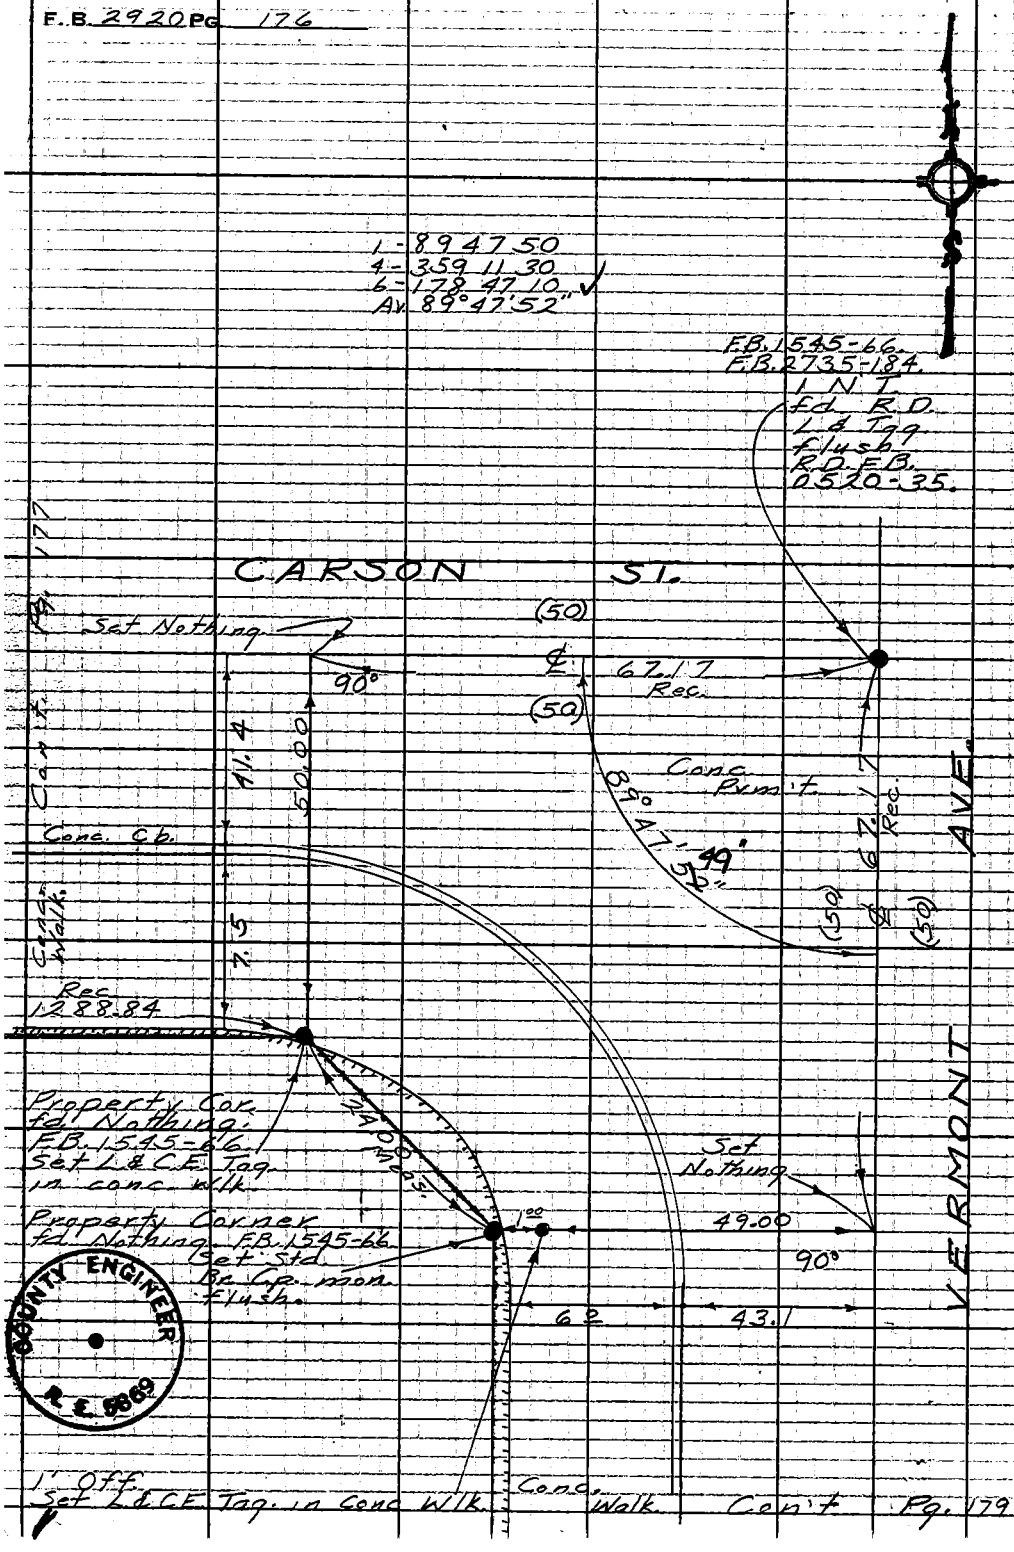

COUNTY ENGINEER
R. E. 5869

M528 B-1

PLEASE RETURN TO
COUNTY OF LOS ANGELES
DEPARTMENT OF COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by H. HOLMAN	Survey of Har. Gen. Hosp.
Map No.	JN 0022.02 Tape 0137 Std. 68 °F
Office Work	Surveyed by English
Checked	Notes Ed. Date 3-71
Date	Indexed [illegible] APR 2 '71

F. B. 2920 PG. 177

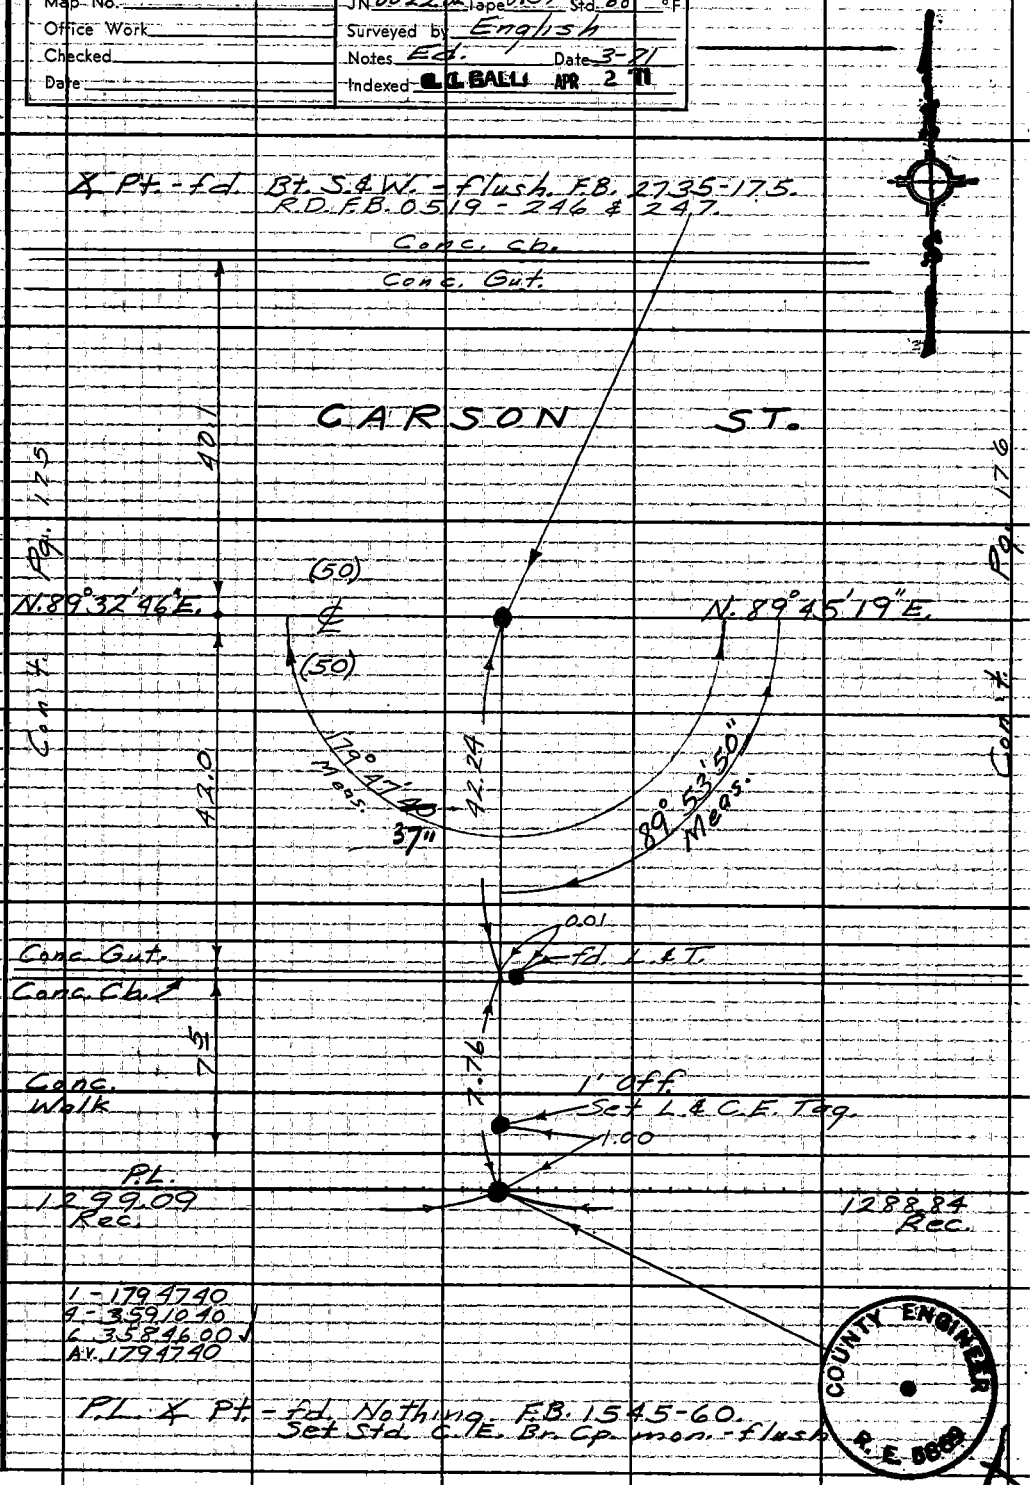

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
COUNTY OF LOS ANGELES
DEPARTMENT OF COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

76F309S CE#310 3-68

F. B. 2920 Pg. 178

Cont. Pg. 175

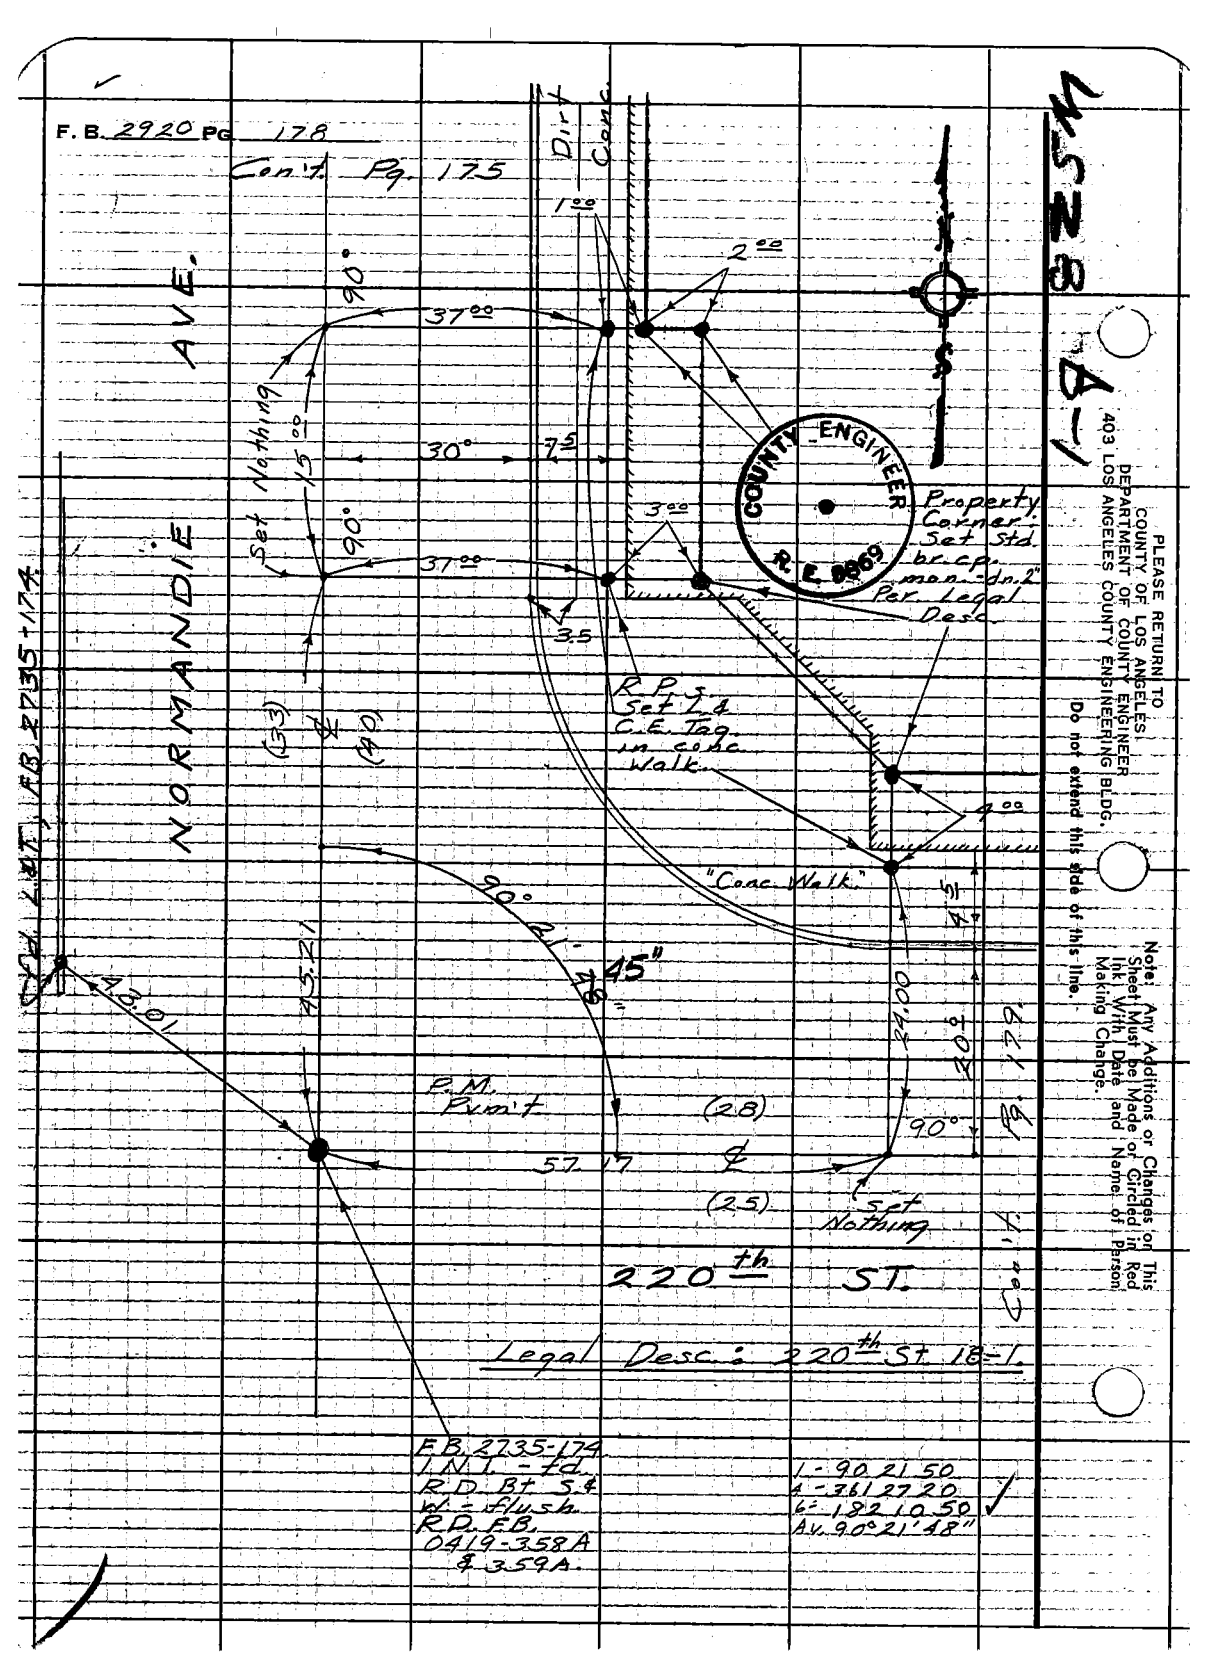

M.S. 28 18-I

PLEASE RETURN TO
COUNTY OF LOS ANGELES
DEPARTMENT OF COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by H. HOLMAN	Survey of Har. Gen. Hosp.	F. B. 2920 PG. 179
Map-No.	JN 0022.02 Tape 137 Std 68 °F	
Office Work	Surveyed by English	
Checked	Notes Ed. Date 3-71	
Date	Indexed G. L. GALLI APR 2 '71	

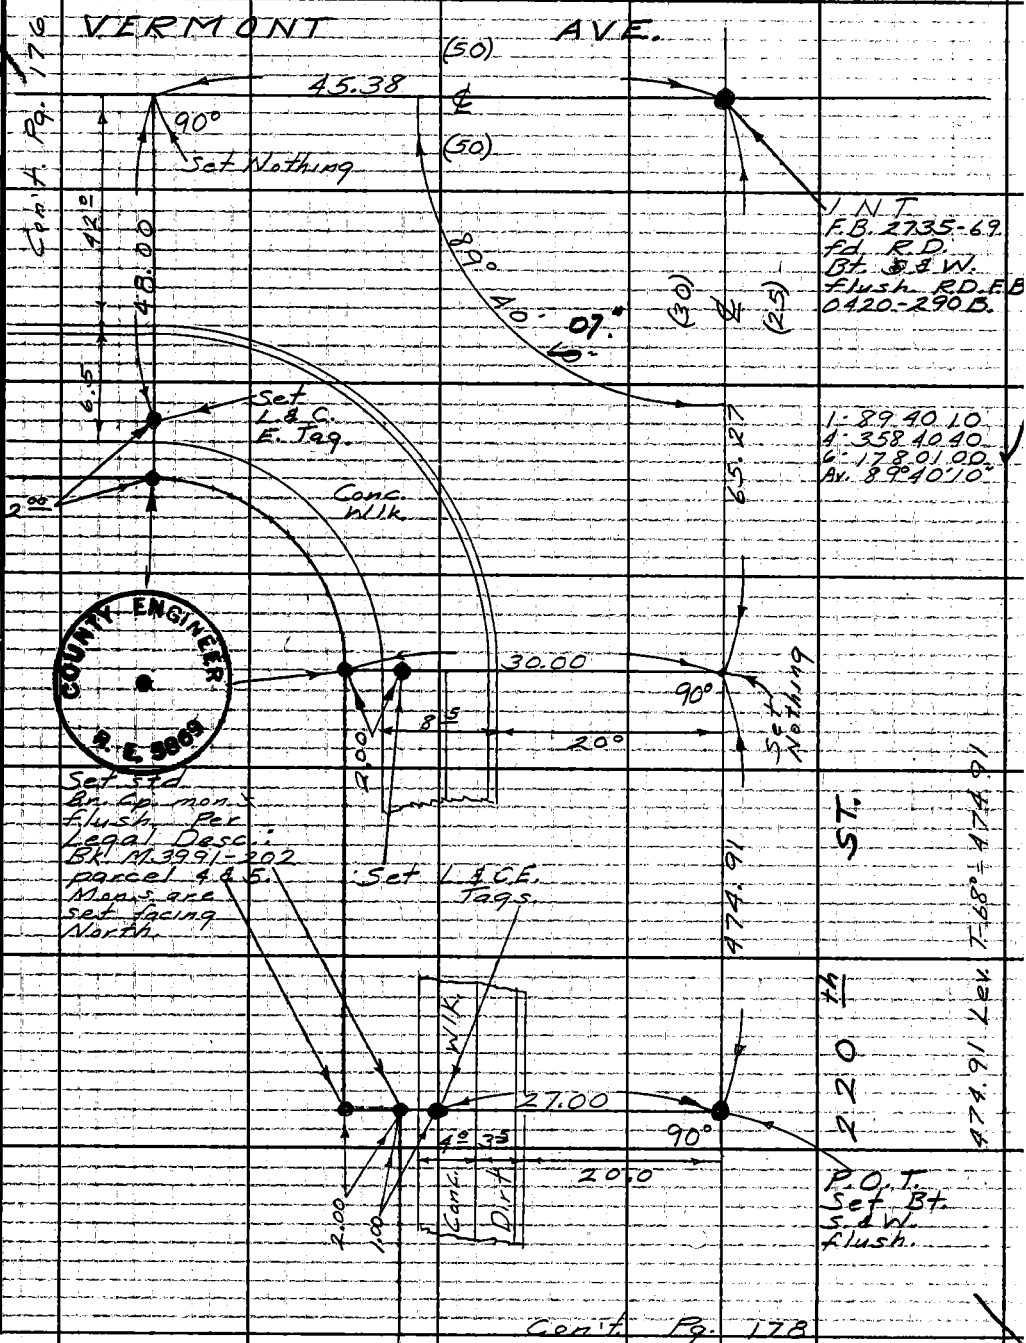

Con't. Pg. 178

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
COUNTY OF LOS ANGELES
DEPARTMENT OF COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

76F309S CE#310 3-68

Notes Ck'd by	Survey of Harbor Gen. Hosp.	F. B. 2920 Pg. 181
Map No.	J.N. 0722.96 Tape 0267 Std. 68 °F	
Office Work	Surveyed by English	
Checked	Notes Ed. Date 6-71	
Date	Indexed G. J. GAHN JUN 24 '71	

HARBOR GENERAL HOSPITAL

J.N. 0722.96

New Psychiatric Service Building Corners.

June 18, 1971
English.
Shoemaker
Clifford

Ref.:
"Geo. T. Kirkpatrick"
Plans - Sh. #1.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

FILE AS RETURN TO
COUNTY OF LOS ANGELES
DEPARTMENT OF COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

F. B. 2920 PG. 182

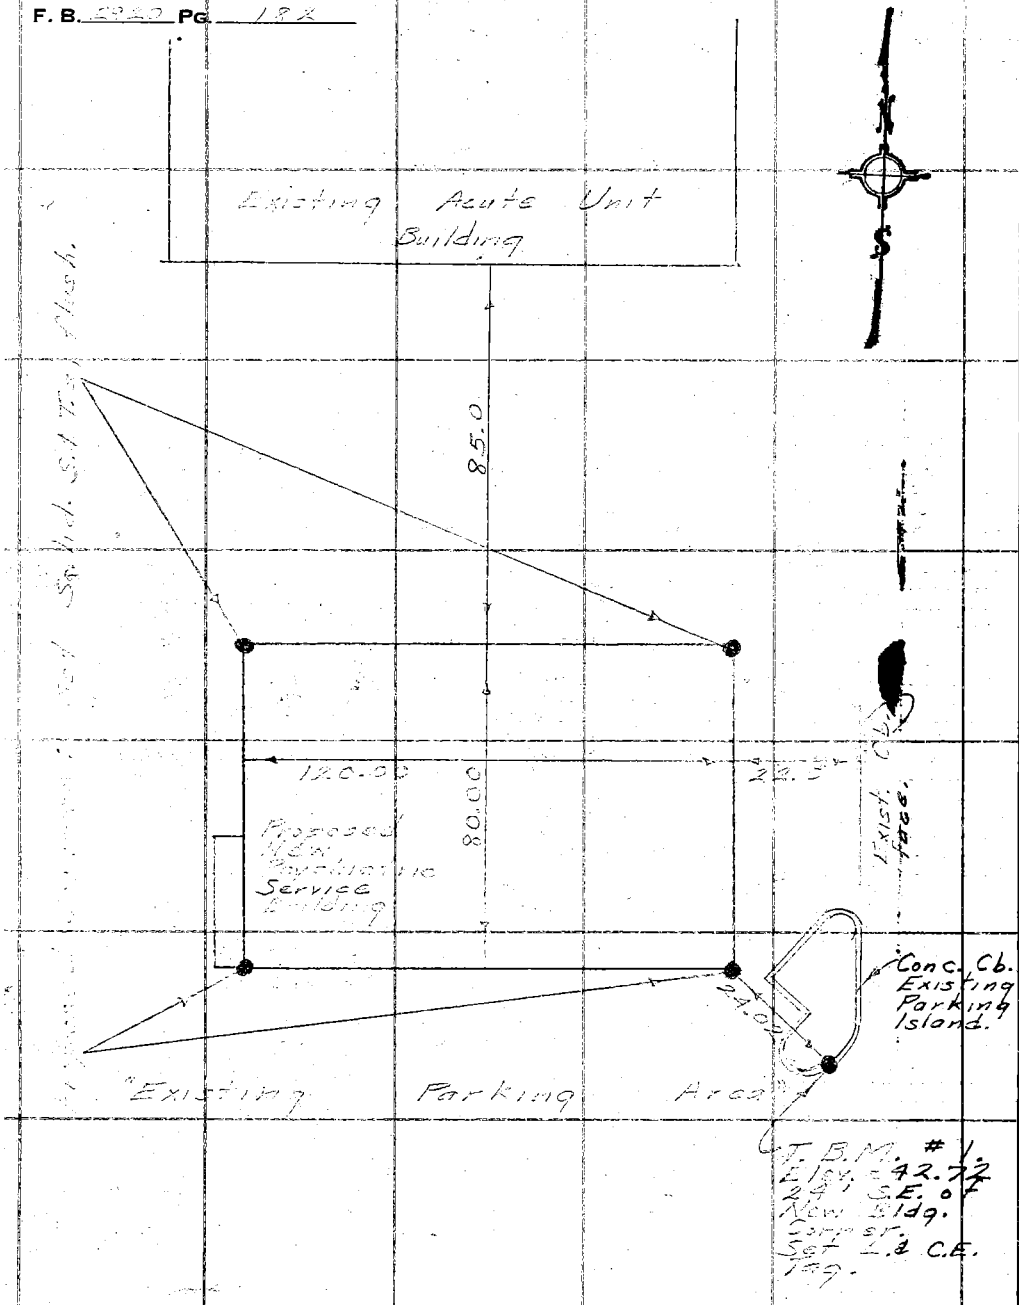

Vertical Control:

[illegible] S.M., el. = 42.45, Pg. [illegible]
L.A. Dept. of [illegible] Works
A [illegible] Br. Tab., 1.3 N. of Flag
Pole 100'± S.E. of main Entr.
[illegible] Harb. Genl. Hosp. [illegible]
[illegible]

PLEASE RETURN TO
COUNTY OF LOS ANGELES
DEPARTMENT OF COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.
