Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Harold Drive Ln. 1225
JN Tape Std °F
Surveyed by HH
Notes Date
Indexed C. J. GALLI APR 14 67

F. B. PG. 3

~~FB 3337~~

Harold Drive Ln. 1225

PRELIMINARY (2nd Section)
INDEX FB 3350-6
~~FB 3350-6~~

NOTE: SEE FB 3337 FOR 1st Section of Survey
" " 3345 " 2ND " "

REFERENCES:

FB 2184
ST 2

Allignment:
FB 3350 2-26 ℄ Storm Drain Redding Ave to Toll Dr. ℄ & Toll Dr to W'LY TR. LINE

1091 MAP

FB 3350- 27-40 ℄ Storm Drain Redding Ave to Toll Dr. ℄ & Toll Dr to W'LY TR. LINE
79-80 Redding Ave ℄ ℄
87-90 ℄ Toll Dr.
103-104 ℄ Toll Dr.
113-116 W'LY LINE TR. 1091

X-SECTIONS
FB 3350- 41-78 ℄ Storm Drain Redding Ave to Toll Dr. ℄ & Toll Dr to W'LY TR. LINE.
81-86 Redding Ave ℄ ℄
91-98 ℄ Toll Dr.
99-102 drain easement N. & S. along Common ℄ of Lots 11 & 12 TR 1091
105-108 ℄ Toll Dr.
109-116 drain easement - Profile
117-124 W'LY LINE TR. 1091

FOR DESIGN PURPOSES ONLY

HH SPRIGGS
MD WALSH
BR THORSMAN
TM HENSLEY

Microfilmed March 85

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

F. B. 3350 PG 4

Notes Ck'd by: W. EDMONDSON
Map No.
Office Work
Checked
Date

Survey of Arroyo Dr SD No 1225
JN 611225 Tape 0216 Std 68 °F
Surveyed by H.H. Springs
Notes AHS Date 3-67
Indexed C. J. GALLI

F. B 3350 PG. 5

Note: Any Additions or Changes on this Sheet Must be Made by Order of & Are to be Initialed, Dated and Name of Person Making Change

Please return to
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.
Do not detach this part of this line

FOR DESIGN PURPOSES ONLY

N611225

ARROYO DR. SD. NO. 1225
PRELIMINARY - (3RD SECTION)

NOTE: SEE FB 3338 FOR 1st SECTION SURVEY
SEE FB 3345 FOR 2ND SECTION SURVEY

STORM DRAIN "A":
POT - "A" & POT Redding Ave. 1346
S. W'LY & INTER. @ Teresita Ave (TR 532)
N. W'LY. along Natural (& existing water course to POT & drain easement
- POT Toll Drive (2946' E'LY of W'LY line TR 11091)
Above includes # Toll Drive Tegner Dr W'LY to Tract Line

INDEX: FB 3345-10
FB 3350-6

LOCATION OF IMPROVEMENTS: FB 3350-27-40
X SECTIONS: FB 3350-41-73

H.H. Springs
M.P. Walsh
D.R. Workman
P.L. Bradley

X

7 OF 3095 CE #3101 1-65

F. B. 3350 Pg. 6

EN 61225

Bixby Dr. SD No. 1225

Index

Cont. Bot. FB 3345-10

Sheet 1

Mohawk Drive

Texas Street

Bixby Dr.

Bailey

Pq 10

Pq 11

Pq 12

Pq 13

Pq 14

Pq 15

Pq 16

Pq 17

Pq 20

Pq 21

Pq 22

Pq 23

Pq 24

Pq 25

Pq 26

Pq 27

Pq 28

Pq 29

Pq 30

Pq 31

Pq 32

Pq 33

Pq 34

Pq 35

Pq 36

Pq 37

Pq 38

Pq 39

Pq

Notes Ck'd by W. EDMONDSON	Survey of Aaron DSDN-1725
Map No.	JN 61225 Tape 02LL Std 68 °F
Office Work	Surveyed by HAK RIPPS
Checked	Notes HLC Date 3-1-67
Date	Indexed C. J. GALLI

F. B 3350 Pg. 7

Cont'd FB 3345-48 Bottom

Set Lg BY SpK in T Flush

Edge Pvmt.

132.32 Line

Transit

Redding Ave. ℄

(60)

52.2'

(30)

Cont'd Pg. 8

166.55 Calc.

89-24-30 Calc.

166.70 Calc.

Impassible Not Set

FOR DESIGN PURPOSES ONLY

25.27 Line @ 0.22 & 25.27

139.27

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

76F309S CE#310 1-65

F. B 3350 PG 8

1. 134-43-00
4. 178-51-00
6. 88-16-30
A. 134-42-45

COUNTY ENGINEER
R. E. 5868

Found Iron Pipe
Mon in Mh
Used For Line
SE NW, & W.
FB 2154-26
1512-16

Set Nail & Tag
+ Conc Wall Cap

Found Iron Pipe
Mon in Mh
FB 2184-24

Set Nail & Tag
+ @ Edg

Cont. Rt. Pg. 10

250.80 R
140.30 R

250.68
436.38
21.79
60.32
134-42-45
86.32
54.06
80.85
32.47
32.64
Toll
Drive
Building Line
Center Dr.
Found Iron Pipe
FB 2181-26
Found Iron Pipe
FB 2154-26
1.39
Found 2"x2" Spike Tag
In Conc Flr
Found Nail & Tag
Flush
Used For Line W/X

Cont. Rt. Pg. 9

Cont. Rt. Pg. 7

S 88° 16' 32" E 1211.79

FOR DESIGN
PURPOSES ONLY

1. 31-29-00
4. 125-55-00
6. 188-52-30
A. 31-28-45

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd By W. EDMONDSON	Survey of Arroyo De S DNo 1725
Map No.	~~JN 611725~~ Tape 0211 Sta 68 °F
Office Work	Surveyed by HH Gomez
~~Checked~~	~~Notes~~ Date 3-22-67
Date	Indexed C. J. GALLI

F. B. 3350 PG. 9

FOR DESIGN PURPOSES ONLY

COUNTY ENGINEER R.E. 5869

Ed SHCE Mon 4" DF B2184-25 1 1/2-14.15 MSR TOP LINES

Conc Valley

Fd L&TK FB2184-25

Conc Drive

Fd L&TK FB2184-25

Fd L&TK FB2184-25

Road

37.33

96.73

322.64

TESTNER DRIVE

39.7

Fd L&TK-Bot Sleep FB2184-25

Fd Spike W-Flush FB2184-25

322.64 @ 999-999 E 322.44

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO LOS ANGELES COUNTY ENGINEER 408 LOS ANGELES COUNTY ENGINEERING BLDG.

75F3093 CE#310 1-65

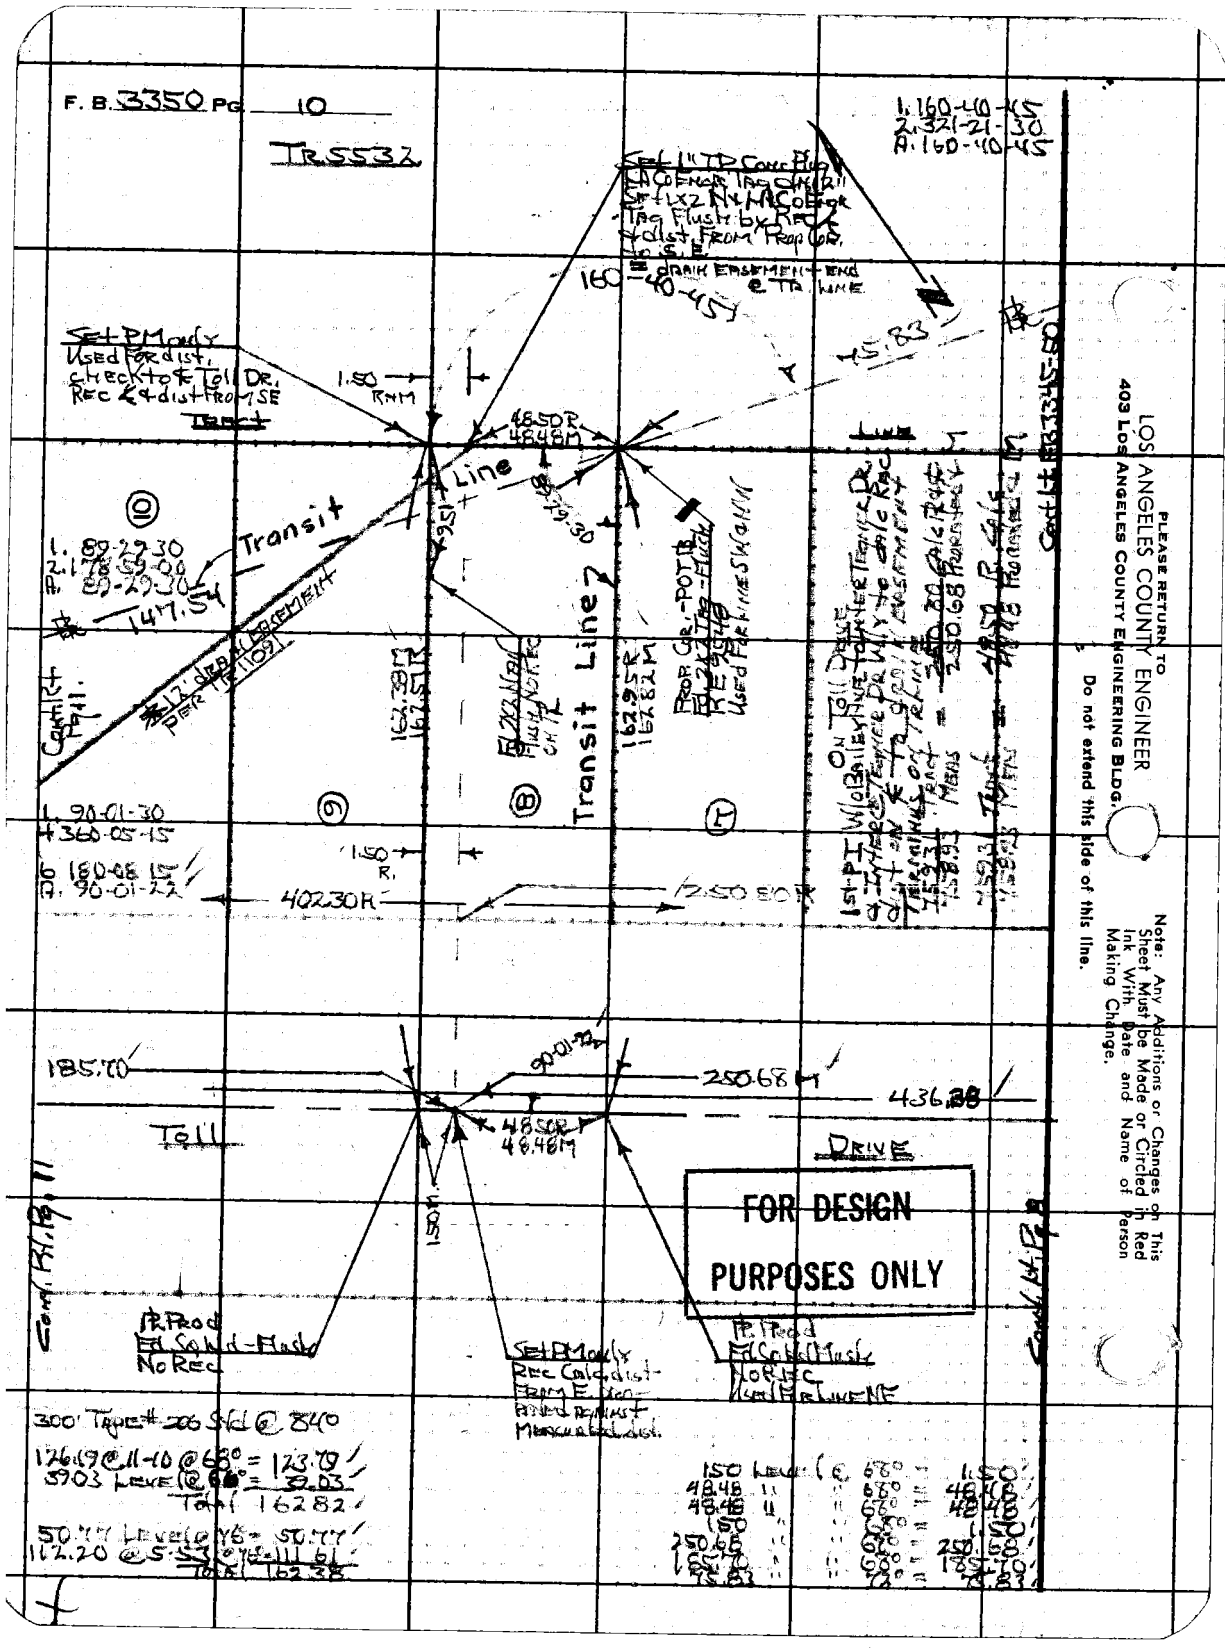

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

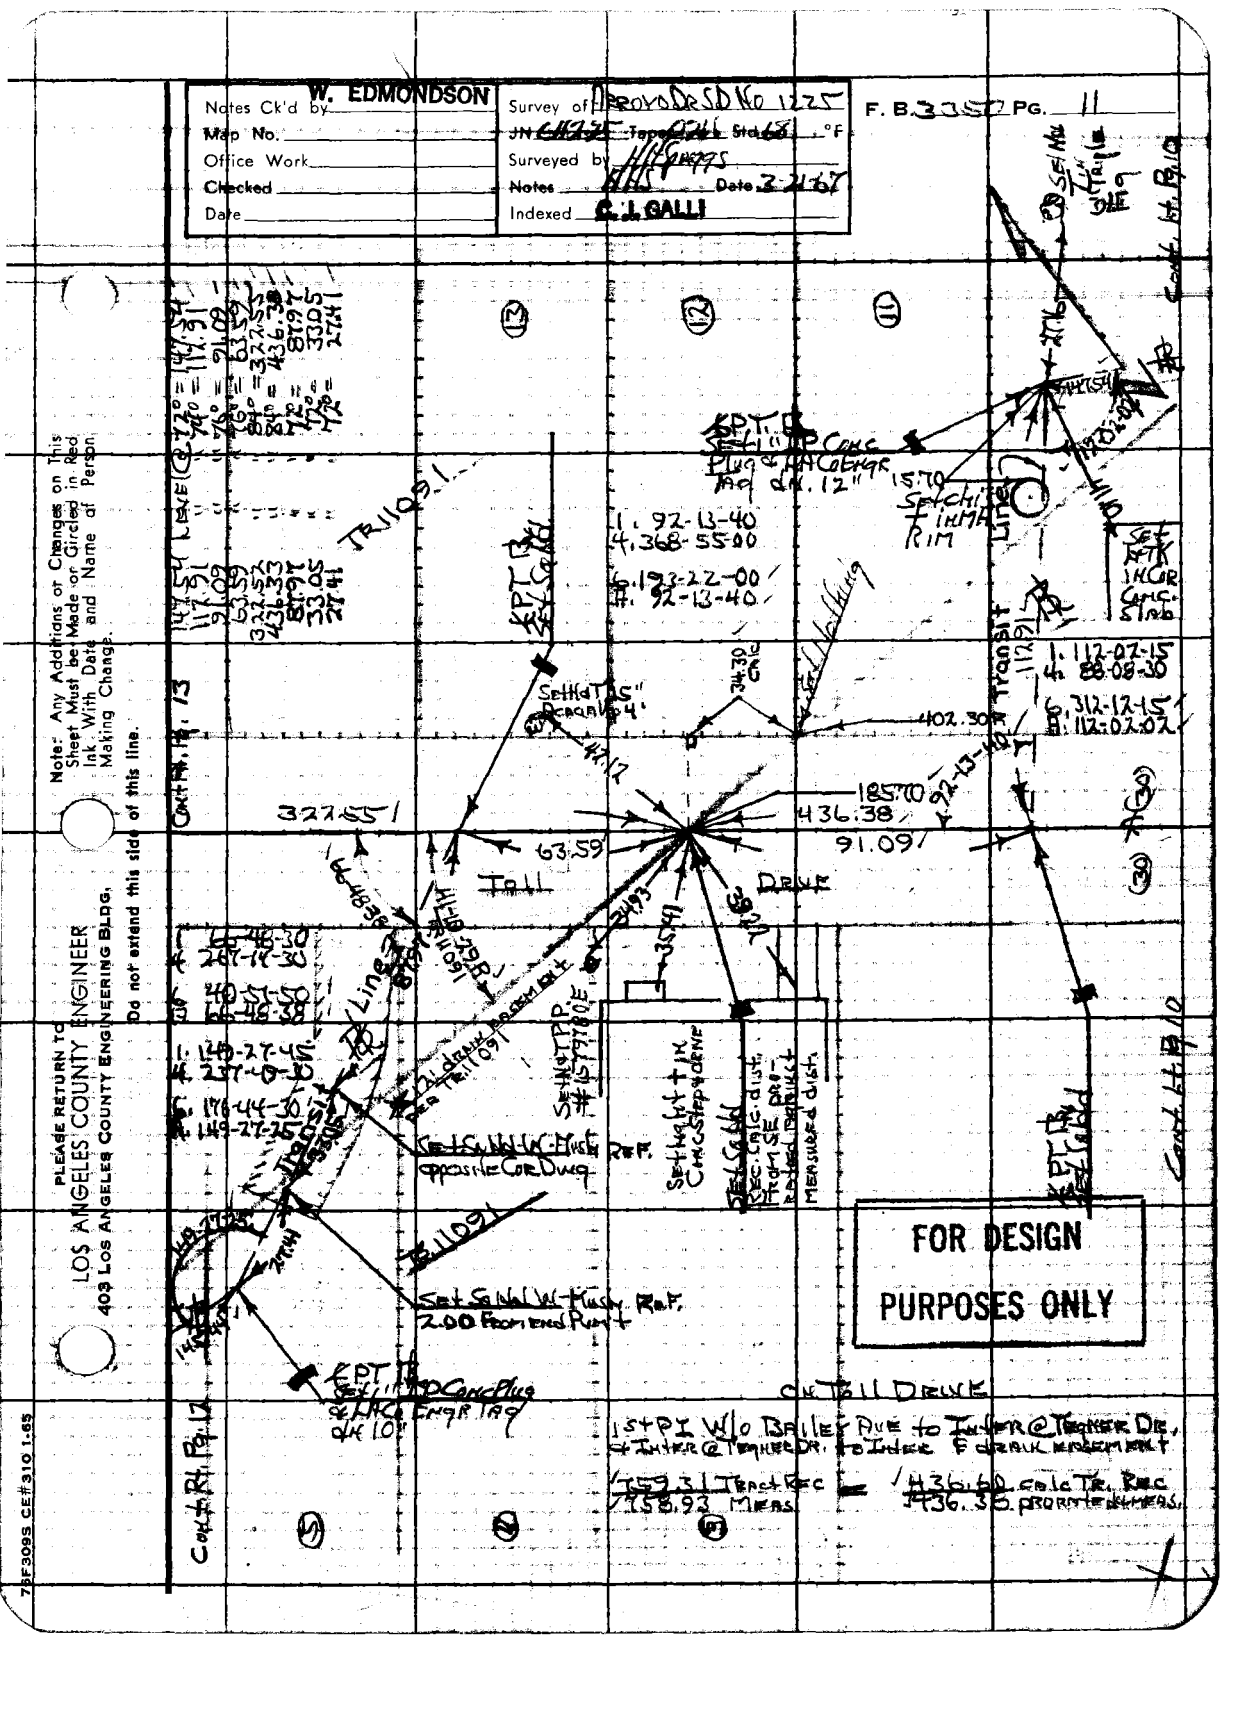
W. EDMONDSON
Notes Ck'd by
Map No.
Office Work
Checked
Date
Survey of PROVO DR SD No 1225
JN C4925 Topo C4U Sta 68 °F
Surveyed by
Notes Date 3-24-67
Indexed C. J. GALLI
F. B. 3352 PG. 11
Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.
Do not extend this line.
PLEASE RETURN TO LOS ANGELES COUNTY ENGINEER 403 Los Angeles County Engineering Bldg.
FOR DESIGN PURPOSES ONLY
Cont. Rt. 13
Cont. Rt. 17
Cont. Rt. 10
Tall Drive
Set Spike & Washer Ref. Opposite Cor. Dwg
Set Spike & Washer Ref. 2.00 From End Point
Set Spike & Washer Ref. Cor. Stepped One
Set Tack & Tag Ref. Cor. Stepped One
Set Tack & Tag Ref. Cor. Stepped One
Set Tack & Tag

F. B. 3350 Pg. 12

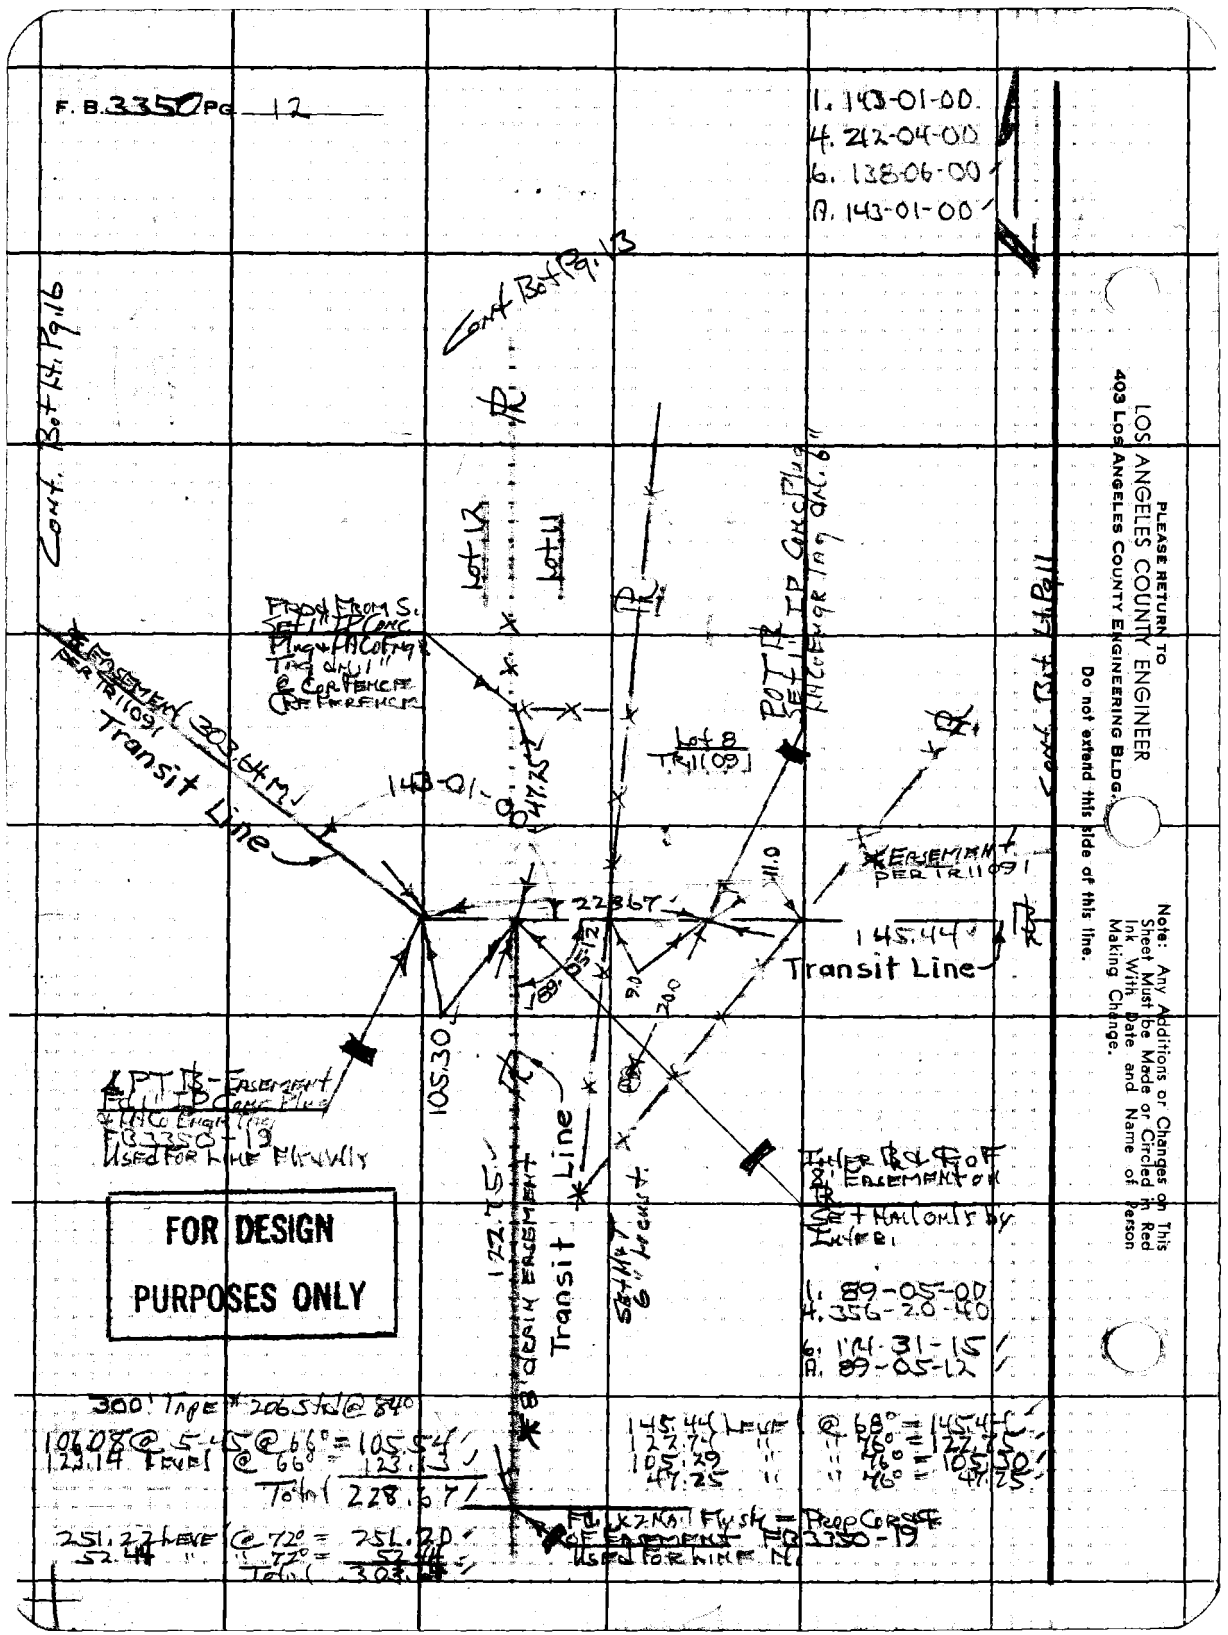

LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

PLEASE RETURN TO

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

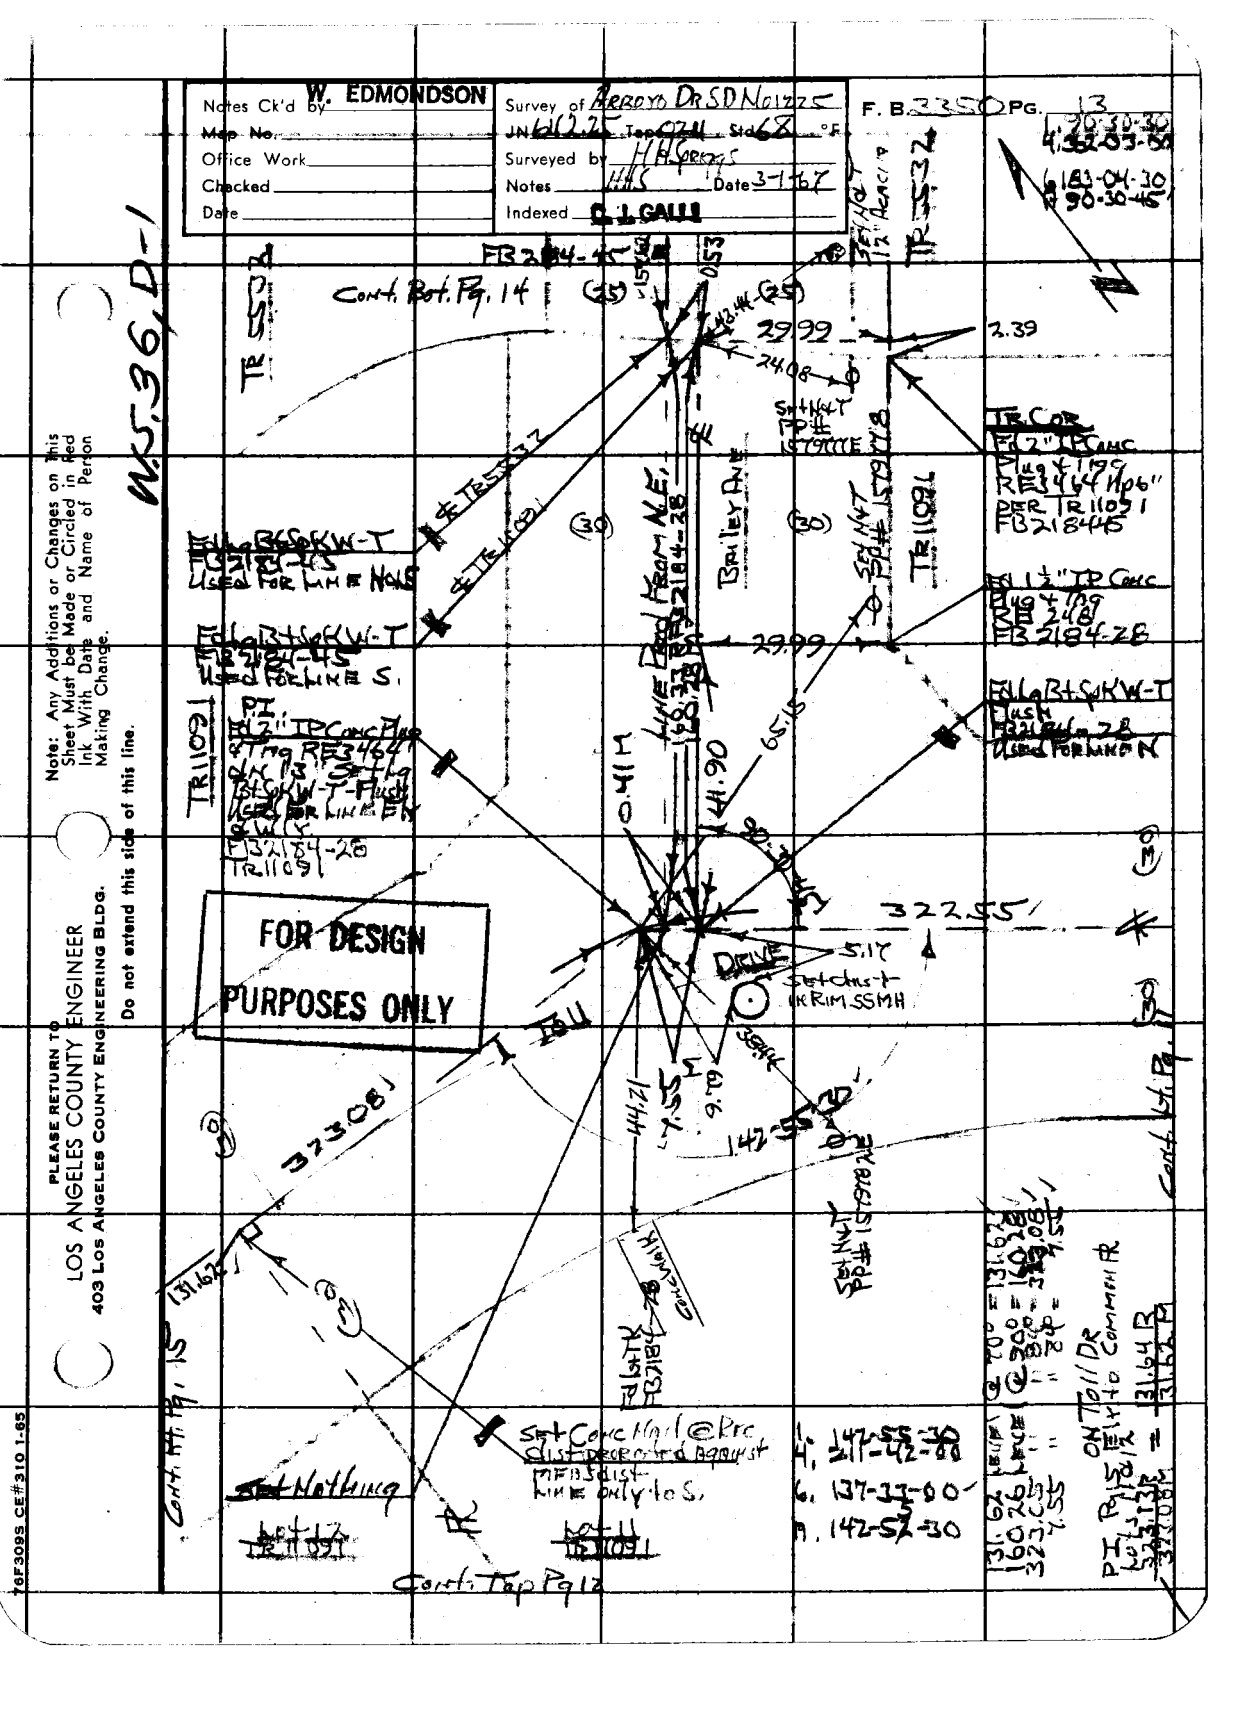
W. EDMONDSON
Notes Ck'd by
Map No.
Office Work
Checked
Date
Survey of Arroyo Dr SD No 1275
JN 1402.25 Top 0711 Std 68 °F.
Surveyed by H.H. Jones
Notes LLLS Date 3-1-67
Indexed C. L. GALLE
F. B. 2350 Pg. 13
W5.36, D-1
Cont. Bot. Pg. 14
Cont. Top Pg 12
Cont. Rt. Pg. 15
Cont. Lft. Pg. 11
Bailey Ave
Lower Broad Hearn N.E.
FOR DESIGN PURPOSES ONLY
Set Nothing
Set Conc Nail @ Pro
Set Catch-t
Set Conc Nail
Tr 11091
Tr 11084
Tr 11085
Tr 11087
Tr 11088
Tr 11089
Tr 11090
Tr 11092
Tr 11093
Tr 11094
Tr 11095
Tr 11096
Tr 11097
Tr 11098
Tr 11099
Tr 11100
Tr 11101
Tr 11102
Tr 11103
Tr 11104
Tr 11105
Tr 11106
Tr 11107
Tr 11108
Tr 11109
Tr 11110
Tr 11111
Tr

F. B. 3350 PG 14

T1S R36 BP-1

Stucco Church Bldg

Fd 4TK No Rec

MOONEY

DRIVE

SET CHISELL + 5" MH RIM

SET CHISELL + IN CONC FENCE POST

7.38

38.39

46.46

33.65

FB 2184-46

NO REC FD 4TK CONC

FD SLD LAC CO ENGR TUNNEL MH FB 2184-58

COUNTY ENGINEER R. E. 5869

FD 4TK FB 2184-46

BAILEY AVE

319.95 R

CONC WALL

FD SLD LAC CO ENGR TUNNEL MH FB 2184-46

FOR DESIGN PURPOSES ONLY

TERESA

AVE

CONC WALK

CONC WALK

157.62 R FB 2184-45

FD 4TK FB 2184-46

FD 4TK FB 2184-46

TR 5532

TR 5532

Cont. Top Pg. 13

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd By: W. EDMONDSON	Survey of: Vermont Ave No 1275	F. B. 3250 Pg. 15
Map No.	JN 6117.25 Tape 11 Std 68 °F	
Office Work	Surveyed by: H.A.C.	
Checked	Notes: Date 3-2-67	
Date	Indexed: C. L. GALLI	

W.S. 39, D-1

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

FOR DESIGN PURPOSES ONLY

Cont. Rt. Pg. 16

Cont. Lt. Pg. 18

Cont. Top Pg 19

Transit Line

Set Conc Nail 27' Rt. W.O. Rec RC per TR 11091 NKE Chly-Tod

PI Fd 2" IP Conc Plug & Tag NE 3464 OM 12" Dep TR 11091 FB 2169-29 Set 1/2" IP 1.5' Rt. Ext. of Tan Used for Ext. Tan. 2.300 Calc'd Ties - Husk

Set Conc Nail

Set Spike & Tag Lowe #1157 BLK

Set Spike & Tag Rec (26.49) & PT.

Set Conc Nail & Tag Lowe #1157 BLK

Set PK in Lamb Scar 0.7' E Elm 14" 6'

Set Nail & Tag #1157 BLK

Set Nail & TK in Top Conc Wall & Cor.

Searched 2' E & 1.36' N for IP Dep TR 11091 Nothing

0.78

31.07

26.49

323.08

131.62

9.00

30.08

43.49

114.16

27.27 Parallel of Ext. of Tan RC - Line Only

169-48-00

9.00 parallel of Ext of Tan RC

352.29 R TR 11091

353.30 Calc R.

353.65 MEAS

TR 11091

TR 11091

TR 11091

TRIO (-Tr. Rec.
1. 169-54-30
4. 319-38-00
6. 299-27-00
A. 169-54-30

Final
1 169-48-00
4 319-12-00
6 298-48-00
A. 169-48-00

1 @ 69.00 = 26.49
68.00 = 9.00
76.49 Level
9.00

1. 89-55-00
4. 359-39-30
6. 179-29-30
A. 89-54-55

76F3095 CE#310 1-65

F. B. 3350 PG 16

FOR DESIGN PURPOSES ONLY

Cont. Bk 48 Pg. 20

Inter ℄ Toll Dr & ℄ Creek
Set Spike-Mark
Calc dist from BC.

Set Conc Nail

274.83 Calc.

Cont. Bk 94 Pg. 17

Cont. Bk 94 Pg. 15

(3) (09)

Toll

141.90

Transit Line

DRIVE

214.16

(3) (10)

Transit Line

N 45°55'-33" W 475.57 Calc.

3-WE Calc.
3041.69
S03°04'M
14-drive ESMT
PER TR 11091

Cont. Bk 11, Pg 12

1. 48-00-00
4. 192-00-00
6. 287-59-45
8. 47-59-57

214.90 at 87° = 214.96

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd By W. EDMONDSON
Map No.
Office Work
Checked
Date

Survey of Arroyo Dr. SDM 1225
JN 611626 Tape C-1 Std 3 °F
Surveyed by Hitpaugh
Notes 1115 Date 3-2-67
Indexed C. J. GALLI

F. B. 3350 PG. 17

C-1

W.S. 36

REC TANGS.	PI
1. 156-24-00	1. 156-21-00
4. 265-35-30	4. 265-14-00
6. 218-23-30	6. 218-06-00
A. 156 23 55	A. 156-21-00

Set 1x2 Hub 1 Flush @ Rec dist (357.66) ft from E. line & 11091 Rec from East.

Set 1x2 Hub 1 Flush @ Rec dist from W. line & 11091 Rec from West.

Center L of Rec Right of Way Pipe from Rec Tangent Intersection

Set Nail in Hub 2.44 ft from Rec dist from W.

156-23-55

156-21-00 M

Transit Line

Set Cald-W Flush - Tie

Set Cald-W Flush - Tie

Set 1x2 Nail Flush @ Rec dist (357.66) ft from E. line & 11091 Rec from East.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.
Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Cont. from Bot. Pg. 20

Toll & Section Line
1. 105-35-00
4. 62-19-30
6. 273-28-45
A. 105-34-47

Additional Ties Set 1965-10-69

Fd 3" TP No Plug Flush No Rec. Used Ctr.

Set 1x2" Brass Nail Stand.

Set Cut Cross Up 0.5' Elev.

Fd 1" TP Conc Plug at LACo Engr Tag dn. 24" Rec. dist. -DRO- Pine & Dahlia St. Meas. Width of Pine St. 66' Mon. Line

105-34-47 1x2 LACo Engr Tag Flush

Transit Line 155.20

Toll Drive

Fd 3" TP Conc Plug Tag LS2661 dn. 30" -Bent Over-Located Ctr @ Mon. Vertical position

Fd 2" TP 0.2' broken off-dn. 30" @ stub No Plug or Tag Located Ctr of Stub @ Mon. Vertical position

Set 1x2" Brass Nail Stand.

Set Cut Cross on Fire Hydrant

Searched For 2" TP per TR 11091 dn. 30" Found Nothing

Set Nail by W. 199 E

Fd 3" TP No Plug Flush No Rec. Used Ctr.

Fd 3" TP No Plug No Rec. Used Ctr.

Set 1" TP Conc Plug Flush at Mon. Line dn. 18"

Set Nail by Twine

Set 1x2 N. -Stand.

Notes See also I.B. 3330-26

Fd 4" TP Conc Plug Tag LS 2104 dn. 32" Rec. dist. -DRO- Pine & Dahlia St. Meas. Width of Pine St. 66' Mon. Line

Fd 1" TP Conc Plug Flush at Mon. Line dn. 18"

Set 1x2 Brass Nail Stand.

Fd 3" TP No Plug Flush No Rec. Used Ctr.

Fd 3" TP No Plug No Rec. Used Ctr.

Set Cut Cross Up 0.4' Elev.

Fd 1" TP Conc Plug at LACo Engr Tag dn. 24" Rec. dist. -DRO- Pine & Dahlia St. Meas. Width of Pine St. 66' Mon. Line

Fd 1x2" Brass Nail Stand.

Fd 3" TP No Plug Flush No Rec. Used Ctr.

Fd 3" TP No Plug No Rec. Used Ctr.

Set 1" TP Conc Plug Flush at Mon. Line dn. 18"

Set Nail by Twine

Set 1x2 N. -Stand.

Notes See also I.B. 3330-26

Fd 4" TP Conc Plug Tag LS 2104 dn. 32" Rec. dist. -DRO- Pine & Dahlia St. Meas. Width of Pine St. 66' Mon. Line

Fd 1" TP Conc Plug Flush at Mon. Line dn. 18"

Set

76F309S CE#310 1-65

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink. With Date and Name of Person Making Change.

Do not extend this side of this line.

Notes Ck'd W. EDMONDSON
Map No.
Office Work
Checked
Date

Survey of
Surveyed by
Notes
Indexed

F. B3350 Pg. 19

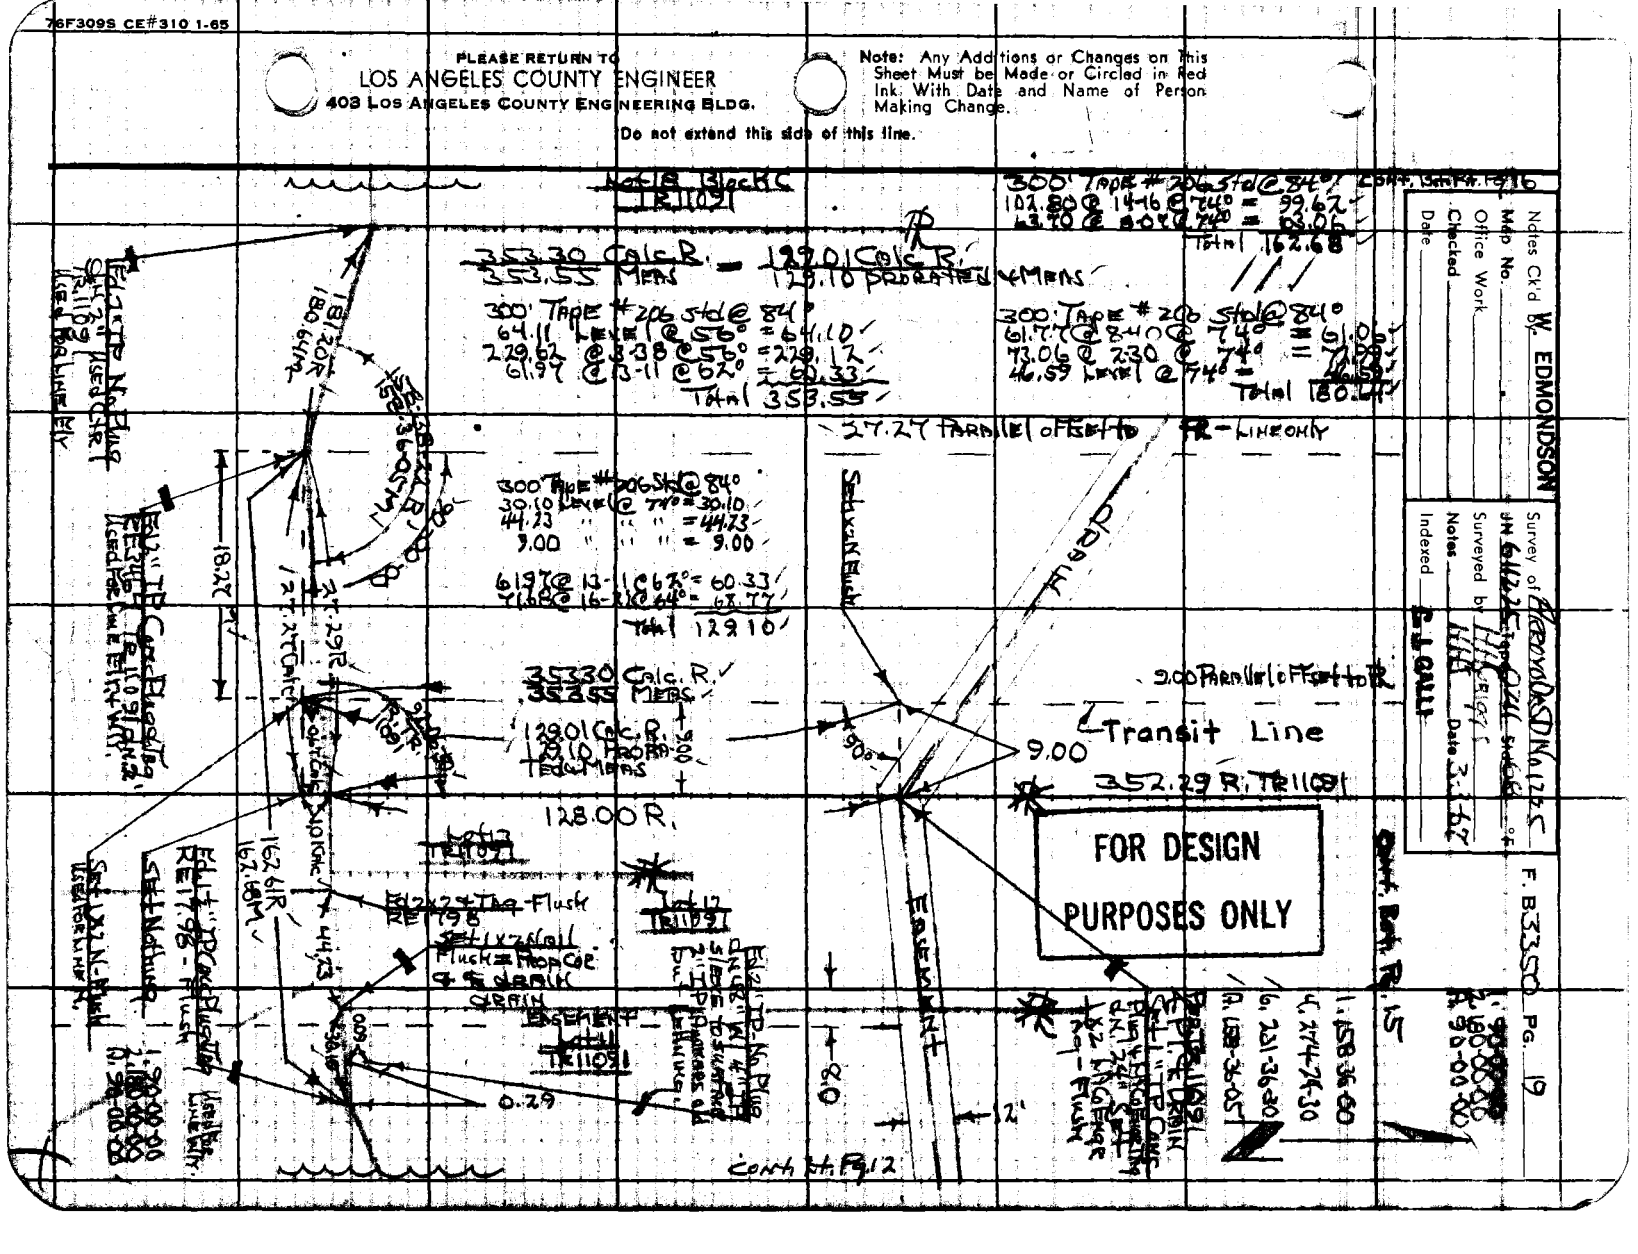
Lot B Block C
TR11021
353.30 Calc R.
353.55 Mens
129.01 Calc R.
129.10 Prorated Mens
300' Tape #206 Std @ 84°
64.11 Level @ 56° = 64.10
229.62 @ 3.38 @ 56° = 229.17
61.97 @ 13-11 @ 62° = 60.33
Total 353.55
300' Tape #206 Std @ 84°
102.80 @ 14-16 @ 74° = 99.67
63.70 @ 80-10 @ 74° = 63.06
Total 162.68
300' Tape #206 Std @ 84°
61.77 @ 84° @ 74° = 51.06
73.06 @ 2.30 @ 74° = 72.99
46.59 Level @ 74° = 46.59
Total 180.64
27.27 Parallel of Ctr Ln to FR-Line Only
Set X-Mark
Easement
2.00 Parallel of Ctr Ln to FR
Transit Line
9.00
352.29 R. TR11021
FOR DESIGN PURPOSES ONLY
Ctr. Ln. Rd. 15
Found Tack
Found Tack Flush
Set 1x24 Lag Flush
Set 1x24 Lag Flush with Top of Curb & Grade
Set 1x24 Lag
Found 1x24 Lag Flush
Found 1x24 Lag
Found 1" IP Flush
Found 1" IP
Found 3/4" IP
Found 3/4" IP Flush
Found 3/4" IP Flush with Top of Curb & Grade
Found 3/4" IP with Top of Curb & Grade

F. B. 3350 Pg. 20

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

FOR DESIGN PURPOSES ONLY

Set Nail

Fd. 3/4" IP Conc Plug & TK Fd 2184-6 Used For NWE S.

Fd. 1" IP Conc Plug & Tag In Conc RE 122 dH 4"

Fd. 3/4" IP Conc Plug & LACo Engr Tag Dated FD 2184-61

(N.W.C. of Tr. 11091) Fd. 1" IP - 1" Conc Plug & Tag Up 3.1' RE 3464 Origin per Tract 11091 Used For NWE S.

Set 1" IP Conc Plug & LACo Engr Tag Dated 12 Used For Line NW & SE Calc Rec Dist - Monuments Against Meas. Dist From N.

Set 1 X 2 Nail

POT - KPT Set Nail

Set 1" IP Conc Plug & LACo Engr Tag dated 12

Set 1 X 2 Nail

Tr. 11091

Tr. Nwe

Tr. 11091

Tr. 11091

Tr. 11091

Notes Ck'd by W. EDMONDSON
Map No.
Office Work
Checked
Date

Survey of Alhambra Dr SD No. 1225
JN 61225 Topo Sta. °F
Surveyed by
Notes Date 7-3-62
Indexed C. J. GALLI

F. B. 3350 PG. 21

Cont. Bot Pg 18

300' Tape #206 Std @ 70°

154.49 Lines (Set) 0+00 = 12+00 Ahd
(2240 Set) 0+00 = 12+00 Ahd

120.95

WALNUT TR 1091

120.56

FOR DESIGN PURPOSES ONLY

0.39

Fd 3/4" IP-Flush Conc Plug & Tag LS266 (1 No Rec

0.45

0.40

Fd 2" IP O.D. Wood Plug & Tag RCE 13128 Existing wood plug is news, portions of old wood plug see evidence this is evidently same 2" IP with RE 1934 Tag per FB 2184-32

154.49 Rad

(SW Cor Lot 23 Blk KC) TR 1091 Fd 2" IP - Conc Plug & Tag S.N.I. RE 3464 Original perfect 1109 L Used for Lines.

Note: See also FB 3350-25

Fd 3/4" IP Conc Plug & Tag LS 3" FB 2184-32 Used for Lines.

SECTION LINE

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

76F309S CE#310 1-65

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

F. B. 3350 PG 22

Notes Ck'd by	Survey of Arroyo Dr SD No 1225
Map No.	JN 61225 Tape 206 Std 84 °F
Office Work	Surveyed by HHS Spraggs
Checked	Notes HHS Date 12-21-66
Date	Indexed

F. B. 3350 PG. 23

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this side of this line.

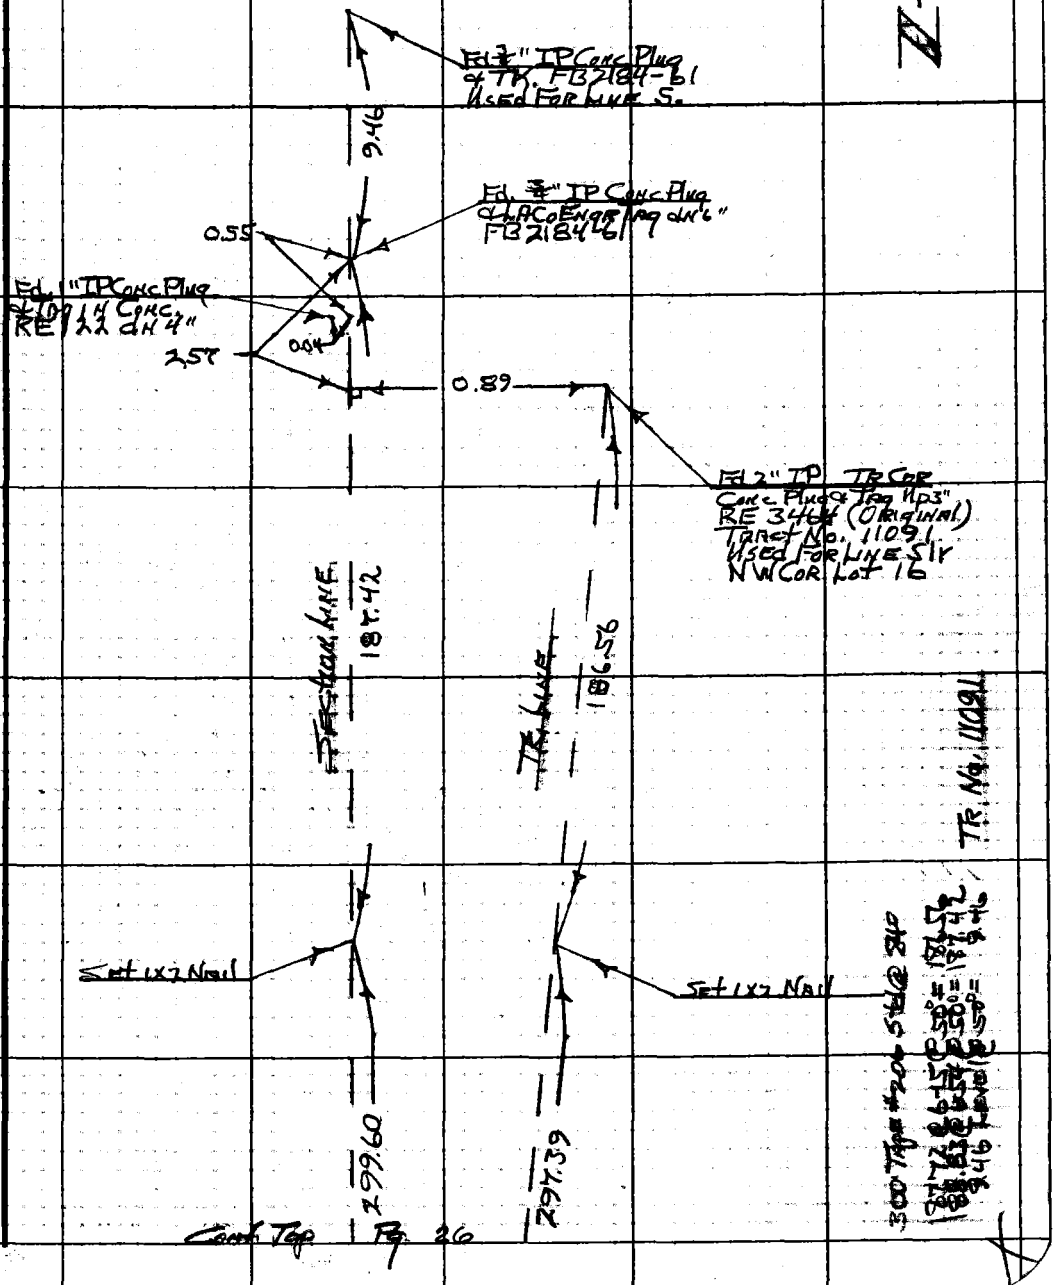

76F309S CE#310 1-65

F. B. 3350 PG 24

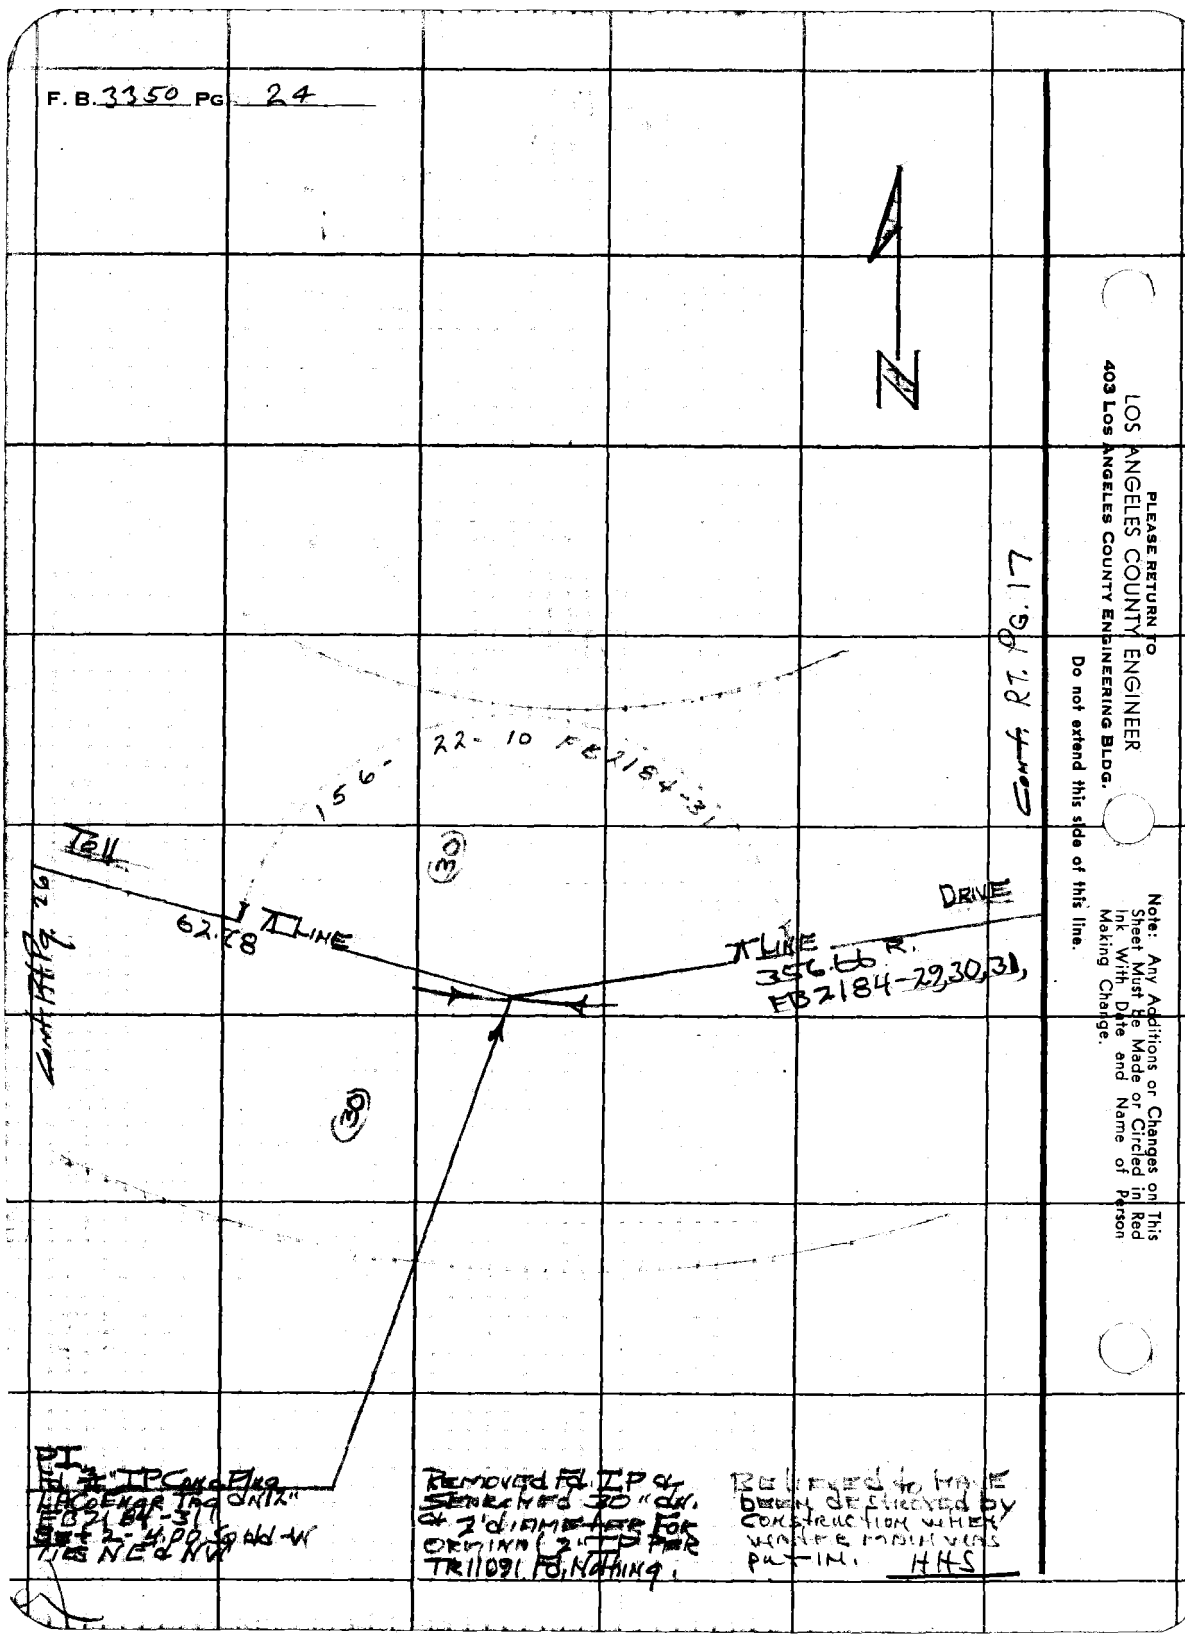

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by	Survey of Alberro Dr SD No 1225
Map No.	JN 6112.15 Tape 200 Std 84 °F
Office Work	Surveyed by HH/Grings
Checked	Notes 1HS Date 12-21-66
Date	Indexed

F. B. 3350 PG. 25

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

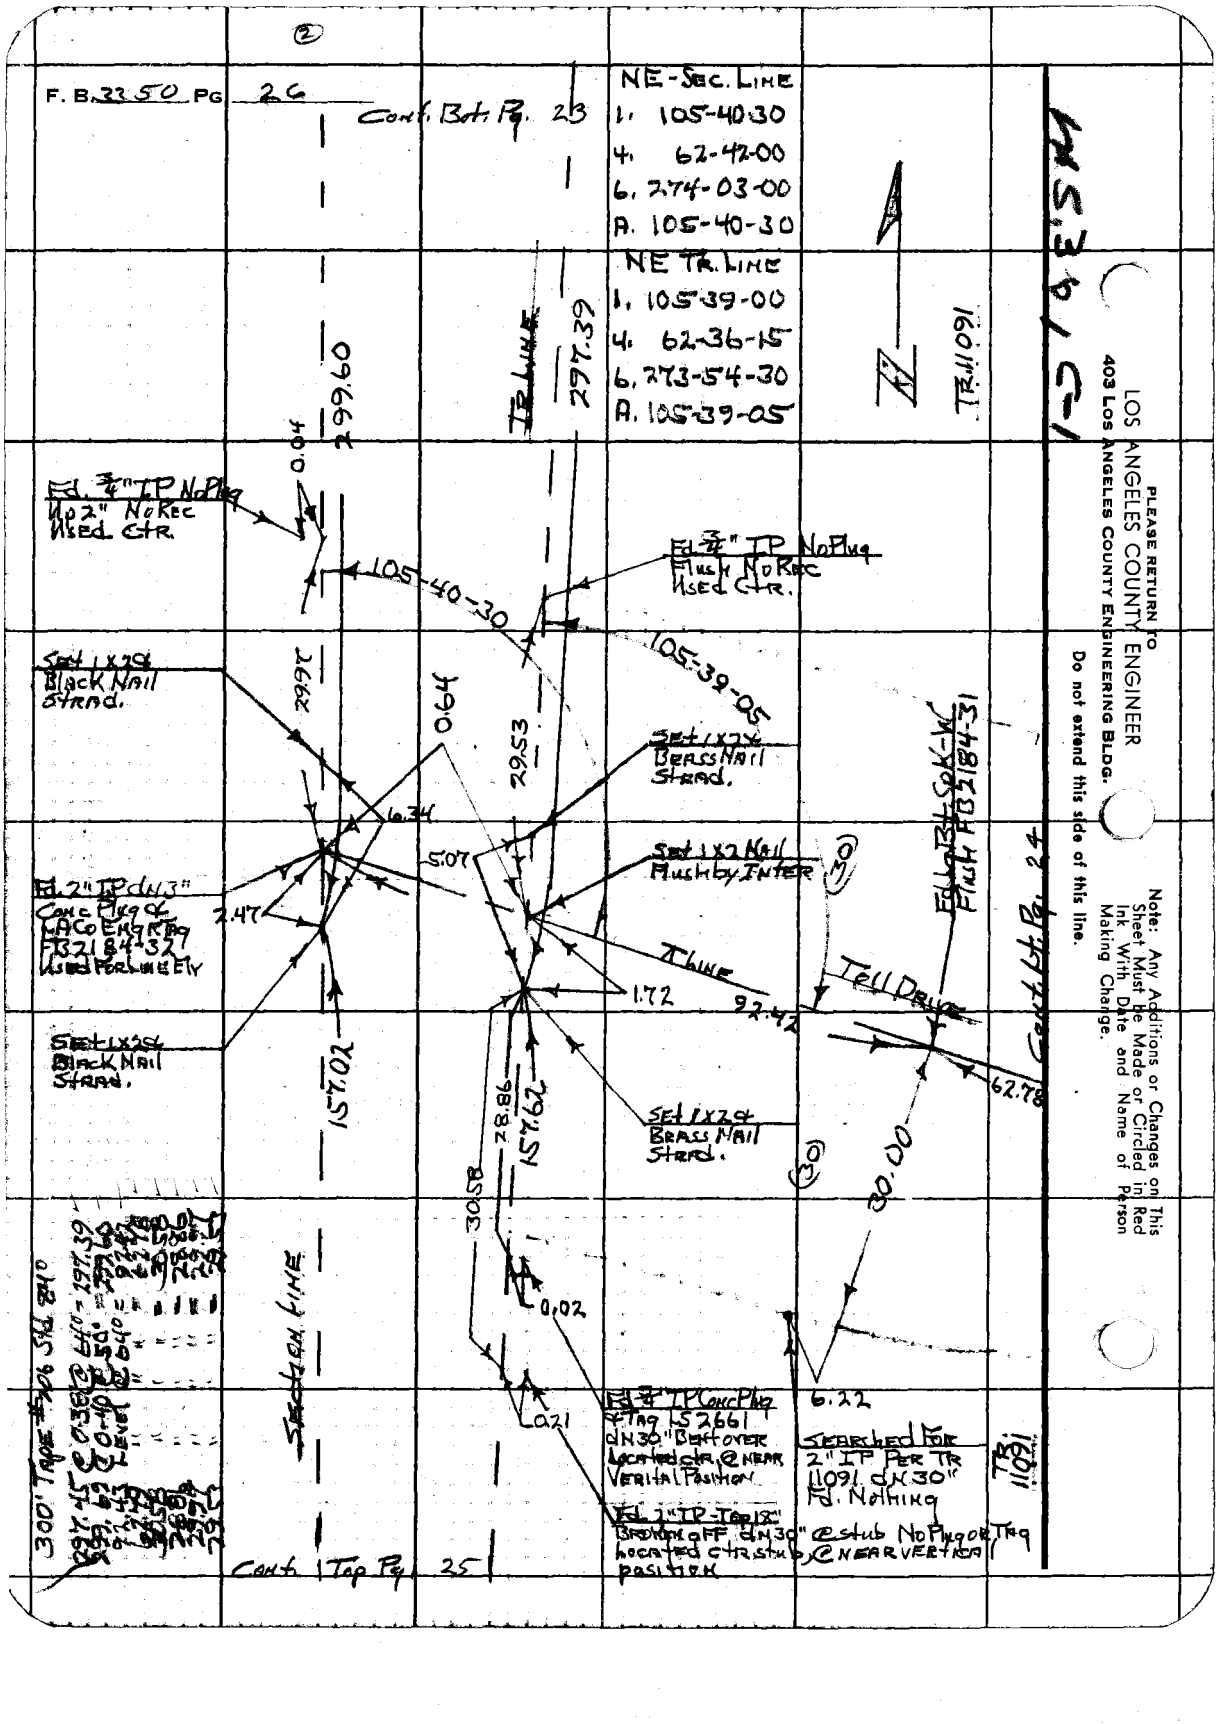
F. B. 3350 PG 26
Cont. Bot. Pg. 23
NE-SEC. LINE
1. 105-40-30
4. 62-42-00
6. 274-03-00
A. 105-40-30
NE TR. LINE
1. 105-39-00
4. 62-36-15
6. 273-54-30
A. 105-39-05
TR. 11091
299.60
0.04
297.39
Fd. 3/4" IP No Plug No 2" No Rec Used Ctr.
105-40-30
Fd. 3/4" IP No Plug Flush No Rec Used Ctr.
105-39-05
Set 1 X 24 Black Nail Stand.
299.7
0.94
29.53
Set 1 X 24 Brass Nail Stand.
6.34
5.07
Fd. 2" IP dN 3" Conc Plug & LACo Eng'rng FB 2184-32 Used For Line Ety
2.47
Set 1 X 2 Nail Flush by Fence
Fd. Nail & Shr. Flush FB 2184-31
Tell Drive
1.72
92.42
Set 1 X 24 Black Nail Stand.
157.02
157.62
28.86
30.58
Set 1 X 24 Brass Nail Stand.
62.78
30.00
0.02
0.21
Fd. 3/4" IP Conc Plug Illegible LS 2661 dN 30" Buried over Located Ctr @ Near Vertical Position
6.22
Searched For 2" IP Per Tr 11091. dN 30" Fd. Nothing
Fd. 1" IP Tag "LS" Broken off dN 30" @ Stub No Plug or Tag located Ctr Stub @ Near Vertical Position
Section Line
Cont. Top Pg. 25
300' Tape Set
Cont. Lot Pg. 24
Tr. 11091
PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.
Do not extend this side of this line.
Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by	Survey of Arroyo Dr. SD No. 1725 F. B. 3350 Pg. 27
Map No.	JN 611225 Tape Std °F
Office Work	Surveyed by [illegible]
Checked	Notes [illegible] Date 3-22-67
Date	Indexed C. J. GALLI

JN 611225

ARROYO DR SD No. 1725

~~Location of Improvements~~

~~BL~~ Sta 12+48.96 N.W'ly = POT R&R of Redding Ave. (TR. 5532) to Sta. 144+50.90 POT Toll Dr. & drain Easement (294.67 Ely of W'ly line TR 11091) Thence S Toll Dr W'ly to Tract Line = Sta. 147+45.57

Alignment FB 3345 - 48, 50, FB 3350 10, 11, 12, 16, 17, 18,

Xsections FB 3350 - 41-78

Notes: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
408 Los Angeles County Engineering Bldg.

78F309S CE#310 1-65

F. B. 3350 Pg. 28

Cont. Bot. Pg. 29

5' Wire Fence

42" RCP

1 Sty. Frame & Shingle Dwg.

2 Car Fr Frame Unfinished

SSMH

15" Pipe

Conc. Drive

8" Conc N Line

Redding Ave

Cont FB 3345 67

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

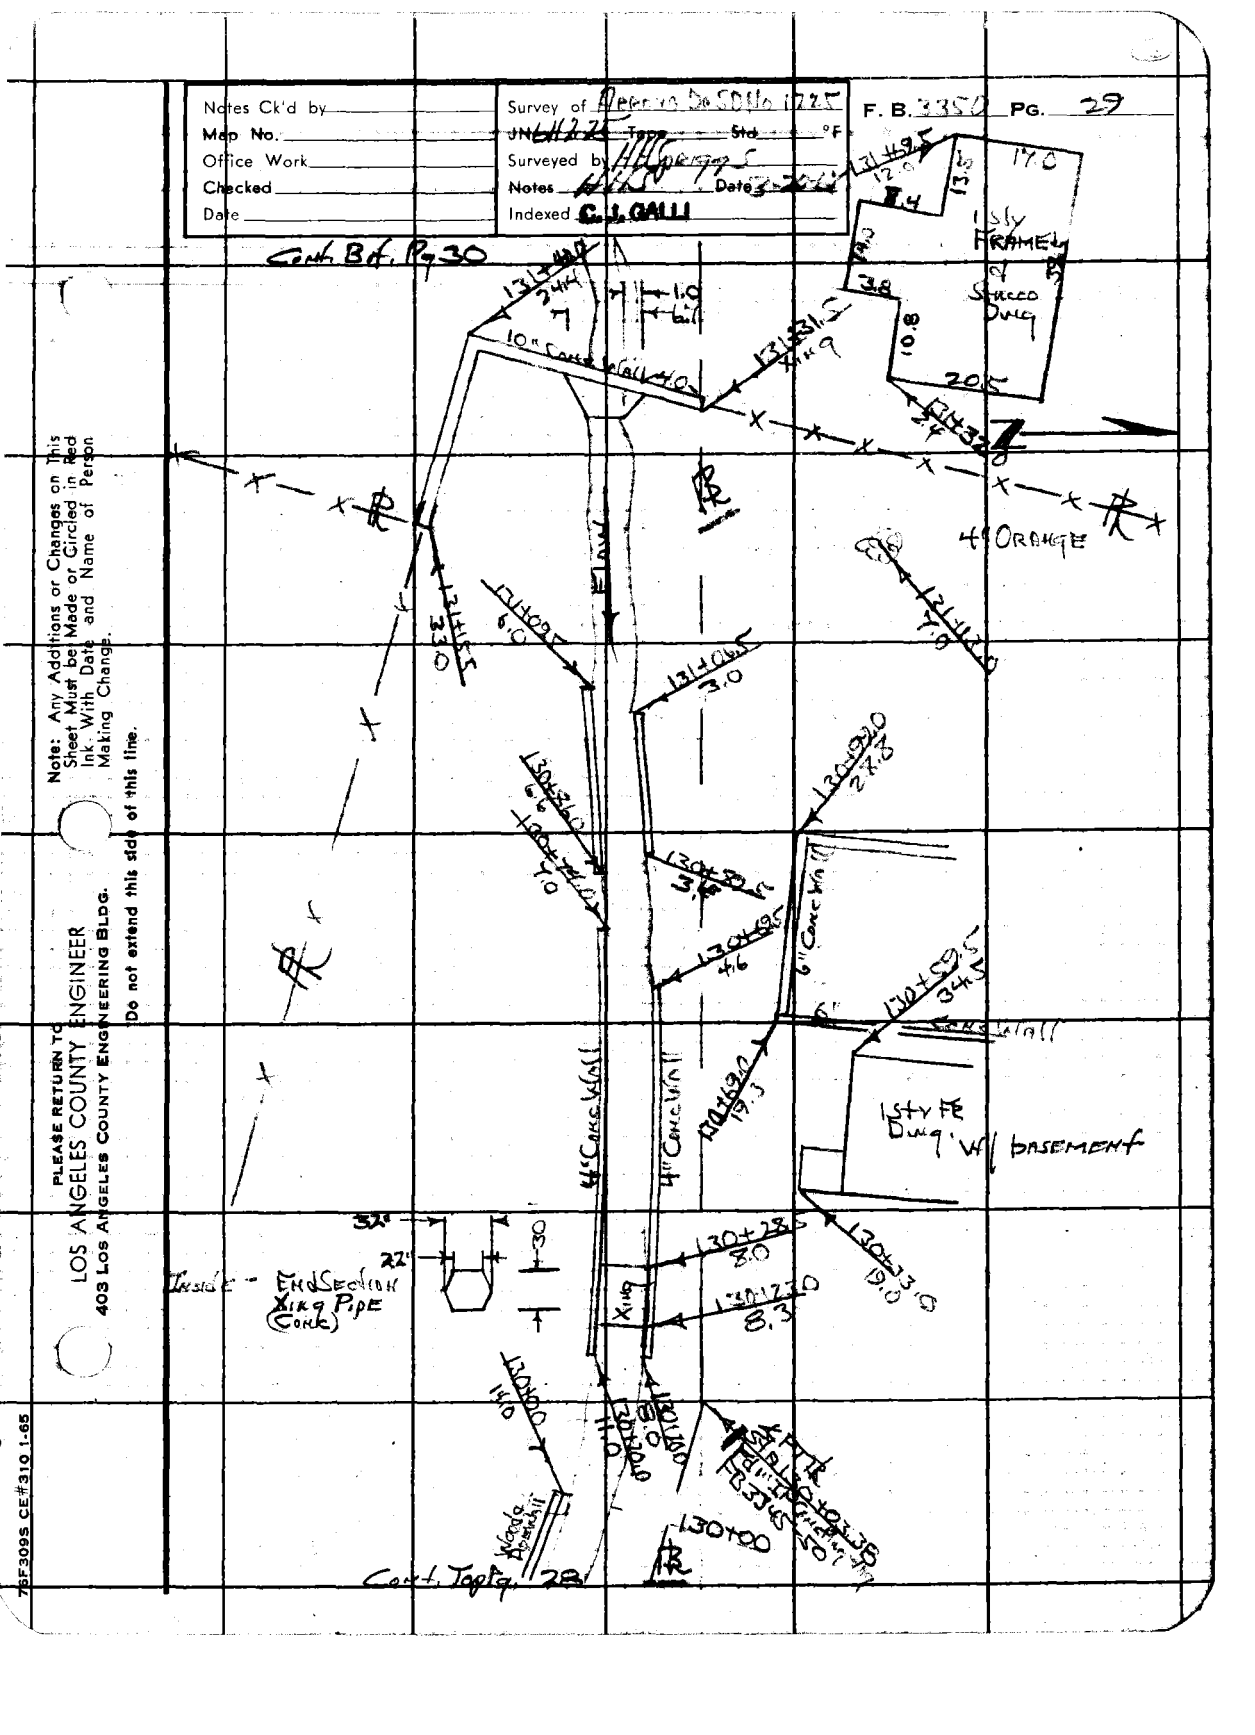
Notes Ck'd by
Map No.
Office Work
Checked
Date
Survey of Pepper Dr SDHo 1725
JN 41225 Topo Std °F
Surveyed by
Notes
Date
Indexed C. L. GALLI
F. B. 3350 PG. 29
Cont. Bk. Pg 30
1 sty FRAME & STUCCO DWG
10" Conc. Wall
4" Conc. Wall
6" Conc. Wall
4" ORANGE
1 sty FR DWG W/ BASEMENT
Inside - END Section XING PIPE (CONC)
Wood Bulkhead
Cont. Topo Pg. 28
Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.
Do not extend this side of this line.
PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.
76F309S CE#310 1-65

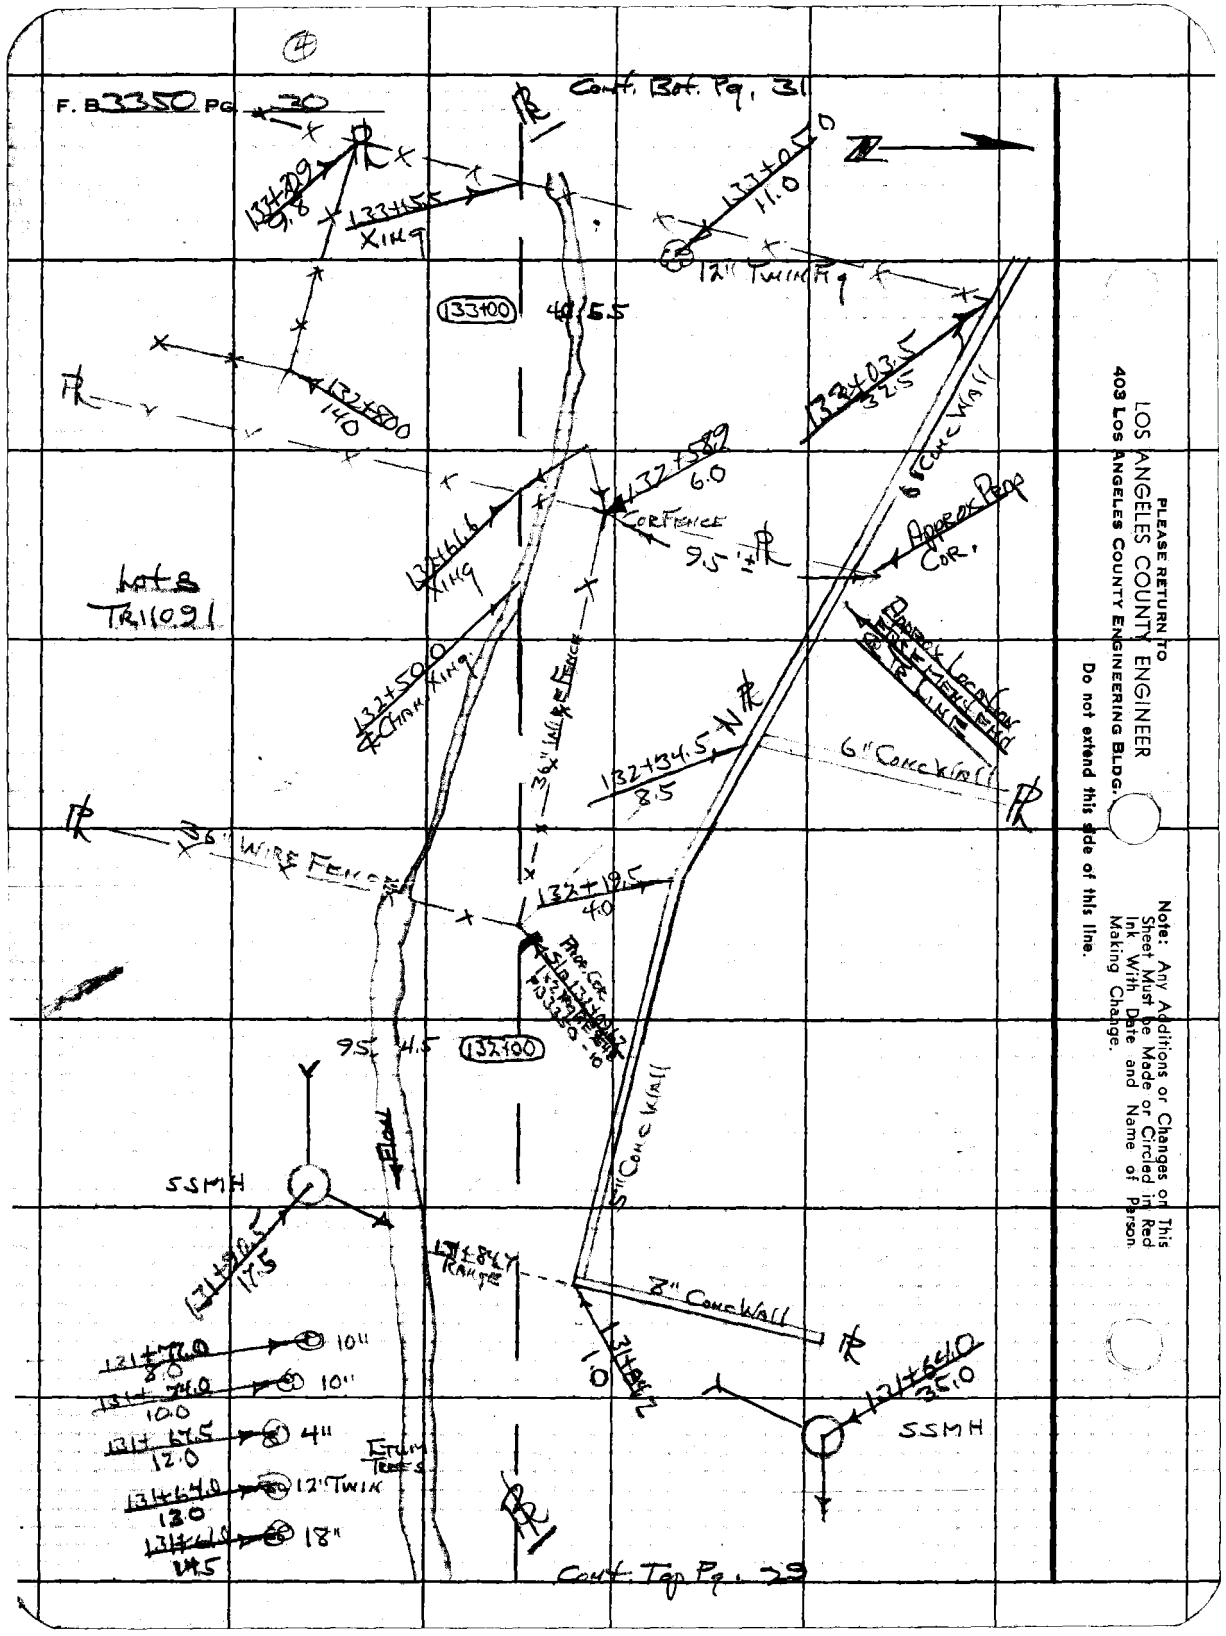
F. B. 3350 PG. 30
Cont. Bot. Pg. 31
133+00
40.5
132+00
Lots
TR 10291
6" Conc Wall
6" Conc Wall
36" WIRE FENCE
36" WIRE FENCE
Approx Prop Cor.
Approx Location of Property Line
SSMH
SSMH
Cont. Top Pg. 29
Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.
PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.
Do not extend this side of this line.

Notes Ck'd by	Survey of Norwalk DR SD No 1225
Map No.	JN 611275 Tape Std °F
Office Work	Surveyed by [illegible]
Checked	Notes [illegible] Date 3-20-67
Date	Indexed C. J. GALLI

F. B. 3350 PG. 31

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Cont. to Pg. 32

NOTE:
THIS CONC BOX DRAIN IS AN EXTENSION OF 36" CMP @ TOLL DR XING
SEE Pg. 32, 88, 89

Conc. Box. Drain
44" Rt. & Span
36" Clear
Conc. Bottom

Cont. Top Pg. 30

76F309S CE#310 1-65

F. B. 3350 PG. 32

PREMIX

136+90.0

XING DRIVE

Cont. Sht. Pg. 33

6" Concrete

Dwg. IN THIS LOCATION SEE Toll Dr. Topog

136+80.0

136+70.0

36"

34"

643 LF 36" CMP

DRIVE

Sta 135+61.16 INTER. of Toll Drive & Premix Entrance Rd SAND-FLUSH FB 3350-11

Sta 136+72.75 PT FB 3350-11 Sheet Topog on Rt

Note: For location of Intersection on Toll Drive SEE FB 3350-87-90

For Xsections on Toll Drive SEE FB 3350 91-98

Approx XPT Pipe

Toll Rd

Lot 11 Th. 11091

Dwg. IN THIS Location SEE Toll Dr. Topog

PREMIX DRIVE

108

Dwg. IN THIS Location SEE Toll Dr. Topog

Sta 136+70.07 XPT FB 3350-11 Shop Topog on Rt

Note: This 36" CMP connects to Cmp Box 2001 SEE Pg 31.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

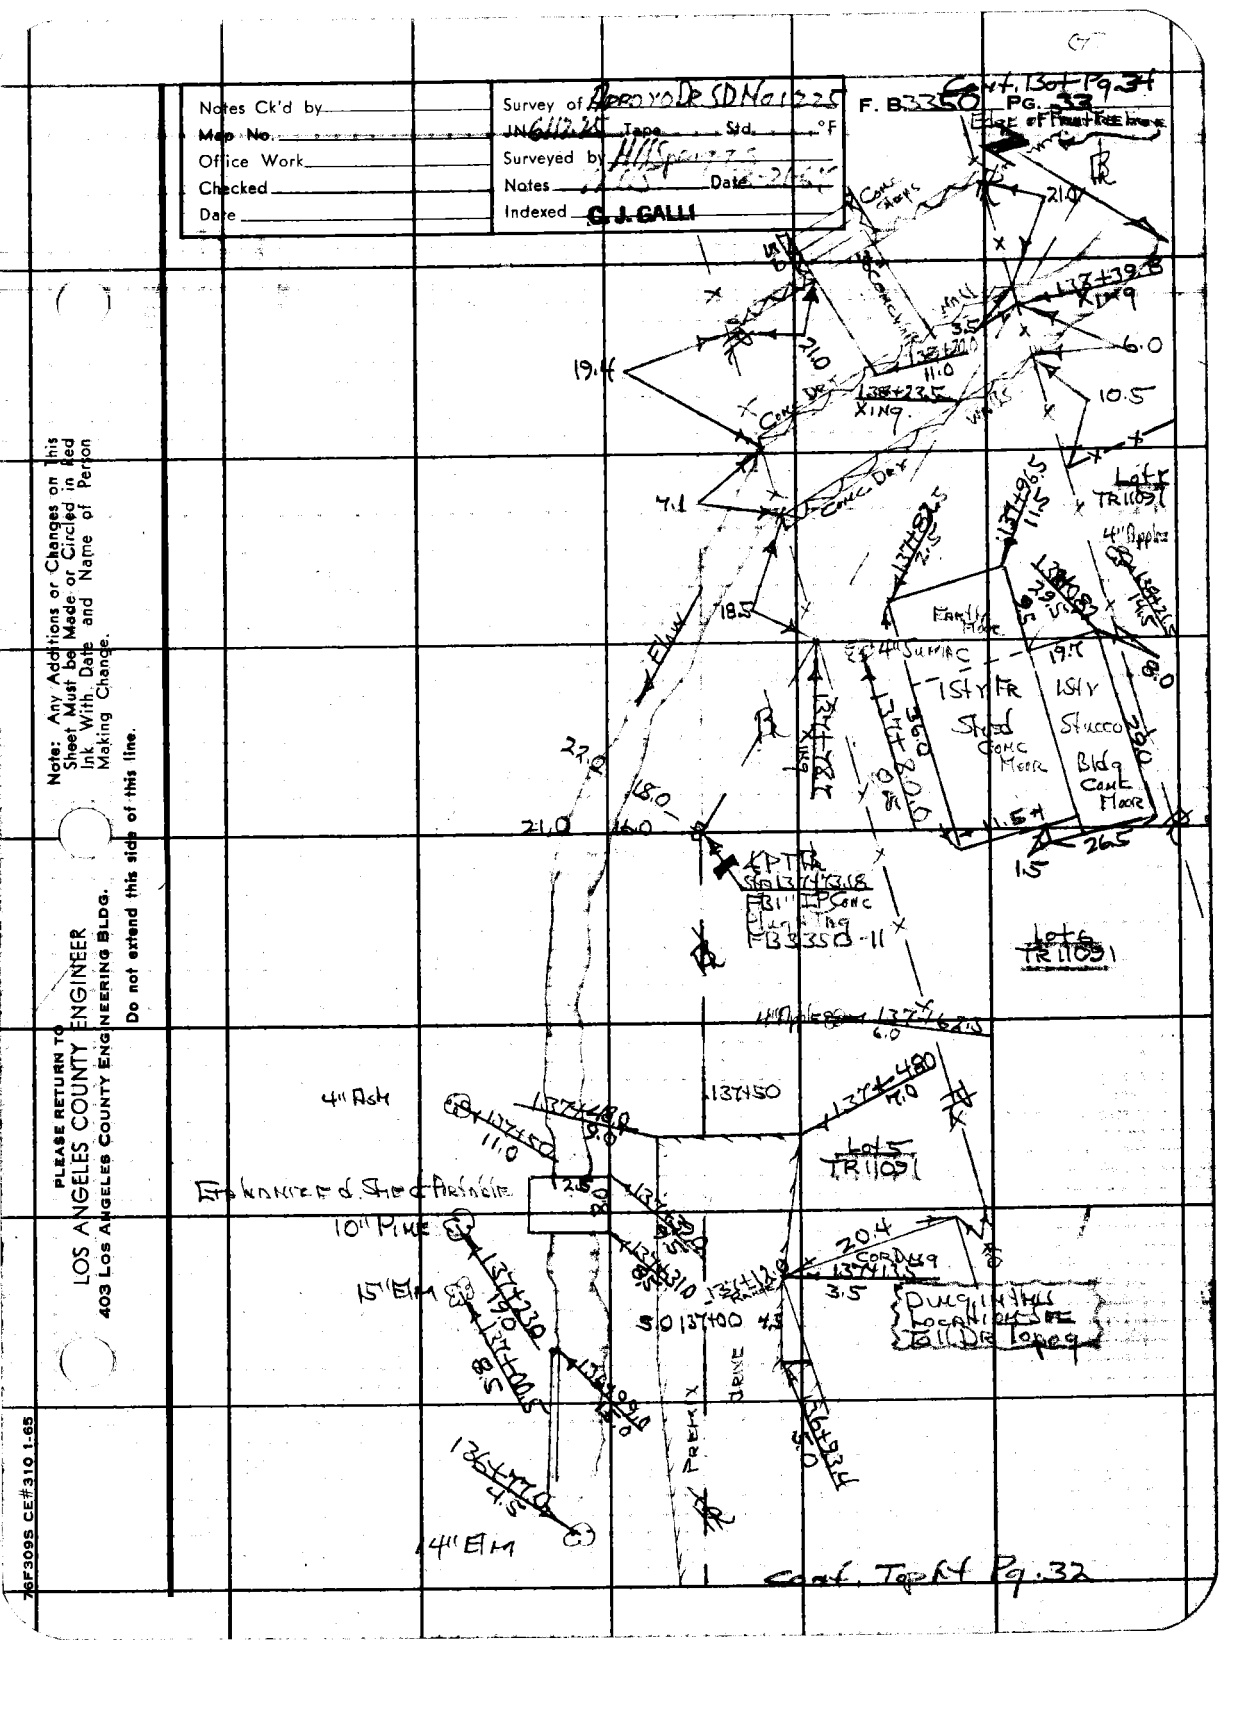
Notes Ck'd by
Map No.
Office Work
Checked
Date
Survey of Aberdeen Dr SD No 1225
JN 6412.25 Tape Std. °F
Surveyed by Hill Spencer
Notes Date
Indexed G. J. GALLI
F. B. 3350
Cert. Top 4 Pg. 34
Pg. 33
Edge of Fruit Tree Line
Conc Curb
Conc Walk
Conc Drive
Curb
Lattice
Fence
Fruit Tree
Family Room
Stucco Bldg
Conc Floor
Lot 6
TR 11091
Lot 5
TR 11091
Lot 7
TR 11091
4" Ash
10" Pine
15" Elm
14" Elm
Drive
Cert. Top 4 Pg. 32
Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.
Do not extend this side of this line.
PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.
76F309S CE#310 1-65

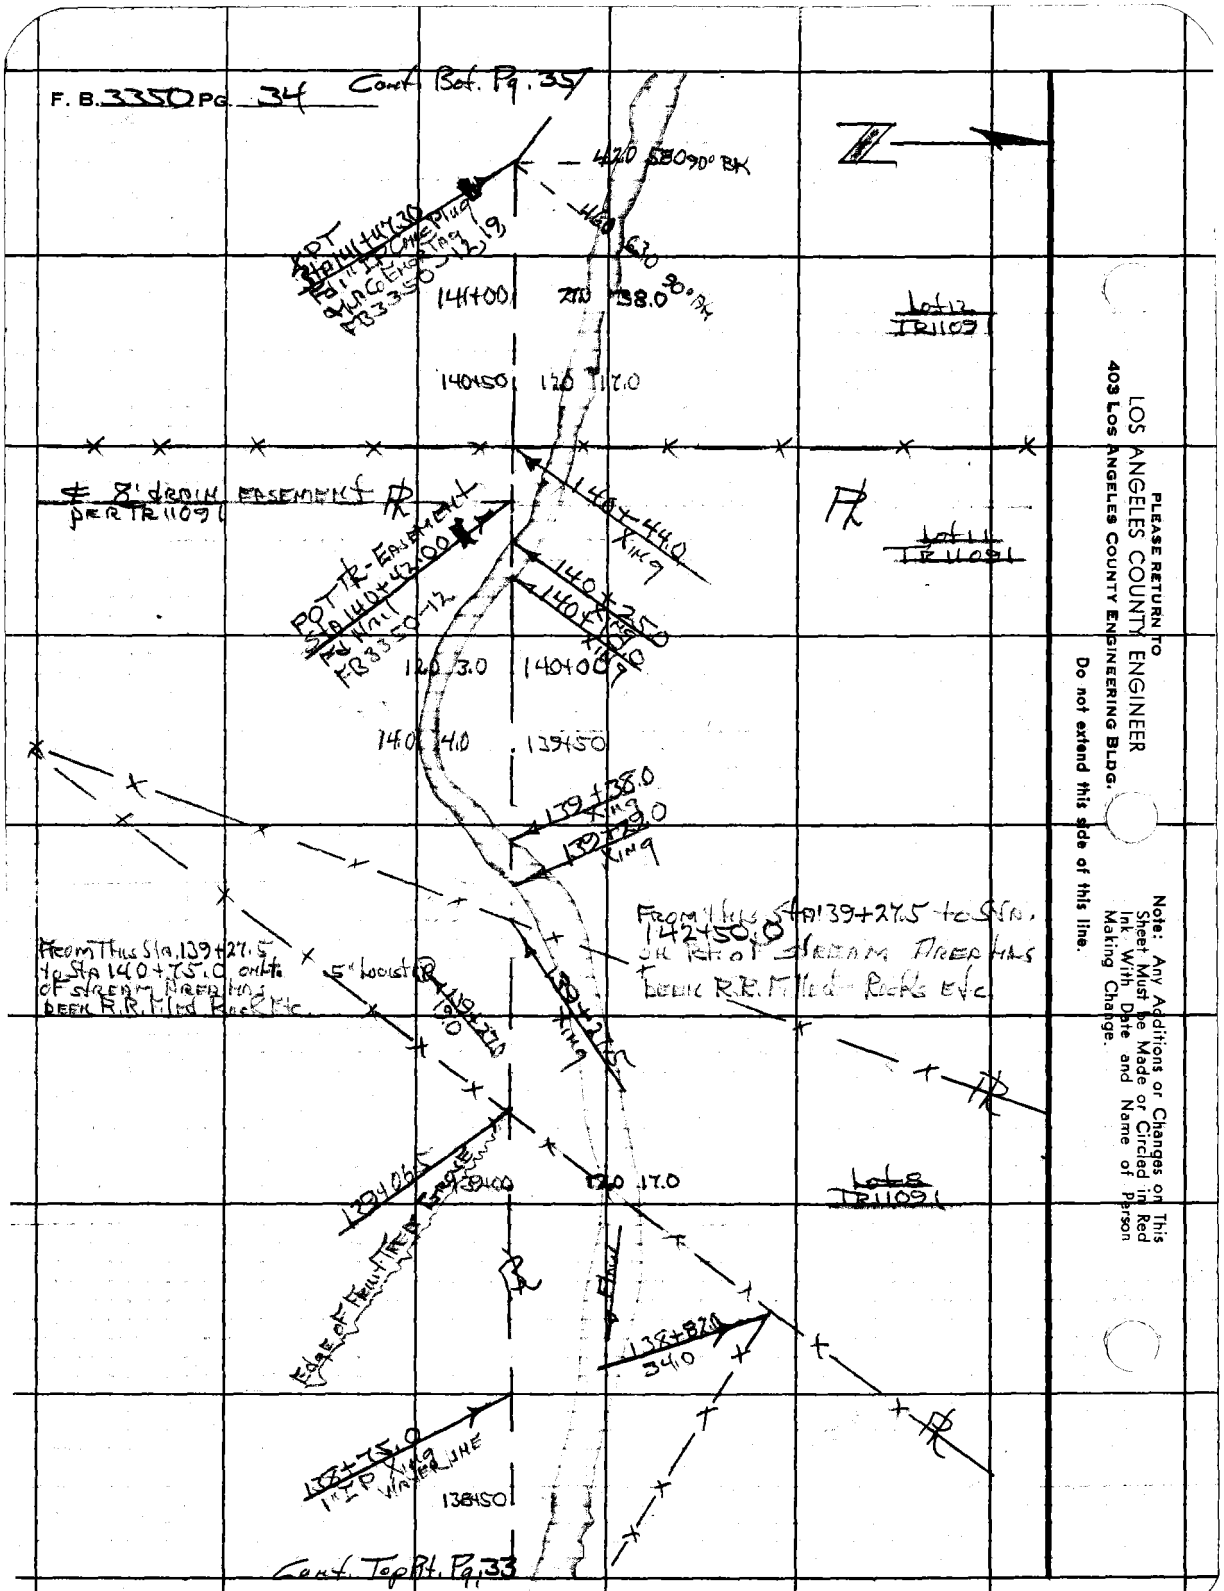

LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

PLEASE RETURN TO

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

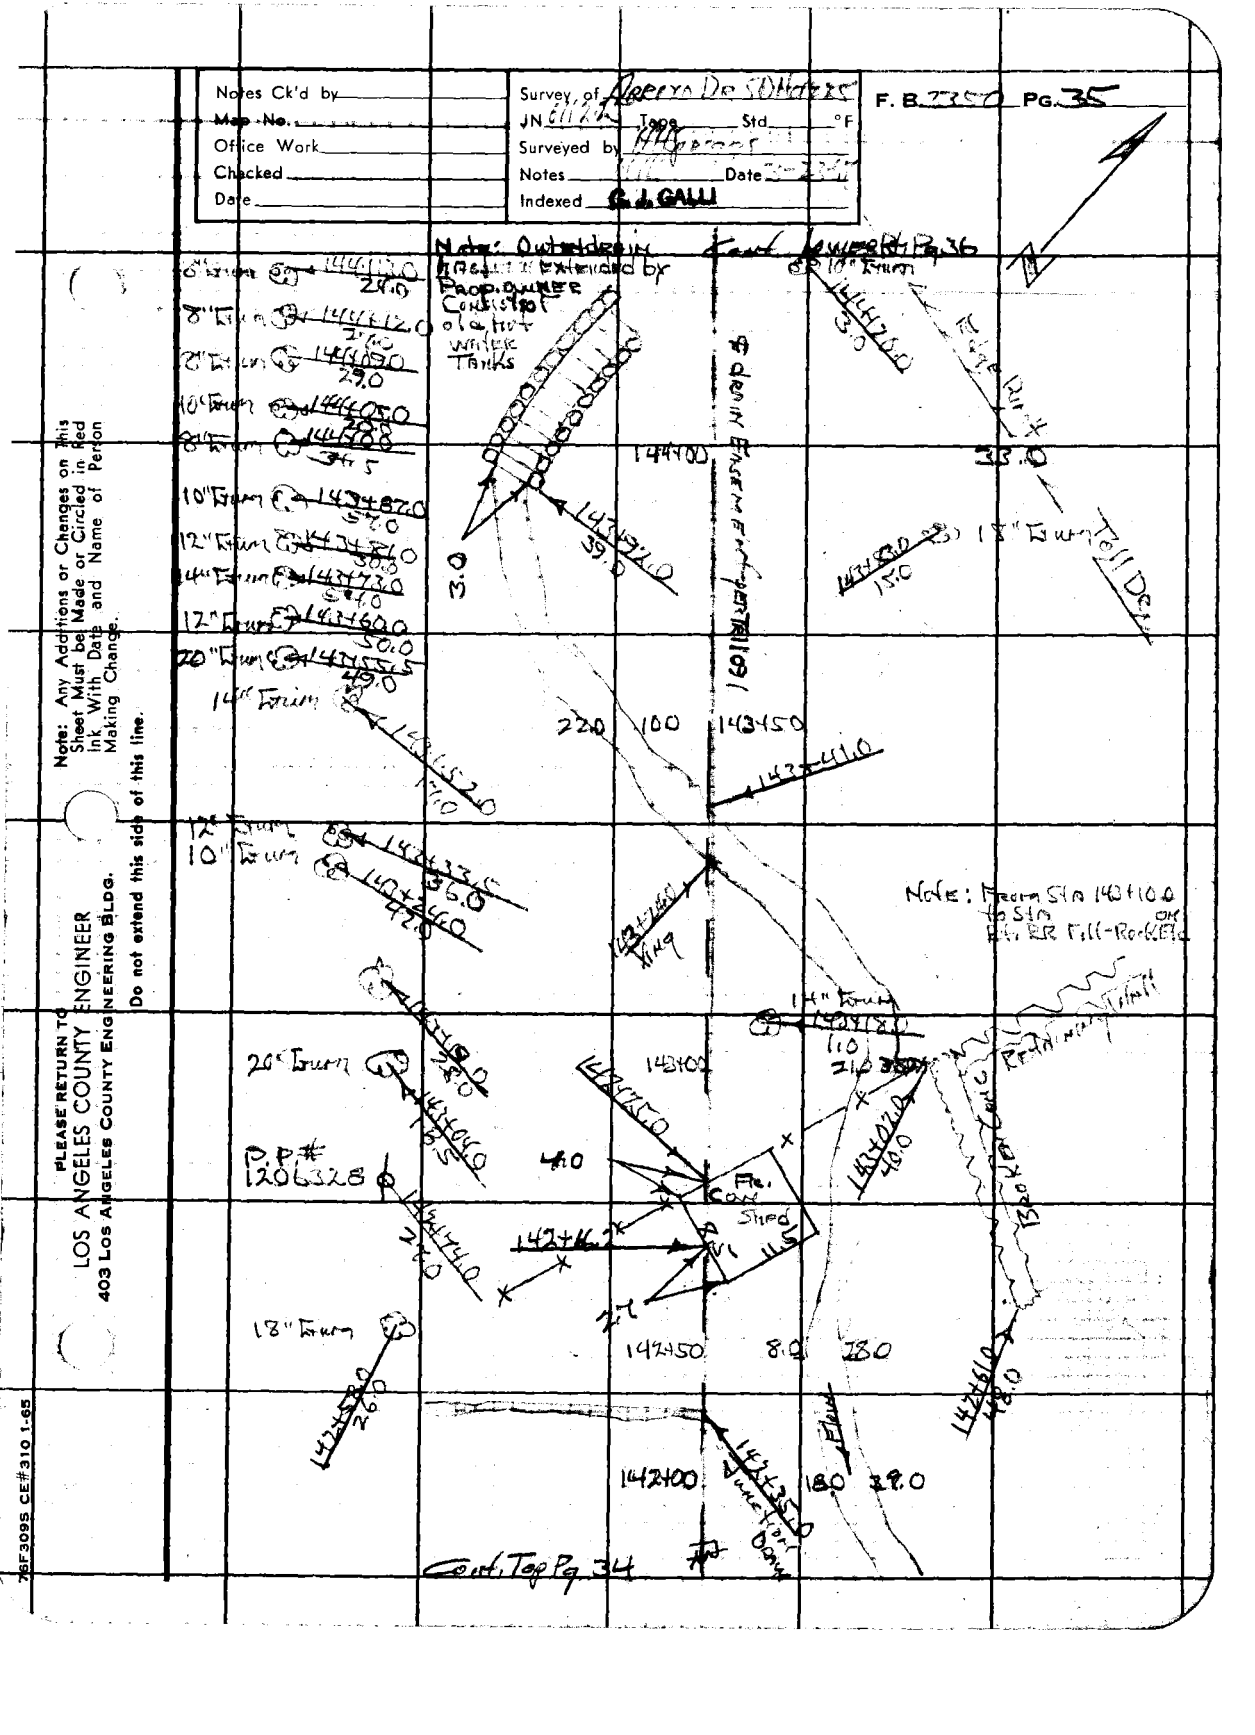
Notes Ck'd by
Map No.
Office Work
Checked
Date
Survey of Queens Dr. Sta 0+00 to 25
JN 611224 Topo Std °F
Surveyed by
Notes Date
Indexed G. J. GALLI
F. B. 7350 Pg. 35
Note: Outbuildings extended by Prop. owner Consist of Plastic water Tanks
Cont. from Pg. 36
Cont. Top Pg. 34
Note: From Sta 140+00 to Sta 142+00 Fill-Rock
Broken Top Pg 1
Tell Dr.
Fence
Shed
P.P. # 120328
PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.
Do not extend this side of this line.
Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.
76F3095 CE#310 1-65

F. B. 3350 Pg. 36

Note:
No Sewers in this portion of Toll Dr
Residents verify this.

N

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

POT & Toll Drive
POT B & C/L Easement
Sta 144+50.90
Fd Spk Nail Flush
PB 3350-16

Toll Drive

See Pg 105 & 117
For Topog & Sections

Sta 144+39.90

Sta 144+40

Sta 144+34.0
14.0

Cont. Pg 35

Cont. Pg 37

Edge of 100-112 Line

Edge of Pavement

Edge of Pavement

Edge of Pavement

76F309S CE#310 1-65

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

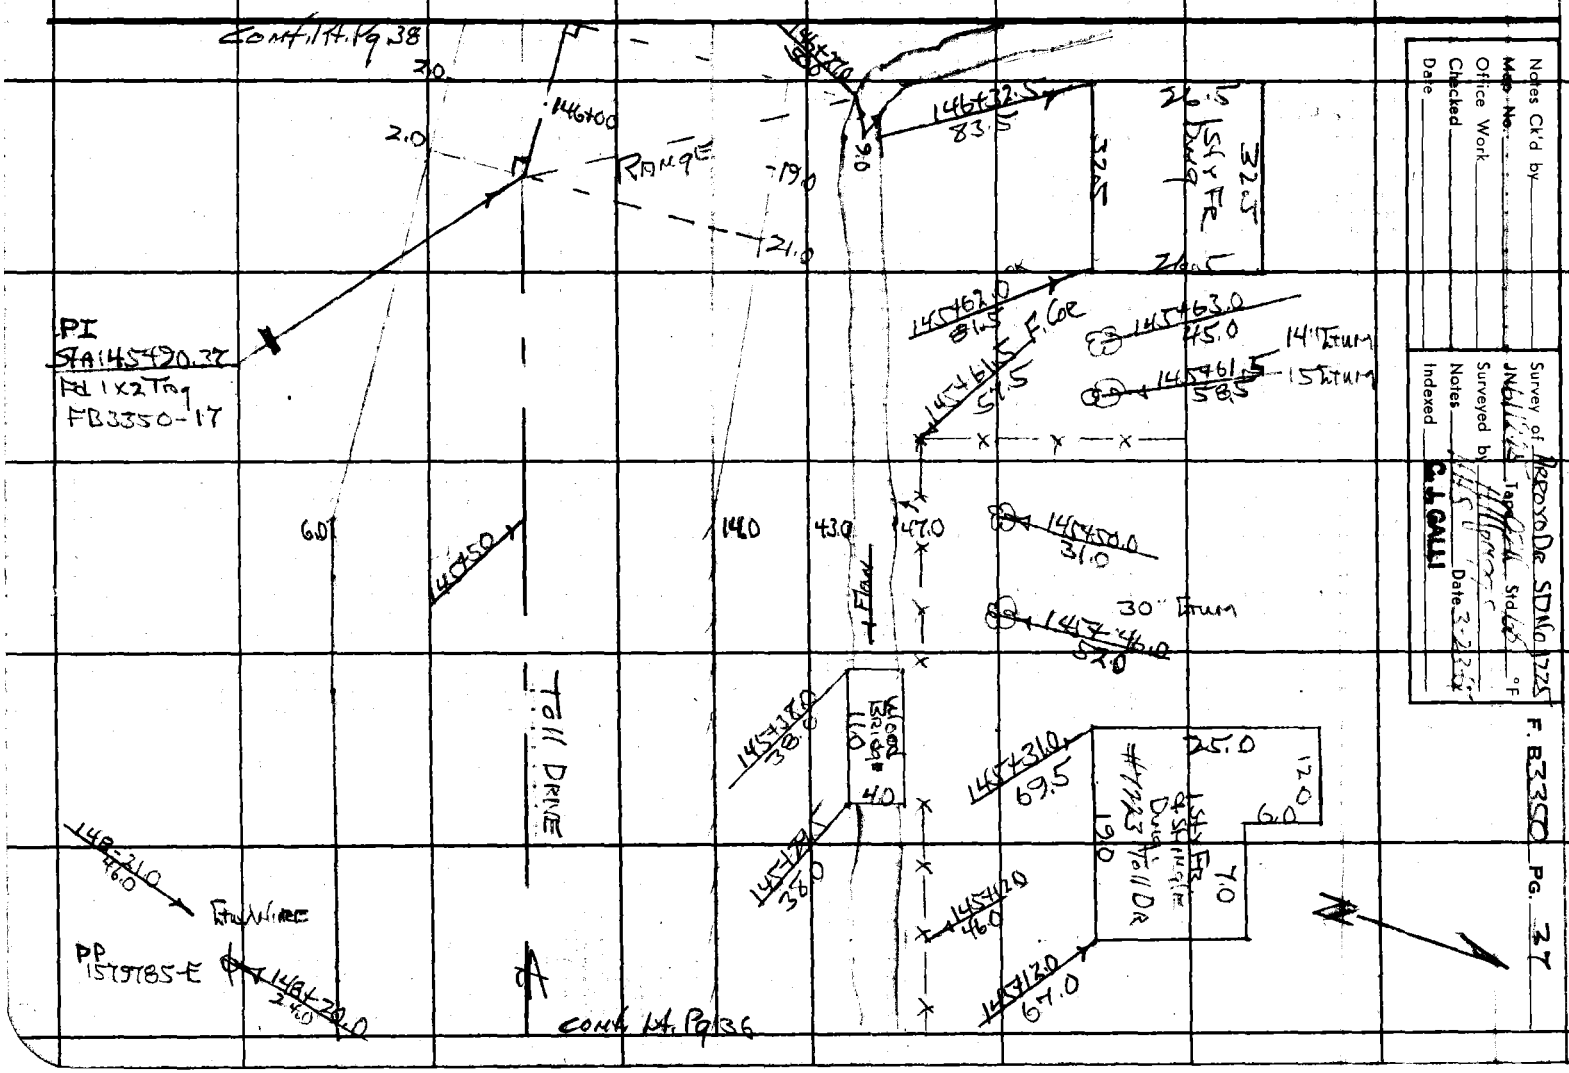

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

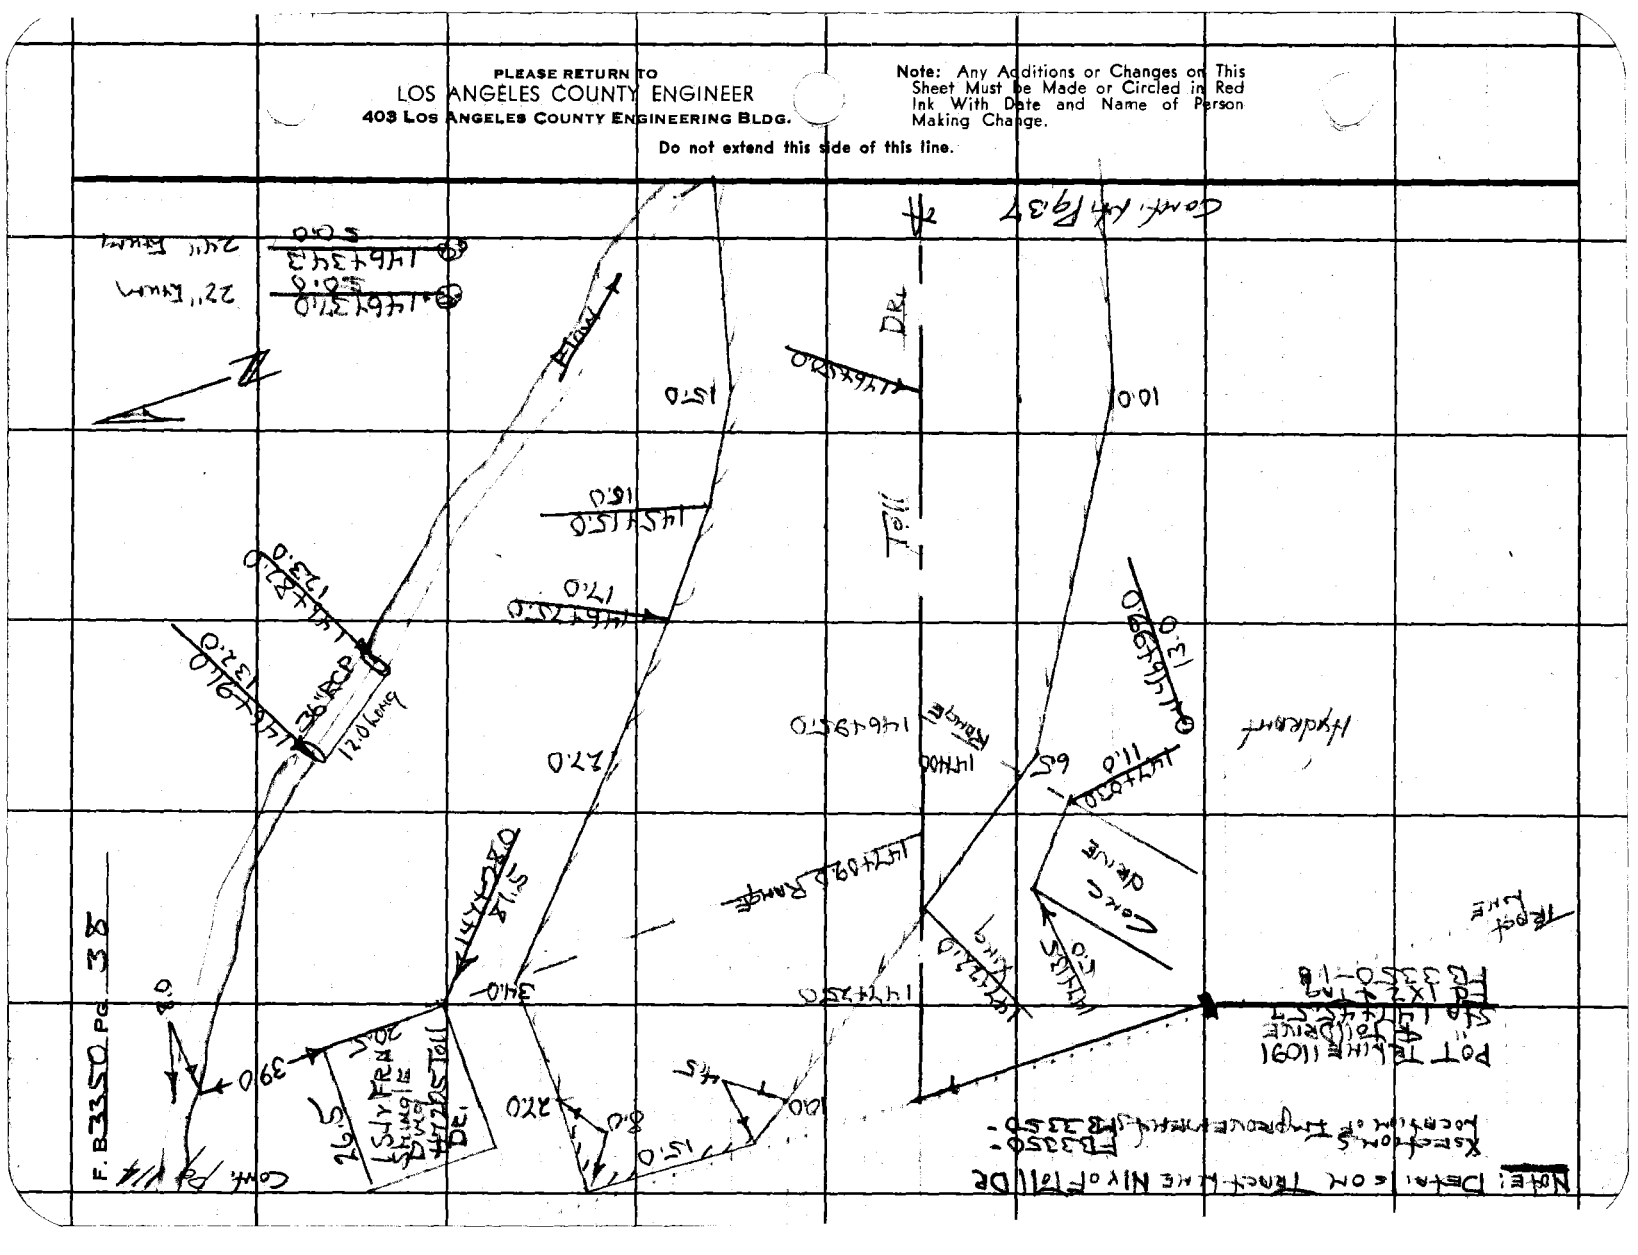

76F309S CE#310 1-65

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

Survey of
JN Tape Std °F
Surveyed by
Notes Date
Indexed

Notes Ck'd by
Map No.
Office Work
Checked
Date

F. B. 3350 PG. 29

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

F. B 3350 P.G. 40

F.B. 3350 Pg. 41

Profile No. ____ X-Sec. No. ____ | Notes Red ____ Date ____ | Notes Chkd. ____ Date ____ | Plotted ____ Date ____ | Checked ____ Date ____

Job No. 6112.25 Division No. ____

Survey of ARROYO DR SD No 1225

Survey by HHGapp Notes HHS Date 3-20-67

Map No. ____ Indexed C. J. GALLI Date ____

~~FN~~ 6112.25

ARROYO DR SD No. 1225

XSECTIONS

~~FB~~ Sta 127+48.96 HWY = POT
~~Sta~~ & Reading Rue (R=5532) to
Sta 144+50.90 POT Toll Dr. &
drain EASEMENT (294.67 ELY
OF WLY LINE TR 11091) THENCE
Toll Dr. WLY to TRACT LINE
Sta 147+45.59

Alignment FB 3345-48, 50,
FB 3350-10, 11, 12, 16, 17, 18,

Location of Improvements FB3350 - 27-40

HHGoggins
M A Walsh
D. R. Workman
T. L. Bensley

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

76-L298 CE 307 3-61

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3350 Pg. 42 | Job No. 6611225 | Division No. | Notes Red | Plotted | Profile
Survey of Hemp Rd DR SD No 122.5 | Date | Date | No.
Survey by Hillgrove | Notes | Notes Chkd. | Checked | X-Sec.
Indexed C.J. Gill | Date | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.		
BMSD 1051				363.34	BMSD1051 Elev. 363.44 FB3338-38 N Redding Ave. E/Yside Approx 33' S/Y ℄ Intse of Terrace Ave +3.5 E/o PK, nail spk in lead in conc wall @ s/y Edge drive	
127+60.0				364.15		℞ Pvmt Xing
127+61.0				362.25		28.3 Ft Inlet of 18" CMP
127+71.0				357.65		30 Ft Inlet of 36" CMP
127+71.5				361.95		6.5 Ft Outlet of 18" CMP
127+73.0				363.34		℞ Top Hdwl
128+00				360.7		℞ drain
				360.7		7.0
				363.8		10.5
				364.31		15.5 Conc drive
				364.67		25.5

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. Gillis Division No.
No.____ Date____ Date____ Survey of Hreljac Dr. SD No. 2
X-Sec. Notes Chkd.____ Checked____ Survey by____ Notes____ Date 2-20-64
No.____ Date____ Date____ Map No.____ Inked C.J. GALLI Date____

F.B. 3350 Pg. 43

STATION	B. S.	H. I.	F. S.	ELEV.			
128+00				365.4		7.5	
S				366.0		25.0	
128+50				361.4			DRAIN
				361.1			5.0
				363.9			7.0
				364.86			18.3
				365.71			23.5
				365.5		5.5	
				366.7		22.5	
128+67.0				367.34	5.5 Elev. Floor Level Dwg		
128+76.5	Rim			364.12	Inlet W	Outlet E	11.2 SSMH
	Inlet W			357.21	364.12 Rim	364.12 Rim	
	Outlet E			357.08	6.24 Mans	6.57 Mans	
					357.88	357.75	
					0.67	0.67	
					357.21	357.08	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3350 Pg. 44 | Job No. 41225 | Division No. | Notes Red | Plotted | Profile
Survey of Arroyo Dr SD No 1225 | Date | Date | No.
Survey by Williams | Notes HHS | Notes Chkd. | Checked | X-Sec.
Indexed C.H.BALL | Date | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.		
129+00				361.7		Drain
				361.8		4.0 "
				365.2		6.0
				365.47		21.5 Conc Drain
				365.81		41.5 " "
				364.7	3.5	
				365.0	6.0 Dwg	
129+21.0				361.73	1.0 Fl. Outlet 42" RCP	
129+27.2				361.70	3.5 Fl. Inlet 42" RCP	
129+50.				365.9		
				365.8		30.0
				365.7	3.0	
				362.2	5.5 Drain	
				362.2	3.5	
				365.4	10.5	
				367.9	16.5	
				368.8	34.0	

76-L298 CE 307 8-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.		
130+00				367.0		
				366.2		30.0
				367.4	8.0	
				365.6	11.5	
				362.3	12.0 DRAIN	
				362.3	14.0	
				365.5	16.0	
				367.1	19.5	
				368.9	25.5	
				370.0	43.5	
130+20.0				364.15	8.3 Top 4" Conc Wall	
				364.12	11.0 " " "	
130+33.0				370.58		25.0 Elev. 1st Floor Level

Profile Notes Red____ Plotted____ Job No. 66-1111 Division No.____
No.____ Date____ Date____ Survey of Lakewood Blvd. SD No. 1275
X-Sec. Notes Chkd.____ Checked____ Survey by [illegible] Notes [illegible] Date____
No.____ Date____ Date____ Map No.____ Indexed [illegible] Date____

F.B. 3350 Pg. 45

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3350 PG. 46 | Job No. 61123 Division No. | Notes Red | Plotted | Profile
Survey of Herb Dr SD No 1225 | Date | Date | No.
Survey by Hilgar 1963 Notes HHS | Notes Chkd. | Checked | X-Sec.
Indexed C.J. Galli | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.		
130450.0				367.57		
				367.6		13.5
				366.1		15.0
				366.2		24.2 Drag
				367.4	2.0	
				366.2	5.0	
				364.16	5.6 Top Wall	
				362.9	5.6 Drain	
				362.9	8.2	
				364.26	8.2 Top Wall	
				366.4	9.0	
				369.1	14.5	
				370.6	19.0	
				374.0	40.5	
130469.0				369.30		19.3 Top 6" Conc Wall
				367.6		21.3 Bot. " " "
130469.5				364.13	4.6 Top 4" Conc Wall	
130474.0				364.26	7.0 " " " "	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. 61122-15 Division No.____
No.____ Date____ Date____ Survey of Reyes De SD Val 225
X-Sec. Notes Chkd.____ Checked____ Survey by [illegible] Notes [illegible] Date [illegible]
No.____ Date____ Date____ Map No.____ Entered [illegible] Drawn [illegible]

F.B. 3350 Pg. 47

STATION	B. S.	H. I.	F. S.	ELEV.		
130+86.0				364.57	6.6 Top 4" Conc Wall	
130+89.5				364.61	3.4 " " " "	
130+89.0				368.37		28.8 Top 6" Conc Wall
				368.3		28.8 Bot. " "
131+00				367.5		
				368.5		30.0
				368.8		45.0
				366.8	30	
				364.66	3.5 Top Wall	
				363.5	3.5 Drain	
				363.5	6.3 Drain	
				366.77	6.3 Top Wall	
				367.5	10.5	
				371.0	16.0	
				376.0	32.0	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3350 Pg. 48 | Job No. 6422 | Division No. 1225 | Profile No. | X-Sec. No.
Survey of Arroyo DR SD No 1 | Notes Red | Plotted
Survey by HH Jorgensen | Notes | Date | Date
Indexed J. GALLI | Notes Chkd. | Checked
Date | Date | Date

STATION	B. S.	H. I.	F. S.	ELEV.		
1314+06.5				364.69	3.0 Top 4" Wall	
1314+09.8				364.91	6.0 " " "	
1314+31.5				363.9	7.3 Chan. @ wall Xing	
				365.46	7.3 V-ditch in wall @ Xing	
1314+32.0				368.21		2H Elev. Floodplain Dwg. - Record of water damage
1314+50.0				367.7		
				367.5		1.5 Dwg
				367.6	5.5	
				365.3	5.5 drain	
				365.7	3.5	
				367.7	8.5	
				370.5	17.5	
				374.0	21.5	
				370.0	31.5	
				382.4	37.0	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Noted Red Plotted Job No. Division No.
No. Date Date Survey of Hanley Dr. SD Proj 225
X-Sec. Notes Chkd. Checked Survey by Notes Date
No. Date Date Map No. Indexed Date

F.B. 3350 Pg. 49

STATION	B. S.	H. I.	F. S.	ELEV.		
1314610	Avg Rim Inlet Outlet	360.25		370.05 359.61 359.32	Inlet S 370.05 Rim 9.77 MEAS 360.28 0.67 359.61	Outlet E 370.05 Rim 10.06 MEAS 359.99 0.67 359.32
1314842 S				370.81 368.9		1.0 Top 3" Conc Liner 1.0 Bot. " "
1314905	Avg Rim Inlet W Outlet N			369.39 360.04 359.89	17.5 SSMH	Inlet W 369.39 Rim 8.68 MEAS 360.71 0.67 360.04
1321.00				376.25 [illegible] 370.82 371.2 371.6 372.8 373.0		2.0 Bot 5' Conc Liner 2.0 Top " 63 17.5 18.5 20.0

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3350 Pg. 50
Survey of Herrero Dr SD No 1225 Division No. Job No 11225 Profile
Survey by HH Notes FHS Notes Red Plotted
Indexed Date Date Date No. X-Sec.
Notes Chkd. Checked
Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.		
132400				3678	30	
				3668	45 Drain	
				3668	95	
				3686	115	
				3680	260	
				3706	345	
				3725	405	
132+12.5				3695		3.5 Bott 5" Concwall
				37104		8.5 Top 5" " "
				37132		8.5 Top 6" " "
132+50.0				3685		
				3685		1.0 Chan.
				3691		1.5
				3711		12.5 Bott 6" Concwall
				3742		12.5 Top 6" Concwall
				3731		13.5 Bot " " "
				3783		30.0

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. 4425 Division No.____
No.____ Date____ Date____ Survey of Tract 35 Ok SD Mp 1265
X-Sec. Notes Chkd.____ Checked____ Survey by [redacted] Notes [redacted] Date 3-21-67
No.____ Date____ Date____ Map No.____ Indexed C.J. BELL Date [redacted]

F.B. 3350 Pg. 51

STATION	B. S.	H. I.	F. S.	ELEV.		
132+50				368.5	1.0	CHAN.
				369.3	1.5	
				369.4	7.5	
				368.0	22.0	
				369.8	27.5	
				370.5	33.0	
				375.5	39.5	
133+00				370.7		
				369.3		4.0 CHAN.
				369.8		5.5
				370.5		6.5
				370.6		23.0
				371.6		32.0 Bot 6" Curb Wall
				373.70		32.0 Top 6" Curb Wall
				370.0	10.0	
				371.9	28.0	
				373.4	39.5	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK. WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3350 Pg. 52 | Job No. 6112.25 | Division No. | Notes Red | Plotted | Profile
Survey of Canyon Dr. SD No 1225 | Date | Date | No.
Survey by HH Consig | Notes | Notes Chkd. | Checked | X-Sec.
Indexed C. LEAL | Date | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.			
133+19.5				366.00	Lt. (2.0) F.L. Outlet ^ Exist 44" Conc Box Drain on conc bottom.		
				365.7	(2.0) F.L. Chan. @ Exist 44" Conc Box Drain		
TP				370.31	Top 133+00 Ctr Stake		
133+50				373.4			
				373.9			25.0
				374.7			50.0
				373.0		25.0	
				373.40		42.0 Edge Slab	
				373.40		55.0 Slab	
133+57.16	BPT			373.5			
133+73.8					Inlet S 3731 Rim 1085 Mens 36226 067 361.59	Outlet NE 373.08 Rim 11.02 Meas 362.06 0.67 361.39	1.3 SSMH
	Inlet S			361.59			
	Outlet NE			361.39			

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 61225 Division No. ____
No. ____ Date ____ Date ____ Survey of Tapparo Dr SD No. 1225
X-Sec. Notes Chkd. ____ Checked ____ Survey by [illegible] Notes [illegible] Date 3-7-67
No. ____ Date ____ Date ____ Map No. ____ Indexed [illegible] Date [illegible]

F. B. 3350 Pg. 53

STATION	B. S.	H. I.	F. S.	ELEV.			
133+75.0				372.9		BP	
				373.1			10.5 Bot Wall
				375.16			10.5 Top Wall
				375.0			12.0 BP Wall
				375.1			25.5
				373.0	12.0		
				372.7	39.0		
				372.3	59.0		
134+00				373.0		BP	
				372.9			8.5
				371.9			9.5
				371.4			23.2 Plug
				373.38	16.4 Edge Slab		
				373.40	31.5		
				374	36.5		

377.88

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3350 Pg. 54 | Job No. 6112.25 Division No. | Profile
Survey of Vesco to Dr SDN 1225 | No. | Notes Red | Plotted
Survey by Hillcrest Notes HHS | X-Sec. | Date | Date
Indexed C.J. GALLI Date | No. | Notes Chkd. | Checked | Date

STATION	B. S.	H. I.	F. S.	ELEV.		
134+18.5						Rt
				374.09		30 Edge Pvm't
				374.1		7.5
				372.8		9.0
				372.6		26.0
				372.5		40.0
				373.5	9.2	
				373.38	17.5 Edge Slope	
				373.42	37.5	
134+50.0				380.34		Rt
134+53.0				380.57		Rt
				380.86		20 Edge Pvm't
				380.2		60
				378.9		180
				378.1		325
				381.31	7.5 Edge Pvm't	
				382.1	21.5	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. Division No.
No. Date Date Survey of
X-Sec. Notes Chkd. Checked Survey by Notes
No. Date Date Map No. Indexed Date

STATION	B. S.	H. I.	F. S.	ELEV.		
134+90				381.10		℄ Edge Rim — Toll Dr.
134+00		℄PTR - POT Toll Dr. FB 3350-11		381.22		℄ Rim
BM SD 1052				382.08	BM SD 1052 Elev. 382.085 FB 3338-3' Toll Dr. N'lyside Approx 326' W/o ℄ Inter @ Tegner Dr & Redding Ave A set spkin conc ctep @ Pr House # 7445 Toll Dr.	
135+00				379.12		℄ Toll Dr
+50				377.39		℄ " "
135+61.16				377.39		℄ Toll Dr & Easement per R11091
136+00				378.41		℄ Toll Dr.

F.B. 3350 Pg. 55

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

37739

Do not extend notes this side of this line.

F.B. 3350 Pg. 56 | Job No. 6112.25 | Division No. | Notes Red | Plotted | Profile
Survey of Agoura Dr SDN & Lts | Date | Date | No.
Survey by [illegible] | Notes | Notes Chkd. | Checked | X-Sec.
Indexed C. J. Ball [illegible] Date | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.		
136+24.75	CPT & POT To Dr Fd Spike FB 3350-11			379.76		BR ℄
136+41.0				379.72		BR Edge Pvmt.
136+48.0				373.39	21.0 F.L. Inlet 36" CMP	
136+50.0				379.6		BR
				380.3		5.5
				380.8'		19.0 Edge Pvmt
				378.1	16.5 Top Wall	
				373.7	17.5 Cline	
				373.7	21.5	
				377.2	21.5 Top Wall	
				377.7	28.0 Drug	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. Division No.
No. Date Date Survey of FLOYD DRSD Date
X-Sec. Notes Chkd. Checked Survey by Notes Date
No. Date Date Map No. Indexed

STATION	B. S.	H. I.	F. S.	ELEV.		
136475.0				380.15		
				380.28		13.5 Edge de
				380.15	1.0 Edge drive	
				380.1	5.5	
				377.2	7.5	
				377.1	12.5 Top wall	
				374.3	13.5 Chan	
				374.3	16.5	
				373.2	17.0 Top wall	
				374.4	22.0 Dwg	
137400				380.14		
				380.15		4.5 Edge drive
				380.2		9.5 Dwg
				380.14	5.0 Edge drive	
				379.3	11.0	
				375.6	12.5 Chan	
				~~375.6~~ 379.8	~~16.5~~ 17.0	
				379.5	~~18.5~~ 22.0	
				~~381.0~~ 382.0	~~22.0~~ 39.0	

F.B. 3350 Pg. 57

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F. B. 3350 PG. 58
Survey of Geneva DR SBN 01725
Survey by HH/RH/GG Notes HH
Indexed C. J. GALLI Date
Job No 6/14/25 Division No. Notes Red Plotted Profile
Date Date No.
Notes Chkd. Checked X-Sec.
Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.		
137+25				380.25		
				380.25		65 Edge drive
				380.5		26.5
				380.2	7.5 Edge drive	
				379.2	11.0	
				377.4	14.5 Chan	
				377.4	17.5	
				380.7	24.0	
				383.3	29.3	
				383.3	31.0	
				386.0	37.5	
137+48.0				380.0		Edge drive
137+50				380.0		
				380.1		14.6
				380.2		20.5 Bldg

76-L 298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 41245 Division No. ____
No. ____ Date ____ Date ____ Survey of Prado to Ute Rd 12/2/5
X-Sec. Notes Chkd ____ Checked ____ Survey by ____ Notes ____ Date ____
No. ____ Date ____ Date ____ Map No. ____ Indexed C.J. CALL Date ____

F. B. 3350 Pg. 59

STATION	B. S.	H. I.	F. S.	ELEV.		
137+50				379.8	13.0	
				378.0	16.0 Chpk	
				378.0	19.5	
				380.3	22.0	
				386.1	30.0	
				387.4	36.0	
				391.4	42.0	
137+73.18	LPT	Fd 1" IP. Tag		380.2		
	RT	FB 3350-11		379.6		7.5
				379.4		17.5 Bldg
				379.8	16.5	
				378.2	19.0 Chpk	
				378.2	22.0	
				380.9	24.5	
				386.0	31.0	
				387.4	44.5	
				390.3	49.0	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3350 PG. 60

Job No. 4112-25 Division No. _____ Notes Red _____ Plotted _____ Profile _____

Survey of Norwalk Dr. SD No. 122.5 Date _____ Date _____ No. _____ X-Sec. _____

Survey by AH Sinks & Notes AH Notes Chkd. _____ Checked _____ No. _____

Indexed C.J. GALLI Date _____ Date _____ Date _____

STATION	B. S.	H. I.	F. S.	ELEV.		
138400				380.5		BK
				380.8		24.5 Bldg
				381.30		24.5 FL. Bldg
				380.8	10.0 Top Wall	
				378.5	10.5 CHAN	
				378.5	12.0	
				380.3	12.5 Top Wall	
				383.4	7.5	
				388.5	43.5	
138425				381.06		BK Xing Top Wall
138425.0				381.06		BK
				378.1		1.0 CHAN
				381.06		1.0 Top Wall
				380.8		16.0
				380.3		36.0
				380.8		50.0
				381.2		65.0

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. 612-65 Division No.
No. Date Date Survey of Redondo Dr. SD No. 1225
X-Sec. Notes Chkd. Checked Survey by [illegible] Notes [illegible] Date 3-24-[illegible]
No. Date Date Map No. Indexed R.J. CALLY Date

STATION	B. S.	H. I.	F. S.	ELEV.	
136+25.0				378.1	8.5 Chain
				382.22	8.5 Top Wall
				383.2	28.0 Bottom
				386.2	28.0 Top Wall
				387.1	43.5
138+50.0				380.7	
				379.2	3.0 Chain
				379.2	6.0
				380.1	8.0
				380.6	20.8 Fence
				380.6	41.0
				382.7	50.0
				381.1	5.0
				382.7	18.7 Bot Wall
				387.4	18.7 Top Wall
				388.0	38.5 Bot Wall
				391.8	38.5 Top Wall
				391.3	50.0

F.B. 2380 PG. 61

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

2184.7
1655.1
528.6

Do not extend notes this side of this line.

F.B. 3350 Pg. 62
Job No. 6411225 Division No. Notes Red Plotted Profile
Survey of Arroyo Dr. Sdwk 1225 Date Date No.
Survey by HH Prog Notes HH Notes Chkd. Checked X-Sec.
Indexed C.J. Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.		
139+00				382.0		℄
				381.5		11.5
				381.9		12.5 CHAN.
				380.9		18.0
				383.1		18.5
				385.1		24.0
				387.0		46.5
				388.4	7.5	
				386.0	17.5	
				390.1	35.0	
				393.0	50.0	
139+25.0				383.8		
139+29.0				382.3		CHAN.
139+38.0				382.3		CHAN.
138+40.0				384.0		

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. 6111-35 Division No.____
No.____ Date____ Date____ Survey of Tract 10 Dr. St. Map 12425
X-Sec. Notes Chkd.____ Checked____ Survey by [illegible] Notes [illegible] Date [illegible]
No.____ Date____ Date____ Map No.____ Indexed C. J. Galli Date [illegible]

F.B. 3350 Pg. 63

STATION	B. S.	H. I.	F. S.	ELEV.		
139+50				385.7		BL
				390.0		10.0
				393.0		15.5
				395.0		47.5
				383.9	4.0 CHAN.	
				383.9	14.0	
				387.8	34.0	
				390.3	50.0	
140+00				384.3		BL
				385.0		6.5
				396.0		27.5
				401.0		40.5
				401.3		55.0
				385.8	3.0 CHAN.	
				385.8	12.0	
				394.6	32.5	
				402.3	45.5	
				404.0	65.5	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3350 Pg. 64 | Job No 6117.75 Division No. | Notes Red | Plotted | Profile
Survey of Norco Dr. SD No. 1225 | Date | Date | No.
Survey by Hill Pargas Notes | Notes Chkd. | Checked | X-Sec. No.
Indexed C.J. Gallt | Date | Date | Date

STATION	B. S.	H. I.	F. S.	ELEV.		
140+10.0				386.9		R Chan.
140+25.0				385.1		L
140+42.00	Fd. No. 1 = Inter			391.6		R
FB 3350-12	Easement Lt.					
T.P.				397.77	1 x 2 Stake RE	12.74 S/O Sta. 140+42.0
140+50.0				395.20		R
				388.9		120 Chan.
				385.9		17.0 L
				400.1		40.0
				400.6		60.0
				397.6	5.0	
				392.0	15.0	
				402.0	42.0	
				403.5	55.0	

76-L296 CE 307 3-61

399.9

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line. 19.3 406.0

Profile Notes Red____ Plotted____ Job No.____ Division No.____
No.____ Date____ Date____ Survey of [illegible] SD No 1225
X-Sec.____ Notes Chkd.____ Checked____ Survey by [illegible] Notes____ Date____
No.____ Date____ Date____ Map No.____ Indexed G.J. CALL Date____

STATION	B. S.	H. I.	F. S.	ELEV.		
141+00				397.9		
				386.5		26.0 CHAN
				386.5		38.0
				393.5		50.0
				398.3		59.0
				398.7		70.0
				399.8	10.5	
				403.3	37.0	
141+47.30	APT D-Tramm PE 1K2 TR9 FD 350-12,9)			400.6		
141+50						
				398.6		170
				388.0		430 CHAN
				388.0		540
				396.6		40.0
				399.4		85.0
				406.0	19.0	

F. B. 7-[illegible] Pg. [illegible]

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

392.06 TP

Do not extend notes this side of this line.

F.B. 3350 Pg. 66 | Job No. 6117.25 | Division No. | Notes Red | Plotted | Profile
Survey of Arroyo Drive No. 1 | Date | Date | No.
Survey by [illegible] Notes | Notes Chkd. | Checked | X-Sec.
Indexed C.J. Ball | Date | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.		
142+00				393.1		BM
				387.8		12.0 CMGH.
				387.8		39.0
				397.8		57.0
				393.5		80.0
				398.6	23.0	
				402.6	45.5	
142+26.0				393.3		BM
142+50.0				388.6		BM
				388.5		8.0 CMGH.
				388.5		28.0
				398.4		50.0
				399.2		70.0
				391.0	17.0	
				391.9	34.0	
				403.7	50.0	
				403.9	60.0	

76-L296 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. 2[illegible] Division No.____
No.____ Date____ Date____ Survey of [illegible] Notes____ Date 3-[illegible]
X-Sec. Notes Chkd.____ Checked____ Survey by [illegible]
No.____ Date____ Date____ Map No.____ Indexed C.J. CALL Date [illegible]

F.B. [illegible] Pg. [illegible]

STATION	B. S.	H. I.	F. S.	ELEV.		
142461.0				392.9		43.0 Back AR
				397.9		Top AR
143+00				390 5		
				389 5		21.0 CMP K
				389.5		35.0
				389 8		38.0 Bot AR
				397.7		41.0 Top AR
				398.3		60.0
				391.1	3.0	
				397.7	26.5	
				399.0	30.5	
				404.5	40.5	
				405.0	51.0	
143+020				389.7		40.0 Back Wall
				397.8		Top Wall

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

399

Do not extend notes this side of this line.

F.B. 3350 Pg. 68 | Job No 6112.25 Division No. Notes Red Plotted Profile
Survey of Arroyo Dr SD No 1225 Date Date No. X-Sec.
Survey by AHH 2951 Notes AHH Notes Chkd. Checked
Indexed C.J. GALLI Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.		
143+24.0				389.0		TR CHAN XING
143+41.0				389.0		RL " "
143+50				391.9		TR
				395.0		11.0
				403.5		25.0
				405.5		53.0
				391.7	7.5	
				389.7	10.0 CHAN.	
				380.7	22.0	
				393.3	42.0	
				396.5	50.0	
				404.4	58.0	
				405.4	74.0	
143+92.0				389.?	39.0	FL. Outlet drain

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. X-Sec. No. Notes Red Date Notes Chkd. Date Plotted Date Checked Date Job No. 6446.25 Division No. Survey of HARO YO DR. SD Survey by [illegible] Notes [illegible] Date 3-7-67 Map No. Indexed [illegible]

F.B. 3350 Pg. 69

STATION	B. S.	H. I.	F. S.	ELEV.		
144+00				401.3		B 329 S E
				402.68		33.0
				401.5	9.0	
				391.7	30.0	
				399.7	50.0	
				403.1	58.0	
				403.6	73.0	
BM SD1054				406.01	BM SD 1054 ELEV. 406.012 FB 3338 40	
					TOP OF DR. STR. SIDE - APPROX. 54' W/o ℄ INLET @ BOTTOM OF CURB, PP# S13963E A SET SPK & LEAD IN IN S/E SIDE POLE	
144+25				401.6		℄
				401.73		16.0
				402.37		28.0
				402.71		41.0

76-L298 CE 307 3-81

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3350 Pg. 70 Job No. 61735 Division No. Profile
Survey of ZR 80 XO DR 80 NO 1 2 5 No. X-Sec.
Survey by [illegible] Notes Date Notes Red Date Plotted
Indexed C.J. GALLI Date Notes Chkd. Date Checked Date

STATION	B.S.	H.I.	F.S.	ELEV.		
144125				401.5	22.0	
				402.2	41.5	
				402.3	50.0	
				403.5	60.0	
144150.0				401.00		Rt Pvmt Xing.
144150.90	APT RT & RH Found FB3350-16			400.99		℄
				400.84		7.5 Edge Pvmt
				400.9		22.5
				400.8		39.0
				401.0		64.0
				400.91	9.5	
				401.6	26.5	
				401.5	50.0	
				402.6	70.0	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.		
144+690				400.72	23.4 Top drain Farmer	
				398.72	F.L. "	
144+856				401.00	24.0 Top drain Farmer	
				399.00	F.L. "	
144+916				394.00		31.0 F.L. Inlet 36" CMP
145+00				401.55		
				401.35		8.5 Edge Pvmt
				401.4		15.0
				398.6		76.0
				394.2		33.5 Ctr.
				394.2		38.5
				397.7		45.0
				400.3		55.0
				401.8		95.0
				405.3		115.0

Profile Notes Red____ Plotted____ Job No. 61 W 25 Division No.____
No.____ X-Sec. Date____ Date____ Survey of Fuerco 52 Line C.D. No. 12.25
No.____ Notes Chkd.____ Checked____ Survey by____ Notes____ Date____
Date____ Date____ Map No.____ Indexed C. J. CALLI Date 7-4-61

F. B. 3350 Pg 41

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3350 Pg. 72
Survey of Arroyo Dr. SD No. 1225 Division No. Job No. 61125 Notes Red Plotted Profile
Survey by HHS Notes HHS Date Date No. X-Sec.
Indexed Date Notes Chkd. Checked No.
Date Date

STATION	B. S.	H. I.	F. S.	ELEV.		
145+00				401.69	10.0	
				402.3	24.5	Bot Wall
				403.41	24.5	Top "
				402.7	52.0	Dwg
				404.77	52.0	Elev. Mech Invert Dwg
145+12.0				400.49		67.0 Elev Floor Inlet Dwg
145+50.0				403.64		
				403.27		14.0 Edge Pavt
				402.4		18.0
				400.1		38.0
				396.1		43.0 Chan.
				396.1		47.0 "
				399.4		50.0
				399.6		71.0
				400.3		98.0
				404.4		114.5
				409.5		130.0

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. 64L2-25 Division No.
No.____ X-Sec. Notes Chkd.____ Checked____ Survey of Lopez Rd & Dr 5004+1225
No.____ Date____ Date____ Date____ Survey by____ Notes____ Date____
Date____ Date____ Map No.____ Indexed C.J. CALL Date 11-64

F.B. 3350 Pg. 73

STATION	B. S.	H. I.	F. S.	ELEV.		
145+50				403.61	6.0 Edge Pvmt	
				404.2	18.5	
				406.5	33.0	
				406.9	50.0	
145+62.0				403.71		81.5 Floor Inlet (Dwg
145+90.37	PI Fd. 1x2 Tag FB 3350-77			406.41		
146+00				407.15		
				406.97		9.5
				406.59		19.0 Edge Pvmt
				406.2		27.0
				401.4		39.0
				400.4		50.0
				397.4		54.0 Chan.
				397.7		60.0
				399.7		79.0
				401.7		115.0
				406.7		126.0
				411.7		141.0
				416.7		154.0

76-L298 CE 307 3-61

3974

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3350 Pg. 74 | Job No 6112.25 Division No. Dr SD No 1225 | Notes Red ____ Date ____ | Plotted ____ Date ____ | Profile No. ____ X-Sec. No. ____

Survey of Hollywood Dr | Notes Chkd. ____ Date ____ | Checked ____ Date ____

Survey by Hyperion Notes ____ | Indexed C. J. GALLI

STATION	B. S.	H. I.	F. S.	ELEV.		
146+00				407.1	2.0 Edge Pvmt	
				407.8	13.0	
				414.6	21.0	
				420.0	36.0	
146+50.0				411.20		
				411.05		15.0 Edge Pvmt
				411.1		23.5
				409.5		35.0
				407.7		50.0
				400.5		61.0
				400.3		79.0
				398.2		88.0 Chan.
				398.2		96.0
				401.0		102.0
				401.7		120.0
				404.7		154.0

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. 6422 Division No.____
No.____ Date____ Date____ Survey of 1980 Xo Dr SD No 1225
X-Sec. Notes Chkd.____ Checked____ Survey by____ Notes____ Date____
No.____ Date____ Date____ Map No.____ Indexed C.I. GALLI Date____

F.B. 30550 PG 75

STATION	B. S.	H. I.	F. S.	ELEV.		
146+50.0				411.00	10.0 Edge Pvmt	
				412.4	18.0	
				416.9	24.0	
				425.0	37.0	
146+82.0				398.06		123.0 Flowline of 36" RCP
146+91.0				398.21		132.0 Flowline of 36" RCP
146+75				412.70		
147+00				413.19		
				413 14		15.0
				413.00		28.0 Edge Pvmt
				413.1		42.0
				~~408.6~~ 408.6		53.0
				~~402.6~~ 402.6		100.0
				~~402.7~~ 402.7		125.0
				~~398.8~~ 398.8		134.0 C&GPM
				~~398.8~~ 398.8		139.0
				~~403.7~~ 403.7		145.0
				~~406.2~~ 406.2		175.0

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

10.0 416.00
25.0 409.00

Do not extend notes this side of this line.

F.B. 3050 Pg. 76 | Job No. 61125 Division No. ____ Notes Red ____ Plotted ____ Profile
Survey of Hacienda Dr. Sta 140+32.5 to 151+87 No. ____ Date ____ No. X-Sec.
Survey by Williams Notes 4/11 Notes Chkd. ____ Checked ____
Indexed C.J. GALLI Date ____ Date ____ No. ____

STATION	B.S.	H.I.	F.S.	ELEV.		
						℄
147+00				413.17	6.5 Edge Pvmt	
				413.4	11.5	
				422.0	22.0	
				426.5	34.0	
147+28.0				407.83		81.5 Floor Level Dwg
147+45.5	P.O.T.			413.6		℄ Toll Dr @ Tr. Line
	℄ 1X2 Tag			413.19		10.0 Edge Pvmt
	FB 3350-18			412.50		27.0 " "
				412.3		35.0
				409.5		46.0
				407.2		77.0 Dwg
				416.0	10.0	
				419.0	75.0	
BM SD1055				406.24	BM SD1055 Elev 406.240 FB 3338-41 Toll Dr. Prod. N'ly side approx 79' W/o W'ly Line Tr. 11091 - 14" Twin Elm 79' N/o ℄ Prod. Reset spike & orange in S. side N. tree	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.		

Profile Notes Red Plotted Job No. 6112 Division No.
No. Date Date Survey of Tierra Dr. SDN 11225
X-Sec. Notes Chkd. Checked Survey by Notes
No. Date Date Map No. Indexed Date Date

F. B. [illegible] Pg. 77

F. B. 3550 PG. 78

Job No._____ Division No._____ Notes Red_____ Plotted_____ Profile

Survey of_____ Date_____ Date_____ No._____

Survey by_____ Notes_____ Notes Chkd._____ Checked_____ X-Sec.

Indexed_____ Date_____ Date_____ Date_____ No._____

STATION	B. S.	H. I.	F. S.	ELEV.	

76-L298 CE 307 3-61

PLEASE RETURN TO

LOS ANGELES COUNTY ENGINEER

403 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Arroyo Dr SD No 1225
JN 61225 Tape Std °F
Surveyed by HHSprings
Notes Walsh Date 3-22-61
Indexed C. J. GALLI APR 14 61

F. B. 3350 PG. 79

JN 61225
Arroyo Dr. SD No 1225
Location of Improvements
Redding Ave (TR 5534 TR 11091)

POT - Redding Ave (131.76 S W'ly & Inter @ Terrace Ave) = Sta. 1+00.00
NE'ly & S. W'ly.

Alignment: FB 3345-48,49
FB 3350-5

Xsections FB 3350 - 81-86

HHSprings
MA Walsh
A.R. Workman
R.L. Benstead

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

76F309S CE#310 1-65

F. B. 3350 Pg. 80

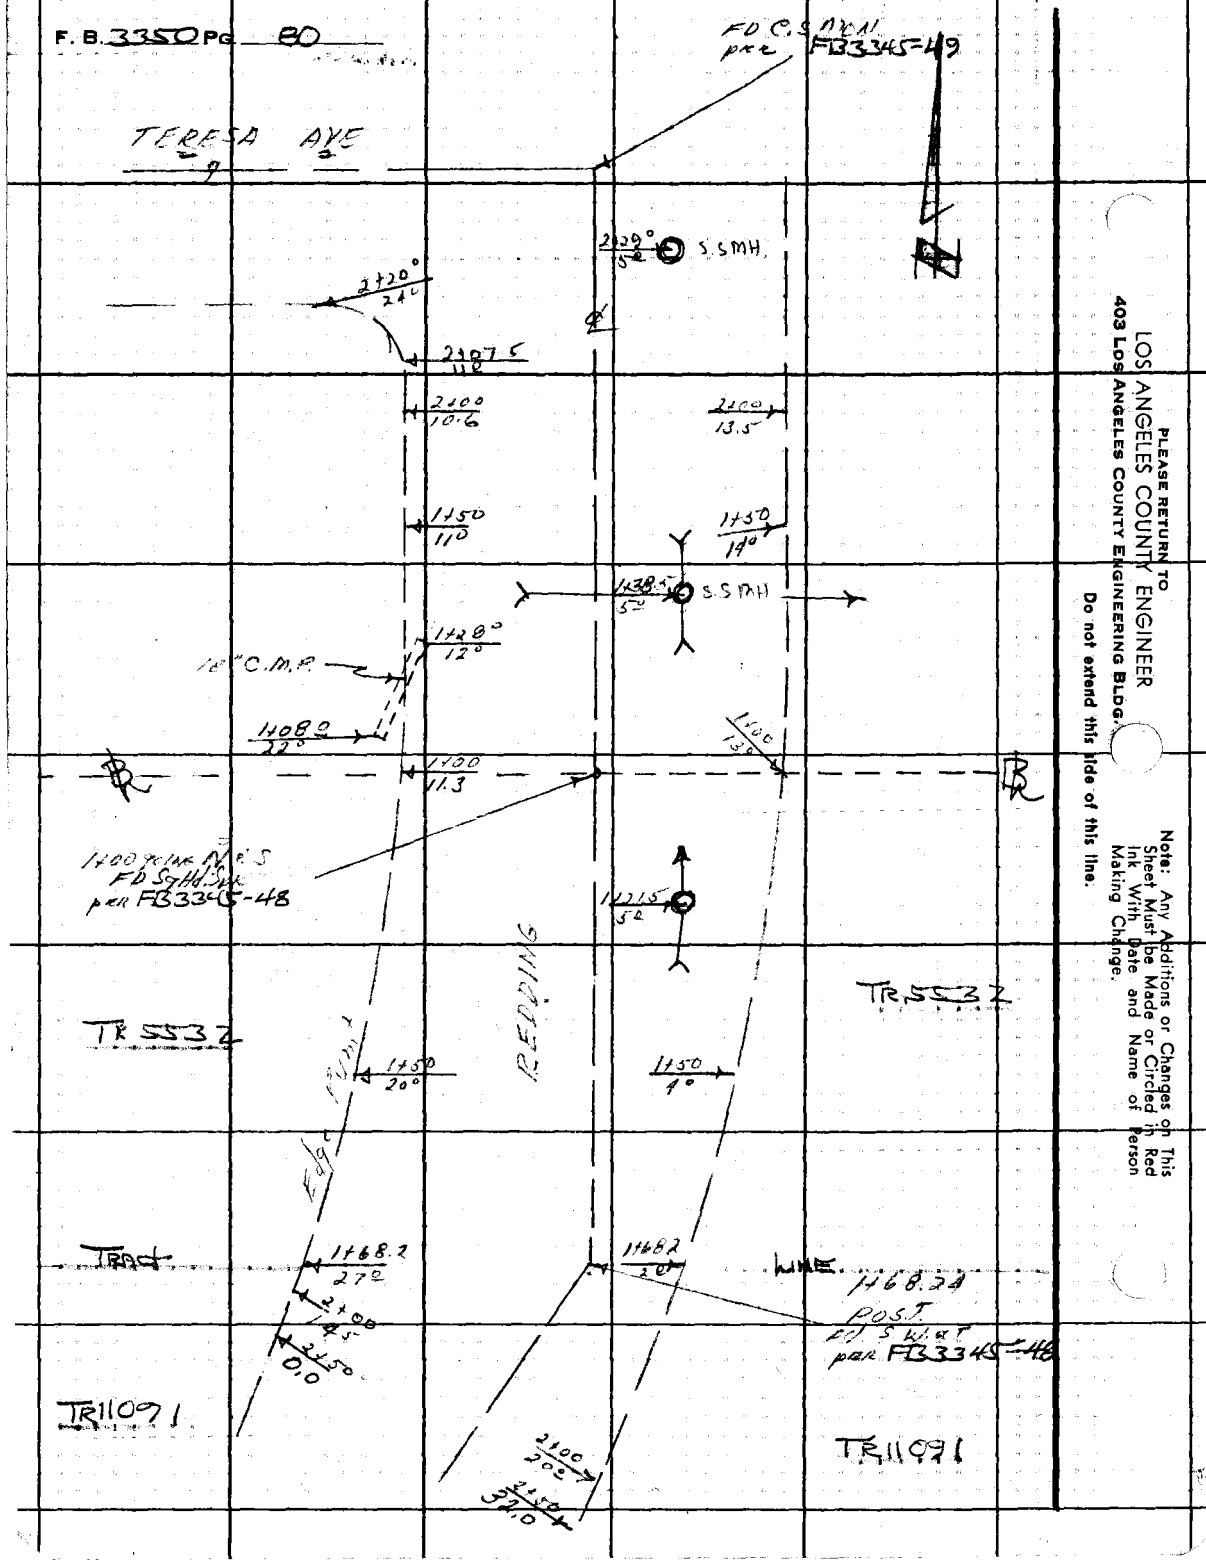

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Do not extend this plat of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

F.B. 3350 Pg. 81

Profile No. ____ Notes Red ____ Date ____ Plotted ____ Date ____ Job No 6111225 Division No. ____
X-Sec. No. ____ Notes Chkd. ____ Date ____ Checked ____ Date ____ Survey of Arroyo Dr SD No 1225
Survey by HHGriggs Notes Wolfe Date 2-21-67
Map No. ____ Indexed C. J. GALLI Date ____

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.	
					IN 6111225 ARROYO DR. SD NO. 1225 X SECTIONS Redding Ave (TR 5532 + TR 11091) P.O.T. Redding Ave (131.76 S. Wly. & Inter. @ Teresa Ave. = Sta 1+00.00 N.Ely & S Wly. Alignment: FB 3345-48, 49, FB 3350-7, Inclusive of Improvements FB 3350-79, 80, H H Griggs M A Walsh R. R. Wiebenson A. L. Bentley

76-L298 CE 307 3-61

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3350 Pg. 82 | Job No 611125 Division No. | Notes Red | Plotted | Profile
Survey of Arroyo Dr. SD No 1775 | Date | Date | No. | X-Sec.
Survey by Hillcrest Notes MB Watch | Notes Chkd. | Checked | No.
Indexed C.J. GALL | Date | Date

STATION	B. S.	H. I.	F. S.	ELEV.	℄	℄	Rt
BMSD1051				363.34	BMSD1051 Elev. 363.344 N. Redhill Ave - Elev. sign Approx. 77' S/℄ & Inter. ℄ Terrace Ave 43.5' E/o ℄ in set spkin Lead in conc wall @ S/y Esplanade Drive		FB 3538-38
1+00 Going North				364 62		℄	
				364 28			13° Ed Pmt
1+15				364 41	14.3 ed Pmt		
1+30				363 89			
				364 41		℄	
				364 17			12° Ed Pmt
				364 87			10± 6Hk
				364 4			25 P/L
				363 91	12° Pmt		
				365 0	11° Pmt Low edge Pmt		
				365 2	25 P/L		
2+00				367 78		℄	
				367 85			12.5 Pmt
				368 32			13.5 ed. Pmt
				366 6			19.0 Bmk
				367 4			25 P/L

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. 6122.23 Division No.____
No.____ X-Sec. Date____ Date____ Survey of Parcel 4 (R/W) Dr 1225
No.____ Notes Chkd.____ Checked____ Survey by [illegible] Notes____ Date____
Date____ Date____ Map No.____ Indexed C.J. GALLI Date____

F.B. [illegible] PG. 83

STATION	B. S.	H. I.	F. S.	ELEV.	LT	℄	RT
2+00				367 67	9.6 pvmt		
				368 26	10.2 ed. pvmt		
				369 1	38° P/L		
2+				370 20		℄	Intsc Fi [illegible]
2+30				371 41		℄	
1+00 Sping		South		364 62		℄	
1+ — 30				369 25		℄	
				369 77			85 ed pvmt
				369 84			20 ed pvmt
				370 4			25° Tp Lnk
				368 4			34° "
				367 8			21° "
				369 02	40 ed. pvmt		
				367 68	75 Lot Lnk		
				366 9	13° Tp "		
				367 5	23°		
				365 5	38°		

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3250 Pg. 64 | Job No. 61122 5 Division No. ____ Notes Red ____ Plotted ____ Profile ____
Survey of Acton Line S.D. to 1225' Date ____ Date ____ No. ____ X-Sec. ____
Survey by Sorensen Notes Lights Notes Chkd. ____ Checked ____ No. ____
Indexed C.J. GALLI Date ____ Date ____ Date ____

STATION	B. S.	H. I.	F. S.	ELEV.	L T	℄	R T
1+66.22	Rr. Ls to bed	Line		371 43		2	1200
				372 19			125 ext. pvmt
				372 86			27 edge pvmt
				373 5			32
				374 2			168
				371 13	2' edge pvmt		
				371 6	35' TP dwl		
				370 7	125'		
				3602	332		
2+00				376 27		4	
				375 03			13 pvmt
				375 6			245'
				371 5			341'
				376 35	25 edge pvmt		
				376 50	18.5		
				376 82	21 edge pvmt		
				3795	20'		

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. 4422-25 Division No.____
No.____ Date____ Date____ Survey of Lawndale Ave S/O Hawthorne
X-Sec. Notes Chkd.____ Checked____ Survey by [illegible] Notes [illegible] Date [illegible]
No.____ Date____ Date____ Map No.____ Indexed C. J. GALLI Date____

F. B. [illegible] Pg. 25

STATION	B. S.	H. I.	F. S.	ELEV.	L ℄	℄	℄'s
2+50				383 34		℄	edge pvmt
				383 8			10'
				381 9			15'
				383 08	2° Rt ℄		
				383 63	17° Rt ℄ RD		
				383 60	23° Rt ℄		
				383 95	24° Rt edge pvmt		
				388 5	41° Rt ℄		
34 00				387 96		℄	pvmt edge
				388 5			11'
				387 58	1° Rt ℄		
				386 19	18° Rt ℄ RD		
				387 60	32° Rt ℄		
				386 35	42° Rt ℄		
T.P.				380 01			
T.P.				371 43			
BM SD 1051				363 34	BM SD 1051 - Elev 363.34 - FB 3338-38		
					N. Redwing Ave - E/y side - Approx 20' S/y		
					℄ Intsn @ Teresa Ave & 3.5' E/O ℄ - A 5/8"		
					Spk in lead - in conc. wall @ S/y edge ditch		

F. B. 3350 Pg. 86

Job No. Division No. Notes Red Plotted Profile

Survey of Date Date No.

Survey by Notes Notes Chkd. Checked X-Sec.

Indexed Date Date Date No.

STATION	B.S.	H.I.	F.S.	ELEV.	

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

76-L298 CE 307 3-61

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of ARROYO DR SD No 1225 F. B. 3350 PG. 87
IN 611225 Tape Std °F
Surveyed by HHGriggs Date 3-21-67
Notes
Indexed C. J. GALLE APR 24 '67

FM 611225

ARROYO DR. SD. No. 1225
Location of Improvements

Toll Drive (TR 1091)

POT - Toll Dr. (H 68.38 W/Y ℄
Hiker & Tegner Dr = ℄ of R/W
Easement per TR. 1091)
= 54 R. 1400.00 N. W/L & S. E/L

Alignment FB 3350 - 10, 11, 13,
Xsections - FB 3350 - 91-98

HHGriggs
MAWalsh
R.R. Workman
P.L. Beasley

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

76F309S CE#310.1-65

F. B 3350 Pg. 88

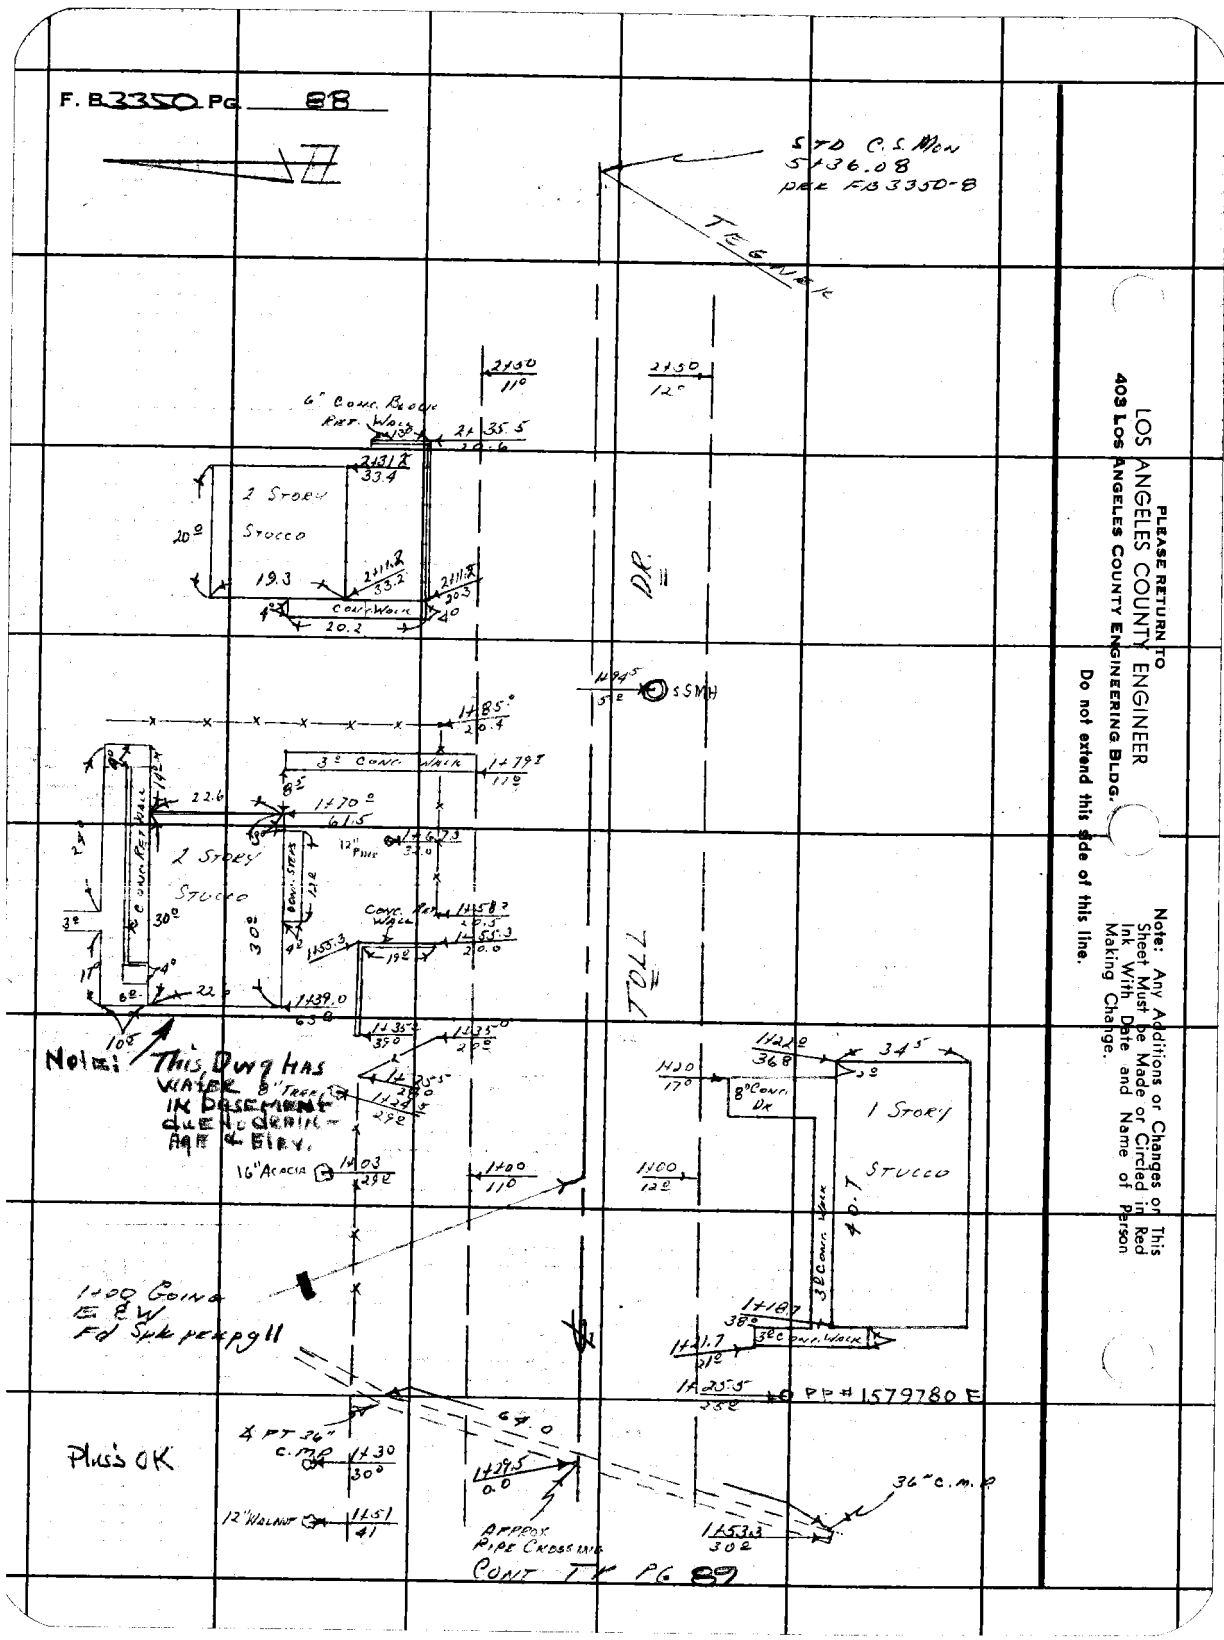

Note: This Dwg has water 8" Trace in basement due to drainage age & Elev.

1400 Going E & W Fd Spk per pg 11

Plus's OK

Cont TY Pg 89

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by	Survey of Arroyo Dr SD #1935	F. B. 3350	Pg. 89
Map No.	JN ____ Tape ____ Std. ____ °F		
Office Work	Surveyed by Soriges		
Checked	Notes Walsh Date 3-21-67		
Date	Indexed C. J. GALLI		

CONT BOT P.B. 88

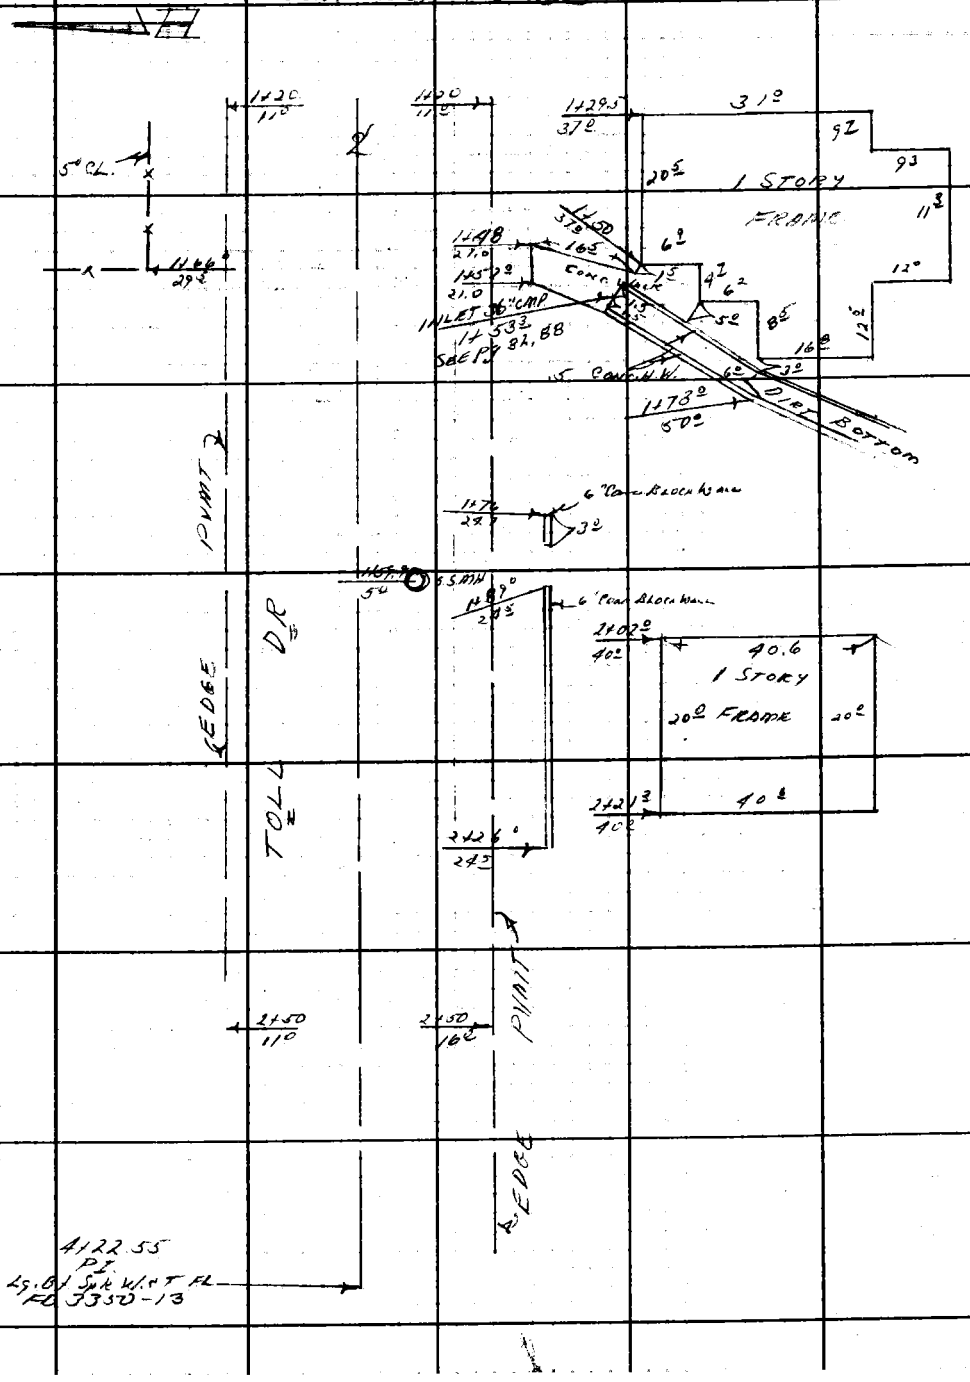

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

76F3095 CE#310 1-65

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

F. B. 3350 PG. 90

F.B. 3350 Pg. 91

Profile No. ____ X-Sec. No. ____
Notes Red ____ Date ____ Notes Chkd. ____ Date ____
Plotted ____ Date ____ Checked ____ Date ____
Job No 6112.25 Division No. ____
Survey of ARROYO DR. SD No 1225
Survey by ____ Notes ____ Date 3-22-67
Map No. ____ Indexed C. J. CALLI Date ____

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.

FH 6112.25

ARROYO DR. SD No 1225

Xsects

℄ TOLL DRIVE (TR 11091)

POT-TOLL DRIVE (436.38 W'ly

℄ INTER. @ TEGNER DRIVE = ℄

DRAIN EASEMENT per TR 11091)

= Sta 100.00 N.W'ly & S.E'ly.

ALIGNMENT: FB 3350-10, 11, 13,

LOCATION OF IMPROVEMENTS FB 3350-87-90

H.H. SMITH
SURVEYOR
P.L. 4[illegible]
P.L. [illegible]

76-L298 CE 307 3-61

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

BMSD1053 38406.5
Mk-step Dwg # 7516

F. B. 3358 Pg. 92 | Job No. 5111.75 Division No. | Notes Red | Plotted | Profile
Survey of Harbor Dr. SD No 12.25 | Date | Date | No.
Survey by Hayworth Notes M.P. Blanchet | Notes Chkd. | Checked | X-Sec.
Indexed C. J. GALLI | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.		
BMSD1052				38208	BMSD1052 Elev. 38208.5 FB3358-39 Toll Dr. - N/Y side - Approx. 326' W/o ℄ Inter@ Tegner Dr. A set spk in conc. step @ R House # 1745 Toll Drive	
1+00 going W				37738	℄	
				37745		11° Ed. Pvmt
				3782		27°
				3784		37
				37711	12° Ed Pvmt	
				3769	14 FL	
				38178	33.5 conc. walk	
				38183 38253	37° R. Hse. FLR Elev	
1+50				37898	℄	
				37897		12 Ed Pvmt
				3800		29
				3805		39
				37832	12.5 Ed Pvmt	
				37756	21.5	

76-L296 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. [illegible] Division No. ____
No. ____ Date ____ Date ____ Survey of Arroyo Dr. Sta 12+25
X-Sec. Notes Chkd. ____ Checked ____ Survey by [illegible] Notes [illegible] Date 3-31-67
No. ____ Date ____ Date ____ Map No. ____ Indexed C.J. GALLI Date 4-3-67

STATION	B. S.	H. I.	F. S.	ELEV.	Lt	℄	Rt
1+60				377 80			37 MSF.
1+59.9				379 90	5° MH		FLR Elev
W Rim				380 82	W	E	
INLET W/				369 65	380.82 Rim	380.67	
E. Rim				380 67	-10.50 MEAS	10.73	
OUTLET E				369 27	370.32	369.94	
2+00				382 09	-.67 dia	-.67	
				381 95	369.65	369.27	11° Ed Run
				382 9			30° P/L
				381 52	16° Ed. Run+		
				381 6	20° BRK		
				381 0	23° Lt brk		
				380 60	40°		
				381 93	FLR Elev		
2+50				385 73			
				385 47			11° Ed Run
				3874			28°
				385 43	16° Ed Run		
				385 9	32°		

F. B. 3350 PG. 93

76-L296 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F. B. 3350 Pg. 94 Job No. 6122.5 Division No. Notes Red Plotted Profile
Survey of Duarte Rd. S.D. # 122.5 Date Date No. X-Sec.
Survey by Surveys Co. Notes Chkd. Checked
C. J. Gallu Date Date
Indexed Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	LT	℄	RT
3+00				389 52		℄	
				389 30			16.5 Ed Pvmt
				390 6			26
				389 18	16.5 Ed. Pvmt		
				389 2	28		
14+00 going E				377 38			
14+50				378 15		℄	
				378 07			12.5 Ed pvmt
				378 4			18.5
				378 2			23
				378 37	10.5 Ed Pvmt		
				377 9	20		
				377 4	38 bot wall		
				377 76	38 " "		
				373 25	69.5 bot "		
				373 2	61.5 @ Hse		
				371 20	Flr. Elev.		

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red Plotted Job No. 442.25 Division No.
No. Date Date Survey of Reserve Line S.D. #1225
X-Sec. Notes Chkd. Checked Survey by [illegible] Notes [illegible] Date 3-31-67
No. Date Date Map No. Indexed C.J. GALLI Date

F.B. 3351 Pg. 95

STATION	B. S.	H. I.	F. S.	ELEV.	Lt	℄	Rt
14 75				380 04		℄	
				379 74			13⁵ Ed. Pvmt
				379 3			16⁵ brk
				380 3			22⁵ "
				385 3			31⁵
				380 19	11° Ed. Pvmt		
				378 3	20° Berm		
				374 3	27° brk "		
				372 3	59° FLAT		
				371 5	70° "		
14 94.5							5° Rt ℄
Rim W				371 22	E	W.	N
INLET W				358 72	371.37 Rim	371.22	371.2
Rim N				371 29	11.87 Meas	11.83	12.2
OUTLET N				358 34	359.50	359.39	358.0
Rim E				371 37	- 67	- 67	- 67
INLET E				358 83	358.83	358.72	358.31

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3350 Pg. 96 | Job No. 61125 Division No. | Notes Red | Plotted | Profile
Survey of Alameda Av S D H 1225 | Date | Date | No.
Survey by Sept 1965 Notes Lyons | Notes Chkd. | Checked | X-Sec.
Indexed C. J. GALLI | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	L ℄	℄	R ℄
2+00				381 83		℄	
				381 46			14° Ed Pvmt
				381 8			20 bnk
				386 8			31
				381 64	11° Ed Pvmt		
				381 22	18° ed dr		
				374 77	45°		
				373 7	50° Toe		
				373 1	13° Flat		
2+11.3				373 96	F/e Elev		
2+50				386 01		℄	
				386 08			12° Ed Pvmt
				3885			23°
				385 59	12° Ed Pvmt		
				389 2	22°		
3+00				390 02		℄	
				389 85			12° Ed Pvmt
				389 9			19°
				389 85	11° Ed Pvmt		
				389 9	23°		

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.		
BM SD 1052				382.08	BM S.D. 1052 - Elev 380.085 - FB 3336-31 Toll Dr - Nly side - Approx 326' W/O ℄ Duffer ⊙ Tegner Dr - A set spike in conc stem ⊙ ℄ Hse 7445 Toll Dr	

Profile Notes Red Plotted Job No. 6113-25 Division No.
No. X-Sec. Date Date Survey of Hillcrest Dr SD #1225
No. Notes Chkd. Checked Survey by [illegible] Notes [illegible] Date [illegible]
Date Date Map No. Indexed C. J. GALLI Date

F. B. 3336 Pg. 97

F.B. 3350 PG 98

Job No._____ Division No._____ Notes Red_____ Plotted_____ Profile

Survey of _____ Date_____ Date_____ No._____

Survey by_____ Notes_____ Notes Chkd._____ Checked_____ X-Sec.

Indexed_____ Date_____ Date_____ Date_____ No._____

STATION	B.S.	H.I.	F.S.	ELEV.

76-L298 CE 307 3-61

PLEASE RETURN TO

LOS ANGELES COUNTY ENGINEER

403 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK. WITH DATE AND NAME OF PERSON MAKING CHANGE

F.B. 3350 PG. 99

Profile No. ____ X-Sec. No. ____
Notes Red ____ Date ____ Notes Chkd. ____ Date ____
Plotted ____ Date ____ Checked ____ Date ____
Job No. 6112.25 Division No. ____
Survey of Arroyo Dr. SD No. 1225
Survey by ____ Notes ____ Date ____
Map No. ____ Indexed C.J. GALLI Date MAR 14 '67

FN6112.25
ARROYO DR. S.D. NO. 1225

XSECTIONS

℄ = ℄ 8' drain easement - Sta. 1+0000
= POT ℄ @ Common Pr. lots 11 & 12
TR11091 - S/Y to Common Prop.
Cor. lots 11 & 12 TR11091 = Sta. 2+22.45 (Above portion of EASEMENT has been filled and is not a natural drain)
Thence profile ℄ easement per TR11091 to ℄ TEGNER DR.
Alignment FB3350-12

H.H. HOLLISTER
MARK M. ...
R.R. MACKINNON
P.L. BEASLEY

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

76-L298 CE 307 3-61

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3350 PG. 100

Job No. 6111.75 Division No. Notes Red Plotted Profile
Survey of Gen'l Dr. SD No. 2275 Date Date No. X-Sec.
Survey by HH Segesta, MA Welch Notes Notes Chkd. Checked No.
Indexed C.J. GALLI Date Date Date

STATION	B. S.	H. I.	F. S.	ELEV.		
BM SD 1054				406.01	BM SD 1054 Elev. 406.012 FB 3338-40 Tail Dr. S'ly side - Appx. 547' W/o E'line @ Bailey Ave. PP# 51 963E Asph. on N. s'ly. side Pole.	
T.P.				397.77	1x2 stake 13.74 S/o ℄ Sta. 1+04+47.0 FB 3350-64	
0+60.0				400.0		℄
0+83.0				385.9		℄ - Chaining
0+88.0				385.9		℄ - " "
1+00.00	Fd. Nail = Inter. Tie 44 E 21 Engineering FB 3350-12			39[illegible]7		℄
1+11				39[illegible]7		℄ Sta.
				39[illegible]0		Std
				391 7	10' Stone	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.			
1+25				399 3			
				400 3			
				400 3			
				399 3			
1+50				400 8			
				400 6			
				400 3			
				407 5			
				408 5			
				404 "			
2+00				406 6			
				406 3			
				414 3			
				413 3			
				406 2			
2+02.15	Fd 1 x 2 H FB 3350-12,19 = Common Prop Cor of Lots 11 & 12 - TR 11091 = POT 3" deep in EASEMENT			407 6			
				411 8			
				416 8			
				407 1			

Profile Notes Red____ Plotted____ Job No. 1245 Division No.____
No.____ Date____ Date____ Survey of Alley Y of SD No 1275
X-Sec. Notes Chkd.____ Checked____ Survey by [illegible] Notes Walsh Date____
No.____ Date____ Date____ Map No.____ Indexed C.I. GALLI Date____

F. B. [illegible] Pg. 101

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3350 Pg. 102 | Job No. 61125 Division No. [illegible] SDM 12.5 | Notes Red ____ Date ____ Notes Chkd. ____ Date ____ | Plotted ____ Date ____ Checked ____ Date ____ | Profile No. ____ X-Sec. No. ____

Survey of [illegible] Notes [illegible]
Survey by [illegible]
Indexed C. I. GALLI

STATION	B. S.	H. I.	F. S.	ELEV.		
2+53				412.5		
2+67				[illegible]		
3417.83	INCOMPLETE SET			415.6	E & PT IN ESM'T	PER TR # 11091
3+50				414.1		[illegible]
4+00				413.0		
4+59				412.1		b.c. WALL
4+59				412.[illegible]		TP
5+08				412.[illegible]		TOE SLOPE
5+16				411.0		TP bnd
5+37.13	Nothing set.			410.[illegible]		INTER w/ 8' RESIDENCIAL DR. PER TR. 11091
TP				417.12		
T.P.				409.60		
T.P.				408.04		
T.P.				406.52		
BM SD 1054				406.[illegible]	SD 1054 - Elev. 402.[illegible] - F03338-90	
					TOE Dr. - Service - Approx. 547' W/of Z	
					Service @ Norway Ave - Pole 5159632-8	
					Set Spike brace in Guy Side Pole	

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of Arroyo Dr S.D #1225
IN 6112-25 Type Stg °F
Surveyed by Spry Bass
Notes M.P. Wm Sm JK Date 2-23-67
Indexed C. J. GALLI MR 3 4 67

F. B. 3350 Pg. 103

Y/N 6112-25
ARROYO DR S.D #1225

Location of Improvements

#1 Toll Drive POT Northerly
#2 Fully Mike Telescoping Sta. 1+00.00
#3 Toll Drive POT Southerly
Sta. 1+59 Toll Drive = Sta. 31

Alignments FB 3350 - 16, 15,
Xsections FB 3350 - 105-108.

N/A Springs
Mid Walls
R.R. Walls
Pk Brooks

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

16F3095 CE#310 1-65

F. B. 3350 PG 104

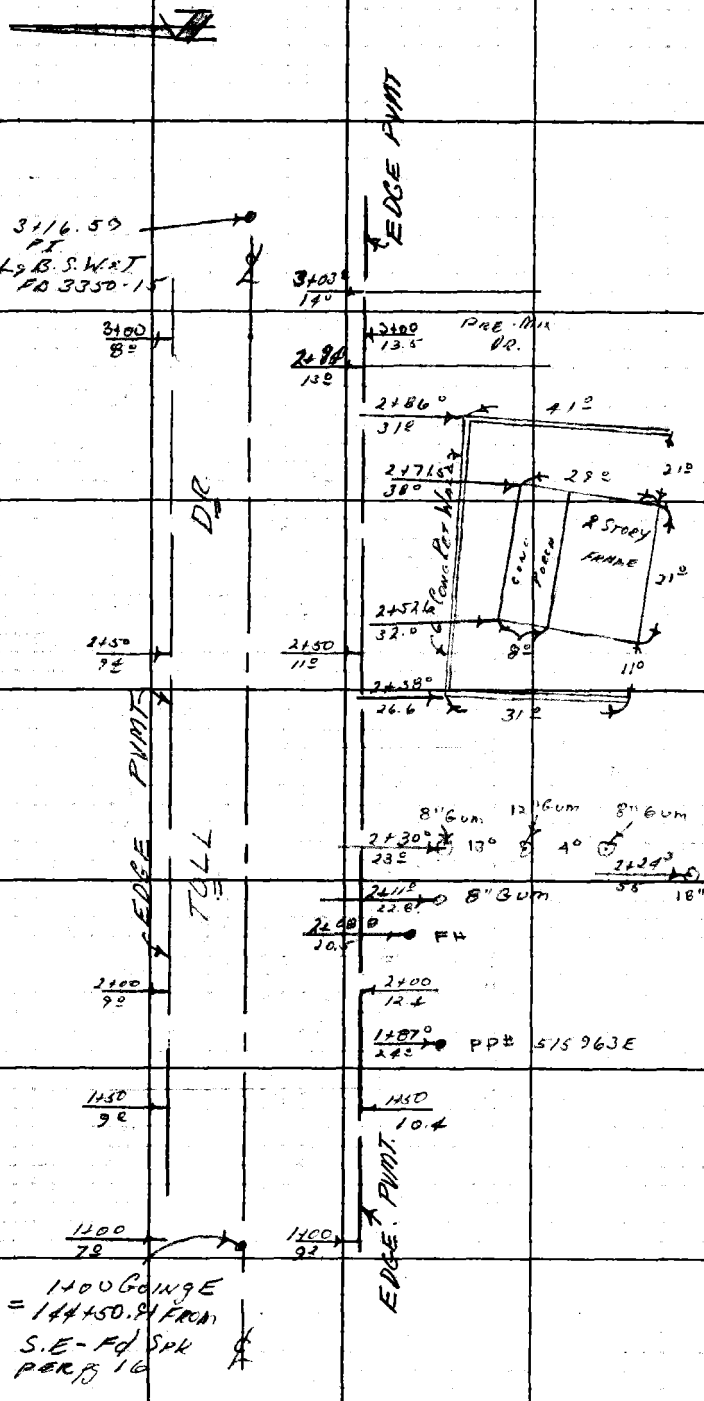

Note:
No Sewers Evident in this portion of Tull Dr. Residents verify this

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

F.B. 3350 Pg 105

Profile No. ____ Notes Red ____ Plotted ____ Job No. 6112.25 Division No. ____

Date ____ Date ____ Survey of GREGORY DR. SD. No. 1225

X-Sec. No. ____ Notes Chkd. ____ Checked ____ Survey by ____ Notes ____ Date 3-27-67

Date ____ Date ____ Map No. ____ Indexed C. L. GALLI Date ____

JN 6112.25

ARROYO DR SD No. 1225

Xsections

Toll Drive POT a drain easement POT (294.67 Ely of WLY line Trilogy) Sta. 1+00.00 Ely to PI Toll Dr. = Sta 3+16.59.

Alignment FB 3350-16,15

Location of Improvement FB 3350-103,104

H.H. Sparks
T. Draft
R. Workman
F.L. Beasley

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

76-L-296 CE 307 3-61

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3350 Pg. 106 | Job No. 6412.25 Division No. Notes Red Plotted Profile
Survey of Traverse Notes Date Date No. X-Sec.
Survey by Hydraulics Notes Notes Chkd. Checked
Indexed Date Date Date No.

STATION	B.S.	H.I.	F.S.	ELEV.	L +	R
BMSD1054				4669	BMSD1054 Elev. 406.912 FB 3338-40 Toll Dr. S/y side. - Approx 54' W/o ℄ Inter. @ Bailey Ave. PP# 515963E A set of Kwikbench in s/y side pole.	
1+00				401 00		℄
				401 00		2.0 Ed Pvmt
				401 +		24.3 To Curb
				401 -		50 Sod
				400 95	7.8 Ed Pvmt	
				400 ?	23.0	
				401 0	33	
				401 5	64	
1+50				402 41		℄
				402 55		10.4 Ed Pvmt
		—		403 1		24.0 To Curb
				399 7		50.0 S.A.
				402 ??	8.0 Ed Pvmt	
				402 9	23.0	
				402 8	33	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	LT	Ø	RT
2450				40 5 45			
				405 08			12.4 [illegible]
				40 4 X			7.6 [illegible]
				40 3 1			50' [illegible]
				3 1 1			20 S.H.
				405 56	0° E/ Plan		
				406 0	17° TOE SLOPE		
				413 8	32 [illegible]		
				407 32			
				406 34			
				408 27			[illegible]
				40 90			26? [illegible]
				40 1 0			37° [illegible]
				406 4			27 6 [illegible]
				406 0			37 [illegible]
				405 0			[illegible]
				408 0	[illegible]		
				403 3	13° TOE SLOPE		
				413 3	26° S.H.		
2503				407 18			10° [illegible]

Profile Notes Red _____ Plotted _____ Job No. 6444 Division No. _____
No. _____ Date _____ Date _____ Survey of Reyd Dec 30 No. 1223
X-Sec. Notes Chkd. _____ Checked _____ Survey by _____ Notes _____ Date 2-27-45
No. _____ Date _____ Date _____ Map No. _____ Indexed C.J. CALLI Date _____

F.B. 3450 Pg 107

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3350 Pg. 108 | Job No. 61122 Division No. | Notes Red | Plotted | Profile
Survey of Arroyo Dr. SD No 1225 | Date | Date | No. | X-Sec.
Survey by [illegible] Notes [illegible] | Notes Chkd. | Checked | No.
Indexed C. J. GATH | Date | Date | Date

STATION	B. S.	H. I.	F. S.	ELEV.	L	R
3+00				410.26		
				[illegible]		
				410.14		
				[illegible]		
				411.05		
				411.6		
				[illegible]		
[illegible]				412.0		

F.B. 3350 PG. 109

Profile No. _____ Notes Red _____ Plotted _____ Job No. 611225 Division No. _____
Date _____ Date _____ Survey of ARROYO DR. S.D. No. 1225
X-Sec. No. _____ Notes Chkd. _____ Checked _____ Survey by HHL Notes HHL Date 3-27-67
Date _____ Date _____ Map No. _____ Indexed C. J. GALLI Date 4-1-67

EN 611225

ARROYO DR. S.D. No. 1225

PROFILE

℄ STRM EASEMENT - POT TOLL DR. (294.67 ELY OF W'LY LINE TR11091), N.W'LY to POT W'LY LINE TR11091 (218.46 N'LY ℄ INTERIOR DRIVE)

STA. 1+00.00 @ TOLL DRIVE
STA. 4+79.83 @ W'LY LINE TR11091

ALIGNMENT: FB 3350-16, 20)

H.H. GOINGS
M.F. WHITE
A.R. VOLKMANN
P.N. BENSLEY

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK. WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

76-L208 CE 307 3-61

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3350 Pg. 110

Job No. 6117.25 Division No. Notes Red Plotted Profile
Survey of Romero Dr. S/O No. Cl225 Date Date No.
Survey by ATK Gregg Notes ATK Notes Chkd. Checked X-Sec.
Indexed C. J. GALLI Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.		
BM SD 1054				406.01	BM SD 1054 - Elev. 406.01 FB 3338-40 Toll Dr S/y side - Approx. sht W/o ℄ ℄ Inter. @ Baileynne. PP ± 5139 E 11 sm top KW brace ims S/y side pole	
1+00.00	POT - Fd Solid FB 3350 - 16			400.99		
1+42.0				399.6		
1+79.0				398.7		
2+32.0				400.3		
2+59.0				405.2		
3+02.5				406.2		
3+11.0				404.0		

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.		
3+51.0				404.5		
3+61.0				406.7		
3+69.0				405.2		
4+21.0				406.0		
4+74.83	POT	FD 1X2-TAG FB 3350-20		406.1		INCHER & EASEMENT & W/V LINE TR 11091
BM SD1055				406.24	BMSD 1055 ELEV 406.24 TOLL DR PROJ. N/V SIDE LINE OF TR 11091-14' PROJ.	FB3338-41 APPROX. 79' N/O W/V TWIN PINE 19' N/O & SPIKE & DISC IN S. SIDE OF N. TREE

Profile Notes Red Plotted Job No. 64-1-35 Division No.
No. Date Date Survey of PARRO XO DR. SD RD 1055
X-Sec. Notes Chkd. Checked Survey by Notes Date
No. Date Map No. Indexed G. J. GALLI Date

F. B. 3350 Pg. 111

F.B. 3350 PG. 112 Job No._____ Division No._____ Notes Red_____ Plotted_____ Profile

Survey of_____ Date_____ Date_____ No._____

Survey by_____ Notes_____ Notes Chkd._____ Checked_____ X-Sec.

Indexed_____ Date_____ Date_____ Date_____ No._____

STATION	B.S.	H.I.	F.S.	ELEV.	

76-L298 CE 307 3-61

PLEASE RETURN TO

LOS ANGELES COUNTY ENGINEER

403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend notes this side of this line.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of ARROYO DR. SD No. 1225 F. B. PG. 113
UN 6112.25
Surveyed by
Notes
Indexed

UN 6112.25

ARROYO DRIVE SD. No. 1225

Location of Improvements

P.I. = W'LY. LINE TR. 11091 - N'LY OF TOLL DRIVE TICKER

Sta 1+00.00 = P.I. TOLL DR @ W'LY LINE TR 11091

Alignment FB 3350 - 18, 20,

X Sections FB 3350 - 117 - 124

HH Sprenger
M.D. Wolcott
A.R. Wilkinson
R.L. Paisley

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

J6F309S CE#310 1-65

(2)

CONT ROT AG 115

F. B. 3350 PG 114

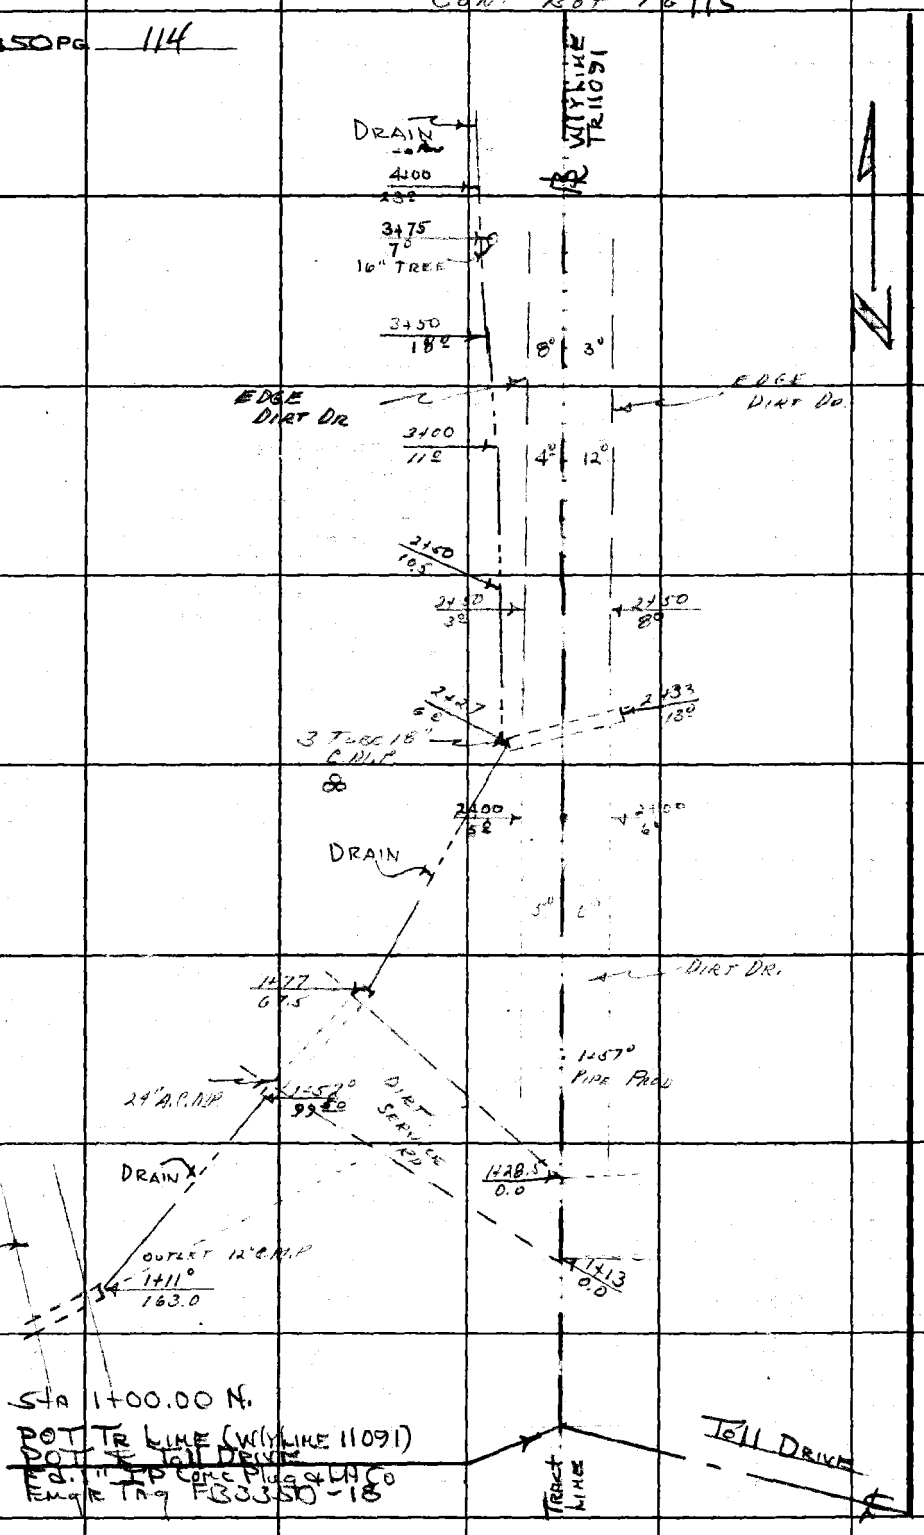

LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

PLEASE RETURN TO

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by		Survey of Approved DPSD 16225	F. B. 3350 PG. 115
Map No.		UNG 11.25 Topo Std °F	
Office Work		Surveyed by HR Coffman	
Checked		Notes Monu'd Date 2-67	
Date		Indexed C. L. CALL	

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

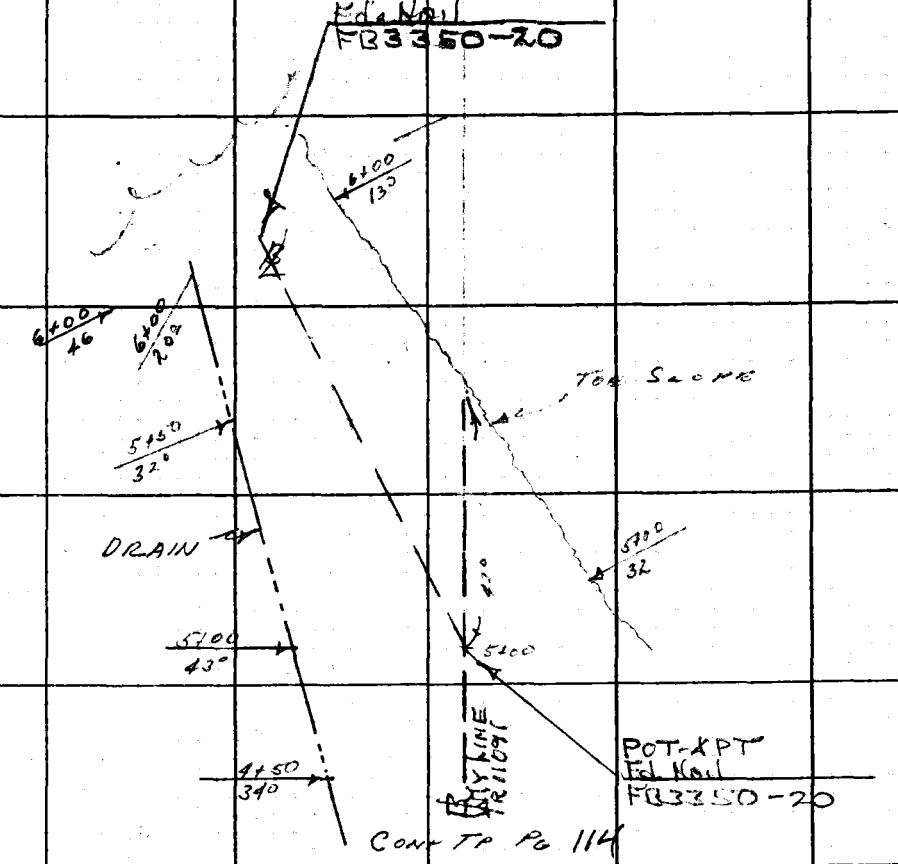

76F309S CE#310 1-65

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

F. B. 3350 PG. 116

F.B. 3350 Pg. 117

Profile No. ____ Notes Red ____ Plotted ____ Job No. 61125 Division No. ____
Date ____ Date ____ Survey of ARROYO DR. SD No. 1225
X-Sec. No. ____ Notes Chkd. ____ Checked ____ Survey by HHG [illegible] Notes MAN Date 3-67
Date ____ Date ____ Map No. ____ Indexed C. J. CALLI Date 3-4-67

JN 61125
ARROYO DRIVE SD No. 1225
X SECTIONS
℄ = W'LY LINE TR. 11091 - N'LY OF
TOLL DRIVE INTER.
STA 1+00.00 = ℄ INTER TOLL DR. ℄
W'LY LINE TR 11091

ALIGNMENT FB. 3350 - 18, 20
LOCATION OF IMPROVEMENTS FB 3350 - 113-116

HHG 11-29-67
MID VALLEY
ARROYO DRIVE
FIELD NOTES

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend notes this side of this line.

76-1298 CE 307 3-61

F.B. 3350 Pg. 118

Survey of NEROD DR. SD. NO 1 Job No 64L125 Division No. Profile

Survey by HH 6/21/65 Notes KMH Notes Red Plotted

Indexed J. CALLE Date Date Date Date Date Notes Chkd. Checked

No. X-Sec. No.

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.	Lt	Rt
BMSD 1055				406.24	BMSD 1055 ELEV. 406.240 FB 3336-41	
					Toll Dr. Prod N/Y. side, approx. 79' W/O	
					W'ly line of Tr. 11091, 14" Twin Elm 79' N/O	
					& Prod A set spk & brnch in S. side of N. tree	
1+00				413.51	TRACT LINE	
				413.37		1½ Ed. Pvmt
				413.29		3½ Pvmt
				414.1	8° brk	
				411.9	31½ "	
				408.6	50° TOE	
				408.5	84°	
1+11°				401.6	163° EL 12" CMP	
				397.7	3rd under fill	
1+50				408.6		℄
				408.6		5° GRD
				408.8		21° "
				408.6	5° ed dr	
				406.1	37° brk	
				408.9	48° Tp "	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red_____ Plotted_____ Job No. 6112-25 Division No. SD
No.____ Date____ Date____ Survey of Alley 20 Dr # 1223
X-Sec. Notes Chkd.____ Checked____ Survey by Surveys Notes 44, 54 Date 3-67
No.____ Date____ Date____ Map No.____ Indexed C. J. CALL Dist. 1

F. B. 3350 Pg. 119

STATION	B. S.	H. I.	F. S.	ELEV.	℄ ℄	TL	P.T.
1+50				407 0	90° brk		
				403 9	100° dv		
				406 5	110 brk		
				408 0	134 gm		
1+52				403 9	99° FL 24" C.M.P.		
1+71				402 7	67.5 FL " "		
2+00				403 7		TL	
—				403 7			6° Srd
				402 2			47° "
				401 9			72° "
				403 7	6° Srd		
				403 7	25° brk		
				400 9	31° bot dv		
				403 3	39° brk		
				404 6	50° TOE		
				407 5	65° S.H.		
2+27				399 9	6° FL 18" C.M.P.		
2+33				399 7			13° FL 18" C.M.P.
—							

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3330 Pg. 170 | Job No 6112.25 Division No. | Notes Red | Plotted | Profile
Survey of Aeroso Dr. S.D. # 1225 | Date | Date | No.
Survey by Sweeney Notes Watson | Notes Chkd. | Checked | X-Sec.
Indexed C.J. GALLI | Date | Date | No.

STATION	B.S.	H.I.	F.S.	ELEV.	L ℄	TL	Rt
2+50				4036		TL	
				4036			6.0 grnd.
				4036			24.0 "
				4036			80.0 grnd
				4036	2° brk		
				4013	8° bot dr		
				4013	13.5 " "		
				4056	17.5 Tp "		
				4120	39.5 TOE SLOPE		
3+00				4056		TL	
				4056			12.0 grnd
				4057			38.0 bot cut
				4116			47.0 Tp "
				4161			58.5 S.H.
				4211			120
				4056	4.5 Tp brk		
				4017	10.5 bot dr.		
				4064	17.0 Tp "		
				4069	21.0 TOE		
				4169	43 S.H.		

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	LT	RT
3+18.5				4061		TL INTER ℄
3+50				4074		TL
				4084		27° 60' cut
				4144		30° TP "
				4184		47°
				4069	5° sed	
				4067	11° TP dr	
				4027	18 60' "	
				4087	22 TP "	
				4132	43 S.H.	
				4182	55° S.H.	
4+00				41247		TL
				4138		15° 60' "
				4167		62° 60' cut
				4200		76° TP "
				4310		91° S.H.
				4113	19° TP dr	
				4102	23° 60' "	
				4128	36° S.H. "	
				4172	50°	

Profile Notes Red ____ Plotted ____ Job No. 61225 Division No. ____
No. ____ Date ____ Date ____ Survey of Alameda Dr. S.D. # 1225 - 67
X-Sec. Notes Chkd. ____ Checked ____ Survey by [illegible] Notes [illegible] Date ____
No. ____ Date ____ Date ____ Map No. ____ Indexed [illegible] Date [illegible]

F. B. 3350 Pg. 121

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3350 Pg. 132 Job No 6112.25 Division No. S.D. # 1223
Survey of Arroyo Dr
Survey by Spriggs Notes W/A Lee
Indexed C.L. GALLI
Profile No. X-Sec. No.
Plotted Date Notes Red Date
Checked Date Notes Chkd. Date

STATION	B. S.	H. I.	F. S.	ELEV.	L	T L	R
4+17				414 3		T L	
4+50				415 6		T L	
				417 8			72° bot cut
				425 5			84° TP "
				429 5			97 S.H.
				415 4	23° brk		
				414 0	29° bot "		
				414 0	34 dk		
				414 7	43° Toe Scarp		
				419 8	60° S.H.		
5+00				416 5		T L	
				419 0			61.6 bot cut
				426 5			80.0 TP "
				430 0			100.0 S.H
				416 2	34° TP brk		
				415 7	43° bot dk		
				416 1	55° brk Toe		
				419 0	65 S.H		
5+00				418 0	@ 90° to Fore Tang		32° bot cut
				416 1	back Tang	T L	prod 42 bot cut

76-L 298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. 6111 25 Division No. Dr. S.D.
No. X-Sec. Date Date Survey of Reservoir # 1225
Notes Chkd. Checked Survey by Sparks Notes Kibler Date 3-
No. Date Date Map No. Indexed G.L. GALLI Date

F.B. 8330 Pg. 123

STATION	B. S.	H. I.	F. S.	ELEV.	L ℄	℄	R ℄
5+50				417 78		℄	
				419 2			23.0 60° out
				423 0			32.0 TP "
				431 0			14.0 S.H
				417 1	32° Lt 1 dr.		
				417 2	43.3 TOE		
				422 4	60 S.H		
6+00				419 0		℄	
				419 2			13° TOE
				426 0			31° S.H
				418 9	20° Lt dr.		
				419 9	16 TOE		
				427 0	60° S.H		
TP				414 22			
TP				413 20			
BMSD1055				406 24	BMSD1055 ELEV 406.240 FB3333-1		
					Toll Dr. Prod. N1Y side Approx 19' W/		
					W. Lake Tr 1109, 14" Twin Elm 19' N &		
					Prod Approx 25' E/ly side Lake N.S. side of		
					N. Tree.		

F.B. 3350 Pg. 124

Job No. 611225 Division No. _____ Notes Red _____ Plotted _____ Profile

Survey of ARROYO DR S.D. # 12225 Date _____ Date _____ No. _____

Survey by SPRIGGS Notes Wash Notes Chkd. _____ Checked _____ X-Sec.

Indexed _____ Date _____ Date _____ Date _____ No. _____

STATION	B.S.	H.I.	F.S.	ELEV.	

76-L298 CE 307 3-61

PLEASE RETURN TO

LOS ANGELES COUNTY ENGINEER

403 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Notes Ck'd by	Survey of ARROYO DR. SD No. 1225 F. B. 3350 PG. 129
Map No.	JN 6112.25 Tape 200' Std 98 °F
Office Work	Surveyed by H.H. & W.H.
Checked	Notes F.A.S. Date 10-11-67
Date	Indexed E. J. GALLI OCT 23 67

JN 6112.25

ARROYO DR. SD No. 1225

Additional Location of ~~Improvements~~

Location of SSMH per office request. 10-5-67

H.H. Apr 1995
W.H. Myers
R. Benavidez
P.L. Beasley

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN to
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

76F3095 CE#310 1-65

F.B. 3350 PG. 130

LOS ANGELES COUNTY ENGINEER
PLEASE RETURN TO
403 KOB ANGELES COUNTY ENGINEERING BLDG.
Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made for Corrected in Red Ink With Date and Name of Person Making Change.

1. 3831-30
2. 177-03-00
A. 3831-30

POT
FD 1X2" PIPE
DEEP FB 3350

FD CHIT FB 3350

SET NAIL
BY SURVEY

FD NAIL

SSMH
NOTE: THIS SSMH SHOWN ON KAISER'S CLEARANCE MAP HAS NOT BEEN FOUND OR OPENED FOR SOMETIME

SSMH

PT. ON CURVE
FD 1" IPE
0.2' DEEP
FB 33

CONC PLUG
FD 1" IPE
0.2' DEEP

1861

115.83

1400

1809

1800

N 15°22'E

N 15°22'E

N 15°22'E

N 15°22'E

F.B. 3350 Pg. 131

Profile No. _____ Notes Red _____ Plotted _____ Job No. 6112.25 Division No. _____
Date _____ Date _____ Survey of Arroyo Dr. SD No. 1225
X-Sec. No. _____ Notes Chkd. _____ Checked _____ Survey by HH Gumpp Notes HH Date 10-11-67
Date _____ Date _____ Map No. _____ Indexed C. J. GALLI Date OCT 23 '67

JN 6112.25
ARROYO DR SD NO. 1225

INVERT ELEV'S S.S.M.H'S
LOCATION PER FB 3350-130
FB 3345-140

H.H. GUMPP
T.L. HYDRICK
R. BEAUCHER
P.N. BRADLEY

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

76-1.298 CE 307 3-61

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3350 Pg. 132 | Job No. 61175 Division No. 1225 | Survey of Arroyo Dr SD No 1225 | Survey by [illegible] Notes [illegible] | Indexed C. J. Kelly | Profile No. | X-Sec. No. | Plotted Date | Notes Red Date | Notes Chkd. Date | Checked Date

STATION	B. S.	H. I.	F. S.	ELEV.			
							(Not Adj.)
BM SD 1049				352.18	BM SD 1049	Elev.	352.178 FB 3338-37
SSMH 18.6 Ely & 44 45.54 Sly							
& PT. PR per FB 3350-130							
Top Rim				357.69			
F.L. Inlet Nly	Main Line			343.79	Inlet Wly	Inlet Nly	Outlet Sly
F.L. Inlet Wly	Lateral			343.90	351.69 Rim	351.69 Rim	351.69 Rim
F.L. Outlet Sly	Main Line			343.71	711 Meas	722 Meas	730 Meas
					3.7458	3.4447	3.4439
					.068 Dia.	.068 Dia.	.068 Dia
					343.90 ✓	343.79 ✓	343.71 ✓
SSMH 18.6 Ely & 259.91 260.91 Sly							HMS
& PT. PR per FB 3350-130							
					Inlet	Outlet	
Top Rim				362.30	362.30 Rim	362.30 Rim	
F.L. Inlet				356.45	5.17 Meas	5.31 Meas	
F.L. Outlet				356.29	357.13	356.97	
					.068 Dia.	.068 Dia.	
					356.45 ✓	356.29 ✓	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red _____ Plotted _____ Job No. 611-6135 Division No. _____
No. _____ Date _____ Date _____ Survey of ARROYO DR. SD No. 12345
X-Sec. Notes Chkd. _____ Checked _____ Survey by [illegible] Notes [illegible] Date 10-11-87
No. _____ Date _____ Date _____ Map No. _____ Indexed [illegible] Date 01 23 88

F.B. 3350 Pg. 132

STATION	B. S.	H. I.	F. S.	ELEV.		
BMSD1051				363.45	BMSD1051 Elev. 363.44 (Adj) FB3332-33 N. Redding Ave. Ely side Approx 99' Sly & Infc. of Teresa Ave. & 3.5' Elc @ A Spkin conc wall @ Sly edge drive.	
BMSD1039					BMSD1039 Elev. 30.939 FB3338-3 Grand View Ave @ Arroyo Dr. Ely side Approx 124' N/o & Infc. A BN in cb.	
SSMH	5.0	Rt. Sta. 2+00.00		FB3345-140		
In/lat Rim				~~299.19~~	In/lat ~~299.19~~ Rim 8.51 Meas 291.18 0.68 Dia 290.50	Out/lat 298.97 Rim 8.51 Meas 290.46 0.68 Dia. 289.78
In/lat F.L.				290.50		
Out/lat Rim				298.97		
Out/lat F.L.				289.78		
BMSD1038				289.89	BMSD1038 Elev. 289.882 FB3337-30 E. Arroyo Dr. @ Hermosa Ave. Sly side. 5' Ely of SE CR. Pspkin cb.	

F.B. 3350 Pg. 134

Job No. Division No. Notes Red Plotted Profile

Survey of Date Date No.

Survey by Notes Notes Chkd. Checked X-Sec.

Indexed Date Date Date No.

STATION	B.S.	H.I.	F.S.	ELEV.

Do not extend notes this side of this line

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE DATED AND CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

76-L298 CE 507 3-61
