Notes C'd by
Map No.
Office Work
Checked
Dated

Survey of
JN Tape Std °F
Surveyed by
Notes Date
Indexed

F.B. 3429 Pg.

Page	Job	Description
		WATERWORKS DISTRICT #37-5375.16
	Loc.of Impr.	On Santiago Rd. from Soledad Cn. Rd. to Sierra Hwy.
	Prof.& X-Sec.	" "
	Loc.of Impr.	On Crown Valley Rd. from Soledad Cn. Rd. to Sierra Hwy.
	Prof.& X-Sec.	" "
	Loc.of Impr.	Soledad Cn. Rd. from Crown Valley Rd. S'ly 2400 ft.
	Prof.& X-Sec.	" "
	Loc.of Impr.	Soledad Cn. Rd. from 4th St. to Santiago Rd.
	Prof.& X-Sec.	" "
	Loc.of Impr.	On Smith Ave.-from 4th St. to Soledad Cn. Rd.
	Prof.& X-Sec.	" "
	Loc.of Impr.	Aliso Cn. Rd. from Soledad Cn. Rd. to Carson Mesa Rd.
	Prof.& X-Sec.	" "
	Loc.of Impr.	Carson Mesa Rd. from Aliso Cn. Rd. to 1655' S'ly.

~~Not~~ microfilmed.

P.M. 11.6.87 Jan 87

(cont'd on next page)

F.B. 3429 Pg.

Page	Job	Description
211-218	Prof.& X-Sec.	Carson Mesa Rd. from Aliso Cn. Rd. to 1655' E'ly.
219-232	Loc.of Impr.	On Escondido Cn. Rd.-from 4th St. to the E.C. at P.I. #7.
233-256	Prof.& X-Sec.	" "

Notes Ck'd by	Survey of
Map No.	JN Tape Std °F
Office Work	Surveyed by
Checked	Notes Date
Date	Indexed H. E. OTT SEP 5 '57

F. B. 3411 PG. 5

LOS ANGELES COUNTY
WATER WORKS DISTRICT # 37
VICINITY - ACTON

SANTIAGO ROAD - IMPROVEMENT
LOCATION - FROM SOLEDAD ROAD N'LY TO SIERRA HIGHWAY.

J.N. 5375.16

REFERENCES:
F.B. 2902

PARTY -
C. L. WRIGHT
H. C. HUBBARD JR.
B. A. PEAVY
J. M. SIDWELL
J. D. GALLAGHER

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink, With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

76F3095 CE #310 6-63

CONT. BOT. PG 7

F. B. 3459 PG 6

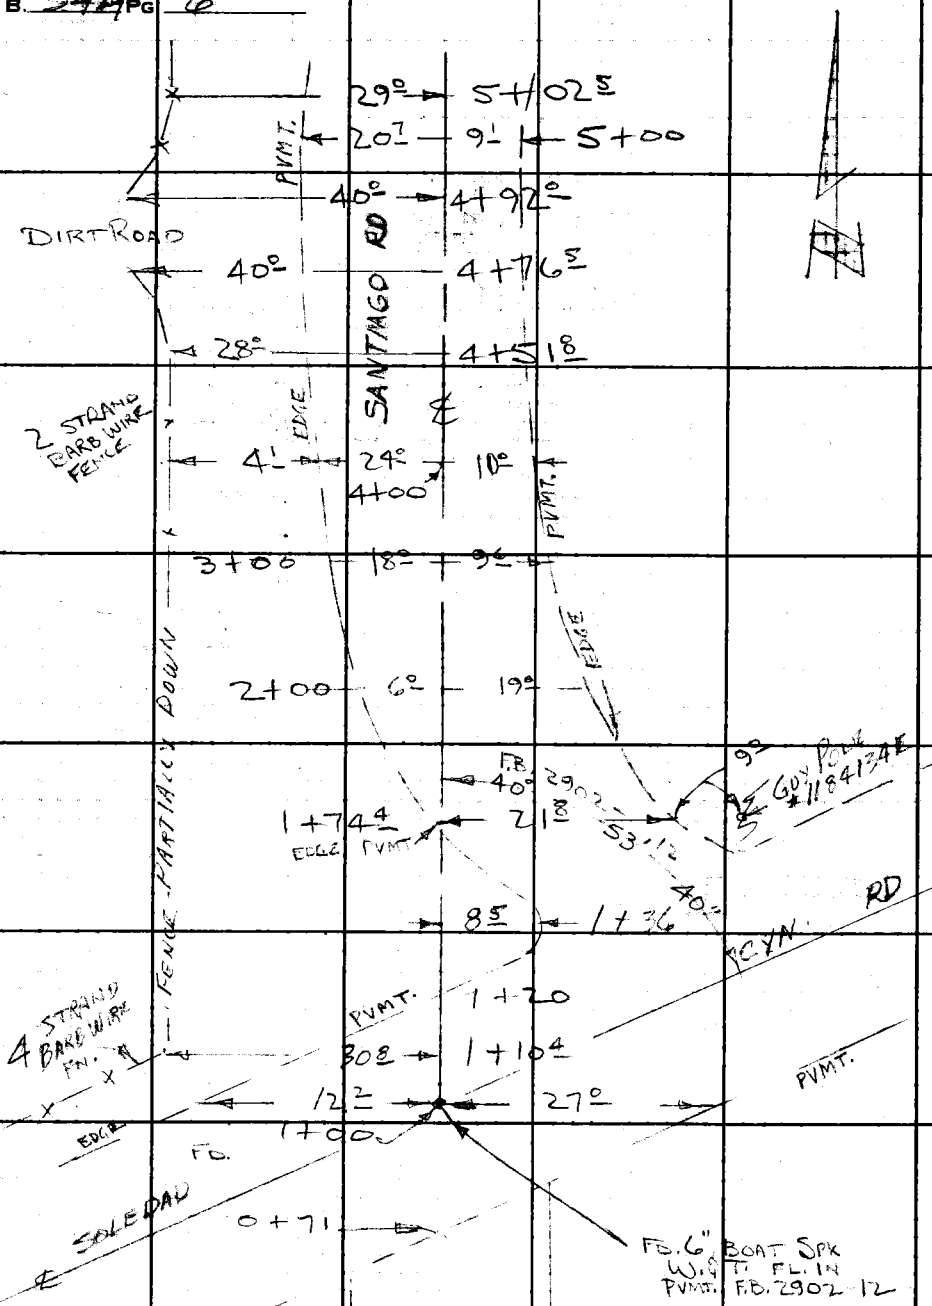

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.
Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of DPW/WKS. DIST 51
JN Tape Std °F
Surveyed by
Notes Date
Indexed H. E. OTT

F. B. 3429 PG. 7

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

70F3095 CE #310 8-63

PARTIALLY DOWN

9³ 11⁸ 18+00
9³ 10⁰ 17+00
9³ 11⁹ 16+00

EDGE PAVEMENT

20⁴ 9³ 10⁹ 15+00
8⁹ 11³ 14+00
30¹ 8² 12⁷ 13+00

SANTIAGO RD

8¹ 12⁷ 12+00
EDGE PAVEMENT
31⁵ 8¹ 12⁴ 11+00

PARTIALLY DOWN

7⁸ 12⁵ 10+00
7⁰ 13⁶ 9+00

FENCE ENDS

22¹ 9³ 14⁹ 8+00
10⁶ 8⁸ 23⁴ 7+00

SPLIT

PI #12
FB 2922-13
P.O.C. ANGLE, A 2" I.P. & BRASS CAP SET IN CONC. DN. 1.35' IN WELL COVER

32⁰
1¹
15⁴
6+57.07

2 STRAND BARB WIRE FENCE

6+00
14⁹
19⁹
14⁸

COUNTY ROAD

F. B. 3429 PG. 8

CONT. BOT RIGHT Pg 9

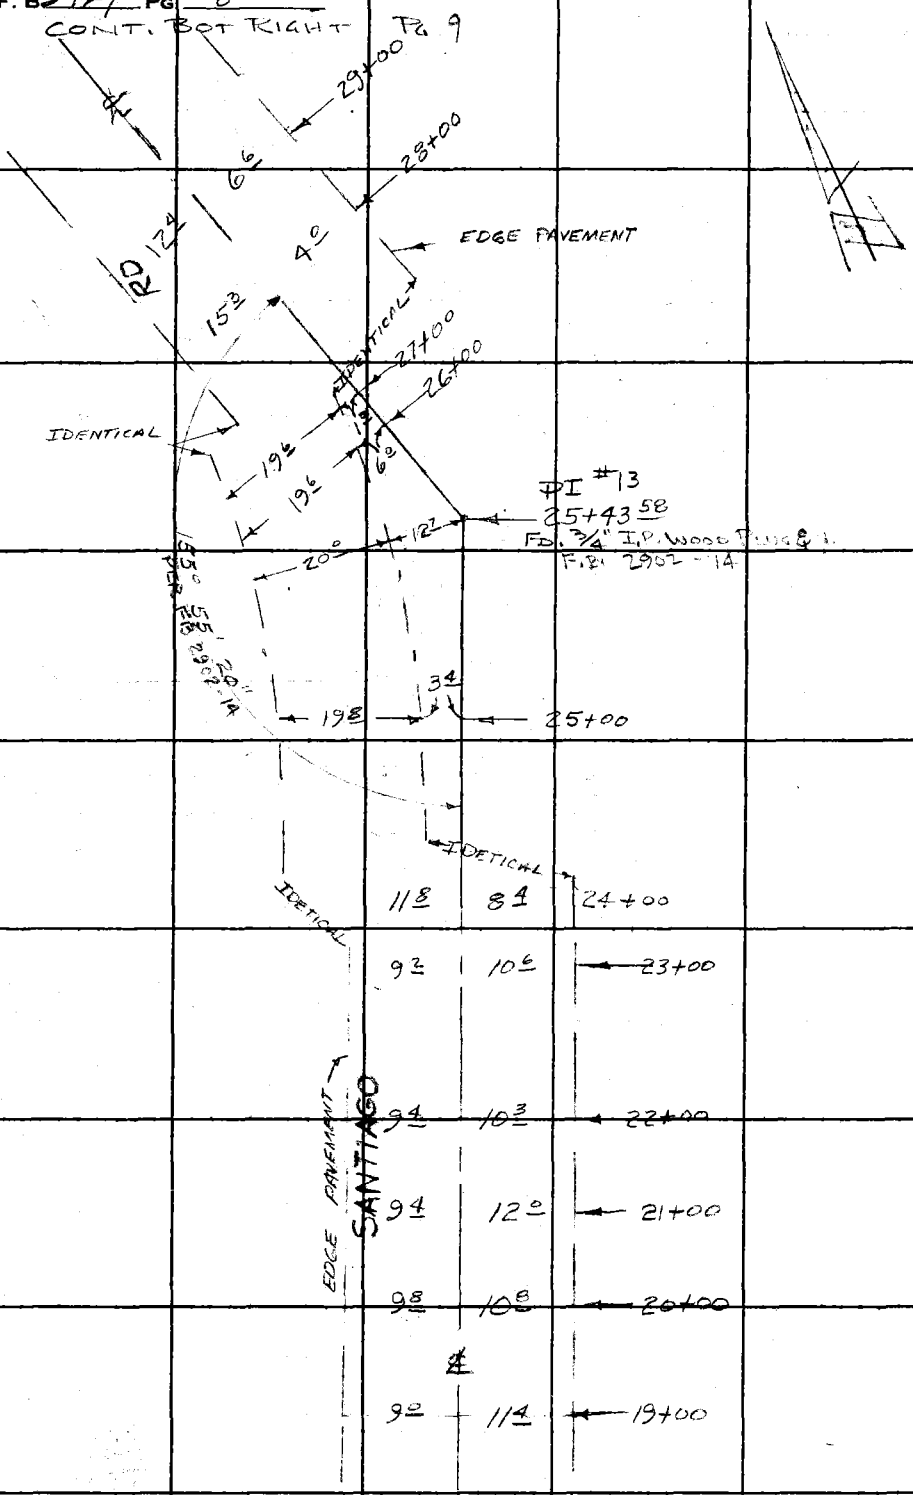

CONT TOP Pg. 7

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.
Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Ink With Date and Name of Person Making Change.

Notes Ck'd by	Survey of WORKS DIST. 29
Map No.	JNS-SJ Tape Std °F
Office Work	Surveyed by [illegible]
Checked	Notes H. C. H. Date 12-[illegible]
Date	Indexed H. E. C.

F. B. 3479 PG. 9

Note: Any Additions or Changes on This Sheet Must Be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

33+44
33+14.7
12°
12°
CONC HEAD WALL
33+00
9'
11'
32+
7½
11.3'
EDGE PAVEMENT
PI #14
31+05.13
FD. 3/4" IP. WOOD PLUG IN. DN. 12"
P.E. 2902-15
19.0
Δ 90°
158.41' P.E. 2902
EDGE PAVEMENT
SANTA ANA
11.4'
30+00
CONT TO LEFT PG 8

7EF3095 CE #310 6/63

CONT. BOT. PG. 11

F. B. 3429 PG 10

CONT. TOP RIGHT PG. 9

LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.
PLEASE RETURN TO

Do not extend this side of this line.

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by	Survey of W. Basin Dist. #51
Map No.	JN 5215 Tape Std °F
Office Work	Surveyed by C.L. Wright
Checked	Notes H.C. Date 11-11-66
Date	Indexed H.E. SEP 5 '67

F. B. 3429 PG. 41

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

76F3095 CE #310 6-63

SANTIAGO RD

OUTSIDE EDGE BRIDGE

4' BARB WIRE FENCE

CONC PILLERS

LIGHT METER

METER BOX

LIGHT STANDARD

2' CONC GUT

6" CONC CRB

DROP IN BOX

SIGN BOARD

CONC DRAINAGE BOX

EDGE PAVEMENT

PVMT.

EDGE

40+48.9 36'
40+43.2
40+36.2 56'
40+34.9
36.3 40+34.1 32.9
29.8 40+28.9
34.3 40+27.2
40+26.3 40.8
40+25.4 35.2
31.4 40+22.1 50.3
40+21.2 40+18.3
40.7 40+18.2
32.3 39+60.9 32.0
39+40.4
39+33.71 31.59
30.7 39+28.0
31.59 39+26.96
39+09.64 31.63'
31.54 39+02.36
39+00.2
10.8 30.3 39.7 20.9
38+00
37+57.1
37+51.88 31.61
31.61 37+45.14
37+27.89 31.63
30.7 37+21.4
31.59 37+21.13
37+18.8
36+89.86

FD. 6" BOAT SPK. IN P.I. - NOT A POINT OF RECORD, BUT LOCATED BY A RELATIVE POSITIONS FROM CONTROL OF F.W.S., P.I. CHECKS & DIST. CHECKS BOTH RECORD & LOCAL TO POINTS OF RECORD.

CONT. TO FD. 10

F. B 3429 PG 12

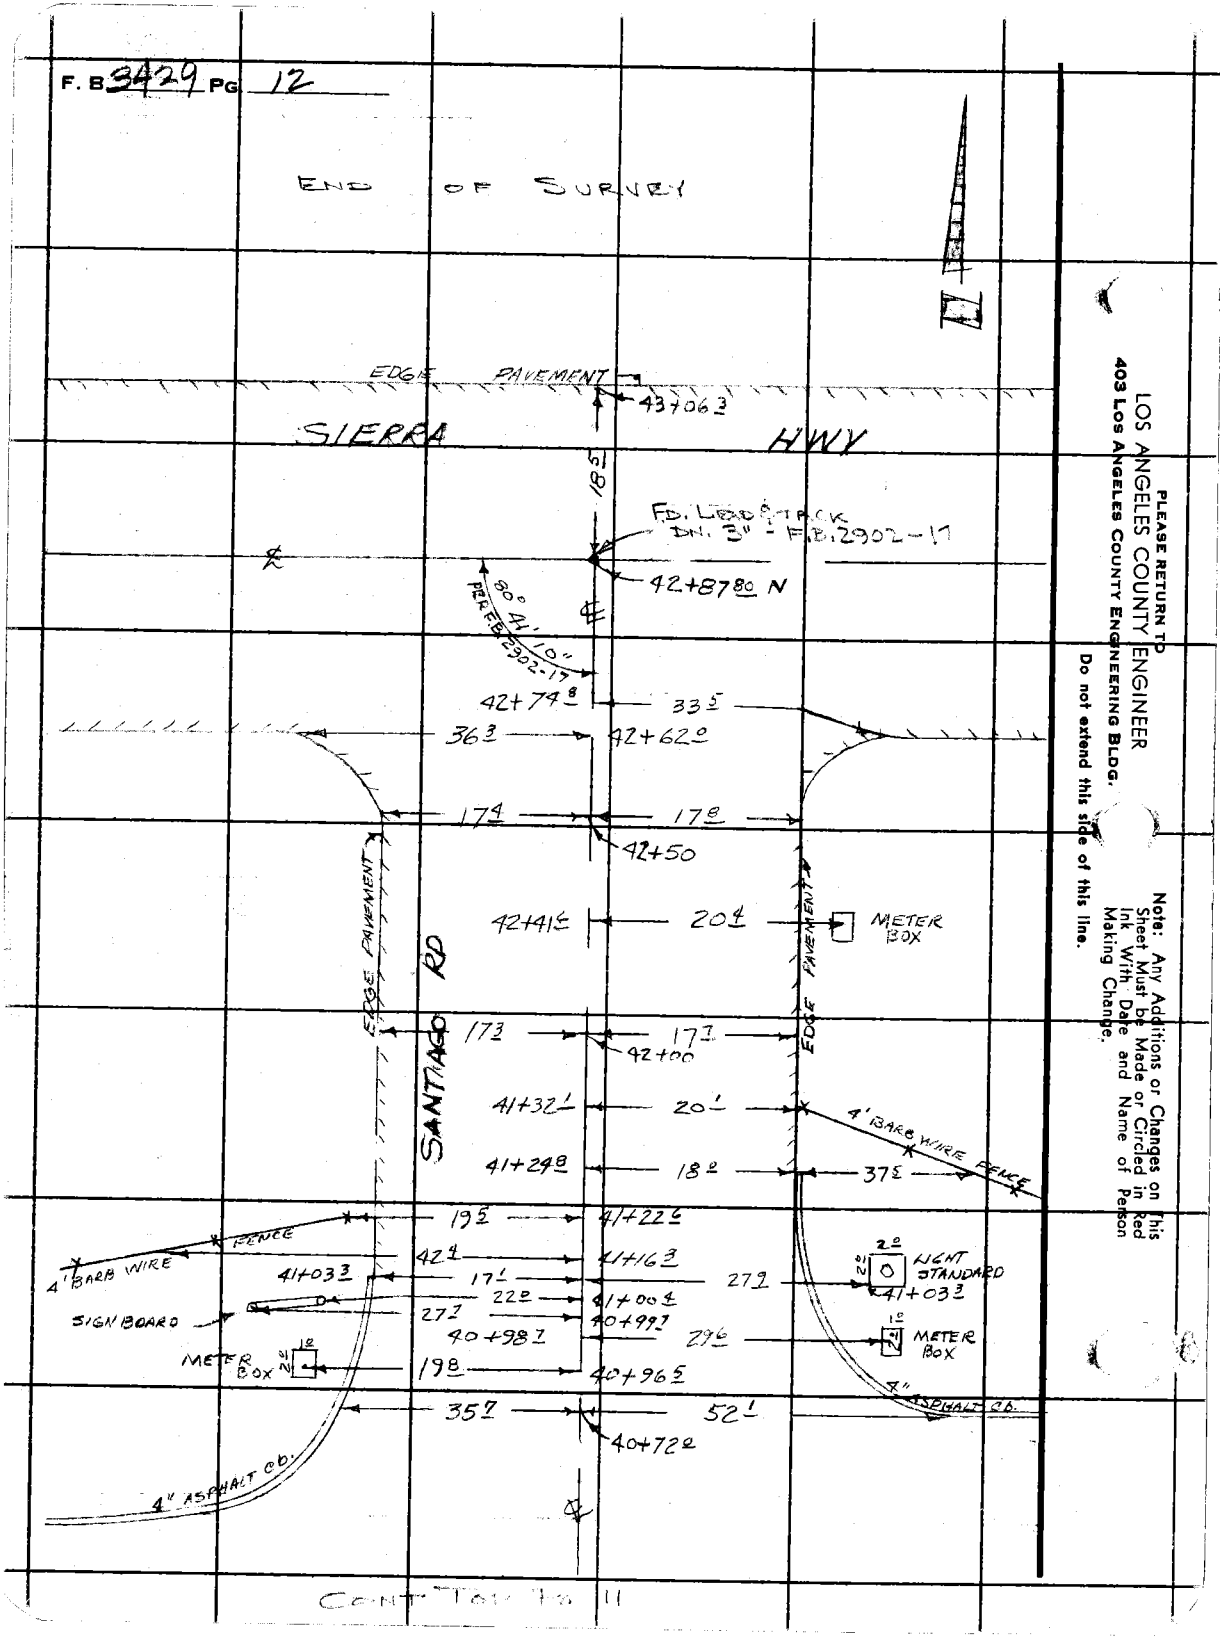

LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

PLEASE RETURN TO

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

F. B. 3429 Pg. 13

Profile No. ____ Notes Red ____ Date ____ Plotted ____ Date ____ Job No. ____ Division No. ____
Survey of ____
X-Sec. No. ____ Notes Chkd ____ Date ____ Checked ____ Date ____ Survey by ____ Notes ____ Date ____
Map No. ____ Indexed ____ Date ____

LOS ANGELES COUNTY
WATER WORKS DISTRICT #37
VICINITY - ACTON
SANTIAGO ROAD - FROM
SOLEDAD CYN. RD. TO SIERRA HI-WAY

PROFILE & X SECTION
J.N. 5375.16

STATION	B.S.	H.I.	F.S.	ELEV.

PARTY:
C. L. WRIGHT
H. C. HOTCHARD
B. A. PEAVY
J. D. GALLAGHER
J. M. SIDWELL

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

76-L-298 CE 307 2-63

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 PG. 14 Job No. 5315.16 Division No. Notes Red Plotted Profile
Survey of LYNWOOD DIST. No. Date Date No. X-Sec.
Survey by C.L.W. Notes C.L.W. Notes Clkd. Checked No.
Indexed Date 11-4-63 Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	SANTIAGO RD.	
BMNC 1138	PD			2868.411	F.B. 3190-29 ELEV.	2868.411
					℄ INT. SOLEDAD CYN. RD. & SANTIAGO RD.	
					BOLT SPK. IN N.W. COR. CONC. WALK 71 FT.	
					S.E. OF INT.	
1+00					℄ INT. SOLEDAD CYN. RD. & SANTIAGO RD.	
					FD. BOLT SPK. WEST	FB. 2902-12
				63.05		27 R EDGE PVMT.
				63.92		32 R GUTTER
				63.82	12 L EDGE PVMT.	
				63.8	22 L GUTTER	
2+00				67.56		℄
				67.50		19 R EDGE PVMT.
				67.8		30 R DIRT
				67.58	6 L EDGE PVMT	
				67.7	33 L FENCE & DIRT	
3+00				72.46		℄
				72.43		96 R, EDGE PVMT.
				72.6		22 R GUTTER
				72.9		33 R NAT. BKA.
				72.4		40 R DIRT

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. Rod Plotted Job No. Division No.
No. X Sec. Date Date Survey of W. Wks. Dist # 37
No. Date Date Map No. Indexed H. E. CTY Date

F.B. 3429 Pg. 15

STATION	B. S.	H. I.	F. S.	ELEV.	SANTIAGO RD.	
3+00				2872 57	18 L EDGE PVMT.	
				73 2	30 L FN. & DIRT	
				73 4	40 L "	
T.P.				76 41		
4+00				78 24		℄
				77 59		11 R. EDGE PVMT.
				770		22 R GUTTER
				79 2		30 R TOP BRK
				787		40 R DIRT
				78 54	24 L EDGE PVMT	
				788	28 L FN.	
				789	40 L DIRT	
5+00				84 46		℄
				84 07		9 R EDGE PVMT
				83 1		19 R GUTTER
				85 5		30 R TOP BRK
				845		40 R DIRT
				84 82	20½ L EDGE PVMT.	
				845	30 L DIRT	
				849	40 L "	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F. B. 3429 Pg. 16 | Job No. 5376.16 Division No. | Notes Red | Plotted | Profile
Survey of 4/Jacks. DIST #37 | Date | Date | No.
Survey by C.L.W. Notes C.L.W. | Notes Chkd. | Checked | X-Sec.
Indexed | Date 11 JULY 67 | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	SANTIAGO RD.	
6+00				289040		℄
				89.12		19½R EDGE PVMT.
				87.9		26 R GUTTER
				90.3		36 R TOP BRK
				89.5		40 R DIRT
				91.12	14½L EDGE PVMT.	
				91.4	22.5 L FENCE	
				91.3	30 L. DIRT.	
BM. 6+57.07 FD.				92.57	C.S. MON. DN. 1.35 FT. IN WELL & COVER	℄
				91.07		32R. EDGE PVMT.
				90.57	NOTE: THIS X SEC. ON SPLIT	38R GUTTER
				92.7		48 R. TOP BRK
				91.2		55 R DIRT
				94.08	2 L EDGE PVMT.	OF P.I.
				94.3	14 L FENCE	
				95.8	30 L DIRT	
7+00				95.12		℄
				93.03		23½R EDGE PVMT.
				92.2		29 R GUTTER
				94.0		39 R TOP BRK
				92.6		46 R BOT BRK

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Noted _____ Plotted _____ Job No. S[illegible] Division No. 1
No. X-Sec. Date _____ Date _____ Survey of W[illegible] DIST 137
No. _____ Date _____ Checked _____ Date _____ Survey by _____ Notes _____ Date _____
Map No. _____ Indexed H. E. OT Date 3-68

F. B. 3429 Pg. 17

STATION	B. S.	H. I.	F. S.	ELEV.	SANTIAGO RD.	
7+00				28 95 53	6 8 L EDGE PVMT.	
				96.1	19 L FN.	
				96.2	30 L DIRT	
8+00				9485		℄
				9666		14 9 R EDGE PVMT.
				960		22 R GUTTER
				974		30 5 R TOP BRK
				962		34 R BOTTOM "
				958		40 R DIRT
				98 34	9 3 L EDGE PVMT	
				982	15 5 L BOT. BRK	
				994	20 5 L TOP BRK	
				998	31 L FN.	
				29002	40 L DIRT	
9+00				289985		℄
				9882		13 6 R EDGE PVMT.
				992		20 R GUTTER
				978		30 R DIRT
				974		40 R "
				29 0020	7 L EDGE PVMT.	
				002	15 L BOT BRK	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 18 | Job No. 5375.16 | Division No. | Notes Red | Plotted | Profile
Survey of W. Tanks Dist. #37 | Date | Date | No.
Survey by L.L.W. Notes L.L.W. | Notes Chkd. | Checked | X-Sec.
Indexed | Date 11-24-67 | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	SANTIAGO RD.	
9+00				290.5	30 L DIRT	
				02 4	40 L "	
10+00				290.80		℄
				00 86		12.5R EDGE PVMT.
				00 9		30R DIRT
				290.00		40R "
				02 10	7.8 L EDGE PVMT.	
				02 0	16 L BOT. BRK	
				02 8	19 L TOP BRK	
				04 0	30 L DIRT	
				04 5	40 L "	
11+00				03 93		℄
				03 17		12.5R EDGE PVMT
				02 2		19.5R GUTTER
				03 4		22R TOP BRK
				02 4		30R DIRT
				02 0		40R "
				04 19	8.5 L EDGE PVMT.	
				04 4	16 L BOT. BRK.	
				05 6	18.5 L TOP "	
				05 8	30 L. DIRT	

5

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No.____ Division No.____
No.____ Date____ Date____ Survey of____
No.____ Date____ Date____ Map No.____ Indexed____ Date____

F.B. 3429 PG. 12

STATION	B. S.	H. I.	F. S.	ELEV.	SANTIAGO RD.	
11+00				2906.6	40 L DIRT	
12+00				05.12		℄
				04.24		12 R E.P.
				03.0		30 R "
				02.4		40 R "
				05.37	8 L E.P.	
				05.3	15 L TOP BRK.	
				06.3	20 L " "	
				06.9	30 L DIRT	
				07.4	40 L " "	
13+00				06.87		℄
				06.34		12 R E.P.
				05.1		18 R TOP BRK.
				06.0		21 R " "
				05.5		30 R DIRT
				05.1		40 R "
				07.00	8 L E.P.	
				06.9	15 L TOP BRK.	
				08.1	18 L " "	
				08.7	30 L DIRT	
				2909.1	40 L "	

Indexed H. E. G.

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 20 | Job No. 53795.16 | Division No. | Notes Red | Plotted | Profile
Survey of LA/Cnty. Dist. 32 | Date | Date | No.
Survey by Cahill Notes LCAMS | Notes Chkd. | Checked | X-Sec.
Indexed | Date 12 July 67 | Date | Date | No.

STATION	B.S.	H.I.	F.S.	ELEV.	SANTIAGO RD.	
14+00				13.75		℄
				07		11 3/4 R E.P.
				03		17 3/4 R Gut.
				01		20 R Top Bnk.
				05		30 R Dirt
				12		40 R "
				13 01	8 3/4 L E.P.	
				09	15 L But. Bnk.	
				11	20 L Top "	
				14	30 L Dirt	
				13	40 L "	
15+00				13 43		℄
				13 21		10 8/8 R E.P.
				12 5		17 R Gut.
				13 6		20 R Top Bnk.
				13 1		30 R Dirt
				12 7		40 R "
				13 16	9 3/4 L E.P.	
				12 5	15 5/4 L But. Bnk.	
				13 1	18 L Top "	
				13 3	30 L Dirt	
				13 4	40 L "	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Rod Plotted Job No. Division No.
No. X Sec. Date Date Survey of W W DIST #37
No. Date Notes Ckkd. Date Checked Date Survey by Map No. Notes Indexed H. E. OTT Date

F. B. 3429 Pg. 21

STATION	B. S.	H. I.	F. S.	ELEV.	SANTIAGO RD.		
16+00				29 17.18		℄	
				16.70		11½' R	E.P.
				16.1		17' "	GUT
				16.9		20' "	TOP BRK
				16.6		30' "	DIRT
				16.6		40' "	"
				17.36	9³ L	E.P	
				17.2	16' "	BOT BRK	
				18.0	19 "	TOP "	
				18.4	30 "	DIRT	
				18.8	40 "	"	
T.P.				18.40			
17+00				21.19		℄	
				20.87		9½' R	E.P.
				19.9		18' "	GUT
				21.2		20' "	TOP BRK
				20.9		30' "	DIRT
				20.9		40' "	"
				21.46	9³ L	E.P	
				21.5	16' "	BOT BRK	
				29 22.7	40' "	TOP "	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

F.B. 3429 PG. 22 Job No. 5375.16 Division No. Notes Red Plotted Profile
Survey of W. W. Dist #37 Date Date No. X-Sec.
Survey by C L W Notes 4 of 4 Notes Chkd. Checked No.
Indexed Date 12 July 67 Date Date

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	SANTIAGO RD.	
17+00				2922.7	30' L	
				22.5	40' "	
18+00				25.12		℄
				24.45		11⅙ R E.P
				23.7		18⅝ " GUT
				24.5		23 " TOP BRK
				24.3		30 " DIRT
				23.7		40 " "
				25.36	9⅜ L E.P	
				25.2	17' " BOT BRK	
				26.0	19' " TOP "	
				26.3	30 " DIRT	
				26.8	40 " "	
19+00				29.42		℄
				28.84		11¼ R E.P
				27.8		19' " GUT
				28.6		23' " TOP BRK
				28.4		30' " DIRT
				27.9		40' " "
				29.71	9º L E.P	
				2929.92	15' " BOT BRK.	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Noted Red Plotted Job No. Division No.
No. Date Date Survey of W. W. DIST #37
X-Sec. Noted Chkd. Checked Survey by C.H.W. Notes C.H.W. Date 1-5-66
No. Date Date Map No. Indexed H. E. OTT Date

F.B. 3429 Pg. 23

SANTIAGO RD.

STATION	B. S.	H. I.	F. S.	ELEV.		
19+00				2931.0	19' L	TOP BRK
				31.4	30' "	DIRT
				31.5	40' "	"
20+00				33.84	℄	
				33.23	10[B] R	E.P
				32.4	19' "	GUT
				33.2	22' "	TOP BRK
				32.9	30' "	DIRT
				32.0	40' "	"
				34.12	9[5]' L	E.P
				34.2	16' "	BOT BRK
				35.5	19' "	TOP BRK
				36.2	30' "	DIRT
				36.7	40' "	"
21+00				38.39	℄	
				37.58	12° R	E.P
				37.0	18° "	GUT
				37.4	22' "	TOP BRK
				37.0	30 "	DIRT
				36.4	40 "	"
				2938.65	9[4] L	E.P

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 PG. 34 | Job No. 5375.16 Division No. Notes Red Date Profile
Survey of W.W. DIST #37 Date No.
Survey by C.L.W. Notes HCH Notes Chkd. Date X-Sec.
Indexed Date 12 JULY 67 Checked Date No.

STATION	B.S.	H.I.	F.S.	ELEV.	SANTIAGO RD.		
21+00				2938.0	18'L	BOT. BRK	
				40.2	21'L	TOP "	
				40.6	30'L	DIRT	
				41.3	40'L	"	
22+00				42.45			℄
				42.25			10^{3}R E.P.
				41.0			30' " DIRT
				40.5			40' " "
				42.61	$9\frac{4}{}$L	E.P.	
				43.4	30' "	DIRT	
				44.5	40' "	"	
23+00				47.11			℄
				47.16			10^{6}R E.P.
				45.5			30' " DIRT
				45.0			40' " "
				46.66	$9\frac{2}{}$L	E.P.	
				46.0	15' "	GUT.	
				49.1	22' "	TOP BRK	
				49.6	30' "	DIRT	
				2950.5	40' "	"	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Noted Red Plotted Job No. 5315 Division No.
No. X-Sec Noted Red Date Date Survey of
No. Date Checked Date Map No. Indexed Date

F.B. 3429 PG. 35

STATION	B. S.	H. I.	F. S.	ELEV.	SANTIAGO RD	
24+00				295.52		℄
				51.7		8.4R E.P.
				51.6		1.3R TOP BRK
				48.4		3.0R DIRT
				47.2		4.0R "
				50.85	11.8L E.P.	
				49.8	17L GUT	
				53.8	2.2L TOP BRK.	
				54.3	3.0L DIRT	
				54.9	4.0L " "	
24+50				53.63		℄
				53.8		4.2R E.P.
				53.7		1.1R TOP BRK.
				47.9		3.0R DIRT
				48.7		4.0R DIRT
25+00				55.56		℄
				55.6		.1R TOP BRK
				51.8		1.2R TOP BRK
				47.8		3.0R DIRT
				55.55	3.4L E.P.	
				54.05	23.5L E.P.	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 36 | Job No. 5375.16 | Division No. | Notes Red | Date | Plotted | Profile
Survey of W/WKS. Dist. # 37 | Date | No. | X-Sec.
Survey by C.L.W. | Notes T.M.S. | Notes Chkd. | Checked
Indexed | Date 12-July '67 | Date | Date | No.

STATION	B.S.	H.I.	F.S.	ELEV.	SANTIAGO RD.	
25+00				2953.4	27 L GUT.	
				56.2	33 L TOP BRK.	
				56.1	40 L DIRT	
25+43.58				55.05		℄
				51.2	+ SEC. TAKEN @ RIGHT ∡ TO BACK TANG.	30 R
				56.8	7 L TOP BRK.	
				56.62	13.5 L E.P.	
				55.10	33 L E.P.	
				54.8	36 L GUT.	
				59.2	42 L TOP BRK.	
				59.7	50 L DIRT	
BM. J C 1134	F.D.			2956.715		
26+00				2958.65		℄
				56.9		20 R DIRT
				56.2		30 R " "
				57.79	6 L E.P.	
				56.22	25.6 L E.P.	
				56.0	27 L GUT.	
				61.6	35 L TOP BRK	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. Division No.
No. X-Sec. Date Date Survey of
No. Date Date Map No. Index No.

F.B. 3429 PG. 37

STATION	B. S.	H. I.	F. S.	ELEV.	SANTIAGO RD.	
26+00				2962.8	50L DIRT	
26+50				58.4		℄
				58.4		1R TOP BANK
				55.2		10R BO. BK.
				53.		30R DIRT
				51.7		40R " "
				58.38	2½L E.P.	
				57.00	22L " "	
				56.7	25L GUT.	
				60.3	31L TOP BRK.	
				61.6	40L DIRT	
27+00				58.79		℄
				58.8		3R TOP BK.
				57.2		10R BO BK
				54.6		30R DIRT
				53.0		40R DIRT
				58.82	1L E.P.	
				57.66	20½L " "	
				57.4	23L GUT.	
				60.4	29L TOP BRK.	
				61.5	40L DIRT	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 38 | Job No. 5315.10 Division No. | Notes Red | Plotted | Profile
Survey of W/WKS Dist #27 | Date | Date | No.
Survey by C.L.W. Notes 1-15-63 S. | Notes Chkd. | Checked | X-Sec.
Indexed | Date 1-3-63 | Date | Date | No.

SANTIAGO RD.

STATION	B.S.	H.I.	F.S.	ELEV.			
27+33							℄ E.P.
							P.R. Top Bk.
							1 R. "
							3L.P. "
							4 R.
27+50							℄
				58.1	17½L	E.P.	
				57.8	21 L	GUT.	
				60.2	35 L	Top Bk.	
				61.0	40 L	DIRT	
27+65				61.37			℄
				57.52			2 R E.P.
				59.0			7 R Top Bk.
				59.[illegible]			3 UR DIRT
				59.[illegible]			4 UR "
27+75				59.[illegible]			℄
				59.41	16 L	E.P.	
				58.2	19 L	GUT.	
				62.6	25 L	TOP BK.	
				64.2	34 L	DIRT	
				63.0	40 L	"	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. X-Sec. No. Notes Red. Date Date Plotted Date Job No. Survey of Map No. Division No. Indexed H.E. Office

F.B. 3429 PG. 37

SANTIAGO RD.

STATION	B. S.	H. I.	F. S.	ELEV.		
28+00				2959.25		
				59.29		4°R E.P.
				59.2		8 R TOP BK.
				56.9		16 R GR. BK.
				54.6		30 R DIRT
				53.3		40 R
				52.5	15L	B.P.
				53.5	18L	BOT. BRK.
				61.6	25L	TOP BRK.
				63.6	40L	DIRT
28+50				59.28		
				59.03	14L	E.P.
				59.0	16L	BOT. BRK.
				68.0	27L	TOP BRK.
				70.3	40L	DIRT
28+70				59.23		
				59.12		5 R E.P.
				57.3		9 R BOT BK.
				61.7		15 R TOP BK.
				59.7		30 R DIRT
				57.9		40 R

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK. WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F. B. 3429 Pg. 40 | Job No. 5315.16 Division No. | Notes Red | Plotted | Profile
Survey of W/MKS. DIST # 37 | Date | Date | No.
Survey by C.L.W. Notes 4 N.S. | Notes Chkd. | Checked | X-Sec.
Indexed | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	DOMINGO RD.	
26+00				1.84		
				57.11		12R E.P.
				57.1		16R TOP BRK
				53		36R TOP "
				53.5		40R DIRT
29+75				51.37		
				51.30		6ZR E.P.
				50		12R TOP BRK
				50.0		32R BOT BRK.
				52.3		40R DIRT
				51.3	18L E.P.	
				51.2	15L BOT BRK.	
				52.3	22L TOP BRK.	
				67.2	40L DIRT	
29+65				51.38		
				51.49		9ER E.P.
				52.9		14R TOP BRK
				50.1		28R BOT "
				53.9		40R DIRT
30+00				51.77		
				52.15		11ER E.P.

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	SANTIAGO RD.	
31+00				2957.2		16R TOP BK
				53.8		27R SL. BK
				52.0		40R DIRT
				58.7	34L #1	
				58.6	15L SLT. BRK	
				61.6	21L TOP BRK.	
				62.6	3 0L DIRT	
				65.2	40L "	
31+05.2				59.8		
				57.20		36R E.P.
				57.71		22R E.P.
				57.4		25R GUT.
				58.1		3 R TOP BRK
				60.1		3 0R DIRT
				61.1	4 L SLT BRK	
				61.9	9 L TOP BRK.	
				61.9	30L DIRT	
31+50				58.90		
				59.07	3L E.P.	
				59.1	10L GUT. BRK.	
				2962.1	11L TOP BRK.	

Profile Notes Red Plotted Job No. Division No.
No. Date Date Survey of
No. Date Date Map No. Indexed
Notes Checked Surveyed by Notes
H. E. G. Date Date

F. B. 3429 PG. 41

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F. B. 3429 PG. 42

Survey of 3 Anks. Dist. #29 Job No. 5515.16 Division No. Notes Red Plotted Profile
Survey by C.L.W. Notes T.M.S. Date Date No. X-Sec.
Indexed Date 3-4-64 Notes Chkd. Checked No.
Date Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	SANTIAGO RD.	
31+00					BK DIKE	
					P.C.	
32+00						
						10R 3
						15R
						30R P.P. SWR.
						50R
						100R
					12	E.P.
					19	BK. DIKE
					BC	TOP CURB
					30	GUTTER
33+00						
						1 R E.P.
						15R GUTTER
						18R TOP CURB
						30R BOT CURB
						40R DIKE
						55R FL. WAY
33+00						
						11 3R E.P. & GUTTER

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ Notes Red ____ Plotted ____ Job No. ____ Division No. ____
No. ____ Date ____ Date ____ Survey of ____
No. ____ Date ____ Date ____ Map No. ____ Indexed ____ Date ____

F.B. 3429 PG. 43

SANTIAGO RD.

STATION	B. S.	H. I.	F. S.	ELEV.		
33+00				2954.0		6R
				51.0		34R
				54.35	9½ L	E.P.
				54	12L	BK. BRK.
				57.8	30L	
				57.4	40L	
33+15				53.69		12R TOP WALL
± 25				54.21		℄
				53.62		12R
				53.3		27R TOP BANK
				52.4		15R F.L. WASH
33+40				54.42		℄
				54.06		9R E.P.
				53.87		13R TOP WALL
				54.0		30R DIRT
				54.6		40R DIRT
				54.60	9L	E.P. & F.L. WASH
				55.7	30L	F.L. WASH
				56.0	40L	DIRT
34+00				57.33		℄
				57.08		11R E.P. & F.L.
				57.9		30R DIRT

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 44 | Job No. 5515.16 Division No. | Notes Red | Plotted | Profile
Survey of W/WKS. DIST. #27 | Date | Date | No.
Survey by C.L.W. | Notes 2 M.S. | Notes Chkd. | Checked | X-Sec.
Indexed | Date 13-JULY 67 | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	SANTIAGO RD	
34+00				295.75		40R DIRT
				56.92	10L E.P.	
				57.1	20L DIRT	
				57.9	40L " "	
35+00				58.01		
				58.18		11½R E.P. & GUT.
				58.5		38R TOP BRK.
				58.2		38R BOT. " BRK.
				58.7		50R DIRT
				65.76	78L E.P.	
				61.9	20L DIRT	
				61.1	40L DIRT	
35+55				65.67		
				65.0		16R E.P. & GUT.
				64.7		30R DIRT
				65.0		40R DIRT
				63.90	25L E.P. & TOP BRK.	
				63.8	36L BOT. BRK	
36+00				68.10		
				67.70		20R PVMT.
				267.45		49½R " GUTTER

76-L.298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. X-Sec. No.
Notes Red. Date Date
Notes Ckd. Date Date
Plotted Date
Checked Date
Job No. Survey of
Map No. Indexed
Division No.
Notes Detail Date

F.B. 3429 PG 45

STATION	B. S.	H. I.	F. S.	ELEV.	SANTIAGO RD.	
36+00				296781	20L P.M.T.	
				6763	46 5/8 L " " GUT.	
36+46				6487	46 5/8 L INVERT INLET 24" CULV	
36+84.86				7219		℄
				7151	X SEC. TAKEN @ RIGHT & TO BACK TANG	32R E.P. GU
				73.0		44R TOP BRK
				72.0		50 5/8 R
				7167	28L E.P.	
				7117	32L TOP BRK.	
				69.6	37L F.L. DRAIN	
				850	60L S.H.	
37+50				7477		℄
				7396		30R E.P. G
				832		45R TOP BR
				838		50 5/8 R
				7416	30L E.P.	
				742	35L TOP BRK.	
				722	29L F.L. DRAIN	
				83.0	56L S.H.	
38+00				76.76		℄
				7611		30R E.P. & G

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 PG. 46 | Job No. 5375 16 | Division No. | Notes Red | Date | Plotted | Date | Profile No.
Survey of 3 / 3 MILES, DIST. 7 | Notes 4 M.S. | Notes Chkd | Checked | Date | X-Sec. No.
Survey by C.L. 33 | Date 14-AUG '64 | Date | Date
Indexed

STATION	B.S.	H.I.	F.S.	ELEV.	SANTIAGO RD.	
38+00				2984.1		42R TOP BRK.
				88.2		50 5R FENCE LINE
				76.25	30L E.P.	
				76.5	35L TOP BRK.	
				74.7	38L F.L. DRAIN	
				75.8	41L TOP BRK.	
				77.0	50L DIRT	
38+20				83.4		50 5R FENCE LINE - ℄ DRAIN
39+00 32				81.10		℄
				80.47		27R E.P. & GUT.
				88.4		42R TOP BRK.
				90.0		50 5R FENCE LINE
				80.35	30L E.P.	
				80.7	3 L TOP BRK.	
				79.7	37L F.L. DRAIN	
				88.4	51L S.H.	
39+39				83.00	37L DRAIN STARTS	
39+68				83.73		32R CONC. DRAINAGE BOX
39+70				85.12		℄
				84.35		30 7R E.P. & GUT.
				93.8		43R TOP BRK.
				94.5		50 5R FENCE LINE

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. [illegible] Division No.____
No.____ X Sec.____ Date____ Date____ Survey of [illegible]
Notes Ckd.____ Checked____ Surveyed by [illegible] Notes____ Details____
No.____ Date____ Date____ Map No.____ Indexed H. E. OT Date____

F. B. 3429 Pg. 47

ANTIOCH RD.

STATION	B. S.	H. I.	F. S.	ELEV.		
39+70				2984.50	30L	E. P. & BOT. BRK
				85.2	32L	TOP BRK.
				86.4	43L	BOT. BRK.
				89.5	51L	S. H.
40+00				87.10		℄
				86.30		3.0R E. P. GUT
				91.0		40R TOP BRK.
				91.6		50.5R FENCE [illegible]
				86.46	30L	E.P. & BOT. BRK.
				87.6	33L	TOP BRK.
				88.2	39L	FENCE LINE
40+50				90.72		℄
				90.29		20R PVMT.
				90.18		40R " "
				90.33	20L	PVMT.
				89.62	40L	" "
40+80				93.10		℄
				92.44		34.5R GUT. & BOT. [illegible]
				99.3		85R TOP BRK.
				91.45	25L	GUT.
				2991.7	40L	DIRT

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F. B. 3429 PG. 48 | Job No. 5575-16 Division No. Notes Red Date Plotted Date Profile No. X-Sec. No.
Survey of 3 / 3 Lks Dist #37 Notes Cl. 3. Notes Chkd. Checked Date
Survey by C. J. W. Date 14 - July '67
Indexed Date

STATION	B. S.	H. I.	F. S.	ELEV.	SANTIAGO Rd.	
41+00				2994.77		℄
				94 30		24R GUT.
				94 8		30R BOT BRK.
				3000 30		43R TOP BRK.
				2994 10	16½L GUT.	
				96 0	24L TOP BRK.	
				94 4	45L DIRT	
41+50				98 91		℄
				98 50		17R E.P. BOT. BRK.
				3004 6		27R TOP BRK.
				3005 8		40R DIRT
				2992 34	17L E.P. GUT.	
				3002 3	26L TOP BRK.	
				02 0	34L " "	
				00 8	40L DIRT	
42+00				03 01		℄
				02 57		17R E.P. BOT. BRK
				09 0		27R TOP BRK.
				11 0		43R DIRT
				02.49	17½L E.P. BOT. BRK.	
				04 2	21L TOP BRK.	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. Date
Notes Rod No. Date
Plotted Date
Job No. Survey of
Division No. Map No.
Indexed Date

F.B. 342 Pg. 49

STATION	B. S.	H. I.	F. S.	ELEV.	SANTIAGO RD.	
42+00				3004.0	26 L. TOP BRK.	
				01.5	37 L. DIRT	
42+50				06 80		℄
				06 38		17 R E. P. BOT. BRK.
				08 8		21 R TOP BRK.
				09 4		33 R BOT BRK
				12 0		45 R S. H
				06 45	17 L E. P. BOT. BRK.	
				07 2	20 L TOP BRK	
				07 4	31 L " "	
				03 0	40 L DIRT	
42+87 80	INT.			07 75		℄
				08 00	X SEC. TAKEN ON ℄ SIERRA HI-WAY	20 R PVMT.
				08 19		40 R PVMT.
				07 52	20 L PVMT.	
				07 33	40 L " "	
42+70	STATION O.K. 1 PM.			07 17	NOTE:	℄ SANTIAGO & GUTTER &
				07 42	X SEC. TAKEN PARALLEL W/℄ SIERRA HIGHWAY	20 R GUTT
				07 58		40 R "
				06 95	20 L GUTTER	
				06 70	40 L "	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 50 | Job No. 5515.16 | Division No. | Notes Red | Plotted | Profile
Survey of W/ WKS. DIST. # 37 | Date | Date | No.
Survey by C.L.W. | Notes C.L.W. | Notes Chkd | Checked | X-Sec.
Indexed | Date | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	SANTIAGO RD	
43+06				300725	℄ SANTIAGO RD. ℄ EDGE PVMT SIERRA HI-WAY	
				0746	X SECT. TAKEN PARALLEL WITH ℄ SIERRA HIGHWAY	20R ℄ EDGE PVMT.
				0766		40R
				0699	20L ℄ EDGE PVMT	
				0677	40L	
BM 201-69				300608		

Notes Ck'd by	Survey of W/ [illegible] #37	F.B. 2692 Pg. 51
Map Ref.		
Office Work	Surveyed by C. L. WRIGHT	
Checked	Notes C. L. W. H. C. H. Date 10/67	
Date	Indexed H. E. O. SEP 5 '68	

LOS ANGELES COUNTY WATER WORKS DISTRICT #37 - VICINITY - ACTON.
CROWN VALLEY ROAD - VICINITY
ANTELOPE VALLEY FREEWAY - IMPROVEMENT LOCATION

J.N. 5375.16

REFERENCES:

F.B. 2692

PARTY:

C. L. WRIGHT
H. C. HUBBARD JR.
B. A. PEAVY.
J. M. SIDWELL
J. D. GALLAGHER

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

7SP3003 CK #310 5-66

F.B. 2429 Pg. 52

CONT. FROM Pg. 53

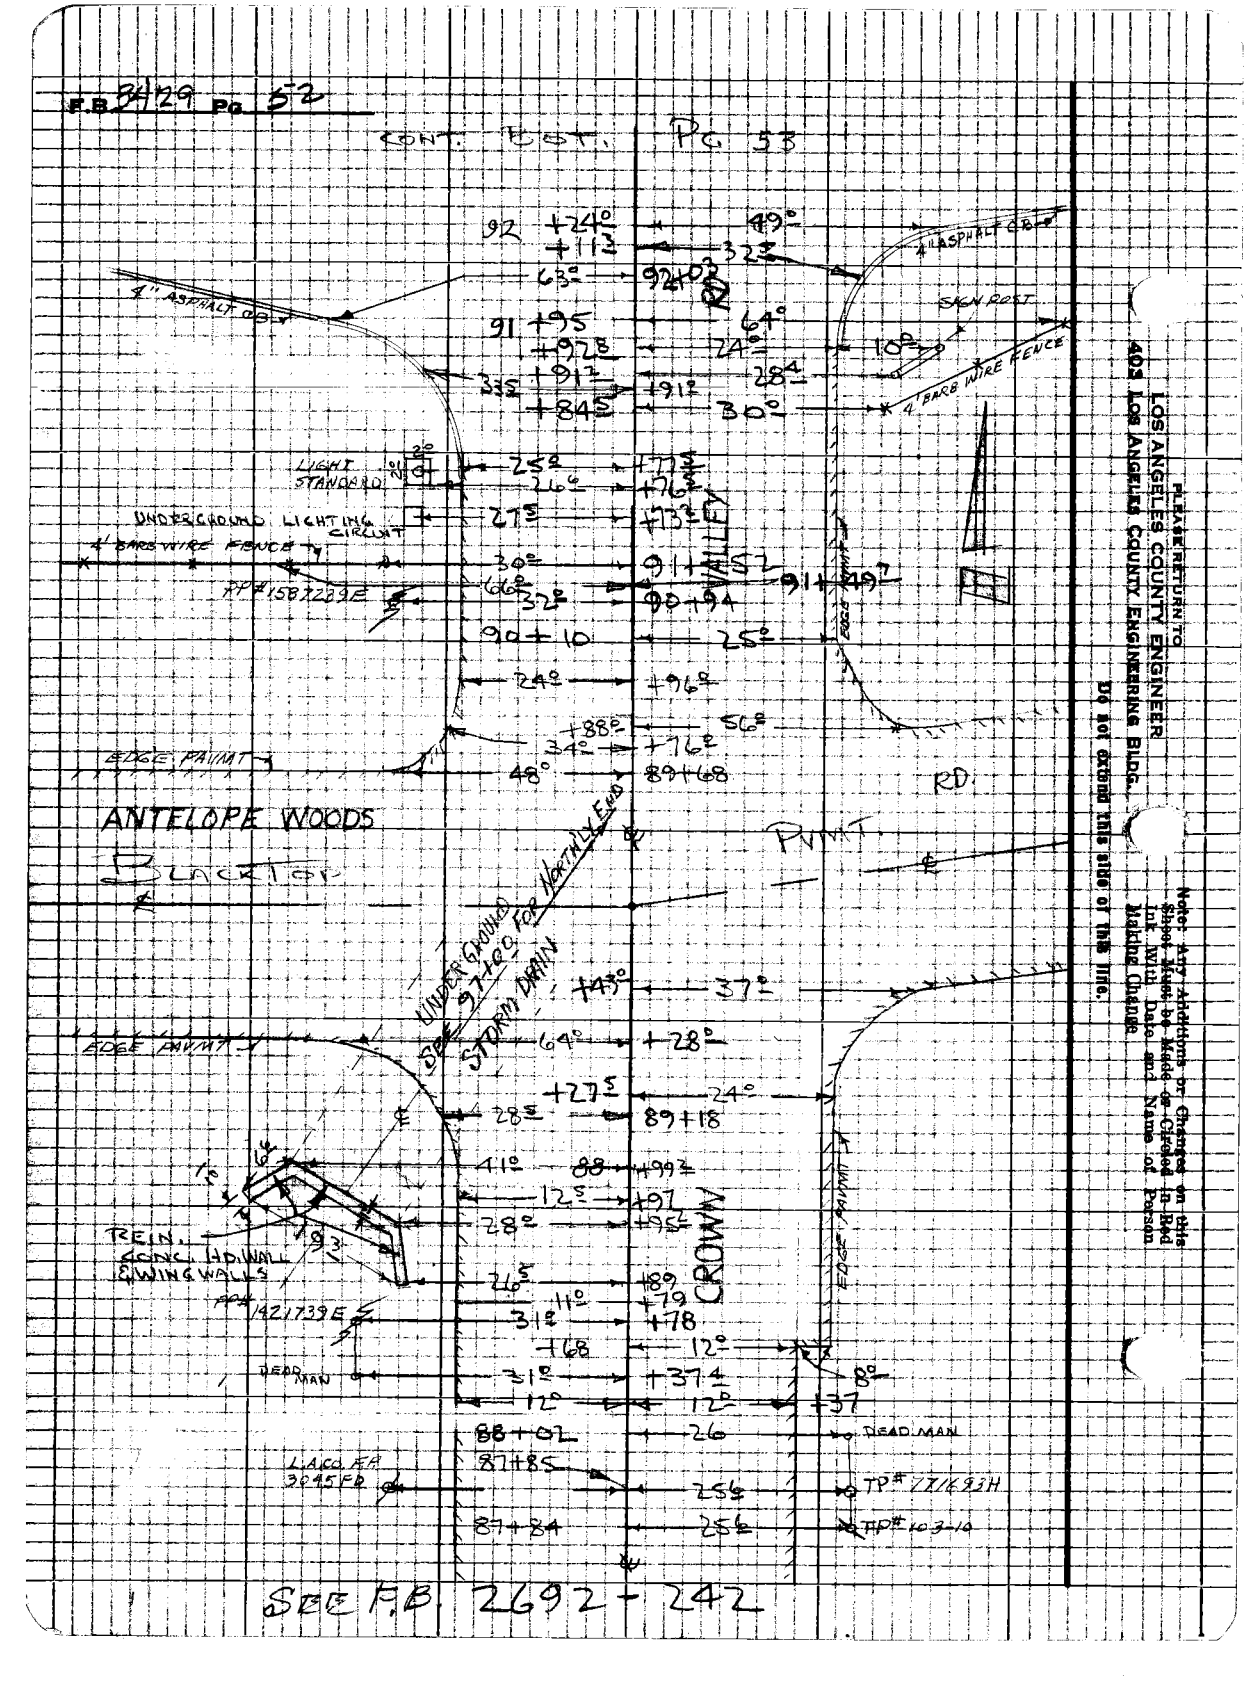

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
402 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this side of the line.

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

SEE F.B. 2692 + 242

Notes Ck'd by _____ Survey of W/O#7127
Map No. _____ Date _____
Office Work _____ Surveyed by C. L. WURTH
Checked _____ Notes C. L. W. Date 11/6/67
Date _____ Indexed H. E. OT. SP 5 W

F.B. 2446 Pg. 53

COUN. RD. 1.46. 54

Notes: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

7-68 3018 CR #310 5-68

94+00
30°
30°
93+75.8
OVERHEAD
93+72.33
31.16
31.13
93+59.47
93+48.35
31.14
UNDERGROUND LIGHTING CIRCUIT
30°
+96.7
31.13
93+35.95
OVERHEAD
93+35.8
33°
93+02
92+83.8
44°
+72.4
37°
+70.3
32°
+65.4
33°
42°
+60.0
30°
+55.8
35°
36°
+55°
34°
+51.3
33°
+48.2
30°
+45°
34°
+40°
64°
92+37.5
CONTI TOP Pg. 52

CONT. BOT PG 55

F.B. 3429 Pg 54

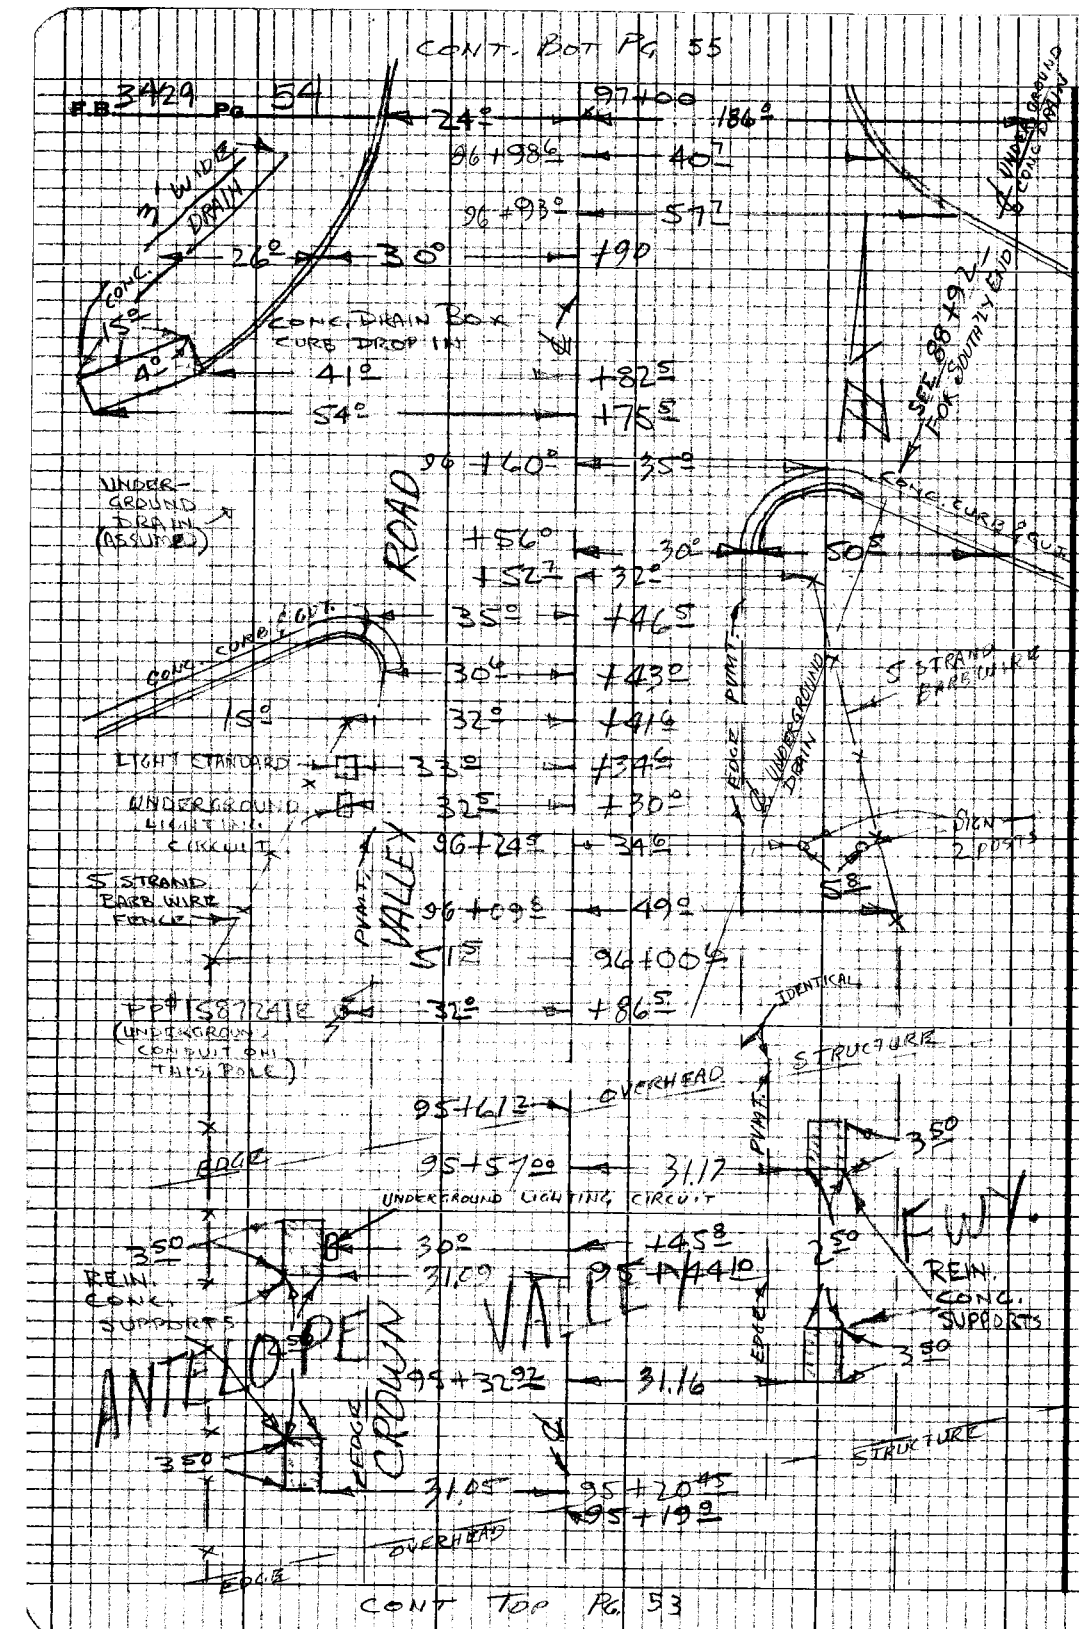

CONT TOP PG 53

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Notice Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line.

Notes Ck'd by _____ Survey of W/Hwy Imp't 57
Office Work _____ Surveyed by C. L. WRIGHT
Checked _____ Notes C [illegible] Date 10/[illegible]/61
Date _____ Indexed H. E. OTT

F.B. 2496 Pg. 55

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Note: Any Additions or Changes on this Sheet Must be Made & Checked in Red Ink With Date and Name of Person Making Change
Do not extend this side of this line.

VALLEY ROAD
HIGHLAND
SIERRA
INT. FD. L.P.
F.L. 269+ 210 243
99+11 56'
SEE F.B. 2602 - 243 FOR REMAINDER OF IMP. LOC.
COUNTY
ANCHOR
21°
P.I. 158+74 E
47°
32°
28°
16°
11°
10°
01°
26°
98+00
21°
64°
25°
51°
25°
39°
30°
30°
36°
49°
27°
24°
27°
25°
21°
23°
97+07
31°
28°
97+01
3°
FIVE CHAIN PALE L.A.C. #3098
CONDUIT GOES UNDERGROUND
T.P. 75/837 H
ANCHOR GUY
STRAND BARB WIRE FEN.
UNDERGROUND LIGHTING CIRCUIT
LIGHT STANDARD
ASPHALT CURB
EDGE PAVT.
CURB
ASPHALT CURB
SIGN POST W/L
5'

CONT. TOP PG. 54

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line.

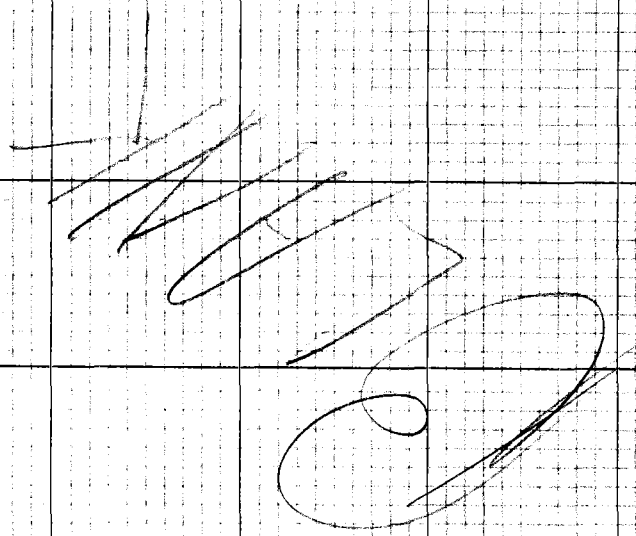

FB 3429 Pg 56

Notes Ck'd by	Survey of W.W. Dist. #37
Office Work	Surveyed by C.L.W.
Checked	Notes C.L.W. Date JULY 67
Date	Indexed H. E. OTT

F.B. 3124 Pg. 57

LOS ANGELES COUNTY WATERWORKS DIST. #37

VICINITY - ACTON

CROWN VALLEY ROAD

ADDITIONAL IMPROVEMENTS

I.N. 5375.16

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Do not extend this slide of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

7582038 CK #310 5-68

F.B. 3429 Pg. 58

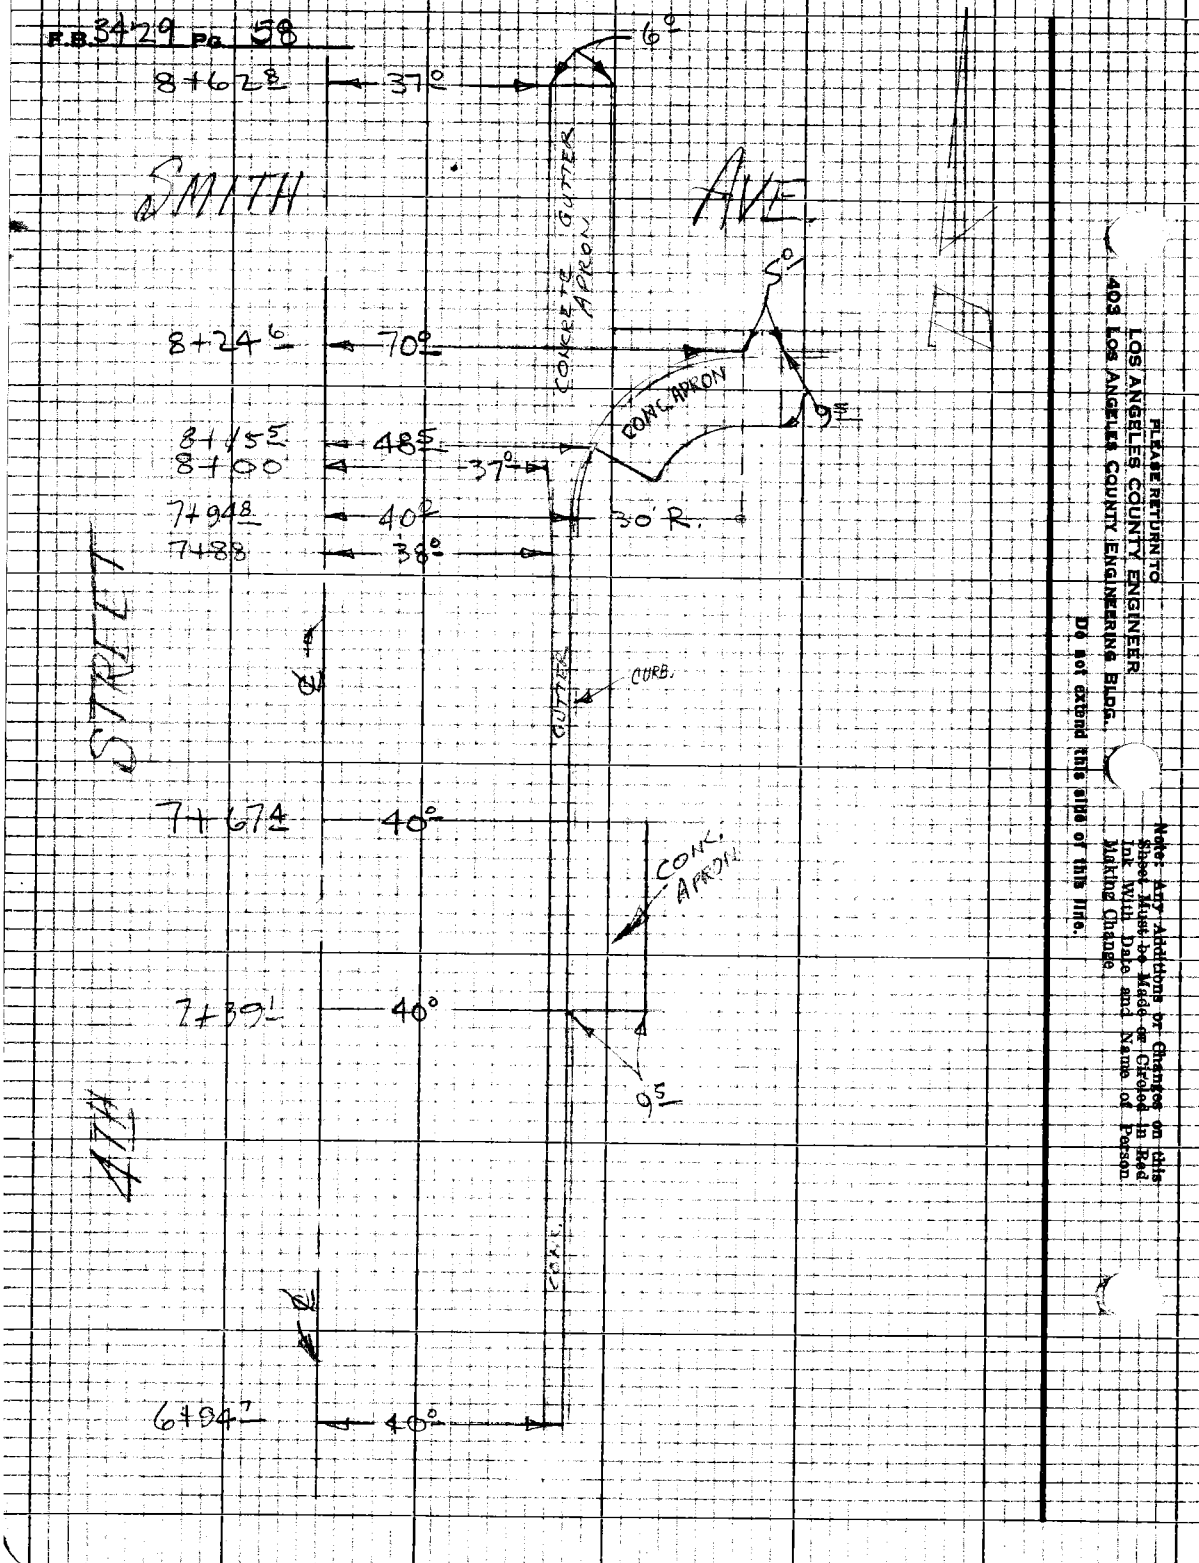

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this sign or this line.

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by		Survey of W. W. Dist #37	F.B. 3419 Pg. 59
Office Work		Surveyed by C.L.W.	
Checked		Notes H.C.H.	Date JULY 67
Date		Indexed H. E. Off	

LOS ANGELES COUNTY WATERWORKS DIST #37

VICINTY - ACTON

CROWN VALLEY ROAD

ADDITIONAL IMPROVEMENTS

JN 5375.16

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

7SP3035 CK #310 5-65

F.B. 3429 Pg. 60

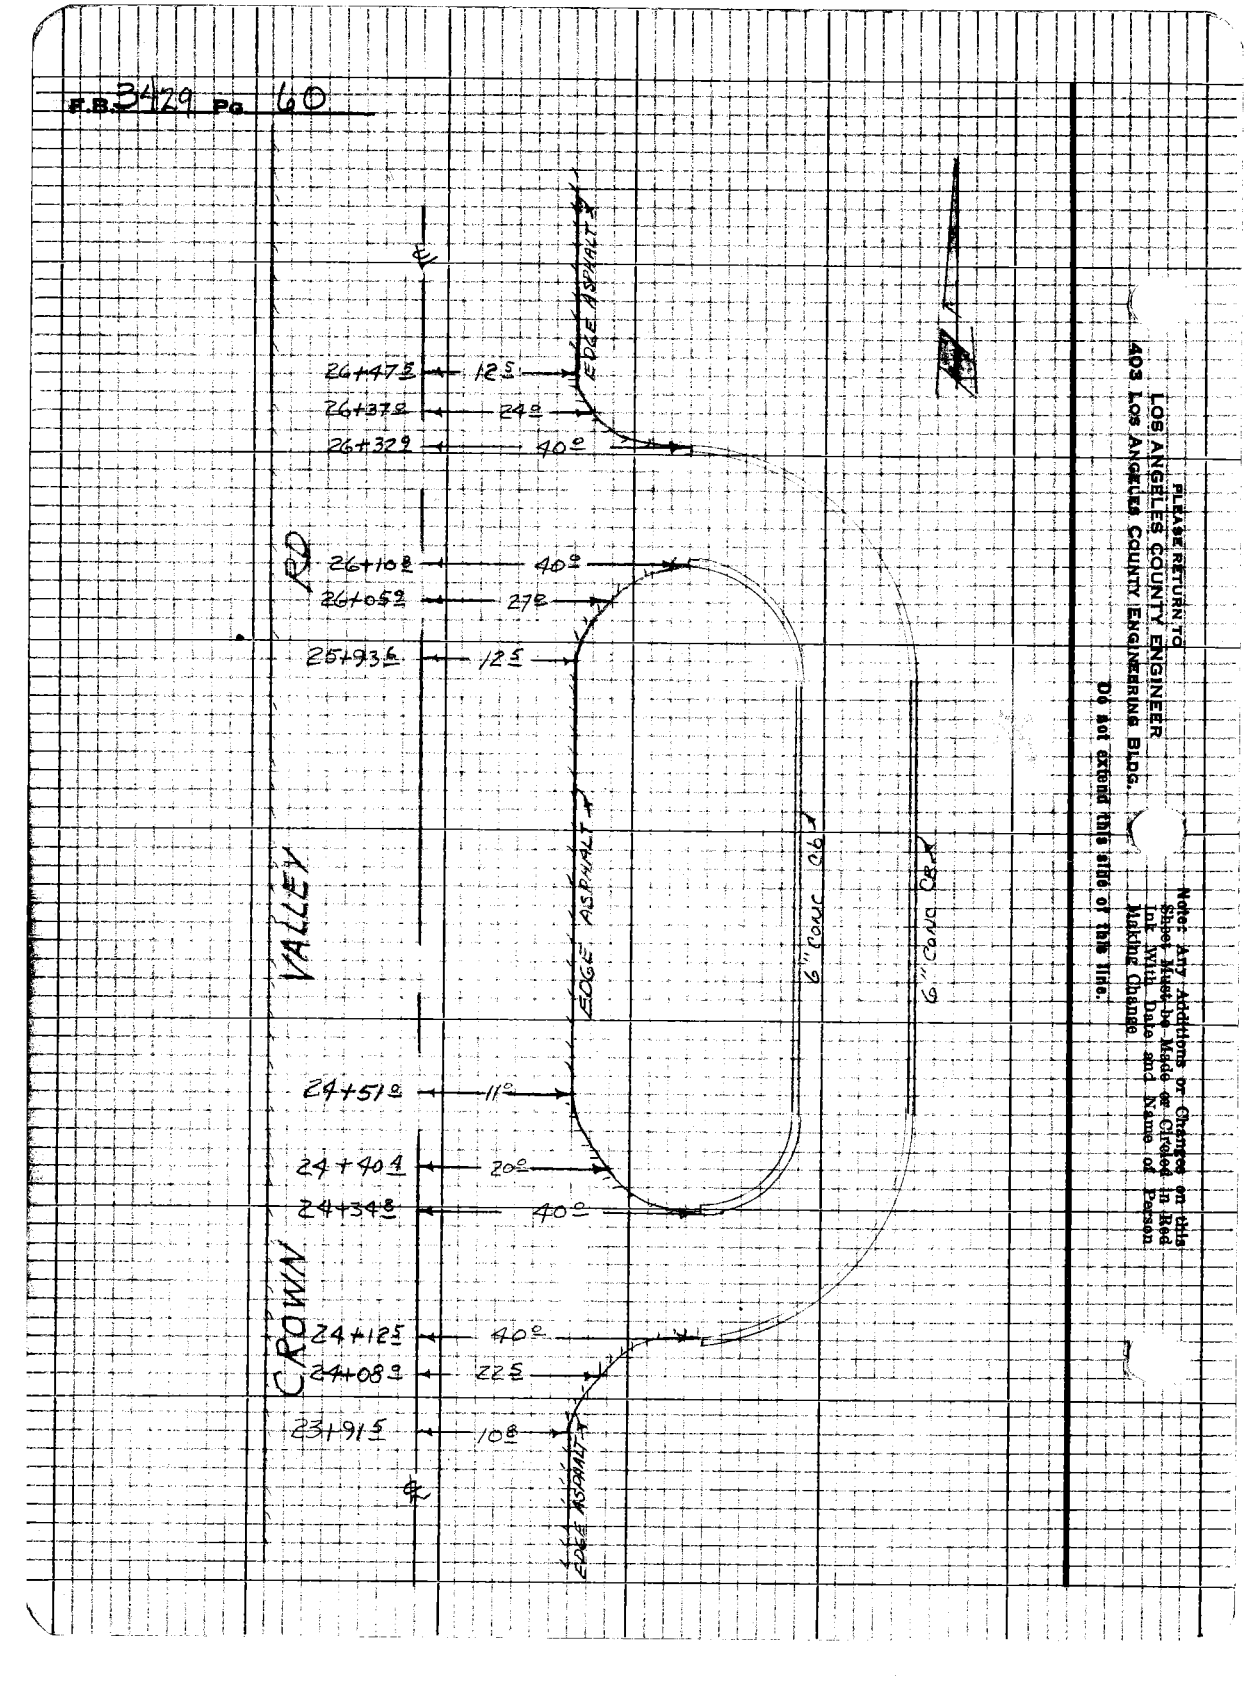

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this side of this line.

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

F.B. 3429 PG. 61

Profile No. _____ Notes Red _____ Date _____ Plotted _____ Date _____ Job No. 5375.16 Division No. _____ Survey of Co. Wide Dist. #37

~~X-Sec. No. _____ Notes Red _____ Date _____ Plotted _____ Date _____ Map No. _____~~ Indexed H. E. OTT Date _____

LOS ANGELES COUNTY WATER WORKS

DISTRICT #37 - VICINITY - ACTON

CROWN VALLEY RD (& 4TH ST.) FROM SOLEDAD CYN RD. TO SIERRA HIGHWAY — PROFILE & X SECTION.

J.N. 5375.16

STATION	B.S.	H.I.	F.S.	ELEV.

PARTY:
C. L. WRIGHT
H. C. HUBBARD, JR.
B. A. PEAVY
J. M. SIDWELL
J. D. GALLAGHER

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

CE 307 2-63

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

76-L-298

Do not extend notes this side of this line.

F.B. 2429 Pg. 62 | Job No. 5375-1/6 | Division No. | Notes Red | Plotted | Profile
Survey of W/Wks. DIST. #37 | Date | Date | No.
Survey by C.L.W. | Notes T.D.G. | Notes Chkd. | Checked | X-Sec.
Indexed | Date 24-JULY 67 | Date | Date | No.

STATION	B.S.	H.I.	F.S.	ELEV.	CROWN VALLEY RD.	
BM. H-53 FD					(BM. H-53 (U.S.1906) ELEV. 2697.865 F.B. 2631-181, 201 1955 ADJ. ELEV. FD. BRONZE DISK U.S.C. & G.S. STAMPED H-53 1926 AT ACTON 0.1 MI. N.E. ALONG S.P.R.R. FROM SECTION FOREMAN QUARTERS AT THE CROSSING OF A PAVED ROAD. 103 FT. N.W. OF AND ACROSS THE TRACKS FROM MILE POST 426, 94 FT. S.W. OF S.W. COR. OF A WOODEN R.R. BRIDGE, 57.8 FT. N.W. OF THE N.W. RAIL, 30.9 FT. N.E. OF THE ℄ OF PAVED RD., 3.4 FT. S. OF A WITNESS POST ABOUT LEVEL WITH TRACK ℄ SET IN TOP OF A CONCRETE POST UP 6" ABOVE GROUND ALSO F.B. 2692-246	
				2697865		
0+00				968	℄	
				971		3 R. BOT BRK
				990		10 R. TOP BRK
				9898		12½ R E.P
				9703		43° R BRK.
				9698		52° R E.P
				981		72½ R. TOP BRK
				951		80° R BOT BRK
0 + 40				963	℄	
				962		8 R. BOT BRK
				937		15 R TOP BRK
				9681		18½ R. E.P
				9646		63° R. E.P
				972		70 R TOP BRK
				976		80½ R BOT BRK

NOTE: FROM 0+00 TO STA. 4+61 ℄ IS THE ℄ SEC. & 15 ℄ PROD. FROM THE NORTH. AS SHOWN IN F.B. 2692-226, 227, 228

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 537-16 Division No. ____
No. ____ Date ____ Date ____ Survey of ____
No. ____ Date ____ Date ____ Map No. ____ Indexed H. E. OTT Date 8-23-63
F. B. 3427 PG. 63

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN MILLER RD.	
0+30				2696.5		℄
				2.56		10.5 R Bot R
				98.40		12.5 R E P
				9833		50.5 R
				99.08		24 P
				96.7		5.5 R GROUND ON HILLSIDE
0+90				920		.02 R AVERAGE F.L.S CULVERTS
1+00				967		℄
				9796		15 R E P & Bot R
				9732		38 R
				9678		91 R AVERAGE F.L.
				932		72 R END CULVERT
1+30						℄
1+50				963		
				9640		10 R E.P
				9605		46 R E.P
				940		54.5 R Bot Bk
				938		75.5 R "
				937		79 R Top Bk
				963	20 L	
2+00				971		℄
				9988		41 R Bot Bk

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

F. B. 3429 PG. 64 | Job No. 5375.1/6 Division No. | Notes Red | Plotted | Profile
Survey of W.W.K.S. DIST #37 | Date | Date | No.
Survey by C.L.W. Notes E. D. G. | Notes Chkd. | Checked | X-Sec.
Indexed | Date 24-JULY '67 | Date | Date | No.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY	RD.
2+00				9694.58		51 R E.P
				93H		50 R F.L. DRAIN
				94A		45℄ R TOP BRK
				96 0		80 R DIRT
				992	6 L TOP BRK.	
				992	25 L DIRT	
2+99				9613		℄
				969	5 L E.P & TOP BRK	
				003	16 L TOP BRK	
				003	30 L	
3+00				9613		℄
				9691		39 R E.P & GUT.
				967		55 R TOP BRK
3+98				9613		℄
				9627	6 L E.P	
				980	26 L TOP BRK	
				98H	40 L DIRT (℄ DRIVE)	
4+00				9655		℄
				955H		31.5 R E.P
				967		44 R TOP BRK
				9660	10 L E.P	

76-L-296 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 5222.1 Division No. ____
No. ____ Date ____ Date ____ Survey of Wilmington Unit #27
No. ____ Date ____ Date ____ Map No. ____ Indexed H. E. O. Date ____

F. B. 3429 PG. 65

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN ALIGN	RD.
4+00				96974	28 L TOP BRK	
				989	40 L	
4+61 65				9[illegible]17		
				9[illegible]00		22 S R E.P.
				968		42 R TOP BRK
				96[illegible]3	20 S L E.P.	
				972	40 L	
5+00				9648		
				9604		27 R C/L
				9616		40 R PLANT
				9660	20 L PLANT	
				9685	40 L PLANT	
5+[illegible]				9708		
				9612		23 R E.P. of Pl
				977		46 R TOP BRK
				9675	17 L E.P.	
				979	31 S L TOP BRK	
				981	40 L	
6+94.8				9659		32 R C/L
7+00				9706		
				96[illegible]		22 R [illegible]

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 66 | Job No. 53751-6 | Division No. | Notes Red | Plotted | Profile
Survey of L.W.W.S. DIST. #37 | Date | Date | No.
Survey by L.W. | Notes T.L.D.G. | Notes Ckd. | Checked | X-Sec.
Indexed | Date 24-JULY 67 | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY	RD.
7+00				98[illegible]	[illegible]	39' R Gut
				97.20		40' R T.C.
				98.1		46' R Top
				96.84	18 L E.P.	
				97.2	28 L Dirt	
				97.2	40 L	
7+98				[illegible]		39' R T.C. Gut
8+00				97.85		
				97.00	20 L E.P. & Gut	
				97.2	32 L Top Bks	
				97.8	[illegible]	
8+24				97.45		
				96.97		24' R Bks
				97.05		40 R Conc Gut
				97.10		70 R Gut
8+[illegible]				9[illegible]		
				97.52		20 R Bks
				97.[illegible]		40 R Conc Gut
				[illegible]	[illegible] L Conc Gut	
				[illegible]	40 L Pvmt	
9+00				97.01		

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. S3[illegible] Division No.____
No.____ Date____ Date____ Survey of W/Ave [illegible] Sta 39
X-Sec. Notes Cked____ Checked____ Survey by [illegible] Notes [illegible] Date [illegible]
No.____ Date____ Date____ Map No.____ Indexed H. E. O'B Date____

F.B. 3429 Pg. 67

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN/ALLEY/RD.
9+00				969.95	16 R
				984	40 R
				9720	20
				981	12
0+00				978	
				9778	15 R E.O &
				980	40 R
				9[illegible]	[illegible] & Gut
				988	[illegible] 38
				986	47
			3.5	9819	
				9768	15 R E.O
				984	40 R
				9780	[illegible]
				981	[illegible]
12+00			3.7	9904	
				9839	16 R E.O &
				993	25 R To [illegible]
				993	40 R
				9838	18 [illegible]
				994	40 R

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F. B. 3429 Pg. 68 | Job No. 5351.16 Division No. | Notes Red | Plotted | Profile
Survey of W.N.R.D. 1st. # 37 | Date | Date | No. X-Sec.
Survey by C.L.W. Notes A.D.G. | Notes Chkd. | Checked | No.
Indexed | Date LA-AUG '67 | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	Ground Valley	Pc.
13+00				269.96		℄
				9.14		15 R E.P.
				9.0		20 R Gut
				2.10.03		31 R Top Brk
				9.9.1		40 R
				9.8.04	17 L E.P. & Gut	
				9.9.11	17 L Top Brk.	
				2.10.02	40 L	
14+00				2.10.18		℄
				9.9.5		16 R E.P.
				9.6		21 R Gut
				2.10.13		32 R Top Brk
				2.10.1		40 R
				9.9.25	16 L E.P. & Gut	
				2.10.09	17 L Top Brk	
				2.10.06	40 L	
14+90.30				2.10.03		℄
				2.10.036		30 R Gut
				2.10.039		40 R Plant
				9.9.23	16 L E.P.	
				5.13	21 L Top Brk	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY	RD.
14+90.38				27.518	19 L	
15+00				28.15		
				[illegible]		15 R 2.0
				4.8		[illegible]
				[illegible]		[illegible]
				[illegible]	[illegible] 2.5 ± EOP	
				28.3	P.I. [illegible] TOP SLOPE	
				[illegible]	25	
17+00				[illegible]		
				027.3		15 R 2.0
				24.0		25 R
				29.7	10 [illegible] 5.9 ± EOP	
				[illegible]	20 [illegible] TOP SLOPE	
				[illegible]	25 [illegible]	
15+00				28.82		
				[illegible]		15 R [illegible]
				25.3		15 R
				28.2	[illegible]	
				25.10	[illegible] TOP SLOPE	
				25.75	10 [illegible]	
16+38				25.33		20 R

Profile Notes Red. Plotted Job No. 5315 Division No.
No. X-Sec. Date Date Survey of W/WK. UNIT # 27
No. Date Date Checked Survey by Map No. Indexed H.E. OTT Date
Notes Chkd. Notes Ext. Dated

F.B. 3429 PG. 69

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3424 Pg. 70 | Job No. 53515-16 Division No. | Notes Red | Plotted | Profile
Survey of W/WKS. DIST #37 | Date | Date | No. | X-Sec.
Survey by C.L.W., Notes J.T.D.G. | Notes Chkd. | Checked | No.
Indexed | Date 24-JULY 67 | Date | Date

STATION	B.S.	H.I.	F.S.	ELEV.	CROWN VALLEY	RD.
18+32				2004.33	17 L GUT.	
				05.26	40 L	
19+00				05.72		℄
				05.57		18½ R EP & GUT
				05.6		40 R
				05.08	14 L EP & GUT	
				06.8	27 L TOP BRK	
				06.5	40 L	
20+00				06.54		℄
				06.09		13½ R EP & GUT
				07.18		31 R TOP BRK
				06.97		46 R
				06.06	14 L EP & GUT	
				05.80	31 L TOP BRK	
				05.80	40 L	
21+00				05.62		℄
				04.26		13 R EP & GUT
				03.83		23 R TOP BRK
				04.13		41 R
				07.00	11½ L EP & GUT	
				09.1	31 L TOP BRK	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ Date ____ Notes Red No. ____ Date ____ Plotted ____ Date ____ Job No. 5215 Survey of W.W. DIST. #29 Map No. ____ Division No. ____ Indexed H.E.O. Date ____

F.B. 3429 PG. 71

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN/VALLEY	RD.
R 1+00				091	HDL	
B.M.				07[illegible]	FD. C.S. MON. S.W. COR. OF SOLEDAD AGUA DULCE (UNDISTURBED) LOT. REC. ELEV. 2708.225 PER R.S. 2692-247 THIS MON. HAS BEEN DISTURBED.	
21+49 E				[illegible]		& [illegible]
				0		[illegible]
				0[illegible]		[illegible]
				0[illegible]		[illegible]
21+66 E				0[illegible]		
				09[illegible]	[illegible]	
				0[illegible]	[illegible]	
22+00				2[illegible]		
				0[illegible]		[illegible]
				0[illegible]		22
				0[illegible]		[illegible]
				2[illegible]	[illegible]	
				0[illegible]	[illegible] GUT.	
				096	29 [illegible] TOP BRK	
				095	[illegible]	
23+00				100[illegible]		&
				0991		12 R [illegible]
				006		22 R TOP [illegible]

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 72 | Job No. 5315.16 Division No. | Notes Red | Plotted | Profile
Survey of W/WKS. DIST #37 | Date | Date | No.
Survey by C.L.W.I. Notes A.D.G. | Notes Chkd. | Checked | X-Sec.
Indexed | Date 25-JULY '67 | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY	FL.
23+00				2709.6		HO R
				99.5	11 L E.P	
				94	21 L GUT	
				107	30 L TOP BRK	
				100	40 L	
24+00				1169		
				1154		11 R E.P
				122		22 R TOP BRK
				112		110
				1154	11 L E.P	
				108	22 L GUT	
				121	30 L TOP BRK	
				116	40 L	
25+00				1387		
				1319		12 R E.P
				137		23 R TOP BRK
				130		40 R
				1320	11 L E.P	
				130	21 L GUT	
				140	29 L TOP BRK	
				134	40 L	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Rod____ Plotted____ Job No.____ Division No.____
No.____ Date____ Date____ Survey of W/LWK + Tie #'s
No.____ Notes Ckd.____ Checked____ Survey by____ Notes____ Date____
Date____ Map No.____ Indexed H. E. OT Date____

F.B. 3429 PG. 73

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY	RD.
26+00				271560		℄
				1550		11 R E.P
				136		H.O R
				1558	10 L E.P	
				154	21 L GUT	
				164	29 L	
				164	H.O L	
27+00				1830		℄
				1813		12 R E.P
				76		21 R GUT
				82		H.O R
				1820	11 L E.P	
				179	23 L GUT	
				192	30 L	
				189	H.O L	
28+00				2113		℄
				2099		14 R E.P
				236		20 R GUT
				210		H.O R
				2094	13 L E.P	
				228	23 L GUT	

F.B. 3429 Pg. 74 | Job No. 5375.16 | Division No. | Notes Red | Plotted | Profile

Survey of W/WKS. DIST. #37 | Date | Date | No. | X-Sec.

Survey by C.L.W. Notes G.L.D.G. | Notes Chkd. | Checked

Indexed | Date | Date | Date | No.

76-L-296 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.	
78+00					
B.M.N.C.-1005					

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. X-Sec. No. Notes Red Date Plotted Date Checked Date Job No. Survey of Map No. Division No. Indexed H. E. Office Date

F. B. 3429 PG. 75

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY RD.
BM. NC 1005				2722.507	
28+18.42				21.15	X SEC. @ RIGHT ℄ FD. C.E. MON. BN.
				21.52	99 R E.P.
				21.8	4½ R FP
				21.52	14½ L E.P.
				21.4	24 L BOT BRK
				22.2	40 L. TO TANGENT AHEAD
29+00				24.30	℄
				24.13	12½ R. E.P.
				23.1	20 R GUT
				25.1	24 R TOP BRK
				25.0	40 R
				24.10	12 L. E.P.
				23.8	22 L GUT
				25.5	40 L
30+00				27.57	℄
				27.42	13½ R. E.P.
				26.8	21 R. GUT
				27.9	25 R TOP BRK

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F. B. 3424 Pg. 76 | Job No. 5315.16 Division No. | Notes Red | Plotted | Profile
Survey of W.W.D.S.D. DIST. # 37 | Date | Date | No.
Survey by C.L.W.W. Notes F.D.S.G. | Notes Chkd. | Checked | X-Sec.
Indexed | Date 28-JULY '67 | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	CENTER LINE	REMARKS
30+00				2728.2		40 R.
				2747	11½ L E.P.	
				266	23 L GUT	
				286	32 L TOP BRK	
				223	40 L	
31+00				3082		&
				3072		12 R E.P
				299		20 R GUT
				313		21½ R TOP BRK
				325		40 R
				3066	11½ L E.P	
				298	23 L GUT	
				278	31½ L TOP BRK	
				311	40 L	
32+00				3405		&
				3392		12½ R E.P
				334		20 R GUT
				360		27 R TOP BRK
				370		40 R
				3388	12 L E.P	
				327	21½ L GUT	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN / ALLEY	R/W
32+00				27347	30 L TOP BRK	
				347	HOL	
32+70				3583		℄
				3568		12 R E.P.
				357		20R R GUT
				319		40 R
33+00				3662		℄
				3645		12 R E.P.
				363		20 R GUT
				309		33 R TOP BRK
				313		40 R
				3651	12 L E.P.	
				356	23 L GUT	
				378	35 L TOP BRK	
				373	40 L	
34+00				3910		℄
				3916		12 R E.P.
				390		20 R GUT
				414		40 R
				389H	13 L E.P.	
				378	25 L GUT	

Profile Noted Red Plotted Job No. 3515 Division No.
No. Date Date Survey of W. Rancho Dist. #37
X Sec. Notes Cked. Date Survey by Date Notes Date
No. Date Checked Map No. Indexed D. E. OT Date
F. B. 3429 Pg. 77

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK. WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 PG. 78 | Job No. 5315.16 Division No. | Notes Red. | Plotted | Profile
Survey of W/NKS. DIST. #37 | Date | Date | No. | X-Sec.
Survey by C.L.W. Notes W.D.G. | Notes Chkd. | Checked | No.
Indexed | Date 10-JULY 67 | Date | Date

STATION	B. S.	H. I.	F. S.	ELEV.	CROSS SALLY 1	F.B.
34+00				27403	32 L TOP BRK	
				399	40 L	
35+00				41.8		℄
						12 R E.P
						21 R GUT
						24 R TOP BRK
						30 R
					125 L E.P	
				3	L GUT	
				4	31 L TOP BRK	
				4	L	
T.B.M #1				27444	906 F.B. 2692-248	
36+00				4303		℄
				4317		12 R E.P
						21 R GUT
				440		24 R TOP BRK
						30 R
				4284	12° L E.P	
				417	24 L GUT	
				448	33 L TOP BRK	
				417	40 L	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. 5315 Division No.
No. X-Sec. Date Date Survey of W. Ave. "I" #27
No. Notes Ckd. Date Checked Date Surveyed by Notes Surveyed Date 1/6 Tested
Map No. Indexed H. E. Ott Date

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY RD.
37+00				2445.05	℄
				43.24	12 R E.P
				45.4	19.3 R GUT
				48.3	40 R
				44.87	12 L E.P
				43.6	25 L GUT
				46.7	33 L TOP SOIL
				46.8	40 L
38+00				47.20	℄
				47.31	11.5 R E.P
				47.2	18.5 R GUT
				48.1	22.5 R TOP SOIL
				49.1	40 R
				47.05	12 L E.P
				46.2	24 L GUT
				48.1	30.5 L TOP SOIL
				47.7	40 L
39+00				49.08	℄
				49.01	12.0 R E.P
				48.8	18.5 R GUT
				52.4	29.5 R TOP SOIL

F. B. 3429 Pg. 79

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 80 | Job No. 5375.16 | Division No. | Notes Red | Plotted | Profile
Survey of W/Wks. Dist. #37 | Date | Date | No.
Survey by C.L.W. Notes by D.G. | Notes Chkd. | Checked | X-Sec.
Indexed | Date 28-July '67 | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	GROUND (FILL)	REMARKS
39 + 00						110 R
				48		
				45	2 30	
					110	
40 + 00				509		℄
						12 R EP
						20 R Gut
						29 R Top Bk
				538		40 R
41 + 00				590		℄
				5290		11 R E.P
				524		19 R Gut
				536		22 R Top Bk
				516		40 R
				5293	12	
				5241	24	

76-1-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Rod____ Plotted____ Job No.____ Division No.____
No.____ Date____ Date____ Survey of ____ X Sec.____
No.____ Date____ Date____ Map No.____ Indexed H. E. OT Date____

F.B. 3429 PG. 81

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN FALLEN	RD.
41+00				276.35	27 L TOP BRK	
				530	40 L	
42+00				534		℄
				536		12 R E.P
				518		20 R S.T
				502		40 R TOP BR
				503		40 R
				506	12 L E.P	
				516	23 L S.T	
				552	26 L TOP BRK	
				541	40 L	
43+00				539		℄
				576		12 R E.P
				574		20 R
				568		40 R
				576	12 L E.P	
				573	20 L	
				562	40 L	
44+00				598		℄
				597		12 R E.P
				596		20 R

F.B. 3429 PG. 82 | Job No. 5375.16 | Division No. | Notes Red | Plotted | Profile

Survey of W/Wks. Dist. # 37 | Date | Date | No.

Survey by C.L.W | Notes L.D.G. | Notes Chkd. | Checked | X-Sec.

Indexed | Date 25-JAN-67 | Date | Date | No.

STATION	B.S.	H.I.	F.S.	ELEV.	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Noted Red Plotted Job No. Division No.
No. Date Date Survey of
No. Date Date Map No. Indexed H. E. OT Date

F. B. 3429 PG. 83

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY RD.	
47+00				776766		℄
				6754		12 R E.P
				671		20 R
				664		40 R
				6756	12 L E.P	
				668	25 L TOP BRK	
				650	33 L BOT BRK	
				619	40 L	
48 - 00				7096		℄
				7075		12 R E.P
				714		28 R TOP BRK
				788		27 R BOT BRK
				786		40 R
				7087	12 L E.P	
				702	25 L TOP BRK	
				787	37 L BOT BRK	
				710	46 L	
49+00				7165		℄
				7152		12 R E.P
				746		23 R TOP BRK
				727		27 R BOT BRK

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 84 | Job No. 5375.1 | Division No. | Notes Red | Plotted | Profile
Survey of W/Buks Dist. #37 | Date | Date | No.
Survey by C.L.W. | Notes 21 D.G. | Notes Chkd. | Checked | X-Sec.
Indexed | Date 25-JULY '67 | Date | Date | No.

STATION	B.S.	H.I.	F.S.	ELEV.	CROWN VALLEY RD.
49 +00				27726	HD R
				7707	12 L E.P.
				7702	23 L Top Bnk
				7697	34 L Bot Bnk
				7692	40 L
49 +70				7744	℄
				7701	11 L E.P
				7712	26 L Gut
				7731	40 L
50 +00				7871	℄
				7853	12 R E.P
				7769	HD R
				7703	11 L E.P
				781	12 L Bot Bnk
				618	31 L Top Bnk
				825	40 L
51 +00				8262	℄
				6248	12 R E.P.
				810	21 R Bot Bnk & Gut
				943	27 R Top Bnk
				849	42 R

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ Date ____ Notes Red ____ Date ____ Plotted ____ Date ____ Job No. 5375.1 Division No. 7 Survey of W/O [illegible] F.B. 3429 Pg. 85 No. ____ Date ____ Map No. ____ Indexed H. E. OTT Date ____

STATION	B. S.	H. I.	F. S.	ELEV.	CROSS FALL R/W	
57+00				2732.46	12 L	E.P.
				822	20 L	Bot Bk
				863	35 L	Top Bk
				912		
58+00				8620		
				8610		11 R 2.9
				918		20 R Bot Bk
				893		35 R Top Bk
				815		40 R
				8609	12 L	E.P.
				876	20 L	Bot Bk
				905	32 L	Top Bk
				895	40 L	
59+00				8942		
				8930		11 R E.P.
				836		18 R Bot Bk
				902		29 R Top Bk
				884		40 R
				8939	12 L	E.P.
				890	20 L	Bot Bk
				910	32 L	Top Bk

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 86 | Job No. 5515.16 Division No. | Notes Red | Plotted | Profile
Survey of W/Wks Dist #27 | Date | Date | No.
Survey by C.L.W. Notes H. D.G. | Notes Chkd. | Checked | X-Sec.
Indexed | Date 25-JULY '67 | Date | Date | No.

STATION	B.S.	H.I.	F.S.	ELEV.	CROWN VALLEY	F.S.
53+00				9992P	40 L	
54+00				9232		℄
				9214		14 R E.P
				9211		19 R Bot Brk
				9191		40 R
				9219	12 L E.P	
				9188	25 L Bot Brk	
				9178	31 L Bot Brk	
				9174	41 L	
54+94.05				9495	+	℄
				9480	Sec.	
				9476		14 R E.P
				9472		20 R
				9492	10 L E.P	40 R
				9389	25 L Bot Brk	
				9388	40 L	
56+00				9756		℄
				9749		12 R E.P
				9711		27 R Bot Brk
				9698		40 R
				9714	12 L E.P	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 5335.16 Division No. ____
No. ____ Date ____ Date ____ Survey of W/Wks. Dist. #37
X-Sec. Notes Red ____ Checked ____ Surveyed by ____ Notes Red ____ Detailed ____
No. ____ Date ____ Date ____ Map No. ____ Indexed H. E. OT Date ____

F. B. 3421 PG. 87

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY RD.	
56+00				2797.1	2.5 L GUT.	
				97.1	4.0 L	
57+00				300.43		℄
				00.25		1.2 R E.P.
				00.2		2.8 R TOP B
				03.1		4.0 R
				00.37	1.2 L E.P.	
				00.1	2.5 L BOT	
				00.8	4.0 L	
58+00				03.61		℄
				03.52		1.1 R E.P.
				03.4		3.0 R BOT
				06.3		4.0 R
				5.30	1.2 L E.P.	
				5.31	2.5 L BOT	
				03.4	3.5 L	
58+43				05.00		℄
				04.87		1.2 R E.P.
				04.5		3.3 R
				05.0		4.0 R
59+00				06.95		℄

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F. B. 3429 PG. 88 | Job No. 5515.16 Division No. Notes Red Plotted Profile
Survey of W.W.K.S. DIST. #37 Date Date No. X-Sec.
Survey by C.L.W. Notes by D.C. Notes Chkd. Checked
Indexed Date 25-AUG-67 Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY	Det.
59+00				1324.69		12 R E.P
				060		33 R Bot Brk
				092		42 R Top Brk
				0677	12 L E.P	
				760	24 L Bot Brk	
				795	32 L Top Brk	
				081	40 L	
60+00				1071		
				1004		12 R E.P
				094		28 R Bot Brk
				119		40 R Top Brk
				0999	12 L E.P	
				090	28 L Bot Brk	
				108	40 L Top Brk	
61+00				1326		
				1318		12 R E.P
				28		31 R Bot Brk
				1244		41 R Top Brk
				1236	11 L E.P	
				31	22 Bot	
				21	130 L Top	

70-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Noted _____ Plotted _____ Job No. 531S Division No. _____
No. _____ Date _____ Date _____ Survey of W/LINE DIST #87
No. _____ Date _____ Date _____ Map No. _____ Indexed _____ Date _____

F. B. 3422 PG. 87

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY RD	
61+00				28[illegible]	210 L	
62+00				28[illegible]		
				[illegible]		11 [illegible]
				[illegible]		35 R [illegible]
				[illegible]		40 R [illegible]
				[illegible]	[illegible]	
				[illegible]	[illegible] BRK	
				[illegible]	[illegible] BRK	
				[illegible]		
B.M.				281634		
63+00				2106		
				2082		11 8 R E.P.
				195		36 R BOT BRK
				23		42 R TOP "
				NO	SHOT	R
				2101	12 L EP	
				2027	24 L BOT BRK	
				2166	31 L TOP "	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F. B. 3429 Pg. 90 | Job No. 5316 Division No. | Notes Red | Date | Plotted | Profile
Survey of W/Wks Dist #37 | Date | No. | X-Sec.
Survey by C.L.W. Notes C.L.W. | Notes Chkd. | Checked
Indexed | Date 26-JULY-67 | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY	R.L.
63+00				2821.8	40 L	
64+00				24.65		℄
				24 41		12 R E.P.
				23 9		30 R
				23 9		40 R
				24 52	12 L E.P.	
				24 2	22 L Bot Brk	
				25 5	28 L Top Brk	
				26 0	40	
65+00				28 55		℄
				28 36		12 R E.P.
				28 2		34 R Bot Brk
				29 8		38 R Top Brk
				30 2		50 R
				28 36	12 3/4 L E.P.	
				27 1	25 3/4 L Bot Brk	
				28 1	29 L Top "	
				29 0	40 L	
66+00				32 31		℄
				32 18		11 R EP
				31 4		22 5/8 R Bot Brk

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. 5382 Division No.____
No.____ Date____ Date____ Survey of W/SW, Sec 4 #37
No.____ Date____ Date____ Map No.____ Indexed H.S.E. Date____

F.B. 5424 PG. 11

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY	Rd.
66+00				2833.0		25 R TOP Brk
				32.6		34 R BOT "
				34.0		38 R TOP "
				34.5		45 R
				32.08	12 L EP.	
				31.3	27 L BOT. BRK.	
				32.2	36 L TOP	
				32.3	40 L	
67+00				35.94		℄
				35.83		113 R EP.
				35.1		21 R BOT BRK
				36.4		32 R TOP "
				36.7		34 R BOT "
				38.4		44 R TOP "
				NO	SHOT	R
				35.87	12 L EP.	
				35.2	25 L BOT BRK	
				37.0	29 L TOP "	
				36.4	40 L	
68+00				39.65		℄
				39.54		115 R EP.

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F. B. 3429 Pg 92 Job No. 5315-16 Division No. Notes Red. Plotted Profile
Survey of W/WKS Dist #37 Date Date No. X-Sec.
Survey by C.L.W. Notes C.L.W. Notes Chkd. Checked
Indexed Date 26-8/10/67 Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY	Rec.
68+00				2838 6		21 5 R Bot. Brk
				40 9		26 R Top "
				40 7		36 R Bot "
				42 2		44 R Top "
				40 95	12 L E.P.	
				38 9	25 L Bot Brk	
				39 9	37 L Top "	
				401	45 L	
T.P.I. #2				3990	FD. S. W.T. & INT. CROWN VALLEY & BENSON — THIS POINT HAS BEEN DISTURBED REC. ELEV. 2840.206 — F.B. 2692-250	
69+00				43 39		℄
				4330		11 R E.P.
				424		24 R Bot Brk
				434		24 R Top "
				437		40 R
				4325	12 L E.P.	
				426	26 L Bot Brk	
				439	30 L Top "	
				440	40 L	
70+00				47 53		℄
				4659		12 R E.P.

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. 5316 Division No.
No. Date Date Survey of Indexed H.E.C. Date
No. Date Date Map No. Date

F.B. 342 Pg 93

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY	Rec.
70+00				2846.5		22 R GUTTER
				47.5		40 R
				4709	12.5 L E.P.	
				466	26 L BOT BRK	
				48.1	30 L TOP "	
				479	40 L	
71+00				5120		℄
				5106		11.6 R E.P.
				504		21.5 R GUTTER
				510		40 R
				5104	12 L E.P.	
				502	25 L BOT BRK	
				512	28 L TOP "	
				504	40 L	
72+00				5484		℄
				5454		11.5 R E.P.
				541		22 R GUTTER
				542		35 R BOT BRK
				554		38 R TO "
				554		42 R
				5465	12 L E.P.	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 94 | Job No. 5315.16 | Division No. | Notes Red | Plotted | Profile
Survey of W.W.D.D. #37 | Date | Date | No.
Survey by C.L.W. | Notes C.L.W. | Notes Chkd. | Checked | X-Sec.
Indexed | Date 26 July 67 | Date | Date | No.

STATION	B.S.	H.I.	F.S.	ELEV.	CROWN VALLEY	RD.
72+00				28 53.9	25 L GUTTER	
				54.5	30 L TOP	
				53.5	40 L	
73+00				58.60		℄
				58.40		11.5 R EP.
				57.6		21 R GUTTER
				57.7		34 R BOT BRK
				58.7		37 R TOP "
				58.6		40 R
				58.48	12 L EP.	
				57.9	24 L GUTTER	
				58.4	27 L TOP BRK	
				56.7	40 L	
74+00				62.63		℄
				62.37		12 R EP.
				61.7		21 R BOT BRK
				61.0		36 R GUTTER
				62.9		40 R TOP "
				62.48	12 L EP.	
				61.9	23 L GUTTER	
				62.4	26 L TOP	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ Date ____ Plotted ____ Date ____ Job No. 5361 Division No. ____
Notes Red. No. ____ Date ____ Survey of W/Ly Sta. 27 Map No. ____ Indexed ____ Date ____

F.B. 3429 Pg. 25

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY RD.	
74+00				2861.0	33 L	
				60.4	40 L	
74+53				64.70		℄
				64.50		12 R EP
				64.1		30 R
				64.3		40 R ℄ Dr
75+00				66.49		℄
				66.39		11.6 R EP
				65.7		31 R Bot. Brk
				66.3		40 R
				66.42	12 L	
				65.6	24 L Gutter	
				66.2	26 L Top Brk	
				64.6	33 L Bot "	
				63.6	40 L	
TBM #3 FD				2866.54	T.B.M. #3 - F.B. 2692-251 ELEV 2685.+0.1+ FD. STD. R.D. BRASS CAP IN WELL COVER - 5' S. OF CENTRAL - W. SIDE CROWN VALLEY RD - 4' W. OF P.P.# 5361 GIE.	
76+00				2870.14		℄
				69.92		12 R EP
				69.6		25.3 R F.L.
				69.7		35 R Bot Brk

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

4 12

F.B. 3429 Pg. 96 | Job No. 5515.16 Division No. | Notes Red | Plotted | Profile
Survey of W. Rowland Dist. #37 | Date | No. | X-Sec.
Survey by C. Lewis Notes C. Lewis | Date | Notes Chkd. | Checked | No.
Indexed | Date 7-JULY-67 | Date | Date

STATION	B.S.	H.I.	F.S.	ELEV.	<CROWN /ALLEY	RT.
76+00				28708		38 R TOP
				709		40 R
				7006	12 L E.P.	
				696	23 L BOT BRK	
				700	25 L TOP "	
				689	33 L BOT "	
				678	40 L	
77+00				7389		℄
				7368		12 R EP.
				731		22 R BOT. BRK
				732		35 R " "
				746		38 R TOP "
				746		40 R
				7382	12 L EP.	
				736	19 L BOT BRK	
				748	25 L TOP "	
				700	33 L BOT. "	
				705	40 L	
78+00				7758		℄
				7735		12 R EP
				766		20 R BOT BRK.

76-L-296 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. S375.16 Division No.
No. Date Date Survey of W.M.D. Dist #37
No. Date Date Map No. Indexed H. E. Ott Date
F. B. 3429 PG. 97

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN (ALLEY)	RD.
78+00				2877.0		33 R Bot. Brk
				783		37 R Top "
				783		40 R
				7738	12 L EP	
				769	24 L Bot Brk	
				776	28 L Top "	
				752	33 L Bot "	
				746	40 L	
79+00				8118		℄
				8104		12 R EP
				803		23 R Bot Brk
				809		33 R " "
				823		38 R Top "
				823		40 R
				8114	12 L EP	
				806	24 L Bot Brk	
				812	27 L Top "	
				767	35 L Bot "	
				766	40 L	
80+00				8503		℄
				8487		11 E R EP.

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 98 | Job No. 5515 Division No. | Notes Red. | Plotted | Profile
Survey of 3/4 Mile Dist. # 37 | Date | Date | No.
Survey by C.L.W. Notes C.L.W. | Notes Ckld. | Checked | X-Sec.
Indexed | Date 26-JUL-67 | Date | Date | No.

STATION	B.S.	H.I.	F.S.	ELEV.	CROWN VALLEY	RD.
80+00				2883.9		22 R BOT BRK
				84.1		32 R " "
				85.8		37 R TOP "
				85.7		40 R
				84.83	12 L EP	
				84.3	24 L BOT BRK	
				85.1	28 L TOP "	
				82.7	33 L BOT "	
				82.3	40 L	
BMNC/008				2885.69		
81+00				88.90		&
				88.70		11.5 R EP
				88.1		20 R BOT BRK
				89.2		36 R TOP "
				89.2		40 R
				88.69	12.5 L EP	
				89.0	24 L BOT BRK	
				89.3	33 L TOP "	
				89.0		
TBM #4 FD.				89.72	(REC ELEV. 2889.887) AD. BRASS CAP W/PT. IN TOP OF CONC. CURB ON CROWN VALLEY @ CEDRAL ST.	F.B. 2652-252,

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK. WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Rod Plotted Job No. Division No.
No. X-Sec. Date Date Survey of
No. Date Checked Survey by Notes
Date Map No. Indexed Date

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN (VALLEY)	RD.
82+00				28 9289		℄
				9263		12 R E.P.
				917		22 R Bot Brk
				924		28 R Top " (+ ?)
				930		40 R
				9264	12 L EP	
				920	24 L Bot Brk	
				918	28 L Top "	
				934	40 L	
83+00				9666		℄
				965		11 5 R EP
				955		22 R Bot. Brk
				960		28 R Top "
				965		40 R
				9650	11 5 L E.P.	
				951	24 L Bot Brk	
				970	30 L Top "	
				957	40 L	
84+00				290068		℄
				043		12 R E.P.
				28997		24 R Bot. Brk

F. B. 34/29 PG 97

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

7½ (Revised)

Do not extend notes this side of this line.

F.B. 3429 Pg. 100 | Job No 5375.16 Division No. | Notes Red | Plotted | Profile
Survey of 3 Wks. Proj. # 37 | Date | Date | No.
Survey by C.L.W. | Notes C.L.W. | Notes Chkd. | Checked | X-Sec.
Indexed | Date 26-JULY'67 | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY	RD.
84+00				2[illegible]5		28 R (FENCE)
				05 5		40R
				0054	L E.P.	
				29999	24 L Bot Brk	
				29011	30 L Top "	
				29999	40	
85+00				296470		℄
				0448		12 R E.P.
				035		22 R Bot Brk
				052		29 R Top "
				048		40 R
				0454	11⅝ L EP.	
				040	24⅝ L Bot. Brk.	
				057	28 L Top "	
				055	40 L	
86+00				0859		℄
				0851		11⅝ R EP.
				076		22⅝ R Bot Brk
				092		28 R Top "
				090		40 R
				0838	11⅝ L EP.	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. 5375 Division No.
No. See Date Date Survey of Water Dist. # 37
No. Notes Ckkd. Date Checked Date Survey by L. L. Map No. Noted L. L. Date L. L.
Indexed D. E. Date

F. B. 3429 PG. 10

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY RD.	
86+00				2°078	24⁵ L Bot. Brk	
				101	28 L Top	
				096	40 L	
87+00				1266		℄
				1255		11⁵ R EP
				122		21⁵ R Bot Brk
				131		25 R Top "
				132		40 R
				1247	12 L EP	
				118	24⁵ L Bot Brk	
				126	27 L Top "	
				097	43 L	
88+00				1657		℄
				1634		11⁵ R EP
				163		23 R Bot Brk
				179		28 R Top "
				180		40 R
				1625	116 L EP	
				156	22 L Gutter	
				160	25 L Top Brk	
				137	29 L Bot "	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 102 | Job No. 5375/6 | Division No. | Notes Red | Plotted | Profile
Survey of W'wks Dist #27 | Date | Date | No.
Survey by C.L.W. Notes C.L.W. | Notes Chkd. | Checked | X-Sec.
Indexed | Date 27-Jul-'27 | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY	RD.
88+00				2912+	40 L	
+96	STA. CK.	14 HI		1569	34 L OUTLET F.L. RE IN. CONC. BOX CULVERT	
88+50				1948	2 BBLS. RA. BBL. 6' WIDE - 3' HIGH	℄
				1931	115 L E.	
				1021	21 L TOP BKR	
				1666	27 L BOT	
				1523	40 L FL. DRAIN	
89+00				2018		℄
				2000		19 R E.
				1999		22 R BOT BKR
				2293		29 R TOP "
				2277		40 R
				2004	155 L E.	
				1923	41 L TOP REIN. CONC. DRAIN BOX	
89+50	STA. CK.	14 HI		2210		℄
				2179		20 R PNT
				2149		40 R "
				2109	L PNT.	
				2182	L "	
89+38				2167		℄
				2107		30 R E. BOT BKR

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted Job No. Division No.
No. X-Sec. Date Date Survey of W/W x SPST #1
No. Date Date Checked Survey by Notes Ckd. Date
Date Map No. Indexed Date

F. B. 3429 Pg. 105

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY RD.	
89+35				2924.0		54R TOP BRK.
90+00				24.21		℄
				23.1		30R E.P. BOT BRK
				26.6		45ER TOP
				23.83	24 L	I.P. TOP BRK.
				21.7	4 L	
90+75				24.65		℄
—				24.13		25R E.P. BOT BRK
				26.9		37R TOP BRK
				26.9		45R
91+00				28.11		℄
				27.65		24R E.P.
				27.1		30R BOT BRK
				26.6		34R TOP
				30.0		45R
				29.59	24 L	E.P. TOP BRK
				25.5	39 L	F.L. DRAIN
91+70				30.05		℄
				29.55		24ER E.P. TOP BRK
—				31.2		R
				29.57	23 L	E.P. R

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK. WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 2429 PG. 104 | Job No. 5375.14 Division No. Notes Red Plotted Profile
Survey of W/WKS. DIST. #37 Date Date No. X-Sec.
Survey by C.L.W. Notes C.L.W. Notes Chkd. Checked
Indexed Date 27 JULY 67 Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY RD.	
91+70				2925	40 L	
92+00				3060		℄
				3066		25 R GUTTER (PAVED)
				3111		40 R
				2020	20 L PVMT.	
				2972	43 L. GUTTER (PAVED)	
92+50				3107		℄
				3072		20 R PVMT.
				3053		40 R "
				3046	26 L E.P. BOT. BRK	
				319	35 L TOP	
				327	45 L	
93+00				3151		℄ 3 R
				3077		30 R E.P. BOT BRK
				321		33 R TOP "
				323		44 R FENCE
				3091	29 L E.P. BOT BRK	
				340	35 L	
				341	43 L FENCE	
93+50				3232		℄
				3166		30 R. E.P. BOT. BRK

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red Plotted Job No. 53754 Division No.
No. X-Sec Date Date Survey of Walnut Hills #37
No. Notes Chkd Date Checked Date Map No. Indexed D. E. O. Date

F. B. 3429 PG. 105

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY RD	
93+50				29 341		35 R TOP BRK
				351		FENCE
				363	30 L E.P. BOT. BRK	
				365	36 L TOP "	
				373	45 L FENCE	
94+00				359		℄
				373		30 R E.P. BOT. BRK
				361		36 R TOP "
				368		46 R FENCE
				376	30 L E.P. BOT BRK	
				386	39 L TOP "	
				377	46 L FENCE	
94+50				3531		℄
				3463		30 R E.P. BOT BRK
					NO SHOT	R TOP "
				382		47 R FENCE
				3445	30 L EP BOT BRK	
				435	43 L TOP "	
				430	48 L FENCE	
95+00				3756		℄
				3676		30 R EP BOT. BRK

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

6 26

Do not extend notes this side of this line.

F.B. 3429 Pg. 106 | Job No. 53751-16 Division No. | Notes Red | Plotted | Profile
Survey of W/Wks Dist #37 | Date | Date | No.
Survey by C.L.W. Notes C.L.W. | Notes Chkd. | Checked | X-Sec.
Indexed | Date 27 July 67 | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN ALLEY RD.	
95+00				2941 5		37 5 R TOP BRK
				427		47 5 R FENCE
				3675	30 L E.P. BOT BRK	
				460	44 L TOP	
				455	49 L FENCE	
95+50				4022		℄
				3950		30 R E.P. BOT. BRK
				443		35 ℄ TOP "
				456		48 5 R FENCE
				3940	30 L E.P. BOT BRK	
				480	44 L " TOP "	
				478	50 5 L FENCE	
96+00				4933		℄
				4255		30 R E.P. BOT. BRK
				472		37 R TOP "
				479		49 R FENCE
				4250	30 L E.P. BOT BRK	
				500	43 L TOP "	
				498	51 L FENCE	
96+23				1490		℄
				440	30 L E.P. BOT BRK	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Rel. Plotted Job No. 5315 Division No.
No. X-Sec. Date Date Survey of W/WORKS DIST. #37
No. Notes Ckd. Date Checked Date Surveyed by [illegible] Date
Date Map No. Indexed By [illegible] Date

F.B. 3429 PG. 101

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY RD.	
96+23				29508	44 L TOP BRK	
+43				4630		℄
				4546		30R E.P. BOT BRK
				492		36R TOP "
				495		40R
96+50				4681		℄
				4610		30R E.P. BOT BRK
				480		35R TOP "
				481		40R
				4647	20 L	
				4695	40 L	
96+75				4859		℄
				4818		20R
				4792		40R
				4825	20 L	
				4768	32 L TOP BRK	
				4627	54 L GUTTER @ DROP IN BOX	
97+00				5027		℄
				4987		20R PVMT
				4924		37R " & GUTTER
				500		R

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 PG. 108 | Job No. 5375.16 Division No. | Notes Red | Plotted | Profile
Survey of W/WKS. DIST. #37 | Date | Date | No.
Survey by C/L. W. Notes C.L.W. | Notes Chkd. | Checked | X-Sec.
Indexed | Date 7-7-JULY 67 | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	CROWN VALLEY RD.	
97+00				2949.80	24 L PVMT. & GUTTER	
				520	40 L TOP BRK	
97+23.8				5196		℄
				5144		23.5 R EP. BOT. BRK.
				538		31 R TOP "
				540		40 R
				5175	20.5 L PVMT. & GUTTER	
				5080	27 L F.L. CONC. DRAIN 1.3 FT. DEEP - 3' WIDE	
				548	38 L TOP BRK	
97+50				5382		℄
				5344		22 R EP. BOT. BRK.
				551		25 R TOP "
				547		40 R
				5356	18 L PVMT. GUTTER	
				5262	23 L F.L. CONC. DRAIN	SEE 7 LINES ABOVE
				559	31 L TOP BRK	
				565	40 L	
98+00				5697		℄
				5654		20.5 R EP.
				566		40 R
				5687	11 L PVMT. & GUTTER	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Rod____ Plotted____ Job No. 5315-15 Division No.____
No.____ Date____ Date____ Survey of CROWN VALLEY RD. STA 98+00 TO 99+11.56
No.____ Date____ Date____ Map No.____ Indexed P.L.C. Date____

F.B. 3427 Pg. 109

CROWN VALLEY RD.

STATION	B. S.	H. I.	F. S.	ELEV.		
98+00				2955.5	17 L	F.L. CONC. DRAIN - 1.3 FT. DEEP - 3' WIDE
				585	27 L	TOP BRK
				584	40 L	
				5606	L	F.L. N. END CONC. DRAIN - SEE 3 LINE ABOVE
98+50				5941		℄
				5906		20 R E.P.
				591		40 R
				5928	10 L	EP TOP BRK
				580	17 L	F.L. DRAIN
				604	26 L	TOP BRK
				605	40 L	
98+81				5984	18 L	F.L. OUTLET CONC. CULVERT BOX
98+93				6143	X	SEC. TAKEN PARALLEL ℄
				6131		20 R
				6120		40 R E.P.
				6145	20 L	℄ SIERRA HIGHWAY
				6151	40 L	EP
99+11.56				6196	X	℄ INT SIERRA HIGHWAY & CROWN VALLEY
				6200		SEC TAKEN ON ℄ 20 R
				6202		40 R
				6198	20 L	℄ SIERRA HIGHWAY

F.B. 3429 Pg. 110 | Job No. 5375.14 | Division No. | Notes Red | Plotted | Profile

Survey of L/W#3, Dist. #37 | Date | Date | No.

Survey by C.L.W | Notes C.L.W | Notes Chkd. | Checked | X-Sec.

Indexed | Date 27 JULY '67 | Date | Date | No.

76-L-298 CE 307 2-83

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.	
99+11 SE					
429					
BM 201-73				296.90	
				61.87	40 L & SIERRA HIGHWAY
				61.90	X SEC.
				61.84	
				61.71	20 L
				61.57	40 L EP
				296.75	
					CROWN VALLEY RD.
					20 R
					40 R EP
					& SIERRA HIGHWAY

Notes Ck'd by		Survey of W.W.#37 - Acton	F.B. 3429 Pg. 111
Map No.			
Office Work		Surveyed by Wright	
Checked		Notes V.N.D.	Date 7-28-67
Date		Indexed H. E. Ott	1965

J.N. 5575:16
Water Works #37
(Acton Area)

Location of Improvements on Soledad Cn. Rd from Crown Valley Rd South for 2400 ft.

7-28-67

Wright
Heavy
Dougherty

Note: Any Additions or Changes on this Sheet Must Be Made or Checked in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
402 LOS ANGELES COUNTY ENGINEERING BLDG.

Zaspoh ct #310 8-68

F.B. 3429 Pg. 112

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this area of this line.

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Notes Ck'd by
Office Work
Checked
Date

Survey of W/W #37
Surveyed by Wright
Notes NVD Date 7-28-47
Indexed H. E. OTT

F.B. 3420 Pg. 112

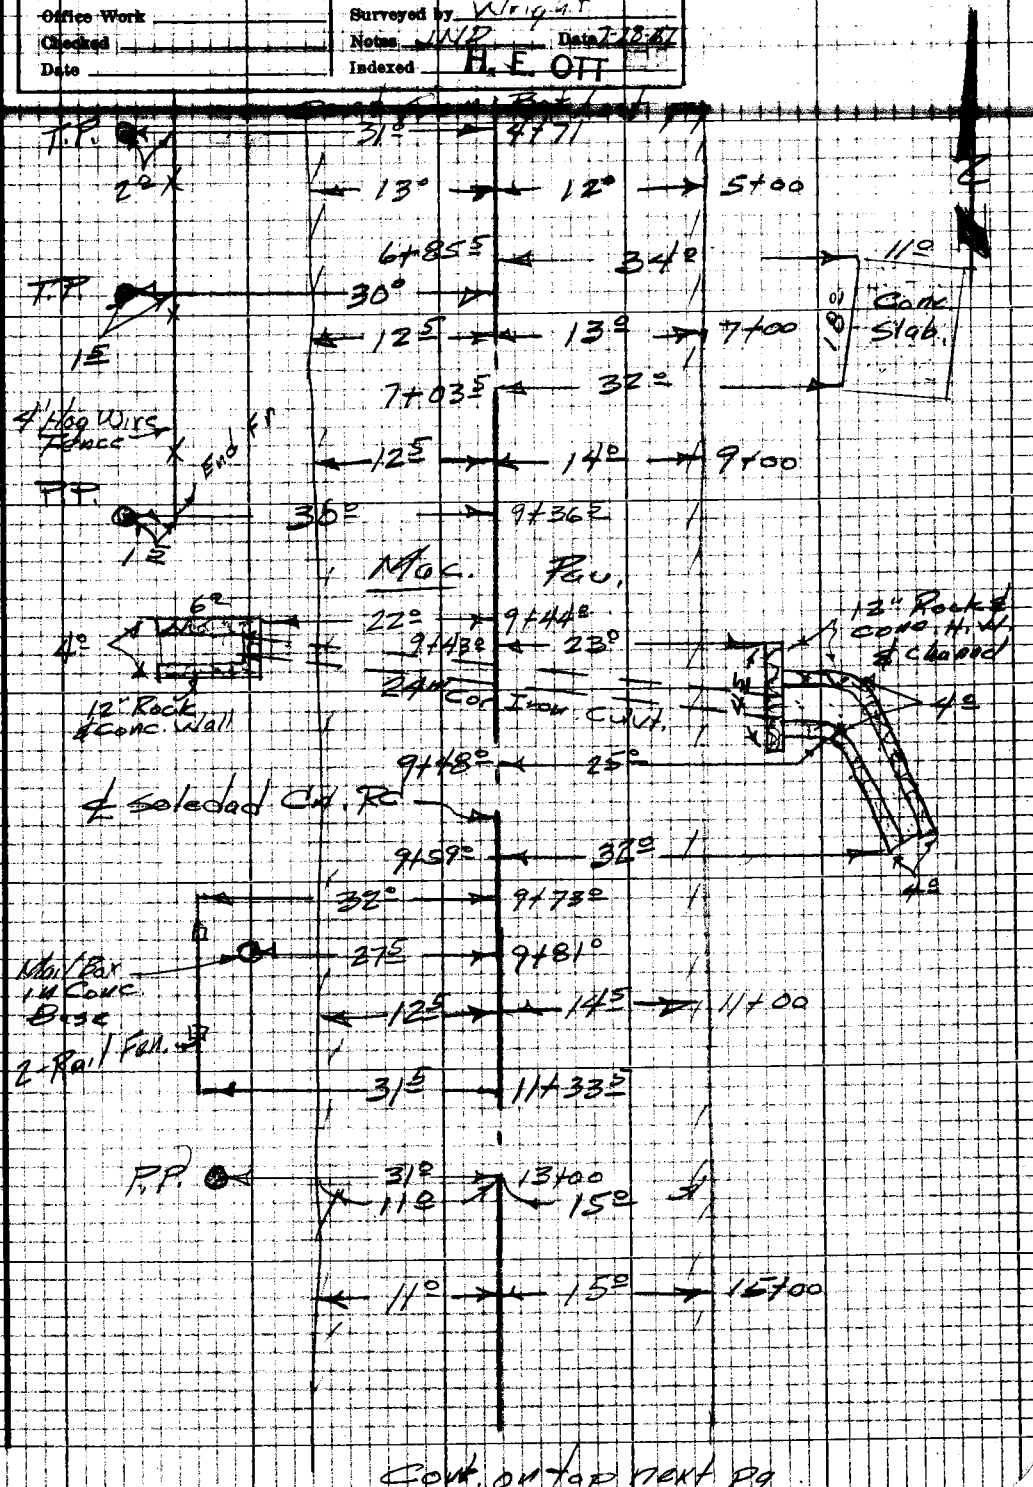

Cont. on Top Next Pg

Note: Any Additions or Changes on this Sheet Must be Made or Checked in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
402 LOS ANGELES COUNTY ENGINEERING BLDG.

(B)

Cont'd from Bot Last pg

F.B. 3429 Pg 114

N/Sec. Pav'd.

℄ Soledad Cyn. Rd.

16+17° — 14°

16+29° — 19°

16+35° — 30°

Misc. Surface Drain

P.P. — 31° — 16+34° — F.L. — 5°

16+46° — 18°

16+56° — 15°

11° — 17+00

P.P. — 31° — 17+57°

17+70°

Dirt Dr. 20°

37° — 18+63.5

17" Rock & Conc. Ret. Wall

34° — 18+68.5

5 ft. Cor. Ir. Culvert

34° — 18+73.5

37° — 18+78.5

18+88° — 44°

12" Rock & Conc. Ret. Wall

19+00 — 17° — 15°

P.P. — 40° — 19+20°

19+66° — 44°

P.P. — 40° — 22+03°

7°

10° — 16° — 22+00

23+62.95°

10° — 16°

P.I. SW 1/4 Per F.B. 3180 Pg 51

Please Return To
Los Angeles County Engineer
403 Los Angeles County Engineering Bldg.

Do not extend this side of this line.

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

F. B. 3429 PG. 115

Profile No. ____ Notes Red ____ Date ____ Plotted ____ Date ____ Job No. 5375.16 Division No. ____ Survey of W/WKS DIST. #37

X-Sec. No. ____ Notes Chkd ____ Date ____ Checked ____ Date ____ Map No. ____ Indexed H. E. OFF Date ____

LOS ANGELES COUNTY WATERWORKS

DISTRICT 37 - VICINITY - ACTON

SOLEDAD CYN. RD. FROM 4TH ST.

S'LY - 2400'±

PROFILE & X SECTION

J.N 5375.16

STATION	B.S.	H.I.	F.S.	ELEV.

PARTY:
C. L. WRIGHT
H. C. HUBBARD JR.
B. A. PRAVY
J. M. SIDWELL
J. D. GALLAGHER

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend notes this side of this line.

76-L-298 CE 307 2-63

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 116 | Job No. 5375.16 Division No. | Notes Red | Plotted | Profile
Survey of W.W. DIST #37 | Date JULY 31-67 | Date | No.
Survey by C.L.W. | Notes HCH | Notes Chkd. | Checked | X-Sec.
Indexed | Date | Date | Date | No.

STATION	B.S.	H.I.	F.S.	ELEV.	SOLEDAD CYN. ROAD
BM H-53 Fd				2697.87	BM H-53 (USGS 1406) Elev. 2697.865 FB 2631-181-201 1955 ADJ ELEV. Fd BRONZE DISK U.S.C.&G.S. STAMPED H-53 1926, AT ACTON 0.1 mi. N.E. ALONG S.P.R.R. FROM SECTION FOREMAN QUARTERS AT THE CROSSING OF A PAVED ROAD, 103' N.W. OF AND ACROSS THE TRACK FROM MILE POST 426, 94' S.W. OF S.W. COR OF A WOODEN R.R. PRICE, 57.8' N.W. OF THE OF N.W. RAIL, 30' N.E. OF THE R OF PAVED RD, 3.4' So. OF A WITNESS POST ABOUT LEVEL WITH TRACK & SET IN TOP OF A CONCRETE POST UP 6" ABOVE GROUND. ALSO F.B. 2692-246
0+18				2697.79	℄ BOT BRK
				993	4' L TOP BRK
				99.28	10.5 L E.P.
				97.29	45' L BRK
				96.90	74' L E.P.
0+30				2699.4	℄ TOP BRK
0+50				2700 2	℄
				2700.03	5' L E.P.
				2697.95	30' L E.P.
				97.24	64' L E.P.
0+80				2700.85	℄ E.P.
				2703.3	30' R
				98.70	28' L E.P. & GUT
				2699.5	47' L TOP BRK

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. X-Sec. No. Notes Red Date Date Date Plotted Job No. Survey of Map No. Division No. Indexed

F.B. 3429 PG. 117

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN. ROAD
1+00				2701.30	℄
				01.62	4'R EP
				04.1	27'R
				05.0	40 R
				2699.51	22'L EP & GUT
				27 008	45'L TOP BRK
2+00				0382	℄
				04.34	12'R EP
				051	21.5R BOT BRK
				06.4	27.5R TOP BRK
				06.8	40'R
				02.75	14'L EP
				03.4	37'L TOP BRK
3+00				06.05	℄
				0635	14'R EP
				070	22'R BOT BRK
				09.2	28'R TOP BRK
				08.8	40'R
				05.92	13'L EP
				05.6	30'L
				2704.8	40'L

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F. B. 3429 Pg. 118 | Job No. 5375.16 Division No. | Notes Red | Plotted | Profile
Survey of W.W. DIST #37 | Date JULY 31-62 | Date | No. | X-Sec.
Survey by C.A.W. | Notes ACH | Notes Chkd. | Checked | No.
Indexed | Date | Date | Date

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN ROAD
4+00				2707.30	℄
				07.60	14' R E.P.
				08.1	22' R BOT BRK
				09.7	28.5' R TOP BRK
				10.0	40' R
				06.75	12.5' L E.P.
				07.0	26' L TOP BRK
				05.4	40' L
5+00 *				2707.27	℄
				07.71	13' R E.C.
				08.2	22' R BOT BRK
				09.7	28' R TOP BRK
				09.8	40' R
				06.66	12' L E.P.
				06.9	22.5' L BRK
				05.4	40' L
6+00				06.84	℄
				07.18	13.' R E.P.
				7.3	21 'R BOT. BRK
				9.4	28. 'R TOP BRK
				9.5	40 'R

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red No. Date Plotted Date Job No. 5376.1 Division No. Survey of SOLEDAD CYN RD. Date Map No. Indexed H. E. OTT Date 8-5-61

F. B. 3429 PG. 111

SOLEDAD CYN RD.

STATION	B. S.	H. I.	F. S.	ELEV.		
6+00				2706.27	13'L E.P.	
				06.4	28'L BRK	
				05.0	40'L	
7+00				05.74		℄
				06.10		125'R EP
				06.4		19'R BOT BRK
				08.0		26'R TOP BRK
				08.2		40'R
				05.05	13'L EP	
				05.2	22'L BRK	
				03.85	32'L EDGE CONC	
8+00				04.82		℄
				05.08		13'R E.P.
				05.4		20.5'R BOT BRK
				07.9		28'R TOP BRK
				06.8		40'R
				04.32	13'L E.P.	
				04.5	21'L BRK	
				02.1	34'L	
9+00				03.74		℄
				2703.97		125'R EP

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 120 | Job No. 53751/4 | Division No. | Notes Red | Plotted | Profile
Survey of W. W. DIST #37 | Date 7-31-67 | Date | No. | X-Sec.
Survey by C.L.W. | Notes 17@H | Notes Chkd. | Checked | No.
Indexed | Date | Date | Date

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN. RD.
9+00				2704.2	21' R BOT BRK
				06.0	27' R TOP BRK
				06.0	40' R
				03.48	14' L E.P.
				3.5	22' L TOP BRK
				00.6	35' L BOT BRK
9+46				2701.77	23' R: F/LINE CULVERT
9+45±				2698.2	24' L F/LINE CULVERT
10+00				2703.02	℄
				03.28	13' R E.P.
				03.5	20' R BOT BRK
				04.9	26.5' R TOP BRK
				05.8	40' R
				02.45	13' L E.P.
				2702.5	25' L TOP BRK
				2699.4	35' L BOT BRK
				2699.0	40' L
11+00				2701.64	℄
				01.80	12.5' R E.P.
				2701.9	21' R BOT BRK

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. ____ Division No. ____
No. ____ Date ____ Date ____ Survey of W.W. DIST #37
X-Sec. Notes Chkd. ____ Checked ____ Survey by ____ Notes
No. ____ Date ____ Date ____ Map No. ____ Indexed H. E. Ott Date

F.B. 3423 Pg. 12

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN RD	
11+00				2704.6		27'R TOP BRK
				05.3		40'R
				01.08	145'L E.P. & GUT	
				2.0	34'L TOP BRK	
				2695.5	48'L BOT BRK	
12+00				2700.07		℄
				0010		12'R E.P.
				000		23'R BOT BRK
				034		29'R TOP BRK
				037		40'R
				2699.58	13'L E.P. & GUT	
				27007	32'L TOP BRK	
				2695.0	45'L BOT BRK	
TBM #10				270285		
13+00 ℄				2698.12		℄
				838		11'R E.P.
				8'		21'R BOT BRK
				2701.5		26'R TOP "
				16		40'R

76-L-298 CE 807 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 12/19 Profile
Survey of W/WKS. DIST. #37 Job No. 5375.16 Division No. Notes Red Plotted
Survey by C.L.W. Notes C.L.W. Date 1-AUG'67 Date Date No. X-Sec.
Indexed Date Notes Chkd. Checked Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN RD.	
13+00				2697.33	15 L E.P.	
				978	25 L Top Brk	
				941	36 L Bot "	
14+00				959		℄
				962.0		11 R E.P.
				962		16.5 R Bot Brk
				973		24 R Top "
				975		42 R
				952.6	15 L E.P.	
				964	32 L Top Brk	
				911	46 L Bot "	
15+00				939.1		℄
				942.5		11 R E.P.
				941		18 R Bot. Brk
				957		24 R Top "
				965		40 R
				932.4	15 L E.P.	
				947	31 L Top Brk	
				916	38 L Bot. "	
				910	43 L Top "	
				889	50 L Bot "	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. [illegible] Division No.____
No.____ X-Sec. No.____ Date____ Date____ Survey of W/ [illegible]
Notes Chkd.____ Checked____ Survey by [illegible] Notes____
Date____ Date____ Map No.____ Indexed____ Date____
L. E. Office
F. B. 3429 Pg. [illegible]

STATION	B. S.	H. I.	F. S.	ELEV.	Goldroad Cyn Rd.	
16+00				2693.15		℄
				9254		R
				923		19 E R Bot Brk
				937		26 R Top "
				946		40 R
				9158	L E.P.	
				918	25 E L Top Brk	
				900	32 L Bot "	
				892	43 L Top "	
				867	51 L Bot "	
16+37				9187		℄
				9102	15 L Brk Pvmt	
				8980	28 L Top " " & F.L.	
				8770	34 L	
16+85				9200		℄
				9232		11 R E.P.
				914		25 R
				912		40 R
17+00				9209		℄
+10				9216		℄
				9242		11 R E.P.

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F. B. 3429 PG. 122 Job No. 65151.6 Division No. Notes Red Plotted Profile
Survey of 3 Lanes Dist. #31 Date Date No. X-Sec.
Survey by C.L.W. Notes Chkd. Checked
Indexed Date 1-AUG 67 Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	SOLROAD CHN.	RD.
17+10				2691.9		20 R TOP BRK
				87.9		27 R BOT "
				88.0		40 R
				91.50	15 L E.P.	
				92.0	22 L TOP BRK	
				88.4	29 L BOT "	
				87.7	40 L TOP "	
17+55				92.46		℄
				92.72		11 R E.P.
				92.0		19 R TOP BRK.
				87.2		31 R BOT "
				87.0		40 R
17+70				92.85		11 R E.P.
				91.1		40 R N EDGE DIRT RD
					NO SHOT	R "
17+90				93.05		11 R E.P.
				91.0		40 R
18+00				93.07		℄
18+10				93.24		℄
				93.3		11 R EP
				92.7		21 R TOP BRK

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red Plotted Job No. Division No.
No. X-Sec. Notes Chkd. Checked Survey Jr. Map No. Indexed
Date Date Date Date Date

F.B. 3449 Pg. 123

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD @ YN RD	
18+10				2685.0		36'R BOT BRK
				85.0		40'R
				92.80	15'L E.P.	
				93.1	23'L TOP BRK	
				82.0	42'L	
18+71				81.4		34'R FLOW LINE CULVERT
18+80				77.4	44'L FLOW LINE CULVERT	
19+00				95.60		℄
				95.45		11'R E.P.
				95.8		25'R TOP BRK.
				84.5		45'R BOT BRK
				84.5		55'R
				95.07	15'L E.P.	
				94.8	24'L TOP BRK	
				82.0	44'L TOE FILL & TOP WALL	
19+50				97.38		℄
				97.21		11'R E.P.
				97.1		19'R TOP BRK
				87.0		37'R BOT BRK
				87.1		45'R.
19+66±				78.4	44'L TOE FILL & TOP WALL	

76-L-298 CE 307 2-63

6.97 T

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

F.B. 3429 PG. 124 | Job No. 5375/6 | Division No. | Notes Red | Plotted | Profile
Survey of W.W. DIST #37 | Date | Date | No.
Survey by CLW | Notes 424 | Notes Ckkd. | Checked | X-Sec.
Indexed | Date 8-1-67 | Date | Date | No.

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.	SOLEDAD CYN RD.
20+00				2699.27	℄
				99.19	11'R E.P.
				99.3	21'R TOP BRK
				95.4	33'R BOT BRK
				95.3	40'R
				98.76	15'L E.P.
				98.4	22'L TOP BRK
				2678.0	54'L TOE FILL
21+00				2704.65	℄
				04.49	10'R E.P.
				05.2	25'R
				06.3	40'R
				04.15	16'L E.P.
				04.6	29'L TOP BRK
				75.0	72'L TOE FILL
22+00				10.51	℄
				10.41	10'R E.P.
				10.3	20'R
				11.8	40'R
				10.00	16'L E.P.
				10.2	36'L TOP BRK

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN.	RD.
22+00				2688.3	70'L TOE FILL	
20+31 (PLUS OR)				2700.78		℄
				00.77		11'R E.P.
				01.4		26'R
				00.7		40'R
23+00				1661		℄
				16.53		10'R E.P.
				16.5		20'R
				17.7		40'R
				1634	16'L E.P.	
				16.9	42'L TOP BRK.	
23+62.95				2031		℄ ON BT. SPK. DN. 3"
				20.44		10'R E.P.
				20.3		20'R
				21.0		35'R BOT BRK.
				23.5		40'R
				2035	16'L E.P.	
				21.0	41'L TOP BRK.	
BM NO. 1224 Fd				2723.06	BM NO 1224 Elev. 2723.085 FB 3180. SOLEDAD CYN RD 0.50 MI. So OF INT. W/47TH ST. 15'± So. OF E-W ℄ SET 1/2" 55'± W. OF ℄ SOLEDAD CYN RD. Fd STD. C[illegible] BUTTON TOP MON. UP 2"	

Profile Notes Red Plotted Job No. Division No.
No. X-Sec. Date Date Survey of W. W. DIST #37
No. Notes Clkd. Checked Survey by Noted
No. Date Date Map No. Indexed Date Date

F.B. 3429 Pg. 175

F. B. 3429 Pg. 126 Job No. Division No. Notes Red Plotted Profile

Survey of Date Date No.

Survey by Notes Notes Chkd. Checked X-Sec.

Indexed Date Date Date No.

STATION	B.S.	H.I.	F.S.	ELEV.	
		BLANK			

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Notes Ck'd by	Survey of W.W. DIST # 37
Map No.	F.B. 3470 Pg. 127
Office Work	Surveyed by J.C. PIERCE
Checked	Notes J.C.P. Date
Date	Indexed H. E. OTT 8/5

J. N. 537516

W. W. DIST. # 37

TRANSIT LINE AT P.I. 88 FOR PURPOSE OF LOCATING IMPROVMENTS

SOLEDAD CYN. RD.

PARTY
PIERCE
KING
TALBOT
McDONOUGH

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

7SP3098 CE #310 8-48

F.B. 3429 Pg 128

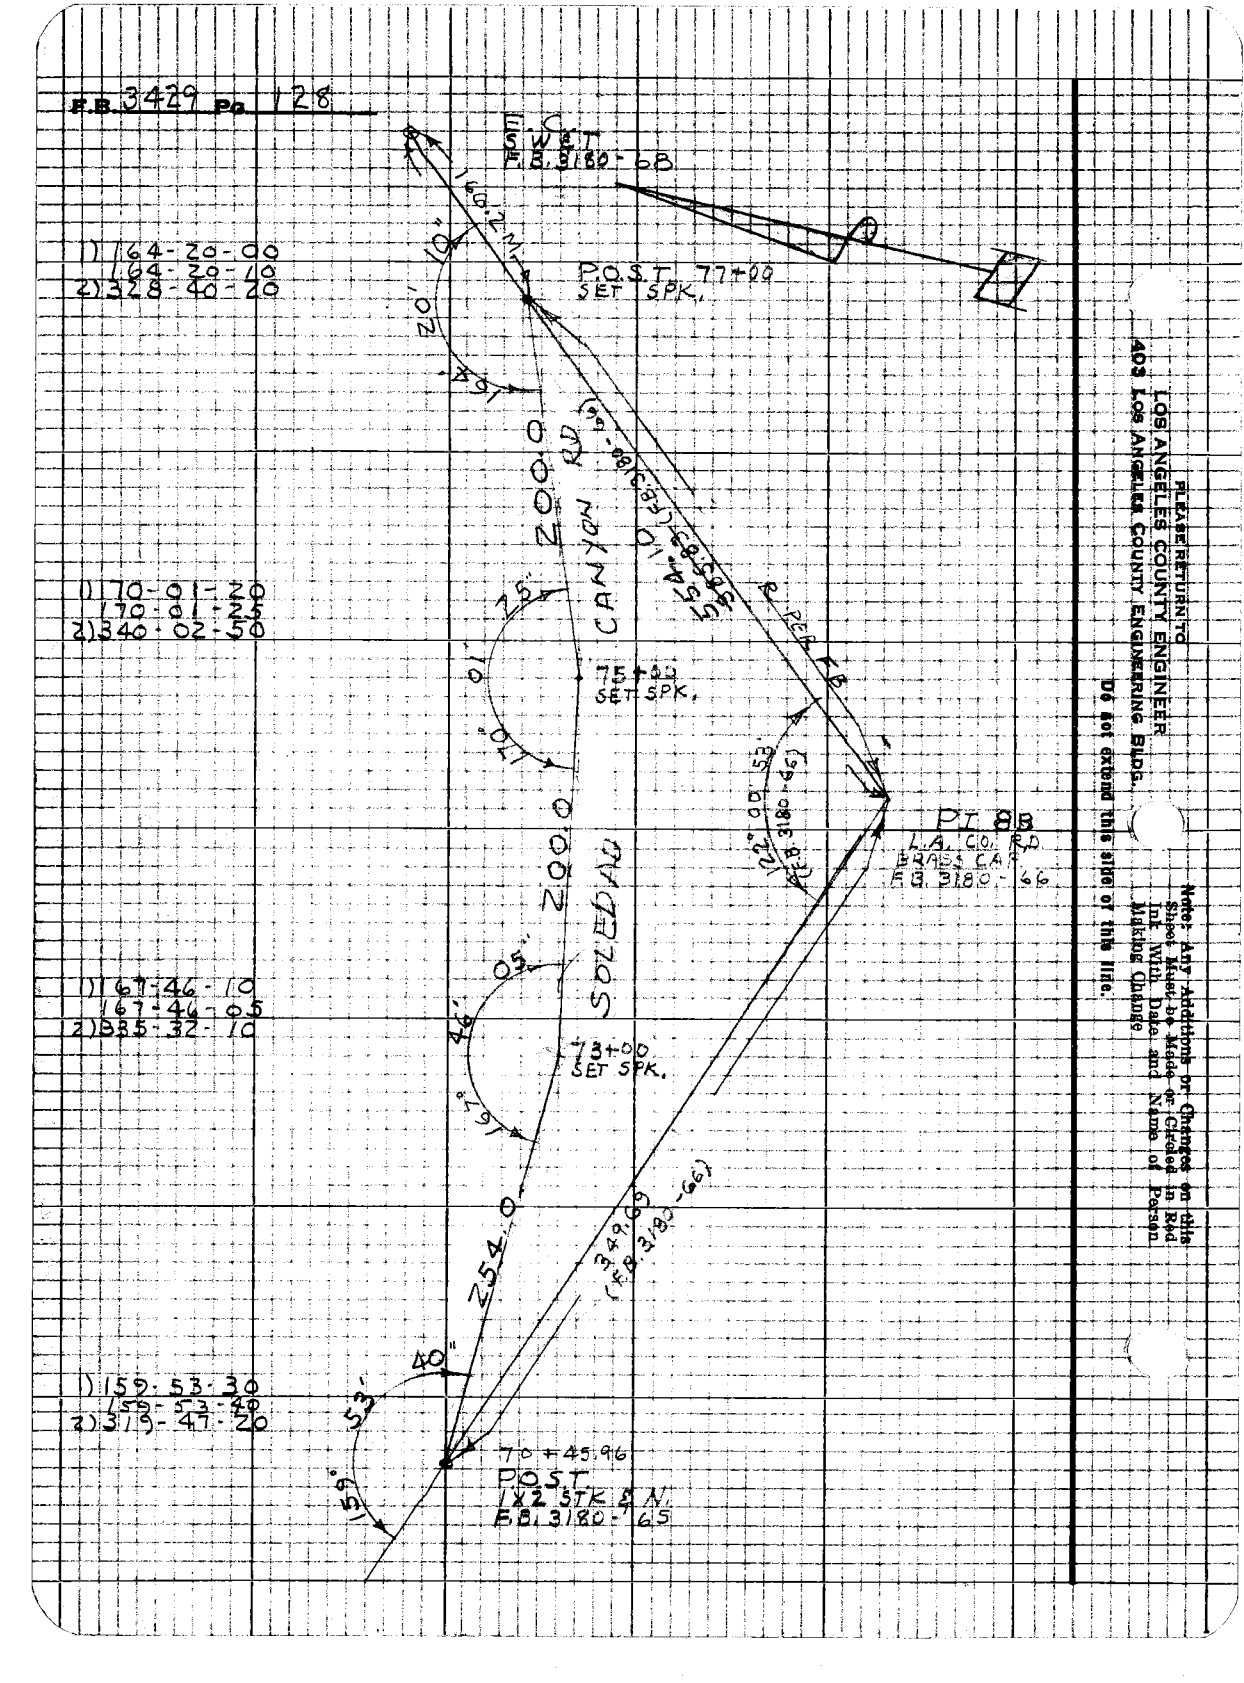

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Do not extend this side of this file.

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Notes Ck'd by	Survey of W.W. DIST # 37
Office Work	Surveyed by J.C.
Checked	Notes Date
Date	Indexed H. E. OTT

F.B. 2179 Pg. 129

J.N. 5375.16

W.W. DIST. # 37

(ACTON AREA)

LOCATION IMPROVEMENTS

SOLEDAD CYN. ROAD

FROM INT. 4TH ST.

TO SANTIAGO RD.

WRIGHT
HUBBARD
SIDWELL
GALLAGHER
PEAVY

PIERCE
KING
TALBOT
Mc DONOUGH

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Do not extend this title of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

7695035 CK #310 8-65

F.B. 3429 Pg. 130

TO BOL PG. 131



MAL PUMT

RD.

13^{P} — 12^{5} — 5+00

13^{0} — 12^{5} — 4+00

12^{5} — 13^{4} — 3+00

9^{2} — 15^{0} — 2+00

CMP

28^{5} — 1+72^{4}

1+53^{4} — 30^{5}

19^{2} — 1+62^{3}

1+49^{1} — 22^{2}

+ MAIN

+ drain

9^{5} — 1+44^{0}

1 FT. CONC. HEADWALL

4' PIPE

1 FT. CONC. Headwall

4' PIPE

4^{0} — 16^{0} — 1+34^{2}

32^{5} — 1+30^{0}

32^{5} — 1+28^{0}

1+18^{8} — 25^{5}

1+09^{4} — 35^{3}

20^{4} — 20^{4}

SOLEDAD ST

1+00^{0} — 38^{5}

TP103-138

0+30^{0}

0+00 TO N.E. COR.

Fd. 2" I.P. in BOX

AB 3180-8

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this side of this line.

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Notes Ck'd by _____ Survey of W. W. [illegible]

Map No. _____ Job No. 5235-[illegible]

Office Work _____ Surveyed by WRIGHT

Checked _____ Notes HUBBARD Date 8-2-67

Date _____ Indexed _____

F.B. 3429 Pg. 131

T.O. BOOK PG. 130

Notes: Any Additions or Changes on this Sheet, Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

7629DS (CE #210 8-66)

9+00

12E

13P

8+94E

23E

TP #5307

8+90

33E

RD

MACADAM PVM'T.

DM

9E

29E

7+90E

PP# 1434292E

7+45E

18E

TP #5305

DM

10E

19E

7+44E

TP# 5306

CWY

7+00

13E

12E

23E

13E

6+50E

4' BARB WIRE FENCE

25E

6+30

6+23.03

ED. P.M. on U

FB 3180-11

52E

6+00

EDGE PAVMT

EDGE PAVMT

COREY AVE

COLEDAD

M&L PVM'T.

5+88E

37E

TP #5304

35E

5+84E

12E

5+79E

DM

41E

5+58

PP# 1434291E ON

28E

5+54E

60E

5+41E

PP# 1434290E

5+40E

51E

29

5+22E

DM

FROM TOP PG. 130

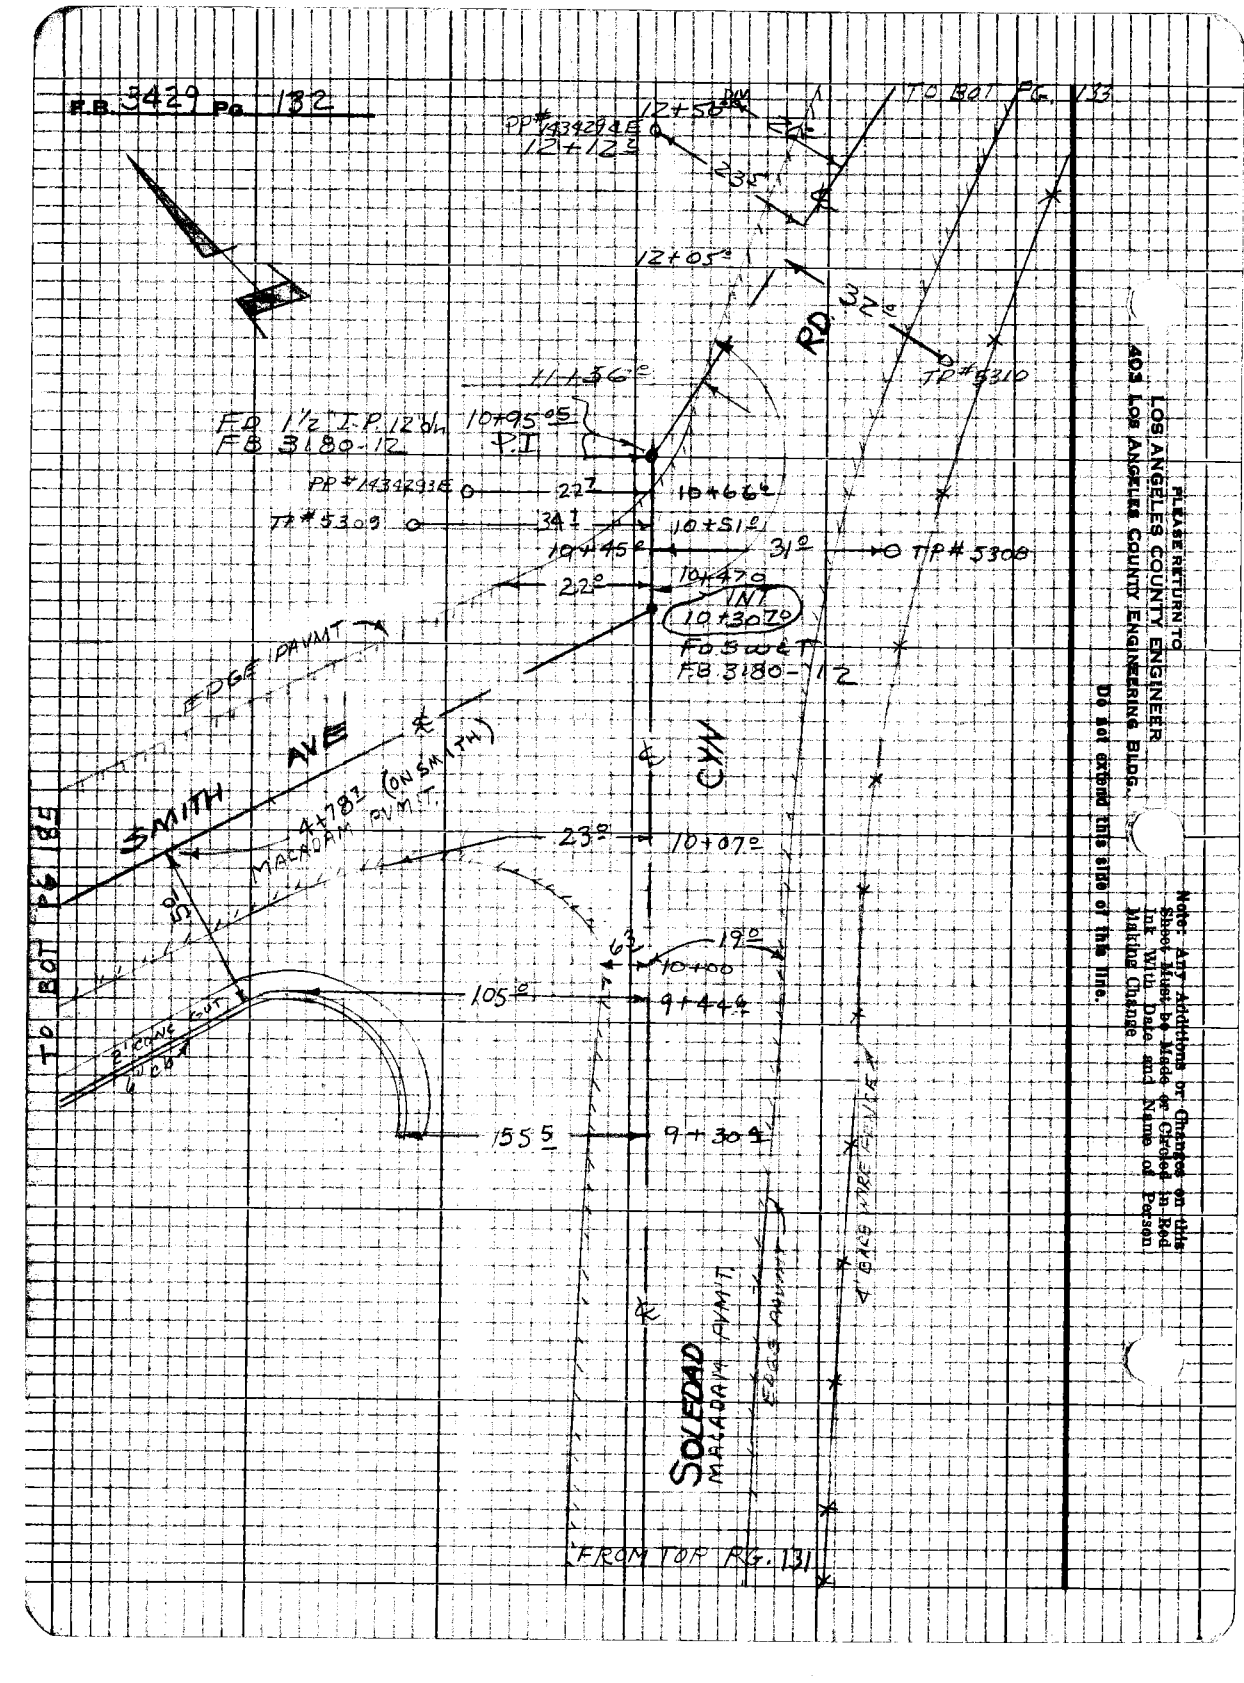
F.B. 3429 Pg. 132
TO BOT Pg. 133
TO BOT Pg. 135
PP #A434293E
12+12
12+50
BM
12+05
RD.
TP #5310
FD 1½" I.P. 12 OL
FB 3180-12
10+95.05
P.I.
PP #A434293E
22
10+66
TP #5309
34
10+51.0
10+45
31
TP #5300
22
10+47.0
INT
10+30.70
FD 5/8" CT
FB 3180-12
EDGE 1PAVMT
SMITH AVE
4+78.2 (ON SM. TH)
MACADAM PVMT
23
10+07
19
10+00
105
9+44.4
155
9+30.4
SOLEDAD
MACADAM PVMT
EDGE PVMT
FROM TOP RG. 131
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.
PLEASE RETURN TO
Do not extend this side of this line.
Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Notes Ck'd by _____
Office Work _____
Checked _____
Date _____

Survey of W.W. DIST #37
Surveyed by WRIGHT
Notes HUBBARD Date 8-2-67
Indexed H. E. OTT

F.B. 2[illegible] Pg. 132

TO BOT PG 130



3 → 23+50
12 → 14 → 23+00
27 → TP # 5318 22+63
12 → 13 → 21+00
27 → TP # 5317 20+92
13
20+83
28
20+55
20+82.58
FD. S.W. & T.
FB 3180-54

ANE
GILLESPIE
MAC. PVM'T.
MALADAY PVM'T.
SOLEDAD CYN RD

45 → 19+90
12 → 19+81
24 → TP # 5316 19+39
25 → TP # 5315 18+83
12 → 13 → 18+00
24 → TP # 5314 16+68
12 → 13 → 16+00
22 → TP # 5313 15+15
12 → 12 → 14+00
23 → TP # 5311 13+57
13+57
BM → 8 → 10 → 17 → TP # 5312
32 → 13+60

TO TOP PG. 132

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change
Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

7870-08 CE #310 5-68

F.B. 3429 Pg. 134

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line.

CONT. BOTTOM NEXT PG. 135

SOLEDAD CANYON ROAD

MALADAM AVNT.

25+58 — 45' — 16

25+00 — 26' —

25+00 — 44' —

DM. — 24° —

GUY POLE #5320 — 4° —

24+21
24+20
24+18

28' — TP 5319

9' — 16° — 24+00

TO TOP PG. 133

Notes Ck'd by	Survey of W. W. Unit #37
Office Work	Surveyed by J. C. PIERCE
Checked	Notes J. C. PIERCE Date
Date	Indexed H. E. OTT

F.B. 3429 Pg. 135

T4 BOTT PG. 136

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this title of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

7-63008 CE #310 5-68

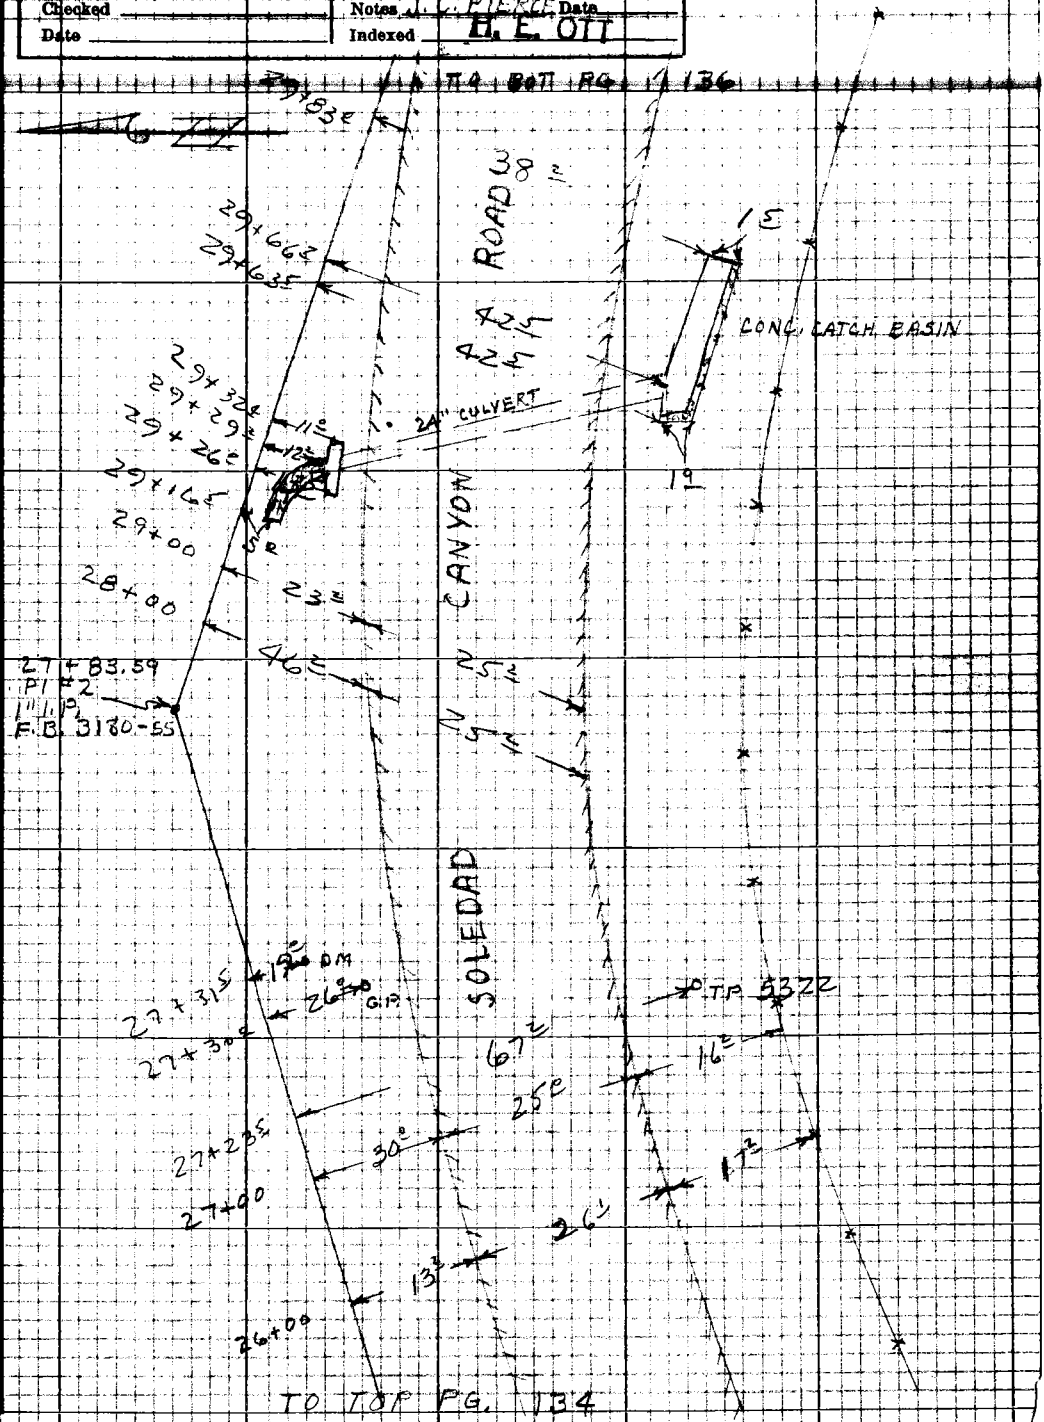

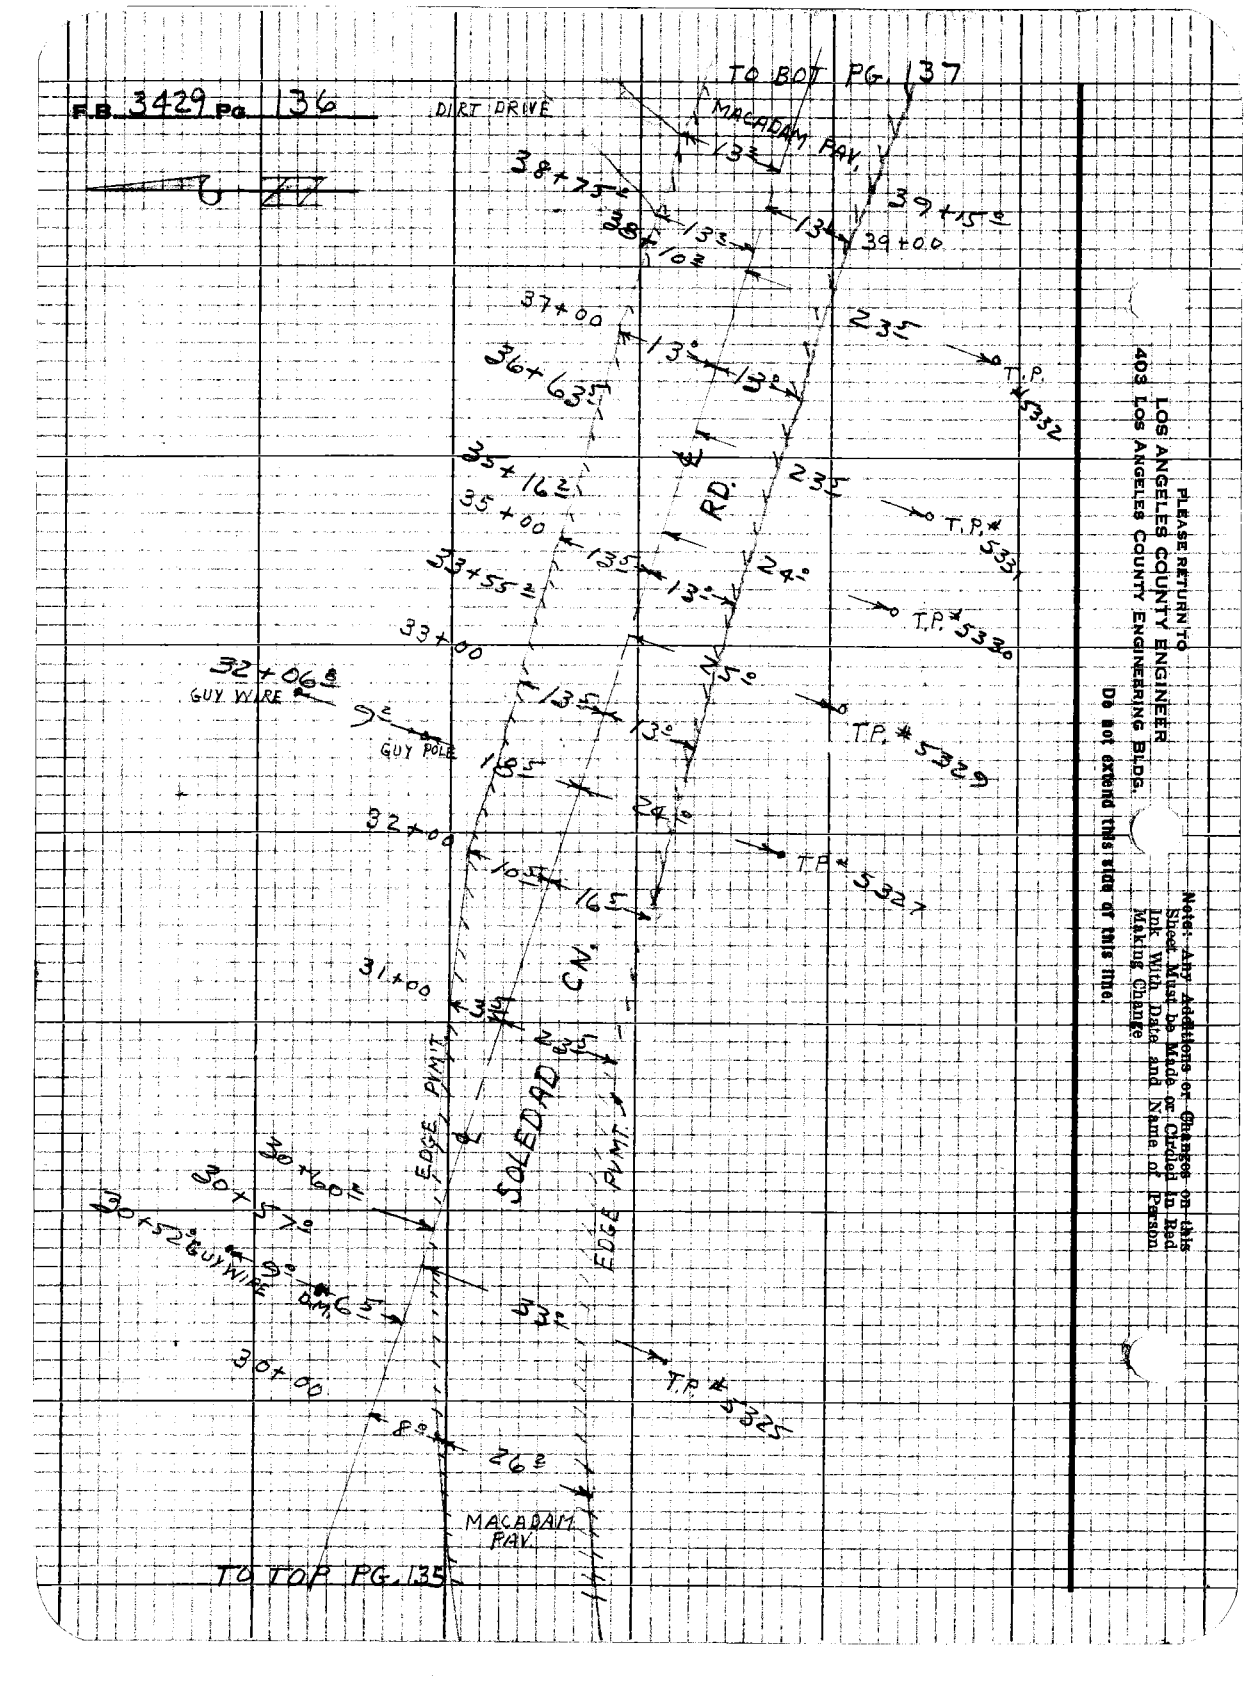
F.B. 3429 Pg. 136
TO BOT PG. 137
DIRT DRIVE
MACADAM PAV.
38+75
38+10
39+15
39+00
37+00
36+63
35+16
35+00
33+55
33+00
32+06
GUY WIRE
GUY POLE
32+00
31+00
30+00
30+52
GUY WIRE
T.P. *5332
T.P. *5331
T.P. *5330
T.P. *5329
T.P. *5327
T.P. *5325
EDGE PVMT.
SOLEDAD CN.
MACADAM PAV.
TO TOP PG. 135
PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.
Do not extend this side of this line.
Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Notes Ck'd by	Survey of W. W. DIST #27
Office Work	Surveyed by J. C. PIERCE
Checked	Notes J.C.P. Date 8-4-67
Date	Indexed H. E. OTT

F.B. 3429 Pg. 137

TO BOT. PG. 138

MAC. PVM'T.

ROAD

CANYON

SOLEDAD

75 225 21 47+00

135 135 46+00

45+12 20°

15° 115 45+00

14° 13° 43+00

GUY WIRE 9° GUY POLE 18° 22° 42+67°

T.P. # 5335

42+64°

41+12° 22° T.P. # 5334

12° 13° 41+00

35+61° 22° T.P. # 5333

TO TOP PG. 136

Note: Any Additions or Changes on this Sheet Must be Made or Checked in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
603 LOS ANGELES COUNTY ENGINEERING BLDG.

7282BA (R. 8-65) #310 5-66

F.B. 3429 Pg. 138

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this side of this map.

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Notes Ck'd by	Survey of W.W. DIST #37
Office Work	Surveyed by J.C. PIERCE
Checked	Notes J.C.P. Date 8-4-67
Date	Indexed H. E. OTT

F.B. 3499 Pg. 139

TO TOR. MAP, PG. 140

61+63 21 21 24" 43 61+44

61+42 22

61+41

61+37 23 CULVERT 40 61+37

41 61+35

40 61+33

61+30

RD. 11 14 61+00

12 13 59+00

SOLEDAD CAN 12 13 57+00

26 56+55

CONC. WALL & BASIN 28 24 56+51

56+50

56+49

56+45 24" CULVERT 26 32 56+37

CONC WALL 56+34

56+32

32 32 13 13 19 55+00

13 12 18 53+00

TO TOR PG. 138

Note: Any Additions or Changes on this Sheet Must be Made or Checked in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line.

PLEASE RETURN TO LOS ANGELES COUNTY ENGINEER 1403 LOS ANGELES COUNTY ENGINEERING BLDG.

Tracings on #310 F-66

F.B. 3429 Pg. 140

TO BOT. PG. 141

MAC. PVMT

23° 22 70+00

12& 12½ 69+00

10½ 15° 68+00

10° 16° 67+00

11° 14½ 65+00

63+57° 26°

63+53

63+51½

63+50°

63+47°

23°

24°

23°

26°

SOLEDAD CYN. RD.

4' CULVERT

63+43°

32°

63+40°

63+39½

63+37

29°

30°

29°

63+34°

32°

12½ 15° 63+00

MAC. PAV.

FROM TOP PG. 139

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this area or this line.

Note:-Any Additions or Changes on this Sheet Must be Made or Ordered in Red Ink, With Date and Name of Person Making Change.

Notes Ck'd by	Survey of W. W. DIST #37
Office Work	Surveyed by J. C. PIERCE
Checked	Notes J. C. P. Date 8-9-67
Date	Indexed

F.B. 3429 Pg. 141

TO BOOK PG. 142

MAC. PVMT.

19°

74+00

6°

SOLEDAD CYN. ROAD

25'

73+00
℄ PT IN ℄ LINE
SEE PG. 128

20'

72+00

5°

28'

71+36

18" CEM. WALL

31'

71+23

35'

CEM. DITCH WITH
ROCK & CONC. WALLS
18" HIGH

35'

46°

71+03.2

70+45.96
1X2 STK.
F.B. 3180-65

MAC. PVMT.
FROM TOP PG. 140

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Tracings of #310 8-66

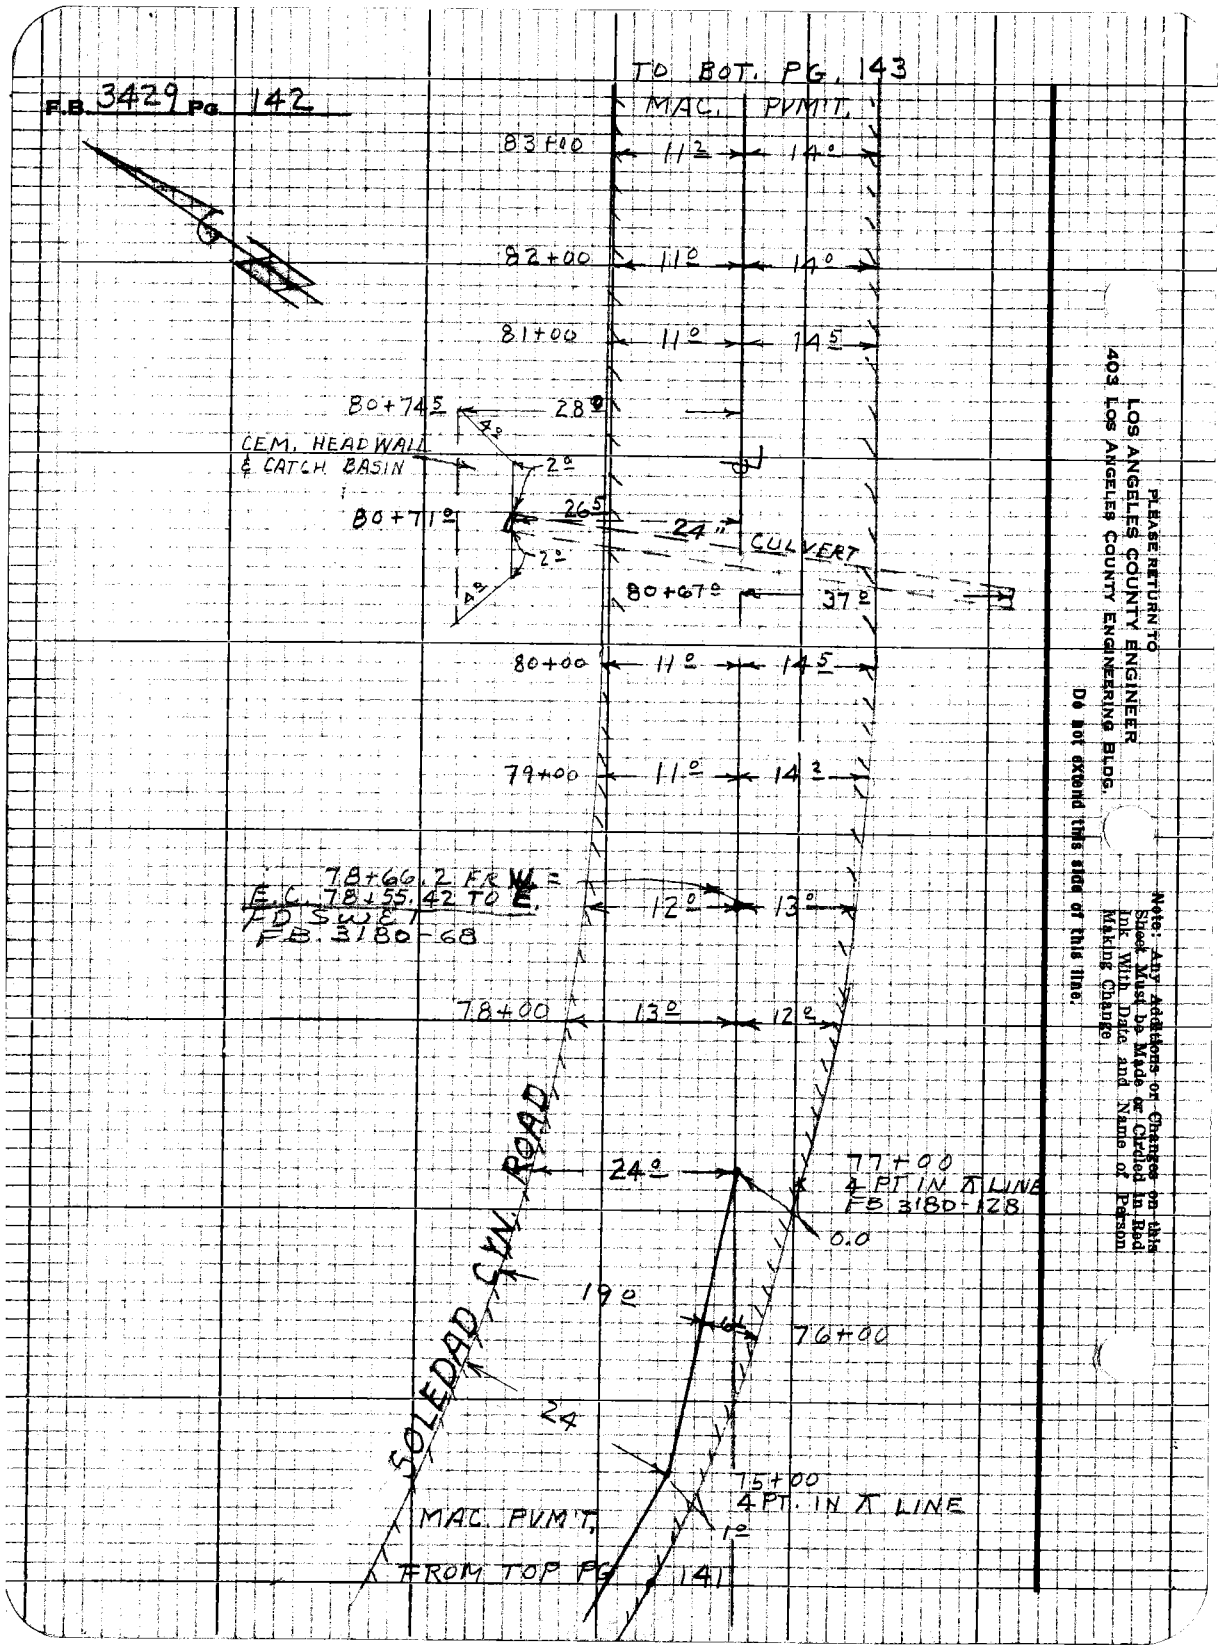
TO BOT. PG. 143
F.B. 3429 Pg. 142
MAC. PVM'T.
83+00
11%
14°
82+00
11°
14°
81+00
11°
14.5
80+74.5
28°
4%
CEM. HEADWALL & CATCH BASIN
2%
80+71°
26.5
24" CULVERT
2%
4%
80+67°
37°
80+00
11°
14.5
79+00
11.0°
14%
78+66.2 FR W =
E.C. 78+55.42 TO E.
FD SWET
FB. 3180-68
78+00
12°
13°
13°
12°
SOLEDAD CYN. ROAD
24°
77+00
4 PT IN Δ LINE
FB 3180-128
0.0
19°
76+00
24
75+00
4 PT. IN Δ LINE
MAC. PVM'T.
1°
FROM TOP PG. 141
PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.
Do not extend this side of this line.
Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by
Map No.
Office Work
Checked
Date

Survey of W.W. DIST. #37
JN 53/618 Topo 65 Sht. 8 of
Surveyed by J.C. PIERCE
Notes J.C.P. Date 8-9-67
Indexed H.E. OTT

F. B. 342.9 PG. 143

TO BOT PG. 144

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

MAC. PVM'T.

92+00 — 11 — 14 —

SOLEDAD CYN. RD.

90+00 — 12 — 13 —

88+00 — 11 — 13 —

25 → B6+37 TP

86+00 — 11 — 13 —

B5+66 — 21 — 24" CULVERT

30°R → B5+62.2

84+00 — 10 — 13

MAC. PVM'T.

TO TOP PG. 142

76F309S CE#310 1-65

TO BOT PG. 145

F. B. 3429 PG 144

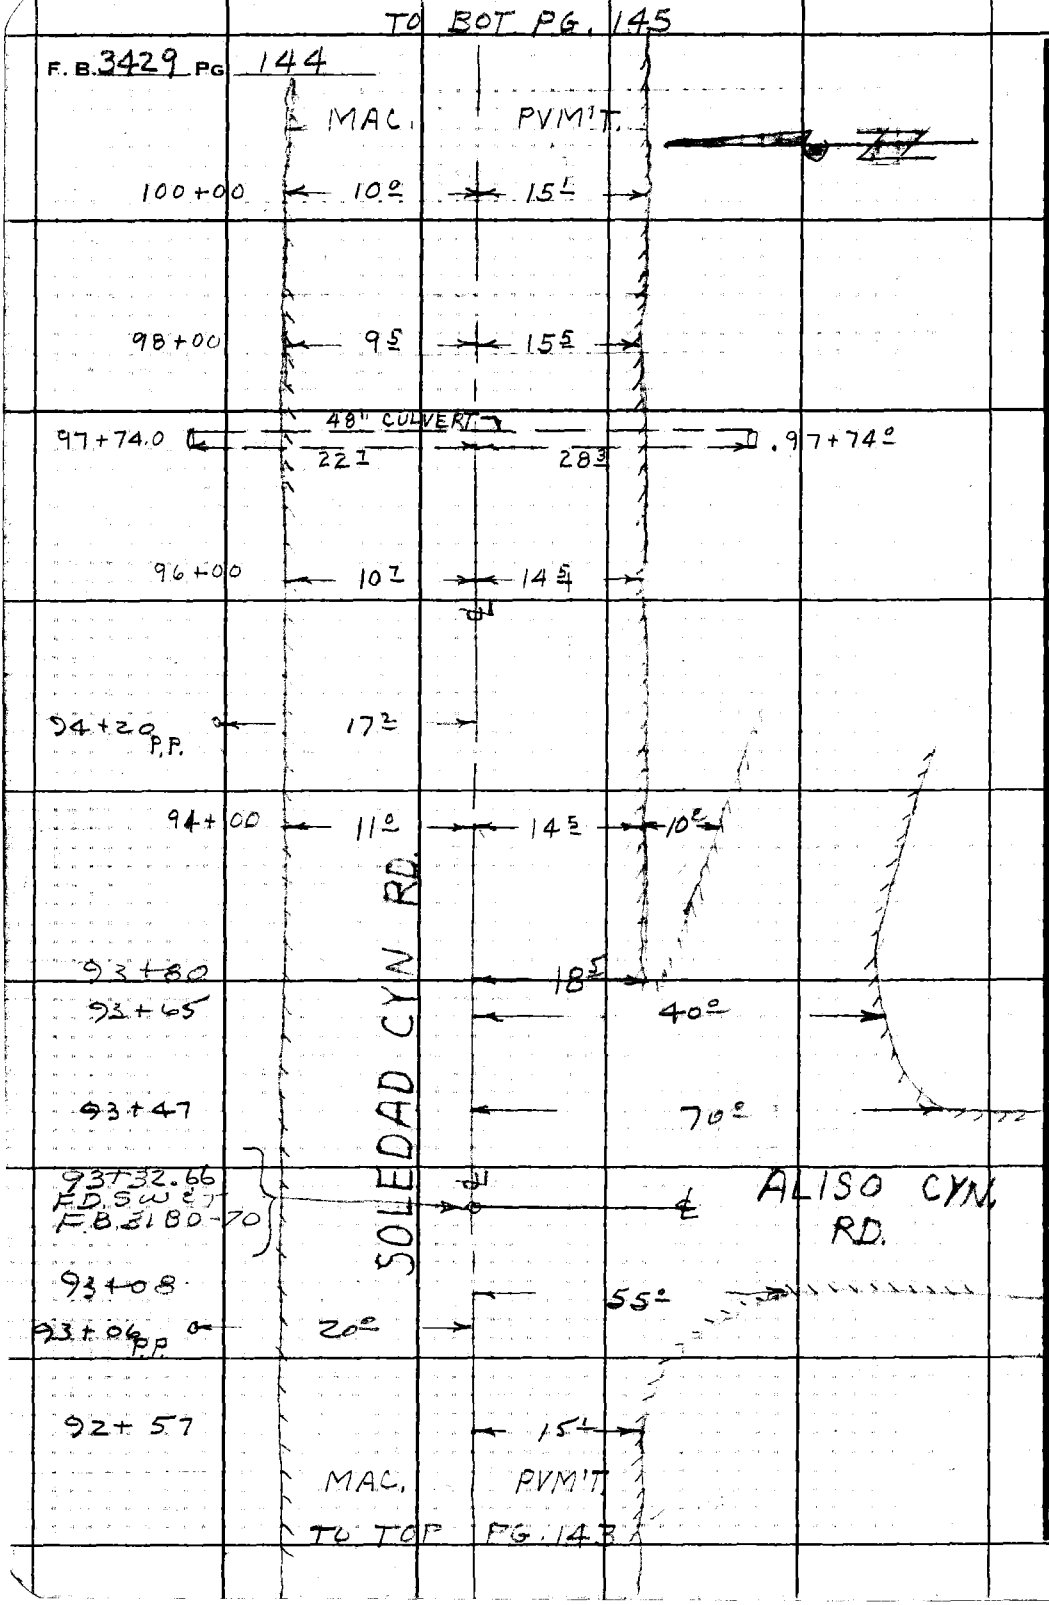

TO TOP PG. 143

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this side of this line.

Note: Any Additions or Changes on This Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Notes Ck'd by		Survey of W. W. DIST # 37	F.B. 3429 Pg. 145
Office Work		Surveyed by J. C. PIERCE	
Checked		Notes J. C. F. Date 8-10-67	
Date		Indexed H. E. OTT	

Note: Any Additions or Changes on this Sheet Must be Made or Checked in Red Ink With Date and Name of Person Making Change

Do not extend this line of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

7-8-2008 CE #310 1 of 6

40°

13°

22°

40°

111+38

111+74.36
℄ INT
SOLEDAD CYN. RD.
& SANTIAGO RD.
FD. SPK. W. & T.
F.B. 2802-12

111+30

111+10

22°

40°

110+00 — 9° — 15°

SOLEDAD CYN. RD.

108+00 — 9 5/8 — 15°

106+00 — 9 5/8 — 15 5/8

℄

104+00 — 9° — 15 5/8

102+00 — 10° MAC. — 15° PVMT.

TO TOP PG. 144

F.B. 3429 Pg. 146

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this side of this title

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Profile No. ____ Notes Red ____ Plotted ____ Job No. 5375.16 Division No. ____ F.B. 3429 Pg. 77

Date ____ Date ____ Survey of W.W. DIST # 37

X-Sec. No. ____ Notes Chkd ____ Checked ____ Survey by ____ Notes ____ Date ____

Date ____ Date ____ Map No. ____ Indexed H. E. O. Date 8/3 67

J.N. 5375.16

WATERWORKS DISTRICT # 37
PROFILE & CROSS SECTIONS
ON SOLEDAD CANYON RD.

FROM: 4TH ST. (ACTON AREA)

TO: SANTIAGO ROAD

PIERCE
KING
TALBOT
McDONOUGH

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B.S.	H.I.	F.S.	ELEV.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

76-L-298 CE 307 2-63

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK. WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 148 Job No 5375-16 Division No. Notes Red Plotted Profile
Survey of W.W. DIST # 27 Date Date No.
Survey by J.C. PIERCE Notes KING Notes Ckd. Checked X-Sec.
Indexed Date Date No.

STATION	B.S.	H.I.	F.S.	ELEV.	SOLEDAD CYN ROAD	
BMNC 1222					BMNC # 1222 ELEV. = 2691.818 F.B. 3180-16 ACTON AREA SOLEDAD CYN. RD. E. SIDE AT 332'± S. OF ℄ CORY AVE. A.C.E. MON. AT S.E. COR WELL SITE #1 50' W. OF ℄ S.P.R.R.	
P.I. 0+00.00				2695.82		℄ 2" I.P. WITH SHELL
0+23				99.4	TOP BRE	CASING CTR. DN 12'
0+23				99.30		3' R EDGE PAVMNT.
0+23				98.44		21' R PAVE
0+23				97.28		37' R PAVE.
0+23				97.17		46' R ED. PVMNT.
0+26				99.31		ED. PVMNT.
1+00				98.42		℄ PVMNT.
"				97.48		20' R ED. PVMNT.
"				97.5		33' R TOP BERM.
"				98.49	15' L TOP BRE PVMNT	
"				97.85	59' L ED. PVMNT.	
1+22				92.60		25' R. FLOW LINE 4' CULVERT
1+39				2693.65	RP & FLOW LINE CULVERT	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Platted____ Job No. 5[illegible] Division No.____
No.____ Date____ Date____ Survey of W. W. [illegible]
X-Sec. Notes Chkd.____ Checked____ Survey by____
No.____ Date____ Date____ Map No.____ Notes [illegible]
Indexed [illegible] Date____
F. B. [illegible] Pg. 1/42

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN. ROAD	
2+00				2697.61		℄
"				96.90		15'R E. Pvmt.
"				94.0		31'R. Gutter
"				95.4		40'R
"				97.91	10'L E. Pvmt.	
"				95.8	28'L Bot Bkk	
"				95.9	40'L Flat	
3+00				97.30		℄
"				96.71		13'R. E. Pvmt.
"				94.7		29'R Gutter
"				97.37	13'L E. P.	
"				95.9	23'L Bot Bkk	
"				95.8	40'L Flat.	
4+00				96.87		℄
"				96.31		13'R. E. P.
"				95.2		28'R Gutter
"				96.98	13'L E. P	
"				95.9	22'L Bot Bkk	
"				95.6	40'L Flat	
5+00*				2696.96		℄
"				2696.46		12'R E. P.

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 150 | Job No. 5375.1 Division No. | Notes Red | Plotted | Profile
Survey of W.W. DIST #37 | Date | Date | No. | X-Sec.
Survey by L.C. PIERCE Notes KING | Notes Chkd. | Checked | No.
Indexed | Date | Date | Date

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN	ROAD
5+00				2695.8		25' R GUTTER
"				97.0		40' R
"				97.09	13' L E.P.	
"				96.2	21' L BOT. BRK	
"				96.4	40' L FLAT	
5+70				97.41	48' L E.P.	
6+00				97.24		℄
"				96.84		12' R E.P.
"				96.5		22' R GUTTER
"				98.6		35' R TOP BERM
"				97.52	13' L PAVE.	
"				97.55	55' L E.P.	
6+46				97.81	12' L E.P.	
7+00				97.89		℄
"				97.49		12' R E.P.
"				96.9		19' R GUTTER
"				98.3		32' R TOP BERM
"				98.14	14' L E.P.	
"				97.8	40' L FLAT	
8+00				98.13		℄
"				2697.80		11' R E.P.

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 53[illegible] Division No. ____
No. ____ X-Sec. ____ Date ____ Date ____ Survey of W. W. DIST #[illegible]
No. ____ Notes Chkd. ____ Checked ____ Survey by [illegible] Notes ____
Date ____ Date ____ Map No. ____ Indexed [illegible] Date ____

F. B. [illegible] Pg. [illegible]

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN. RD.	
8+00				2697.6		18' R GUTTER
"				98.8		27' R TOP BANK
"				98.54	13' L E.P.	
"				98.7	40' L FLAT	
9+00				98.75		℄
"				98.14		13' R E.P.
"				98.2		18' R GUTTER
"				99.2		29' R TOP BANK
"				99.05	11' L E.P.	
"				98.93	21' L BOT BANK	
"				99.8	40' L FLAT	
10+00 *				99.37		℄
"				98.65		19' R E.P.
"				98.6		26' R GUTTER
"				99.5		35' R TOP BANK
"				99.60	6' L E.P.	
"				99.90	30' L E.P.	
10+90				99.96		℄ E.P.
10+95.05				2699.85		PI # 1
				2700.00		2.5 R E.P.
				2699.77		17' R ℄ PAVE

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 152 | Job No 5375.1 | Division No. | Notes Red | Plotted | Profile
Survey of W.W. DIST #37 | Date | Date | No.
Survey by W.C. PIERCE Notes KING | Notes Chkd. | Checked | X-Sec.
Indexed | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN RD	
10+95.25				2699.27		30' R E.P.
				99.2		37' R Gutter
				2700.5		47' R Top Berm
				00.0	6' L Bot Berm	
				01.8	18' L Top "	
11+35				00.36	℄	E.P.
12+00				00.77	℄	
				00.07		19' R E.P
				00.0		26' R Gutter
				02.2		33' R Top Berm
				00.88	6' L E.P	
				01.2	15' L Bot Brk	
				02.7	24' L Top Berm	
13+00				01.15	℄	
				00.69		14' R E.P.
				02.5		28' R Top Berm
				01.47	10' L E.P	
				03.9	25' L Top Berm	
14+00				01.80	℄	
				01.32		13' R E.P.
				2701.4		17' R Gutter

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

SOLEDAD CYN RD

STATION	B.S.	H.I.	F.S.	ELEV.			
14+00				2704.1			26' R TOP BERM
"				02.00	12' L	E.P.	
"				04.3	20' L	TOP BERM	
"				04.7	40' L	FLAT	
15+00 *				02.29			℄
				01.96			12' R E.P.
				01.9			16' R BOT BERM
				05.7			26' R BEGIN ℄
				02.37	12' L	E.P.	
				02.2	17' L	BOT BKK	
				05.5	26' L	TOP BKK	
				05.6	40' L	FLAT	
16+00				02.98			℄
				02.64			12' R E.P.
				03.0			17' R BOT CUT
				03.18	12' L	E.P.	
				03.2	14' L	BOT BKK	
				07.2	22' L	TOP BKK	
				07.1	40' L	FLAT	
17 + 00				03.63			℄
				2703.26			13' R E.P

Profile Notes Red. ____ Plotted ____ Job No. 5516 Division No. ____
No. ____ Date ____ Date ____ Survey of W.W. DIST #37
X-Sec. Notes Chkd. ____ Checked ____ Survey by ____ Notes ____ Date ____
No. ____ Date ____ Date ____ Map No. ____ Indexed D.E. Date ____

F.B. 3429 Pg. 153

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 154 Job No. 5375-K Division No. Notes Red Plotted Profile
Survey of W. W. DIST # 37 Date Date No. X-Sec.
Survey by FIERCE Notes KING Notes Chkd. Checked No.
Indexed Date Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN RD	
17+00				270.33		15' R GUTTER
"				03.90	12' L E.P.	
"				03.9	15' L BOT BKE	
"				07.7	23' L TOP "	
18+00				04.31		℄
"				03.84		13' R E.P
"				03.8		15' R BOT CUT
"				04.55	12' L E.P	
"				04.6	17' L BOT BKE	
"				07.8	25' L TOP "	
"				05.7	40' L	
19+00				04.91		℄
				04.45		12' R E.P
				05.9		25' R END CUT
				05.24	12' L E.P	
				05.4	21' L TOP BERM	
				03.0	29' L BOT FILL	
19+80				05.7	22' TOP BERM	
				01.7	35' BOT FILL	
				02.3	49' " "	
				270.60	55' TOP FILL ℄ E.P.	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. [illegible] Division No.____
No.____ Date____ Date____ Survey of [illegible] F.B. 3469 Pg. 155
X-Sec. Notes Chkd.____ Checked____ Survey by [illegible] Notes [illegible]
No.____ Date____ Date____ Map No.____ Indexed H. E. Office

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN. RD.	
20+00				2705 43		℄
				04 87		12' R E.P
				05.6		25' R Top
				05.73	13' L	FUNNT
				04.82	69' L	E.P
21+00				05.85		℄
				05 42		13' R E.P.
				06.3		23' R Bo
				06.11	13' L E.P	
				06.2	20' L TOP FILL	
22+00				06 53		℄
				06.03		13' R E.P.
				06.8		22' R Bot
				06.84	13' L E.P	
				07.1	19' L TOP FILL	
23+00				07 54		℄
				06 98		13' R E.P
				07 7		21' R Bot
				07 97	11' L E.P.	
				08.2	19' L TOP FILL	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 156 | Job No. 5375.1 | Division No. | Notes Red. | Plotted | Profile
Survey of W. W. DIST # 37 | Date | Date | No.
Survey by PIERCE | Notes KING | Notes Chkd. | Checked | X-Sec.
Indexed | Date | Date | Date | No.

STATION	B.S.	H.I.	F.S.	ELEV.	SOLEDAD CYN RD	
24+00*				2709 21		℄
				08 40		16' R E.P
				090		20' R BOT CUT
				0951	10'L E.P	
				09 2	14'L TOP FILL	
25+00				7/1 85		℄ E.P.
				11.41		12' R ℄ P.AVMNT
				10.67		25' R E.P.
				11.3		29' R BOT CUT
				11.9	8'L TOP FILL	
25+63				14.4		℄ TOP FILL
26+00				13 43		℄ END FILL BEGIN CUT
				150		6' R TOP BRK
				1532		13' R EP
				1487		26' R ℄ PAVT
				1415		39' R EP
				14.2		42' R GUTTER
BMNC #1227				2719 81	B.M.N.C. # 1227 ELEV. 2719.838 F.B. 3180-24	
					SOLEDAD CYN. RD. (W. SIDE) 131' ± S;WLY. OF P.I. #2	
					ON SEMI-TAN A STD. BUTTON TOP C.E. MON. UP 2"	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Noted Plotted Job No. 5326 Division No. 4
No. Date Date Date Survey of W.W. DIST. # 37
No. Date Date Map No. Indexed H.E. Date
F.B. 3429 PG. 157

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN. RD.	
BMNC #1227				2719.83	B.M.N.C. 1227 ELEV. = 2719.830 SEE PRECEDING PG.	F.B. 3180-24
27+00				19.8		25'R Bot C
				19.77		28'R E.P.
				19.14		41'R & PAVMNT
				18.35		54' R E.P.
				18.4		56' R Bot Cu
28+00				23.7		42'R Bot C
				23.42		44'R E.P.
				23.00		56'R & Pum
				22.30		68'R E.P.
				22.0		71'R Bot C
29+00				28.0		20'R END C
				27.66		23'R E.P.
7.32*				27.25		35'R & PVMNT
				26.61		48'R E.P.
				26.6		49'R Bot C
29+28				24.03		10'R Bot 24" C.G.S.T.
29+56				27.25.58		44'R Bot 24"

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F. B. 3429 Pg. 158 | Job No. 5256 | Division No. 11 | Notes Red | Date | Plotted | Date | Profile No. | X-Sec. No.
Survey of W.W. DIST. # 37 | Date | Notes Chkd. | Date | Checked | Date | Indexed | Date
Survey by J. PIERCE & NOTES K.K.

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN. RD.
30+00				2731.78	8'R BOT CUT & E.P.
				31.28	20'R & PAVE
				30.63	33'R E.P.
				30.6	36'R BOT CUT
30+37				33.5	& BOT CUT
30+62				34.32	& E.P.
31+00				35.78	&
				35.49	9'R & PVMNT
				34.90	22'R E.P.
				34.9	26'R GUTTER
				35.87	3'L E.P.
				36.1	6'L BOT CUT
32+00				39.12	&
				38.45	16'R E.P.
				38.4	20'R BOT CUT
				39.28	10'L E.P.
				40.6	17'L TOP BERM END CUT
				40.6	40'L FLAT
33+00				41.80	&
				41.36	13'R E.P.
				2741.3	17'R B.T CUT

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 5215/6 Division No. 4
No. X-Sec Date ____ Date ____ Survey of W.W. DIST #37
No. ____ Date ____ Date ____ Map No. ____ Indexed H.E. OTT Date ____
F.B. 3429 PG. 159

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN. RD.	
33+00				2742.03	13'L E.P.	
				42.7	24'L TOP BERM	
				42.7	40'L	
34+00*				44.00		℄
				43.59		13'R E.P.
				43.5		16'R BOT CUT
				44.13	14'L E.P.	
				45.0	25'L TOP BERM	
				45.0	40'L	
35+00				46.08		℄
				45.73		12'R E.P.
				45.8		17'R BOT CUT
				46.39	13'L E.P.	
				47.6	25'L TOP BERM	
				47.7	40'L FLAT	
36+00				48.20		℄
				47.72		12'R E.P.
				48.0		17'R BOT CUT
				48.44	12'L E.P.	
				49.6	22'L TOP BERM	
				27.496	40'L FLAT	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 160 | Job No. 5225-16 Division No. // Notes Red Date Plotted Profile
Survey of W.W. DIST #37 Date No. X-Sec.
Survey by J. PIERCE Notes K.K. Notes Chkd. Date Checked Date No.
Indexed Date Date

STATION	B.S.	H.I.	F.S.	ELEV.	SOLEDAD CYN. RD.
37+00				2750.15	℄
				49.64	12' R E.P.
				49 8	16' R BOT CUT
				50.55	13' L E.P.
				51 3	22' L TOP BERM
				51 3	40' L
38+00 *				52.12	℄
				51 60	13' R E.P.
				51 8	19' R GUTTER
				52 43	13' L E.P.
				53 3	23' L TOP BERM
				53 4	40'
39+00				54 14	℄
				53 63	13' R E.P.
				53 4	18' R BOT CUT
				54 42	13' L E.P.
				54 6	40' L
40+00				56 02	℄
				55 43	13' R E.P.
				55 2	19' R BOT CUT
				2756 30	13' L E.P.

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 5327.16 Division No. 11
No. ____ Date ____ Date ____ Survey of W.W. DIST. #37
No. ____ Date ____ Date ____ Map No. ____ Indexed H. E. Otte

F.B. 3429 Pg. 161

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN. RD.
40+00				2756.4	40'L FLAT
41+00				57.73	℄
				57.31	13'R E.P.
				56.9	17'R Bot C.
				58.05	13'L E.P.
				58.5	40'L
42+00				59.51	℄
				59.01	13'R E.P.
				58.7	21'R Gutter
				58.88	13'L E.P.
				60.1	40'L
43+00				61.27	℄
				60.90	13'R E.P.
				60.2	19'R Bot
				61.50	13'L E.P.
				61.6	40'L
44+00				63.03	℄
				62.56	11'R E.P.
				62.1	19'R Bot C.
				62.21	14'L E.P.
				2763.3	40'L

76-L-295 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 PG. 162 Job No. 5325:16 Division No. 11 Notes Red Date Plotted Profile
Survey of W.W. DIST # 37 Date No. X-Sec.
Survey by J. PIERCE Notes K.K. Notes Chkd. Checked No.
Indexed Date Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN. RD.	
45+00				2764.70		℄
				64.06		11'R E.P.
				63.7		17'R Bot Cut
				65.18	15'L E.P.	
				65.4	40'L	
46+00				66.21		℄
				65.31		13'R E.P.
				65.3		16'R Bot Cut
				66.68	12'L E.P.	
				66.6	40'L	
BMNC #1228				2766.33 ~~34~~	B.M.N.C.# 1228 ELEV = 2766.330 F.B. 3180-25	
					SOLEDAD CANYON ROAD (S. SIDE) @ E. LINE	
					SEC. 36 C.E. MON. FLUSH 35'± S. OF ℄ RD.	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red Plotted Job No. 5337-16 Division No. 11
No. X-Sec. Date Date Survey of W.W. DIST #37
No. Date Date Map No. Indexed H E Date

F.B. 3429 Pg. 163

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN RD.
47+00				2768 22	℄
				67 02	22'R E.P.
				66 4	27'R Bot C
				68 9	41'R Top
				68 37	4'L E.P.
				68 5	17'L TOP BERM
				67 6	40'L
47+35				68 96	℄ E.P.
48 00				69 9	℄ TOP BERM
				69 96	10'R E.P.
				69 32	23'R ℄ DUM
				68 53	36'R E.P.
				67 82	42'R GUTTER
				70 2	60'R TOP C
				70 0	14'L FLAT
48+83				71.0	℄ TOP BERM
49+00				71. 2	℄
				71 22	5'R E.P.
				70 63	18'R CTR PU
				69 65	31'R E.P.
				27 69 1	36'R GUTTER

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 164 | Job No. 3375:6 Division No. 11 | Notes Red ____ Date ____ | Plotted ____ Date ____ | Profile No. ____
Survey of W. W. DIST #37 | Notes Chkd ____ Date ____ | Checked ____ Date ____ | X-Sec. No. ____
Survey by J. PIERCE Notes K.K. | Indexed ____ Date ____

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN. RD.	
49+00				2771.0		55' R TOP BRK
				70.2	6' L BOT BRK	
				70.2	25' L FLAT	
50+00				72.38		℄
				70.88		19' R E.P.
				70.5		25' R GUTTER
				72.2		45' R TOP BRK
				72.80	7' L E.P.	
				72.8	15' L TOP BERM	
				71.0	17' L BOT BRK	
				71.0	30' L FLAT	
51+00*				73.83		℄
				73.00		14' R E.P.
				72.0		28' R GUTTER BEGIN FILL
				73.0		36' R TOP BRK
				74.17	12' L E.P.	
				74.0	20' L TOP BERM	
				71.8	24' L BOT BRK	
				72.0	40' L	
52+00				75.54		℄
				2774.92		13' R E.P.

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK. WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Rod Plotted Job No 5375.16 Division No. 11
No. X-Sec. Date Date Survey of W.W. DIST #37
No. Notes Cked. Checked Survey Notes Date
No. Date Date Map No. Indexed Date

F. B. 3429 Pg. 165

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN. RD	
52+00				2675.0		22'R TOP FILL
				75 77	15'L E.P.	
				75 2	22'L TOP FILL	
				73 0	25'L BOT "	
				73 4	40'L	
53+00				77 14	℄	
				76 52		12'R E.P.
				76 6		21'R TOP FILL
				77 34	14'L E.P.	
				76 8	22'L TOP FILL	
				74 8	26'L BOT FILL	
				750	40'L	
54+00				78 91	℄	
				78 36		13'R E.P.
				78 4		20'R TOP FILL
				79 10	13'L E.P.	
				76 5	30'L BOT FILL	
				76 8	40'L	
55+00				80 48	℄	
				79 87		13'R E.P.
				2780 3		20'R TOP FILL

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 166 Job No. 5225.16 Division No. 11 Notes Red Date Plotted Date No. Profile
Survey of W.W. DIST. # 37 Date Date No. X-Sec.
Survey by J. PIERCE Notes K.K. Notes Chkd. Checked
Indexed Date Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN. RD.
55+00				2780.67	14' L E.P.
				78.9	29' L Bot Brk
				79.5	40' L
56+00				81.89	℄
				1.44	13' R E.P.
				1.7	22' R Top Fill
				2.00	12.5' LEFT E.P.
				0.7	28' Bot Cut
56+				73.80	1' R 24" Culvert
56+ (56+50)			—	78.33	1' L 24" Culvert
57+00				83.43	℄
				3.04	13' R E.P.
				3.1	22' R Top Fill
				3.29	12.5' L E.P.
				3.2	22' L Bot Cut
58+00				5.26	℄
				5.18	13.5' R E.P.
				5.3	30' R Flat
				84.89	12.5' L E.P.
				2784.0	26' L Bot Cut

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red Plotted Job No. 5375 Division No. 11 F.B. 3449 Pg. 161
No. X-Sec. Date Date Survey of W.W. DIST #37
No. Date Notes Chkd. Date Checked Date Survey by A. PEREZ Notes by A. PEREZ Date 8-8-67
Date Map No. Indexed L.E. Opp. to

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN RD.	
59+00				2787.07		℄
				87.10		135' R E.P.
				88.0		30' R FLOW
				86.61	12' L E.P.	
				86.1	25' L Bot Cut	
60+00				88.58		℄
				88.64		135' R E.P.
				88.3		26' R Top Fill
				88.25	11.5' L E.P.	
				87.5	25' L Bot Cut	
61+00*				90.07		℄
				90.17		14' R E.P.
				90.4		27' R Top Fill
				89.71	12' L E.P.	
				89.1	25' L Bot Cut	
61+		Interchange 2 Lt & Rt		86.26	'L 24" Culvert	
61+				89.79		'R 24" Culvert
62+00				91.81		
				91.88		15' R E.P.
				91.2		28' R Top Fill
				2791.44	N 5° L E.P.	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 168 | Job No. 5335.14 Division No. 11 Notes Red Date Plotted Date Profile No. X-Sec. No.
Survey of W. W. DIST #37 Date Notes Cked Date Checked Date
Survey by J. PIERCE Notes K.K. Date
Indexed Date

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN. RD.
62+00				3790.1	21' L Bot Cut
63+00				94.00	℄
				94 12	15' R E.P.
				94 2	27' R Top Fill
				93 51	11' L E.P.
				92 8	26' L Bot Cut
63+				91 74	1' L 24" Culvert
63+				86 50	1' R 24" Culvert
64+00				96 26	℄
				96.41	15' R E.P.
				959	24' R Top Fill
				95 87	10 5' L E.P.
				96 2	18' L Top Fill
				94 0	24' L Bot Ditch
65+00 *				9886	℄
				9900	14 5/4 R E.P.
				986	27' R Top Fill
				9851	10' L E.P.
				97 9	16' L Begin Cut
66+00				2801 30	℄
				01 50	16' R E.P.

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted. Job No. 5335-16 Division No. 11
No. X-Sec. Date Date Survey of W.W. DIST # 37
No. Notes Ckkd. Checked Surveyed by H.E. Notes by H.E. Date 8-5-63
Date Date Map No. Indexed H. E. Date

F. B. 3769 Pg. 169

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN. RD.	
66+00				2801 6		33' R TOP FILL
				01 05	9' L E.P.	
				2800 9	13' L BOT CUT	
67+00				03 70		
				03 96		16' R E.P.
				03 7		36' R TOP FILL
				03 31	9½' L E.P.	
				03 0	14' L BOT CUT	
68+00				06 08		
				06 35		15' R E.P.
				06 4		20' R TOP FILL
				05 56	10' L E.P.	
				05 9	32' L BOT CUT	
LOVE				08 66		
				09 40		12½' R E.P.
				09 4		16' R TOP FILL
				07 86	12' L E.P.	
				08 6	22' L BOT CUT	
70+00				11 97		
				12 02		2' R E.P.
				2812 4		8' R TOP FILL

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 120 Job No. 5375.16 Division No. 11 Notes Red Plotted Profile
Survey of W.W. DIST #37 Date Date No. X-Sec.
Survey by J. PIERCE Notes K.K. Notes Chkd. Checked No.
Indexed Date Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN. RD.	
70+00				2811.09	10'L & PAVE	
				2809.90	23'L E.P.	
				2810.7	33'L TOP FILL END CUT	
71+00		3.44		14.44		℄ E.P.
				15.0		8'R TOP FILL
				14.58	12'L & PAVE	
				12.31	25'L E.P.	
				13.0	30'L TOP FILL	
71+30				13.1	25'L BEGIN CUT	
BM NC #1230				2817.82 ~~80~~	B.M.N.C. #1230 ELEV. = 2817.820 F.B. 3180-26 SOLEDAD CYN. ROAD (S. SIDE) 562' W. & 17' N. OF PI #8A A C.E. BUTTON TOP MON. FLUSH	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 5375 Division No. 11
No. ____ Date ____ Date ____ Survey of W.W. Dist. #37
No. ____ Date ____ Date ____ Map No. ____ Indexed W. E. Opie
X Sec. Notes Checked ____ Date ____ Date ____ Map No. ____ Indexed ____

F. B. 3429 Pg. 77

SOLEDAD CYN. RD

STATION	B. S.	H. I.	F. S.	ELEV.		
BM NO# 1230				2817.82	B.M.N.C. # 1230 ELEV. = 2817.820 F.B. 3180-2. SEE DESCRIPTION ON PRECEDING PG.	
71+61				16 4		7'R Begin Cut
72+00				16 44		℄
				16 72		5'R E.P.
				16 9		8'R Bot Cut
				15 84	8'L & Pave	
				14 70	20'L E.P.	
				14 7	23'L Bot Cut	
73+00				17 9		℄ E.P.
				17 9		2'R Bot Cut
				17 80	15'L E.P.	
				16 88	13'L & Pave	
				15 84	25' L E.P.	
				15 8	28'L Bot Cut	
74+00				17 43		℄
				17 77		6'R E.P.
				17 7		10'R Bot Cut
				16 97	6'L & Pave	
				15 90	19'L E.P.	
				28156	24'L Bot Cut	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 172 | Job No 5375.16 Division No. 11 Notes Red Date Plotted Date Profile No.
Survey of W.W. Dist # 37 Date X-Sec. No.
Survey by J. Pierce Notes K.E. Notes Chkd. Checked
Indexed Date Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN. RD.	
75+00				2816.75		℄
				16.77		1'R E.P.
				16.9		5'R Bot Cut
				15.99	10'L ℄ Pave	
				14.85	24'L E.P.	
				14.6	28'L Bot Cut	
76+00				14.68		℄
				14.96		6'R E.P.
				15.0		10'R Bot Cut
				14.28	6'L ℄ Pave	
				13.20	19'L E.P.	
				12.9	24'L Bot Cut	
77+00				12.79		℄ E.P.
				12.8		5'R End Cut
				12.05	11.5'L ℄ Pave	
				10.94	24'L E.P.	
				10.7	29'L Bot Cut	
78+00				09.34		℄
				10.04		12'R E.P.
				10.5		22'R Top Fill
				08.35	13'L E.P.	

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. ____ Notes Red ____ Plotted ____ Job No. 5211-15 Division No. 11
X-Sec No. ____ Date ____ Date ____ Survey of [illegible] Dist. # 37
Notes Cked ____ Date ____ Checked ____ Date ____ Map No. ____ Indexed H. E. Opte

F. B. 3429 Pg. 122

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN RD.
78+00				2808.0	17' L Bot Cut
79+00				07.13	℄
				07.60	14' R E.P.
				07.5	26' R Top Fill
				06.65	10½' L E.P.
				06.2	16' L Bot Cut
80+00				06.17	℄
				06.41	14½' R E.P.
				06.8	30' R Top Fill
				05.67	11' L E.P.
				05.1	17' L Bot Cut
80+67				27.94.3	37' R 24" Culvert
80+71				28.01.2	26½' L 24" Culvert
81+00*				06.17	℄
				06.52	14½' R E.P.
				07.2	27' R Top Fill
				05.59	11' L E.P.
				06.0	23' L FLAT
82+00				06.46	℄
				06.72	14' R E.P.
				2807.3	26' Top Fill

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 174 Job No. 5335-1 Division No. 11 Notes Red Plotted Profile No.
Survey of W.W. DIST #37 Date Date X-Sec. No.
Survey by J. PIERCE Notes K.K. Notes Chkd. Checked
Indexed Date Date Date

STATION	B.S.	H.I.	F.S.	ELEV.	SOLEDAD CYN. RD.	
82+00				2806.15	11 'L E.P.	
				06.2	14 'L BOT. CUT	
83+00				07 03		℄
				07 11		14 'R E.P.
				08 0		29 'R TOP FILL
				06 77	11 'L E.P.	
				06 8	14 'L BOT CUT	
84+00				07 50		℄
				07 68		13 5/1 R E.P.
				08 3		24 'R TOP FILL
				07 10	10 5/1 L E.P.	
				07 1	14 'L BOT CUT	
85+00				07 85		℄
				08 00		13 'R E.P.
				08 4		26 'R TOP FILL
				07 47	11 'L E.P.	
				07 4	16 'L END CUT BEGIN FILL	
85+62				01 43		30 'R 24" CULVERT
85+66				03 62	21 'L 24" CULVERT	
86+00				08 27		℄
				08 42		13 'R E.P.

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 5475 Division No. 4
No. ____ Date ____ Date ____ Survey of W.W. DIST. # 37
X-Sec. Notes Chkd ____ Checked ____ Surveyed by [illegible] Notes by [illegible] Date [illegible]
No. ____ Date ____ Date ____ Map No. ____ Indexed ____ Date ____

F.B. 5462 PG. 175

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN. RD.
86+00				2809.0	26'R Top Fill
				07 82	11'L E.P.
				08.0	19'L End Fill
				057	27'L Bot Ditch.
87+00*				0879	℄
				0890	13'R E.P.
				089	24'R Top Fill
				0845	11'L E.P.
				074	25'L Bot Cut
88+00				0946	℄
				0961	13'R E.P.
				093	21'R Top Fill
				0904	12'L E.P.
				082	26'L Gutter
89+00				1004	℄
				1016	13'R E.P.
				095	21'R End Fill
				0969	12'L E.P.
				085	26'L Gutter
90+00				1052	℄
				1053	13'R E.P.

76-L-295 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 176 Job No. 5375.1 Division No. 11 Notes Red Date Plotted Date Profile No.
Survey of W.W. DIST # 37 Date Date X-Sec. No.
Survey by J. Pierce Notes K.K. Notes Chkd. Date Checked Date
Indexed Date Date

STATION	B.S.	H.I.	F.S.	ELEV.	SOLEDAD CYN. RD.	
90+00				2810.1		21' R TOP BERM
				1006	12' L E.P.	
				092	26' L GUTTER	
91+00				1100		℄
				1107		13' R E.P.
				106		22' R TOP BERM
				1064	12' L E.P.	
				099	26' L GUTTER	
92+00				1127		℄
				1127		14' R EP
				110		23' R TOP BERM
				1107	11.5' L E.P.	
				102	30' L GUTTER	
92+58				1131		14' R E.P.
				105		27' R TOP BERM
93+00				1201		℄
				1025		37' R E.P.
				1212	11' L E.P.	
				122	16' L GUTTER	

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. Plotted. Job No. Division No.
No. X-Sec. Notes Chkd. Checked. Survey of W.W. DIST # 37
No. Date Date Date Survey by Notes
Date Map No. Indexed Date

F.B. 3422 Pg.

STATION	B.S.	H.I.	F.S.	ELEV.	SOLEDAD CNYN. RD.
BM NC#1231				2812 71	B.M.N.C. 1231 ELEV. = 2812.718 F.B. 3180-28 SOLEDAD CANYON ROAD & ALISO CANYON ROAD N.E. COR. A C.E. BUTTON TOP MON 55' N. & 75' E. OF ℄ INT.
94+00				13 41	℄
				13 05	14.5' R E.P.
				13 0	30' R FLAT
				13 51	11' L E.P.
				13 5	14' L BOT CUT
95+00				15 00	℄
				14 40	14.5' R E.P.
				14 0	30' R FLAT
				15 11	10.5' L E.P.
				15 1	13' L BOT CUT
96+00				16 96	℄
				16 35	14.5' R E.P.
				16 0	25' R GUTTER
				17 06	10.5' L E.P.
				17 1	14.5' L BOT CUT
97+00				18 67	℄

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 178 Job No. 5325-6 Division No. 11 Notes Red Date Plotted Profile
Survey of W.W. DIST # 37 Date Date No.
Survey by J. PIERCE Notes K.K. Notes Chkd. Date Checked X-Sec.
Indexed Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN. RD.
97+00				2818 03	15' R E.P.
				17 8	24' R BEGIN FILL
				18 80	11' L E.P.
				18 8	14' L END FILL BOX CUT
97+74				11 00	28' R 48" CULVERT
97+74				13 38	23' L 48" CULVERT
98+00				20 45	℄
				20 23	15.5' R E.P.
				20 8	21' R TOP FILL
1.76				20 54	9.5' L E.P.
				20 5	20' L TOP FILL
99+00				22 57	℄
				22 23	15.5' R E.P.
				22 5	22' R END FILL
				22 66	9.5' L E.P.
				22 9	18' L TOP FILL
100+00				24 58	℄
				24 04	15' R E.P.
				23 0	25' R BOT CUT
				24 75	9.5' L E.P.
				2824 8	19' L END FILL

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red. ____ Plotted ____ Job No. 3[illegible] Division No. 11
No. ____ Date ____ Date ____ Survey of W.W. DIST # 37
X-Sec. Notes Chkd. ____ Checked ____ Survey by ____ Notes ____
No. ____ Date ____ Date ____ Map No. ____ Indexed H. E. Date ____

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD SYN. RD.	
101+00				2827 17		℄
				26 75		15'R E.P.
				25 8		25'R GUTTER
				27 25	9.5'L E.P.	
				27 2	18'L GUTTER	
				27 9	30'L FLAT	
102+00 *				30 46		℄
				30 15		15'R E.P.
				29 7		26'R END CUT BEGIN FILL
				30 52	10'L E.P.	
				30 2	19'L GUTTER	
				32 2	30'L FLAT	
103+00				33 83		℄
				33 39		16'R E.P.
				34 0		24'R TOP FILL
				33 91	9.5'L E.P.	
				33 8	20'L BEGIN FILL	
				34 3	30'L FLAT	
104+00				37 32		℄
				36 77		15.5'R E.P.
				37 1		23'R TOP FILL

F. B. [illegible] Pg. [illegible]

76-L298 CE 307 3-61

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 PG. 180 | Job No. 5375-16 Division No. 11 Notes Red Date Notes Chkd. Date Indexed Date | Profile Plotted Date Checked Date | X-Sec. No. No.

Survey of W.W. DIST # 37
Survey by J. PIERCE Notes K.K.

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN RD
104+00				2837 49	75' L E.P.
9.79				368	18' L TOP FILL
105+00				4062	℄
				4027	15' R E.P.
				406	23' R TOP FILL
				4075	95' L E.P.
				404	18' L TOP FILL
106+00				4391	℄
				4350	14' R E.P.
				433	26' R GUTTER
				4415	95' L E.P.
				440	19' L TOP FILL
107+00				4734	℄
				4690	15' R E.P.
				462	25' R GUTTER
				4752	95' L E.P.
				475	18' L TOP FILL
48.76				472	30' L FLAT
108+00				5050	℄
				5008	15' R E.P.
				493	24' R BOT CUT

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No. X-Sec. No. Notes Red Date Noted Chkd Date Plotted Date Checked Date Job No. 5325 Division No. 11 Survey of W.W. DIST # 37 Map No. Indexed H.E.O. Date F.B. 3429 PG. 181

STATION	B. S.	H. I.	F. S.	ELEV.	SOLEDAD CYN RD	
108+00				2850 60	95' L E.P.	
				50 3	18' L BEGIN CUT	
109+00				53 75		℄
				53 32		15' R E.P.
				53 0		25' R GUTTER
				53 94	9' L E.P.	
				53 6	18' L BOT CUT	
110+00				57 19		℄
				56 90		15' R E.P.
				56 4		25' R GUTTER
				57 29	9' L E.P.	
				56 9	18' L BOT CUT	
111+00				60 54		℄
				59 95		16' R E.P.
				9 2		30' R FLAT
				60 70	9' L E.P.	
				59 9	18' L END CUT	
111+34				60 72		20' R INT. OF VALE
				62 84		℄
				61 99		17' R E.P.
				61 5		30' R FLAT

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 182 Job No. 5325.16 Division No. 11 Notes Red Plotted Profile
Survey of W.W. DIST # 37 Date Date No. X-Sec.
Survey by J. PIERCE Notes K. K. Notes Chkd. Checked
Indexed Date Date Date No.

STATION	B.S.	H.I.	F.S.	ELEV.	SOLEDAD CYN. RD.
111+43				2863.17	9'L E.P.
				63.3	17'L BOT BRK
BMNC#1232				2862.42	B.M.N.C. # 1232 ELEV. = 2862.411 F.B. 3180-29
					SOLEDAD CANYON RD. AT SANTIAGO RD.
					BT. SPK. IN NW COR. CONC. WALK 70'± S.E. OF
					℄ INT.

Notes Ck'd by		Survey of	
Office Work		Surveyed by	
Checked		Notes	Date
Date		Indexed	H. E. OTT

F.B. 3429 Pg. 182

J.N. 5375.16

W.W. DIST. #37

(ACTON AREA)

LOCATION OF IMPROVEMENTS

SMITH AVE. BET. 4TH ST. & SOLEDAD CYN. RD.

8-3-67

PIERCE
TALBOT
MC DONOUGH

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

7-62 3008 CT #310 5-68

F.B. 3429 Pg. 184

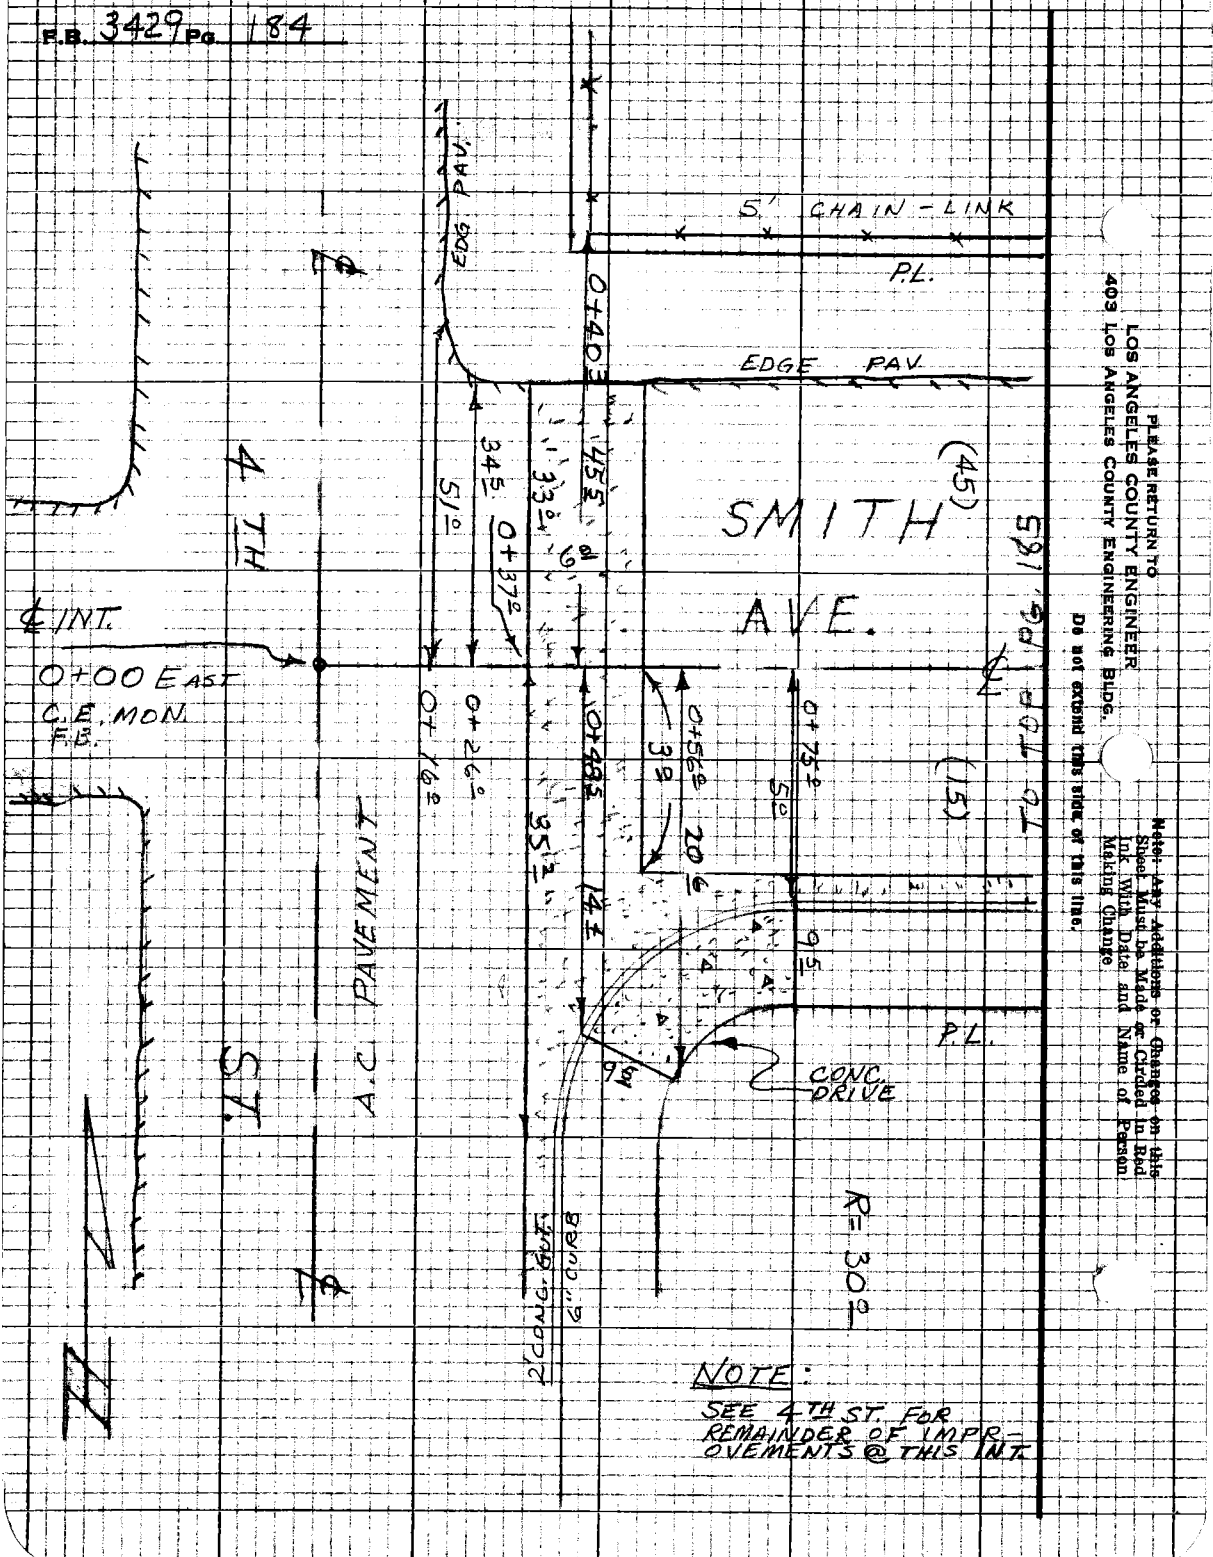

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this block of this line.

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Notes Ck'd by _____ Survey of W. W. DIST #37
Map No. 5375 Sheet 65 Sheet 64
Office Work _____ Surveyed by PIERCE
Checked _____ Notes TALBOT Date 8-3-67
Date _____ Indexed H. E. OTT SEP 5 '67
F.B. 2129 Pg. 195

TO LEAF PG. 184

(15) (43)

5° 28° 17.5 1+00

1+26.5 14" PINE 111° P.P. 7.5

1+42.3 10" CEDAR 18.4

1+46.2 D.M. 7.4

1+52.4 9.5

4" STOCK WIRE 1+59.3 11.1

9.5 5° 1+75.5 7.5 1+79.4

CONC. DRIVE P.P. GUTTER

7' BOARD FEN.

W. E. PAVEMENT

18.1 48° 1+82.5 4" STAND PIPE

2+00 28.2

2+21.4 17.5

2+76.3 9.5

46.6 2+43.8 10" TOPLAR

EDGE

3+04° CONC. DRIVES 5.4

CONC. CURB 2'

SMITH

5' CHAIN-LINK FENCE

3+72.7 9.5

4+00.0 P.C. 5.9 29.8 45.4 P.C. 4+09.2 END FN

TO LEFT PG 132

Note: Any Additions or Changes on this Sheet Must be Made or Checked in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Facebook cr #310 8.66

F.B. 3429 Pg. 186

BLANK

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this side of this line.

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

F. B. 3429 Pg. 187

Profile No. ____ Notes Red ____ Date ____ Plotted ____ Date ____ Job No. 5375.16 Division No. ____

X-Sec. No. ____ Notes Chkd ____ Date ____ Checked ____ Date ____ Survey of W. W. DIST # 37 Survey by PIERCE Notes by ____ Date 6-14-57

Map No. ____ Indexed H. E. O. Date 6-19-57

J.N. 5375.16

WATERWORKS DISTRICT # 37

CROSS SECTIONS ON SMITH AVENUE

FROM: 4TH ST. (ACTON)

TO: SOLEDAD CYN. RD.

STATION	B.S.	H.I.	F.S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

76-L-298 CE 307 2-63

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 188 | Job No. 5375.16 Division No. 11 Notes Red Date Plotted Profile
Survey of W.W. DIST # 37 Date No. X-Sec.
Survey by PIERCE Notes KING Notes Chkd. Checked
Indexed Date Date Date No.

STATION	B.S.	H.I.	F.S.	ELEV.	SMITH	AVE
BM-202-18				2698.90	BM# 202-18 1967 ADJ. ELEV. = 2698.897 F.B. 2878-75 IN ACTON 4TH ST. (CROWN VALLEY ROAD) AND SMITH AVENUE IN THE S.E. COR. 57.6 FT. E & 57' FT. S. OF ℄ INT. A L.&T. 2.5 FT. S. OF N. END OF GAS PUMP ISLAND AT THE OLD ACTON STORE	
0+00				97.85		℄ PAVE
0+37				97.45		℄ CMT GUTTER
				97.58	33'L END GUTTER	
0+75				97.84		℄
				97.50		4ᴱR GUTTER
				98.19		5°R TOP CURB
				98.40		14ᴱR BACK DRIVEWAY
1+00				97.87		℄
				97.52		4ᴱR GUTTER
				98.20		5°R TOP CURB
				98.6		15R P.L.
				98.12	28'L E.P.	
				98.8	43ᴱL FENCE	
1+53±				97.65		4ᴱR GUTTER
				98.32		5°R TOP CURB
				98.5		14ᴱR BACK DRIVEWAY
1+75±				2697.69		4ᴱR GUTTER

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	SMITH	AVE
1+75				2698 38		5' R TOP CURB
				986		14' R BACK DRIVE
2+00				800		
				777		4' R GUTTER
				842		5' R TOP CURB
				80		14' R P.L.
				818	28' L E.P.	
				79	45 L FENCE	
2+76				805		4' R GUTTER
				9871		5' R TOP CURB
				989		14' R BACK DRIVE
3+00 *				9845		
				9845	29' L E.P.	
				983	45' L FENCE	
3+04				9822		4' R GUTTER
				9890		5' R TOP CURB
				9912		14' R BACK DRIVE
3+72				9868		4' R GUTTER
				9937		5' R TOP CURB
				996		14' R BACK DRIVE
4+00				2699 17		

Profile Notes Red Plotted Job No. 5325/16 Division No. 11
No. Date Date Survey of W.W. DIST # 37
No. Date Date Map No. Indexed by L. E. Opie Date SEP 5 '67
F.B. 3429 Pg. 189

76-L-298 CE 307 2-63

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE

Do not extend notes this side of this line.

F.B. 3429 Pg. 190 | Job No. 532516 Division No. 11 Notes Red Date Plotted Date Profile No.
Survey of W.W. DIST # 37 Date Date X-Sec. No.
Survey by PIERCE Notes KINS Notes Chkd. Checked
Indexed Date Date

STATION	B.S.	H.I.	F.S.	ELEV.	SMITH	AVE
4+00				2698.90		45 R GUTTER
				99.57		5° R TOP CURB
				99.82		14 E R BACK DRIVE
				99.47	28 E L E.P.	
				992	45' L FENCE	
4+78.2				99.48		45 R GUTTER B.C.R.
				2700.14		5° R TOP CURB B.C.R.
5+00				2699.98		
				99.84		45 R E.P.
				99.50		13 E R GUTTER
				2700.10		14° R TOP CURB
				00.16	29°L E.P.	
				2699.61	45°L GUTTER	
5+85				99.87		45 R EP
				99.8		15' R P.L.
6+00				99.85		
				2700.25	29'L E.P.	
				2700.0	38'L GUTTER	
B.M.N.C.1223				2696.42	B.M.N.C. 1223 ELEV. = 2696.914 F.B. 3180-16 ACTON AREA SOLEDAD CYN. RD. E. SIDE S. PROP LINE CORY AVE & W. LINE OF S.P.R.R. A C.E. MON. FL. N.E. COR WELL SITE #1	

Notes Ck'd by	Survey of A. W. DIST # 37
Office Work	Surveyed by J. C. PIERCE
Checked	Notes J. C. P. Date 8-11-67
Date	Indexed H. E. OTT

F.B. [illegible] Pg. 191

J.N. 5375.16

WATERWORKS DISTRICT # 37

ALASO CANYON ROAD

LOCATION OF IMPROVEMENTS

FROM: SOLEDAD CANYON RD.

TO: CARSON MESA RD.

PIERCE
KING
TALBOT
MC DONOUGH

Note: Any Additions or Changes on this Sheet Must be Made or Checked in Red Ink With Date and Name of Person Making Change.

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
402 Los Angeles County Engineering Bldg.

7283SB ICE #310 R-66

F.B. 3429 Pg. 192

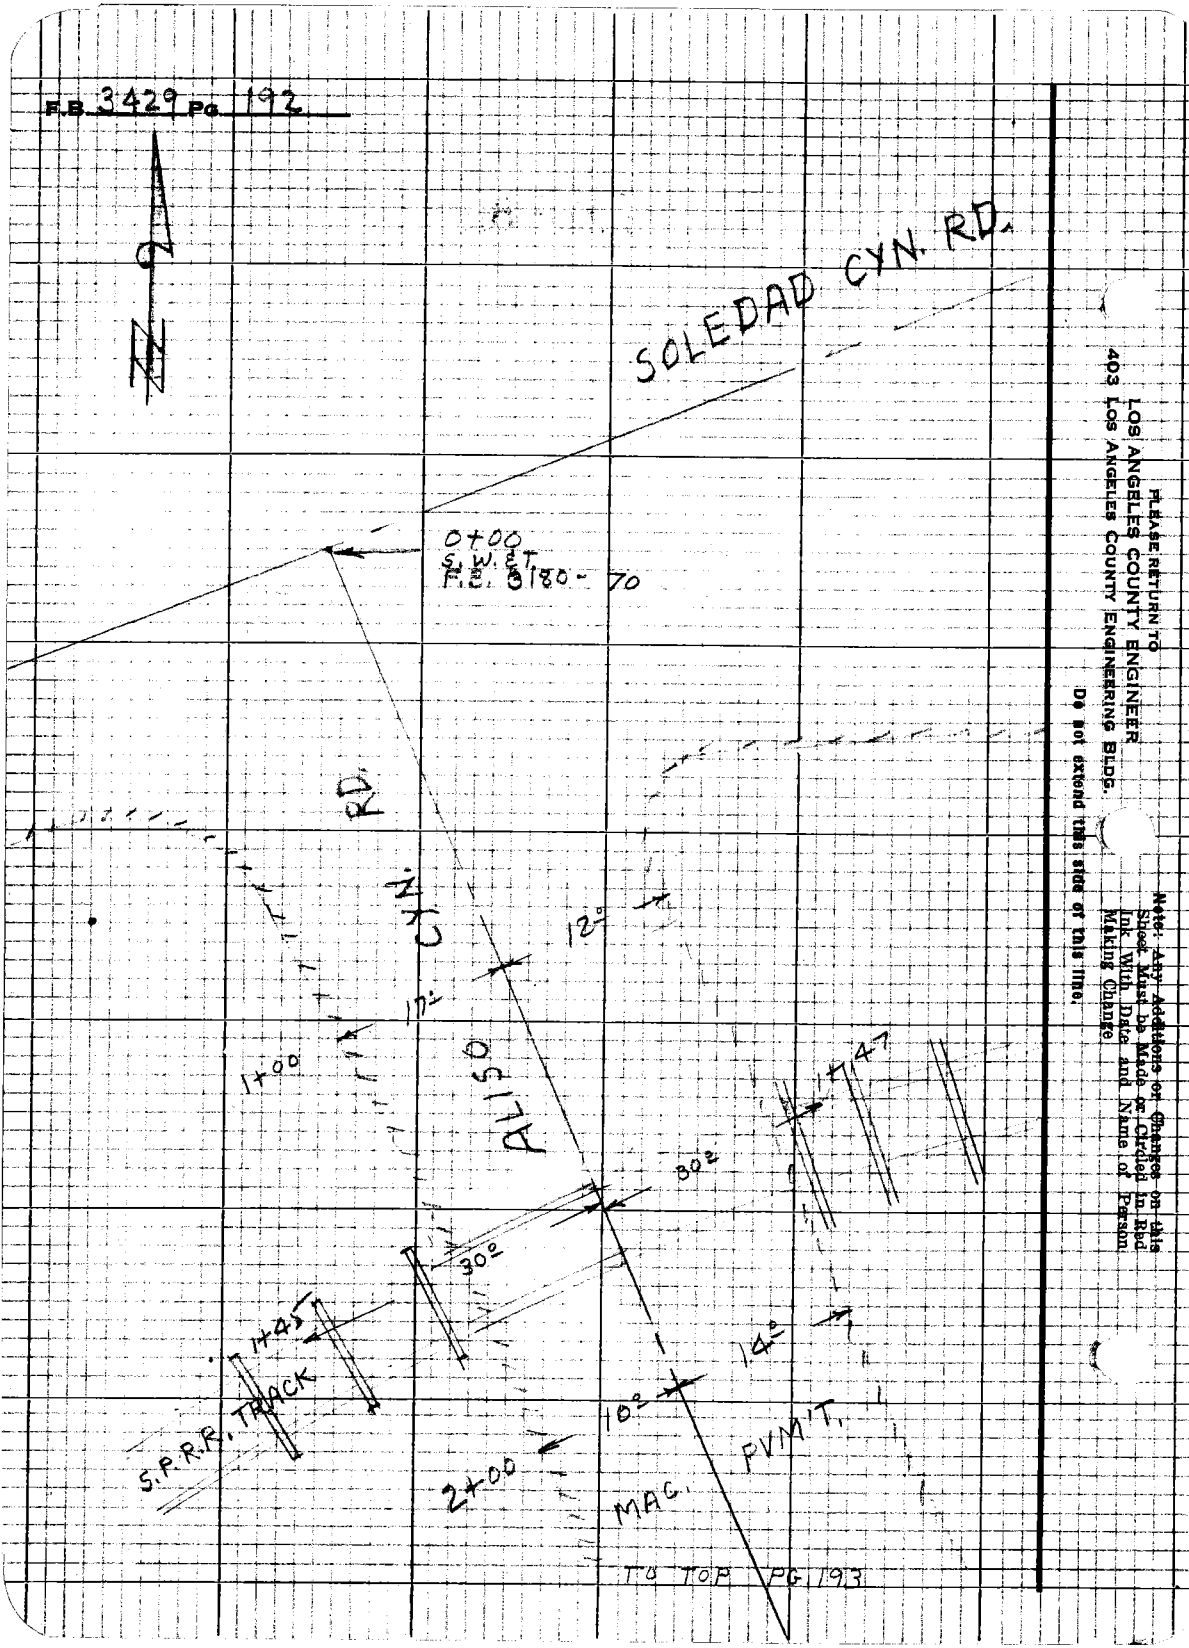

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this side of this line.

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Notes Ck'd by _____
Office Work _____
Checked _____
Date _____

Survey of W. W. DIST # 37
Surveyed by J. C. PIERCE
Notes J. C. P. Date 8-11-67
Indexed E. E. OTT

F.B. 3429 Pg. 193

T10 B&T Pg. 192

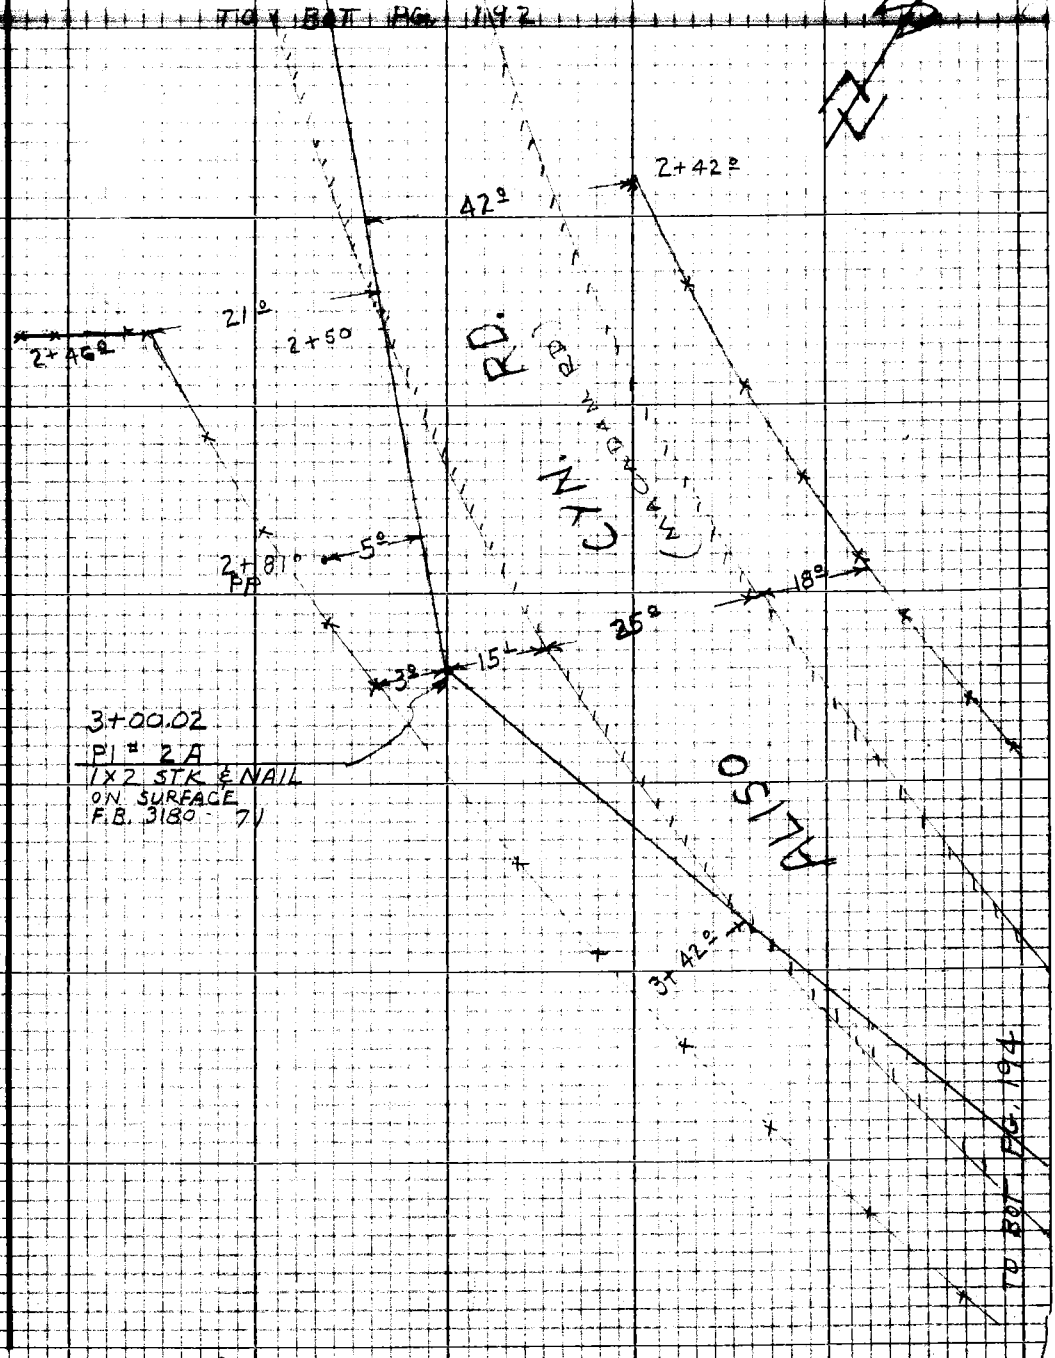

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

7-62 500 CR #310 3-65

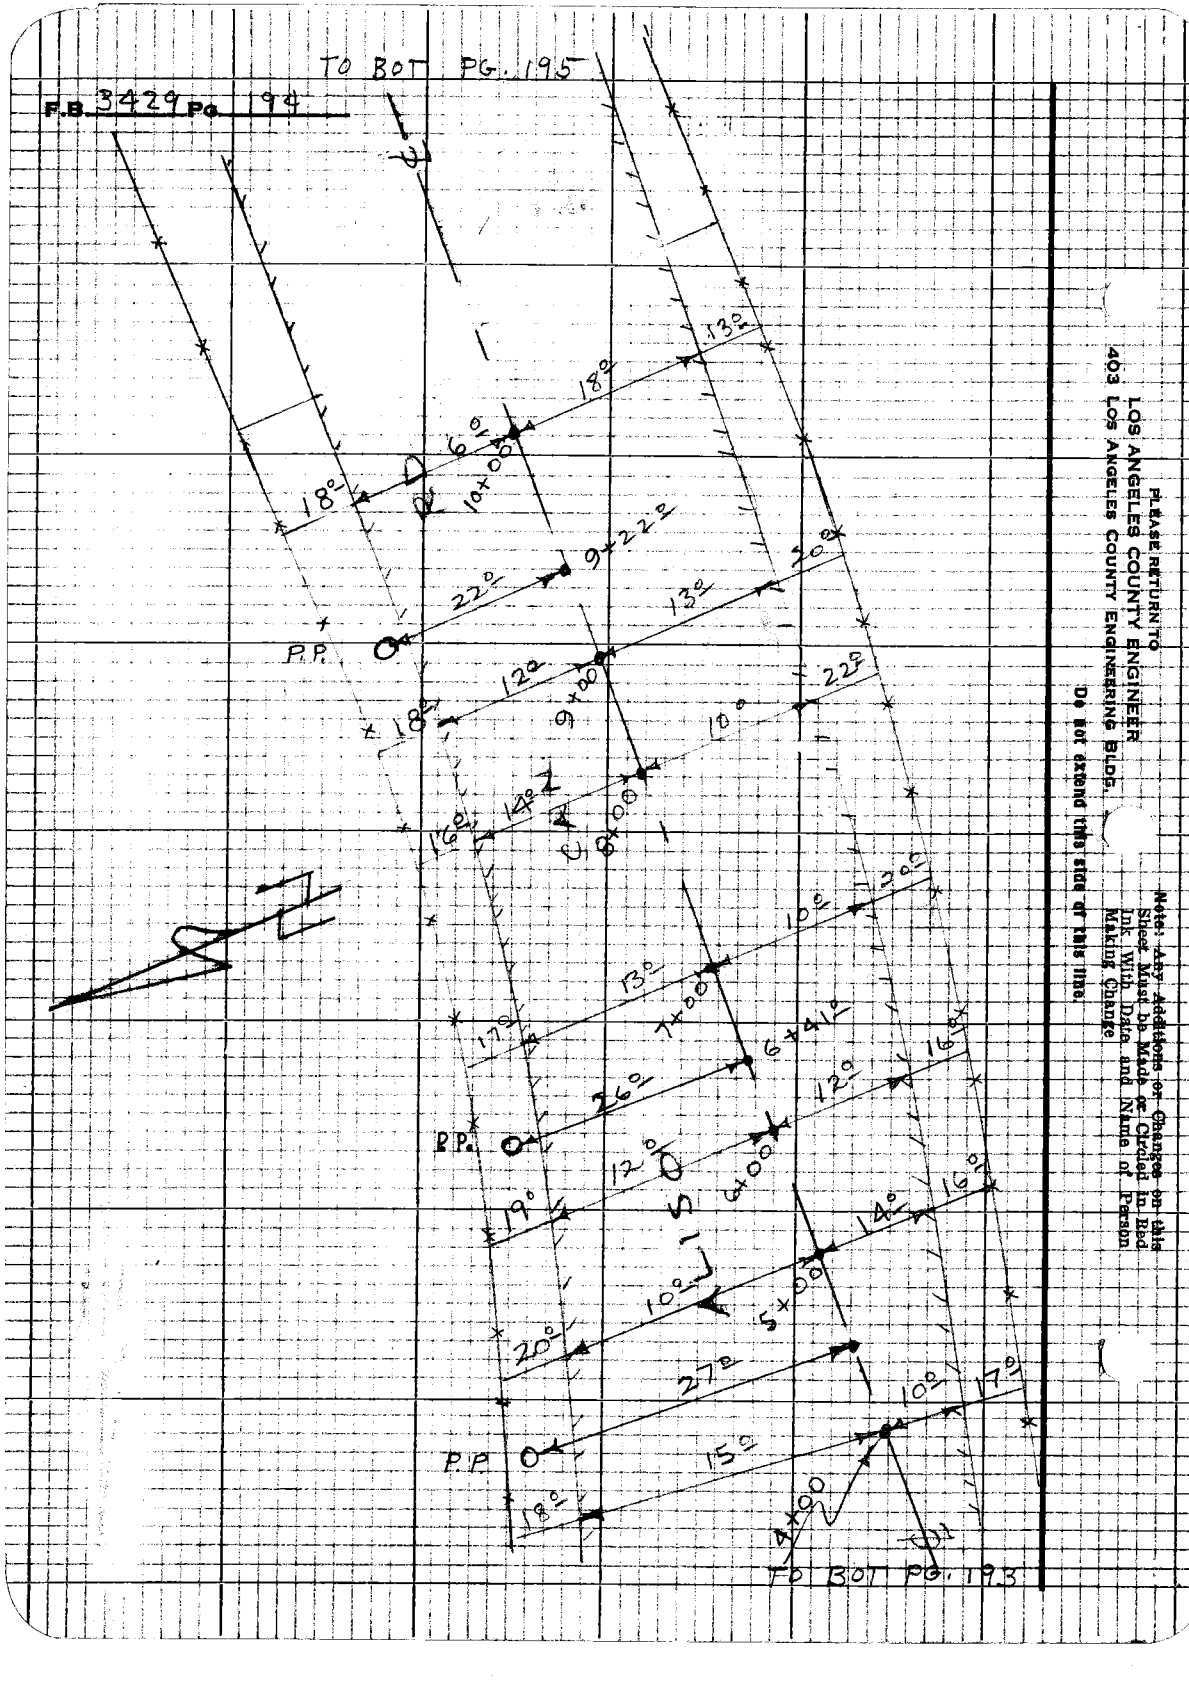
TO BOT PG. 195
F.B. 3429 Pg. 194
13°
18°
6°
10+00
18°
9+22
22°
22°
13°
20°
P.P.
12°
9+00
18°
22°
16°
14°
8+00
10°
20°
13°
7+00
17°
6+41
16°
26°
12°
P.P.
12°
4+00
19°
15°
14°
10°
5+00
20°
27°
10°
17°
P.P.
15°
18°
0+00
FD BOT PG. 193
PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.
Do not detach this slip or this line.
Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Notes Ck'd by _____
Map No. _____
Office Work _____
Checked _____
Date _____

Survey of [illegible] F.B. 2149 Pg. 195
Surveyed by PIERCE
Notes TALBOT Date 8-12-60
Indexed H. E. CTT

TO TOP PG 196

Notes: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change
Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

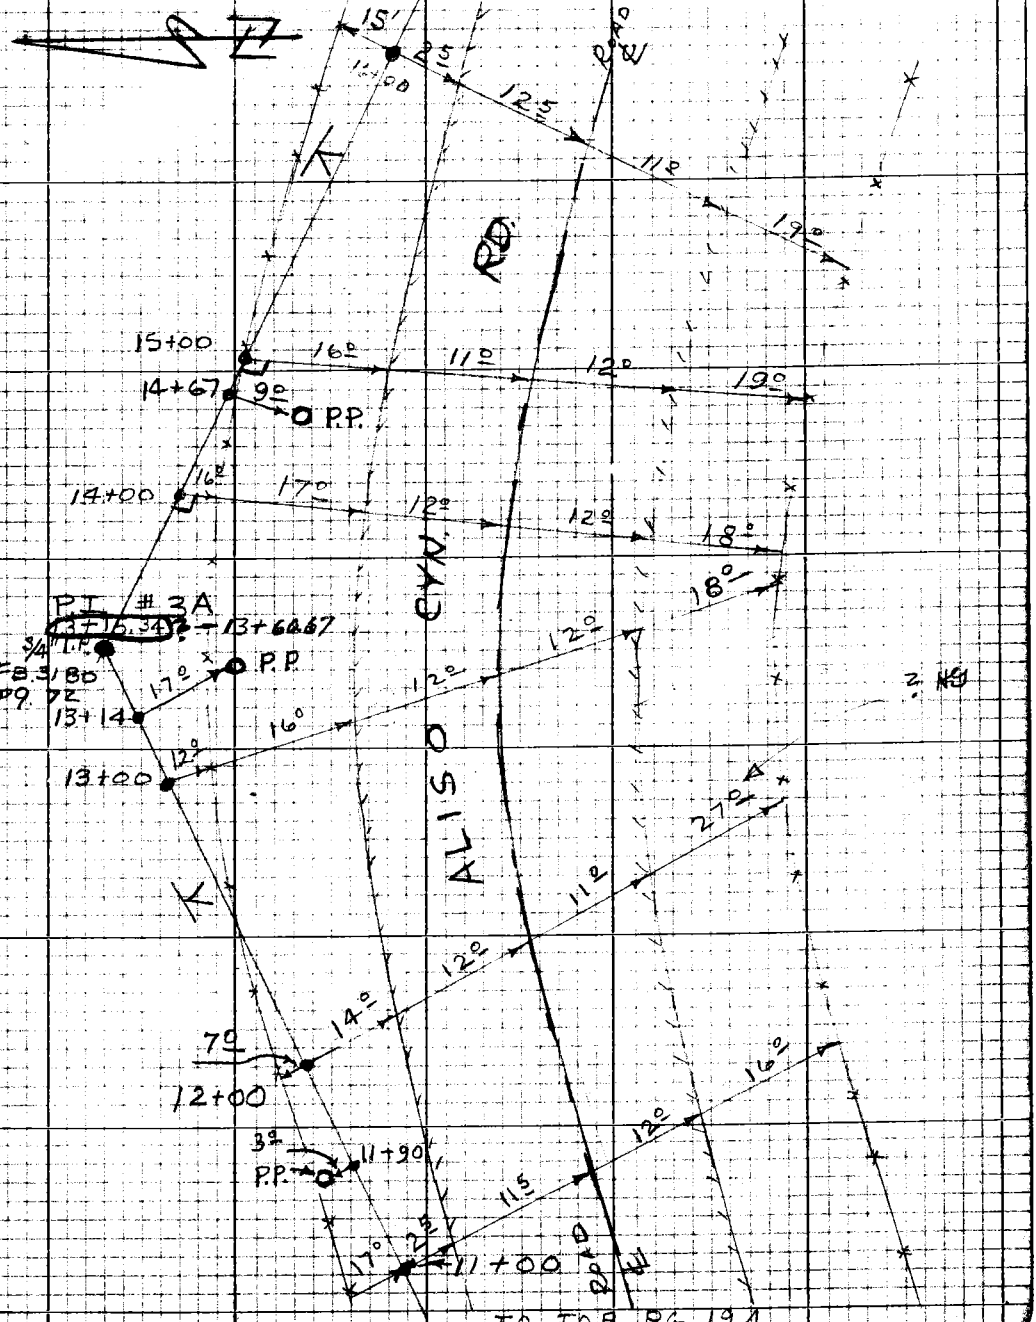

TO TOP PG. 194

7EP3058 CE #210 8-65

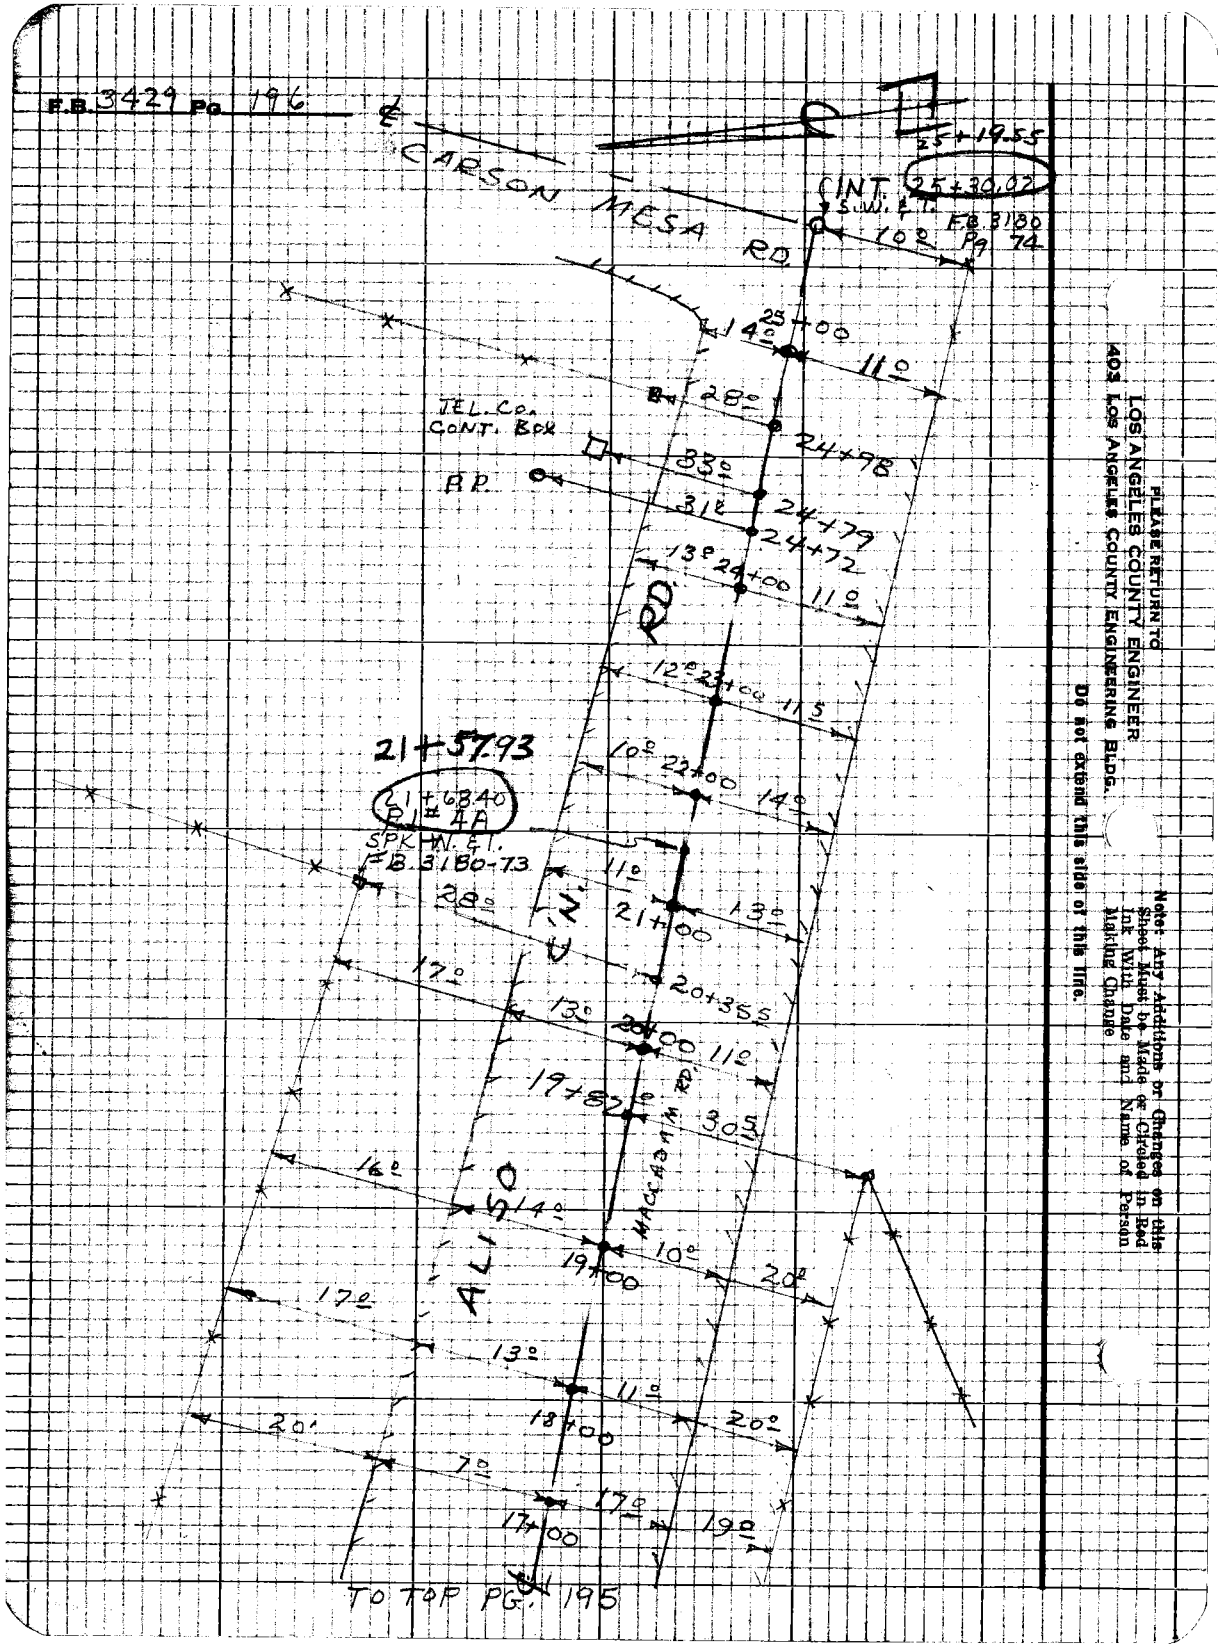
F.B. 3429 Pg. 196
℄ CARSON MESA RD.
25+19.55
CINT. 25+30.02
S.W.L. F.B. 3180 Pg. 74
10°
25+00
14°
11°
TEL. Co. CONT. BDK
B.P.
28°
24+78
35°
31°
24+79
24+72
13°
24+00
11°
RD.
12°
23+00
11.5
21+57.93
21+68.40
BLM AA
SPK W.L. F.B. 3180-73
10°
22+00
14°
11°
28°
21+00
13°
17°
20+35.5
13°
20+00
11°
19+82
RD.
30.5
MACADAMIA
16°
14°
19+00
10°
20°
17°
13°
11°
18+00
20°
7°
17°
17+00
19°
ALISO
TO TOP PG. 195
PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.
Do not extend this side of this Tie.
Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

F. B. PG.

Profile No. Notes Red Plotted Job No. Division No.
Date Date Survey of W. W. DIST. # 37
X-Sec. No. Notes Chk'd. Checked Survey by Notes Date
Date Date Map No. Indexed H. E. Date

J. O. 22716.1

WATERWORKS DISTRICT # 37

ALISO CANYON ROAD

PROFILE AND CROSS SECTIONS

FROM: SOLEDAD CYN. ROAD

TO: CARSON MESA ROAD

PIERCE
KING
TALBOT
McDONOUGH

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.

76-L-298 CE 307 5-66

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 3429 PG. 198 Job No. 5325.1 Division No. 11 Notes Red Date Notes Chk'd. Date Profile No.
Survey of W.W. DIST #37 Date Checked Date X-Sec. No.
Survey by Pierce Notes Date
Indexed Date

STATION	B. S.	H. I.	F. S.	ELEV.	ALISO CYN RD.	
B.M.N.C. 1231				2812.72	B.M.N.C. 1231 ELEV. = 2812.718 F.B. 3180 - 28	
					SOLEDAD CYN. RD. & ALISO CYN. RD N.E. COR.	
					A C.E. BUTTON TOP MON.	55' N. & 75' E. OF ℄ INT.
0+49				1070		℄ PAVE
				0995		21' R E.P.
				096		30' R DIRT
				1115	20' L E.P.	
				125	30' L DIRT	
1+00				0933		℄ PAVE
				0875		17' R E.P.
				076		30' R TOP FILL
				0944	11' L E.P.	
				103	30' L TOP FILL	
1+45				1772		℄ RR TRACK
				172		30' R RR. ROCK
				083	30' RR. ROCK	
1+68				0760		℄ PAVE
				070		20' R TOP FILL
				047		30' R BOT "
				2837	15' L TOP FILL	

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. 25[illegible] Division No.____ F. B. 4 Pg.
No.____ Date____ Date____ Survey of [illegible] Notes____ Date____
X-Sec. Notes Chk'd.____ Checked____ Survey by [illegible] Notes____ Date____
No.____ Date____ Date____ Map No.____ Indexed H. E. Otte Date [illegible]

STATION	B. S.	H. I.	F. S.	ELEV.	ALISO CYN RD.
1+68				2805 5	23' L Bot Fill
2+00				07 20	℄
				07 35	10' R E.P
				07 5	17' R Top Fill
				07 0	30' R Bot "
				06 75	14' L E.P.
				06 7	21' L Top Fill
				06 30	30' L Bot "
2 + 50				06 50	℄ E.P.
2 + 80				06 2	℄ Top Fill
3 + 00				05 26	℄ Bot Fill
				05 25	3' R Fence
				05 0	9' L Top Fill
5.5				04 547	15' L E.P.
				04 470	27' L ℄ Pavg
				04 00	40' L E.P.
				03 30	58' L Bot Brk
3+29				03 51	℄ Top Fill
3+42				03 472	℄ E.P.
4+00				03 374	℄
				2804 00	10' R E.P

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 3429 PG. 200 | Job No. 5375.1 Division No. 11 Notes Red Date Plotted Profile No.
Survey of W.W. DIST #37 Date No.
Survey by J. PIERCE Notes K.I.E. Notes Chk'd. Date Checked X-Sec. No.
Indexed Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	ALISO CYN RD.
4+00				2803 2	20' R GUTTER
				03 5	27' R FENCE
				03 10	15' L E.P.
				02 3	24' L GUTTER
				02 7	33' L FENCE
5+00				04 20	℄
				04 03	14' R E.P.
				04 5	30' R FENCE
				03 82	10' L E.P.
				03 2	21' L GUTTER
				04 2	30' L FENCE
6+00				04 95	℄
				05 00	12' R E.P.
				05 1	28' R FENCE
				04 72	12' L E.P.
				03 9	22' L GUTTER
				04 9	31' L FNCE
7+00				05 81	℄
				05 56	10' R E.P.
				05 0	19' R GUTTER
				2805 7	30' R FNCE

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. ____ Division No. ____
No. ____ Date ____ Date ____ Survey of ____ F. B. ____
X-Sec. Notes Chk'd. ____ Checked ____ Survey by ____ Notes ____ Date ____ Pg. ____
No. ____ Date ____ Date ____ Map No. ____ Indexed H. E. Date ____

STATION	B. S.	H. I.	F. S.	ELEV.	ALISO CYN RD.
7+00				280590	13'L E.P.
				0548	26'L GUTTER
				0555	30'L FENCE
8+00				0665	℄
				0630	10'R E.P.
				061	18'R GUTTER
				070	21'R TOP BK
				068	32'R FENCE
				0693	14'L E.P.
				069	26'L GUTTER
				071	30'L FENCE
9+00				0746	℄
				0690	13'R E.P.
				064	22'R GUTTER
				080	33'R FENCE
				0788	12'L E.P.
				074	23'L GUTTER
				078	29'L FENCE
10+00				0874	℄
				0780	18'R E.P.
				28070	28'R GUTTER

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 3429 Pg. 202 | Job No. 5375 Division No. 11 Notes Red Date Plotted Date Profile No.
Survey of W. W. DIST # 37 Date Date No. X-Sec.
Survey by PIERCE Notes K. K. Notes Chk'd. Date Checked Date No.
Indexed Date

STATION	B. S.	H. I.	F. S.	ELEV.	ALISO CYN RD.
10+00				2809 1	31' R TOP BRK.
				08 93	6' L E.P.
				08 86	20' L GUTTER
				08 84	24' L FENCE
11+00				09 72	℄
				09 80	25' R E.P.
				09 18	14' R ℄ PAVE
				08 50	26' R E.P.
				07 5	36' R GUTTER
				10 5	42' R TOP BRK
				09 8	17' L FENCE
12+00				10 6	℄ DIRT
				10 75	14' R E.P.
				09 96	26' R ℄ PAVE
				09 35	37' R E.P.
				08 3	46' R GUTTER
				10 6	53' R TOP BRK & FENCE
				10 6	7' L FENCE
13+00				12 3	12' R FENCE
				11 57	28' R E.P.
				2810 85	40' R ℄ PAVE

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red_____ Plotted_____ Job No. 375-1.6 Division No. 11
No._____ Date_____ Date_____ Survey of [illegible] DIST # 27
X-Sec. Notes Chk'd._____ Checked_____ Survey by [illegible] Notes_____ Date_____
No._____ Date_____ Date_____ Map No._____ Indexed H. E. OTT Date 8-5-68

F. B. [illegible] Pg. [illegible]

STATION	B. S.	H. I.	F. S.	ELEV.	ALISO CYN RD.
13+00				2810 34	52' R E.P.
				096	62' R GUTTER
				120	70' R [illegible]
14+00				132	16' R FACE
				1262	33' R E.P.
				187	45' R [illegible]
				1126	57' R E.P.
				105	66' R GUTTER
				125	75' R FENCE
15+00				143	℄ FENCE
				1357	16' R E.P.
				1287	27' R ℄ P.U.
				1212	39' R E.P.
				116	48' R GUTTER
				134	58' R TOP BANK FENCE
16+00				1478	℄
				1480	25' R E.P.
				1411	15' R ℄ PAVE
				1352	26' R E.P.
				128	36' R GUTTER
				2846	45' R TOP BANK FENCE

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 3429 PG. 204 | Job No. 5375-1 Division No. 11 Notes Red Date Plotted Date Profile No.
Survey of W.W. DIST # 37 Date No. X-Sec.
Survey by PIERCE Notes K.K. Notes Chk'd. Checked
Indexed Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	ALISO CYN RD.
16+00				2815.0	15'L FENCE
17+00 *				1623	℄
				1555	17' R E.P.
				143	27' R GUTTER
				153	36' R TOP BRK & FNCE
				1641	7' EP
				157	27' FENCE
18+00				1772	℄
				1717	11' R E.P.
				158	21' R GUTTER
				196	31' R TOP BRK & FNCE
				1825	13'L E.P.
				185	20'L BOT CUT
				200	22'L TOP "
				201	30'L FENCE
19+00				1952	℄
				1924	10' R EP
				176	20' R GUTTER
				228	30' R TOP CUT & FNCE
				1995	14'L EP
				2820.5	20'L BOT CUT

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. 2.1.15 Division No.____ F. B.____ Pg.____
No.____ Date____ Date____ Survey of____ Notes____ Date____
X-Sec. Notes Chk'd.____ Checked____ Survey by____ Indexed H. E. OB Date____
No.____ Date____ Date____ Map No.____ Date____

STATION	B. S.	H. I.	F. S.	ELEV.	ALISO CYN RD.	
19+00				2823.8	23' TOP CUT	
				23.9	30' L FENCE	
19+41				21.2	23' L END CUT	
20+00			>	21.57		℄
				21.14		11' R E.P.
				19.95		23' R GUTTER
				20.4		30' R
				21.73	13' L E.P.	
				21.9	30' L FENCE	
21+00 *				23.29		℄
				22.80		15' R E.P.
				21.8		25' R [illegible]
				22.4		37' R TOP [illegible]
				23.48	11' L E.P.	
				22.9	23' L GUTTER	
				24.3	29' L TOP BRK	
22+00				25.48		℄
				24.97		14' R E.P.
				24.1		28' R GUTTER
				26.3		40' R TOP [illegible]
				2825.68	10' L E.P.	

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 3429 PG. 206 | Job No. 5925-16 Division No. 11 Notes Red Date Plotted Date Profile No.
Survey of W.W. DIST # 27 Notes Chk'd. Date X-Sec. No.
Survey by PICNESE Notes K.K. Checked Date
Indexed Date

STATION	B. S.	H. I.	F. S.	ELEV.	ALISO CYN RD.
22 +00				2824 9	21'L GUTTER
				277	27'L TOP BRK
23 +00				274 6	℄
				2706	115'R E.P.
				265	21'R GUTTER
				271	30'R SLOPE
				2782	12'L E.P.
				270	22'L GUTTER
				293	30'L TOP BRK
24+00				2924	℄
				2889	11'R E.P.
				287	30'R GUTTER
				2942	13'L E.P.
				287	23'L GUTTER
				316	30'L TOP BRK
24+78				3017	13'L E.P.
25+00				3045	℄
				3026	11'R E.P.
				282	30'R FLAT
				3015	24'L E.P.
				315	30'L FENCE

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	ALISO CYN	RD.
				2830 67		℄
				30 51		10' R E.P.
BM NO # 1238				2833 55	B.M.N.C.# 1238 ELEV. = 2833.528 F.B. 3160	
					ALISO CANYON ROAD & CARSON MESA RD,	
					N'LY. CORNER 50' NW & 8' N.E. & INT A U.S.	
					GEOLOGICAL SURVEY BM STAMPED "2E4(9/2	
					BM 41"	

Profile Notes Red Plotted Job No. Division No.
No. Date Date Survey of
X-Sec. Notes Chk'd. Checked Survey by Notes
No. Date Date Map No. Indexed H. E. Date
F. B. Pg.

F. B. 3429 PG. 208 Job No. Division No. Notes Red Plotted Profile

Survey of Date Date No.

Survey by Notes Notes Chk'd. Checked X-Sec.

Indexed Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	
		BLANK			

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

76-L-298 CE 307 5-66

Notes Ck'd by	Survey of W&O DIST 37
Office Work	Surveyed by PIERCE
Checked	Notes TALBOT Date AUG '67
Date	Indexed H. E. OTT

F.B. [illegible] Pg. [illegible]

J. N. 5375.16

WATERWORKS DIST. # 37

CARSON MESA RD.

LOCATION OF IMPROVEMENTS

FROM: INT. ALISO CYN. RD.

TO 1655'± E'LY.

PARTY

PIERCE
KING
TALBOT
McDONOUGH

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

78P3098 CE #310 8-68

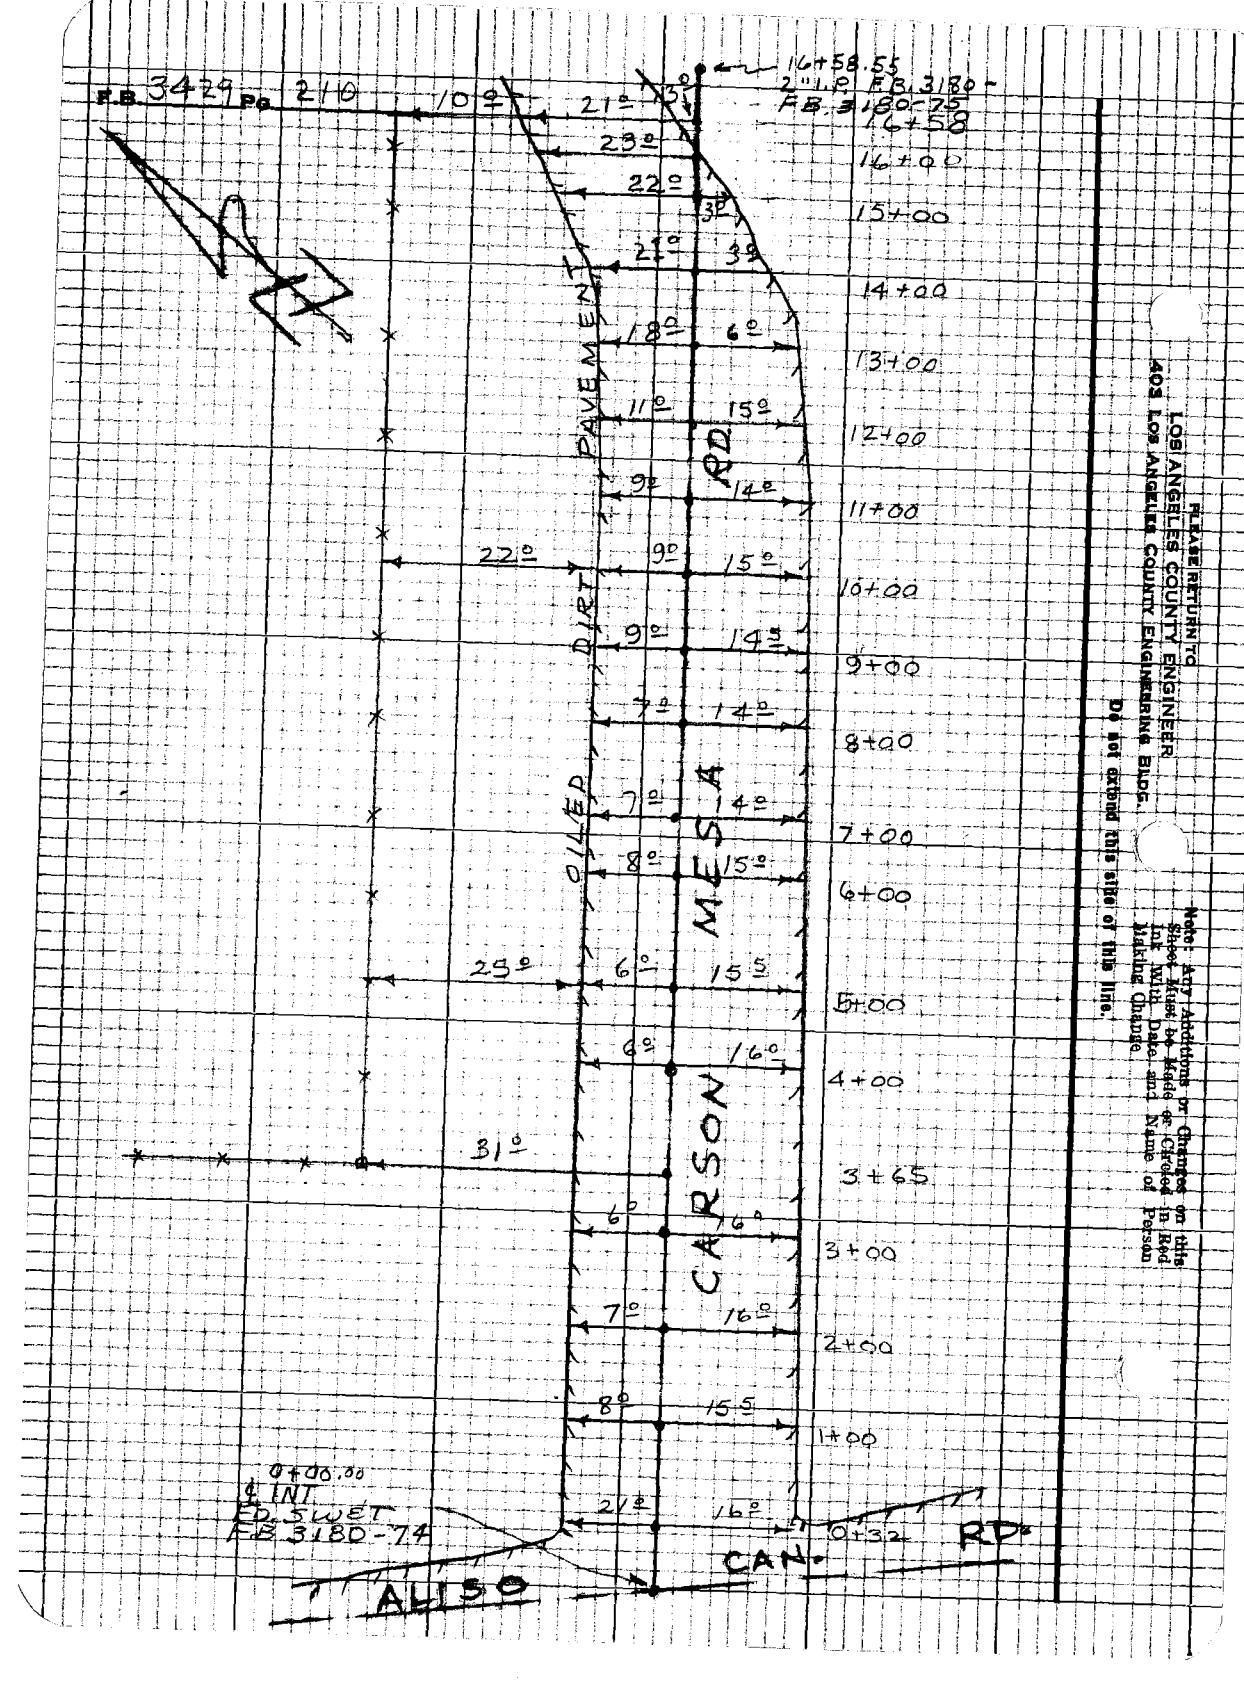
F.B. 3429 Pg. 210
16+58.55
2" I.P. F.B. 3180-75
16+58
16+00
15+00
14+00
13+00
12+00
11+00
10+00
9+00
8+00
7+00
6+00
5+00
4+00
3+65
3+00
2+00
1+00
0+32
0+00.00
℄ INT
ED. S W ET
F.B. 3180-74
ALISO
CANYON RD.
CARSON MESA
OILED DIRT PAVEMENT
RD.
10±
21±
23±
22±
21±
18±
11±
9±
22±
9±
9±
7±
7±
8±
29±
6±
6±
7±
8±
21±
31±
13°
32
32
6°
15°
14°
15°
14°
14°
14°
15°
15°
16°
16°
16°
16°
PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.
Do not extend this side of this line.
Note: Any Additions or Changes on this Street Must be Made & Circled in Red Ink With Date and Name of Person Making Change.

F. B. 34-1 PG. 61

Profile No. ____ Notes Red ____ Plotted ____ Job No. 5375.16 Division No. ____
Date ____ Date ____ Survey of W. W. DIST. #37
X-Sec. No. ____ Notes Chk'd. ____ Checked ____ Survey by J. E. Talbot Notes King Date 8-11-67
Date ____ Date ____ Map No. ____ Indexed H. E. OTT Date SEP 5 '67

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Do not extend notes this side of this line.

J. N. 5375.16

WATERWORKS DISTRICT #37

CARSON MESA ROAD

PROFILE & CROSS SECTIONS

FROM: ALISO CANYON ROAD

TO: NORTH, SOUTH & OF SEC. 32

PIERCE
KING
TALBOT
Mc DONOUGH

STATION	B. S.	H. I.	F. S.	ELEV.

76-L-298 CE 307 5-66

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 3429 PG. 212 | Job No. 5375.16 Division No. | Notes Red | Plotted | Profile
Survey of W. W. DIST # 37 | Date | Date | No.
Survey by J.C. FIERCE Notes KING | Notes Chk'd. | Checked | X-Sec.
Indexed | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	CARSON MESA RD.
BMNC = 1238				283353	B.M.N.C. = 1238 ELEV. = 2833.528 F.B. 3180 - 38
					ALISO CYN. RD. & CARSON MESA RD. N'LY. COR. 50' N'WLY. & 80' N.E. OF ℄ INT. A U.S. GEOLOGICAL SURVEY BM STAMPED " 2846 1914 BM 41"
0+32				3118	℄
				3120	16'R INT OF PAVE
				3156	21'L E.P.
				3208	25'L GUTTER
				3223	30'L TOP BRK
1+00				3200	℄
				3208	15'R E.P.
				3214	27'R GUTTER
				3225	30'R TOP BRK
				3155	8'L E.P.
				3172	24'L GUTTER
				3330	30'L TOP BRK
2+00				3395	℄
				3384	16'R E.P.
				3331	28'R GUTTER
				3344	30'R TOP BRK
				3360	7'L E.P.
				28333	24'L GUTTER

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Rel____ Plotted____ Job No. 5236.16 Division No.____
No.____ Date____ Date____ Survey of W W [illegible]
X-Sec. Notes Chk'd.____ Checked____ Survey by____ Notes____
No.____ Date____ Date____ Map No.____ Indexed____ Date____

F. B. 5423 Pg. 2/3

STATION	B. S.	H. I.	F. S.	ELEV.	CARSON MESA RD.	
2+00				28349	30'L TOP BRK	
3+00				3565	℄	
				3555		16'R E.P
				350		28'R GUTTER
				359		30'R TOP BR
				3544	6'L E.P	
				350	25'L GUTTER	
				369	30'L TOP BRK	
4+00				3735	℄	
				3737		16'R E.P
				365		27'R GUTTER
				376		30'R TOP BR
				3723	6'L E.P	
				369	26'L GUTTER	
				384	31'L FENCE	
5+00				3878	℄	
				3835		15.5'R E.P.
				376		26'R GUTTER
				388		30'R TOP BR
				3867	6'L E.P.	
				28386	26'L GUTTER	

H. E. Ott

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 3429 PG. 214 | Job No. 5375(6) Division No. 11 Notes Red Plotted Profile
Survey of W. W. Dist # 37 Date Date No. X-Sec.
Survey by Pierce Notes Kings Notes Chk'd. Checked
Indexed Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	CARSON MESA RD.
5+00				2839 9	31'L FENCE
6+00				40 43	℄
				3990	15'R E.P.
				394	27'R GUTTER
				40 2	30'R TOP BRK
				4047	8'L E.P.
				400	25'L GUTTER
				+13	32'L FENCE
7+00				+191	℄
				+171	14'R E.P.
				408	26'R GUTTER
				418	30'R TOP BRK.
				+180	8'L E.P.
				+12	26'L GUTTER
				+23	32'L FENCE
8+00				+359	℄
				+344	14'R E.P.
				+24	26'R GUTTER
				+35	30'R TOP BRK
				+345	7'L E.P.
				2842 9	27'L GUTTER

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. 5252 Division No. 11
No.____ Date____ Date____ Survey of W.W. Dist. #37
X-Sec. Notes Chk'd.____ Checked____ Survey by K.T.S. Notes
No.____ Date____ Date____ Map No.____ Indexed H.E.C. Date

F. B. 3120 Pg. 15

STATION	B. S.	H. I.	F. S.	ELEV.	CARSON MESA RD.
8+00				28438	31'L FENCE
9+00				4557	℄
				4530	14.5'R E.P.
				444	25'R GUTTER
				455	30'R TOP BRK
				4567	9'L E.P.
				452	25'L GUTTER
				459	31'L FENCE
9+45				4591	℄ TOP BRK
9+90				444	30'R BOT WASH
10+00				4548	℄ BOT WASH
				4512	15'R E.P.
				447	25'R GUTTER
				454	30'R TOP BRK
				4535	9'L E.P.
				453	27'L GUTTER
				470	32'L FENCE
10+21				450	32'L BOT WASH
11+00 *				4808	℄
				4800	14'R E.P.
				473	26'R GUTTER

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 3429 PG. 216 | Job No. 53251 Division No. 11 Notes Red Date Plotted Profile
Survey of W. W. Dist # 37 Date No.
Survey by Pierce Notes Kings Notes Chk'd. Checked X-Sec.
Indexed Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	CARSON MESA RD.
11+00				28482	30'R TOP BRK
				4765	9'L E.P.
				473	26'L GUTTER
				488	32'L FENCE
12+00				5010	℄
				4952	15'R E.P.
				486	25'R GUTTER
				50 0	30'R TOP BRK
				4995	11'L E.P.
				492	26'L GUTTER
				506	31'L FENCE
13+00				5186	℄
				5175	6'R EP
				514	12'R GUTTER
				523	30'R FLAT
				5157	18'L E.P.
				509	25'L GUTTER
				521	32'L FENCE
14+00				5332	℄
				5308	3'R EP GUTTER
				532	30'R FLAT

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red_____ Plotted_____ Job No. 3375-16 Division No. 1
No._____ Date_____ Date_____ Survey of Carson Mesa Rd. Hwy. 5
X-Sec. Notes Chk'd_____ Checked_____ Survey by_____ Notes
No._____ Date_____ Date_____ Map No._____ Indexed H. E. O'Date Date

F. B. 3426 Pg. 217

STATION	B. S.	H. I.	F. S.	ELEV.	CARSON MESA RD.	
14+00				2853.00	21' L	E.P.
				52.9	26' L	Gutter
				53.8	32' L	Fence
15+00				55.12		℄
				54.93		3' R E.P. & Gutter
				54.7		30' R Flat
				55.02	22' L	E.P. & Gutter
				55.3	31' L	Fence
16+00				56.37		℄ E.P. & Gutter
				56.1		30' R Flat
				56.27	23' L	E.P. & Gutter
				57.1	31' L	Fence
16+58 Ex				57.6		℄ Dirt
				57.1		30' R Dirt
				57.42	3' L	E.P. & Gutter
				57.30	21' L	" "
				58.0	31' L	Fence
BMNC #1239				2856.60	B.M.N.C. #1239 ELEV. = 2856.606 F.B. 3180 - 39	
					CARSON MESA RD. 1550' ± E,LY OF ℄ ALISO	
					A C.S. MON, FLUSH STAMPED "CTR, SEC. 32"	
					77' ± S'LY. OF ℄ RD.	

F. B. 3429 PG. 218 | Job No. | Division No. | Notes Red | Plotted | Profile

Survey of | Date | Date | No.

Survey by | Notes | Notes Chk'd. | Checked | X-Sec.

Indexed | Date | Date | Date | No.

STATION	B. S.	H. I.	F. S.	ELEV.	
		BLANK			

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend notes this side of this line.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

76-L-298 CE 307 5-66

Notes Ck'd by	Survey of W.W. Dist # 37
Office Work	Surveyed by J.C. Pierce
Checked	Notes King Date 8-15-57
Date	Indexed H.E. Ott 8-15-57

F.B. 2170 Pg. 210

J.N. 5375.16

LOCATION OF IMPROVEMENTS

ESCONDIDO CANYON RD.

FROM 4TH ST

TO E.C. AT P.I. # 7 (1.5 MI. ±)

PARTY
PIERCE
KING
TALBOT
McDONOUGH

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

7812bas CE #310 5-65

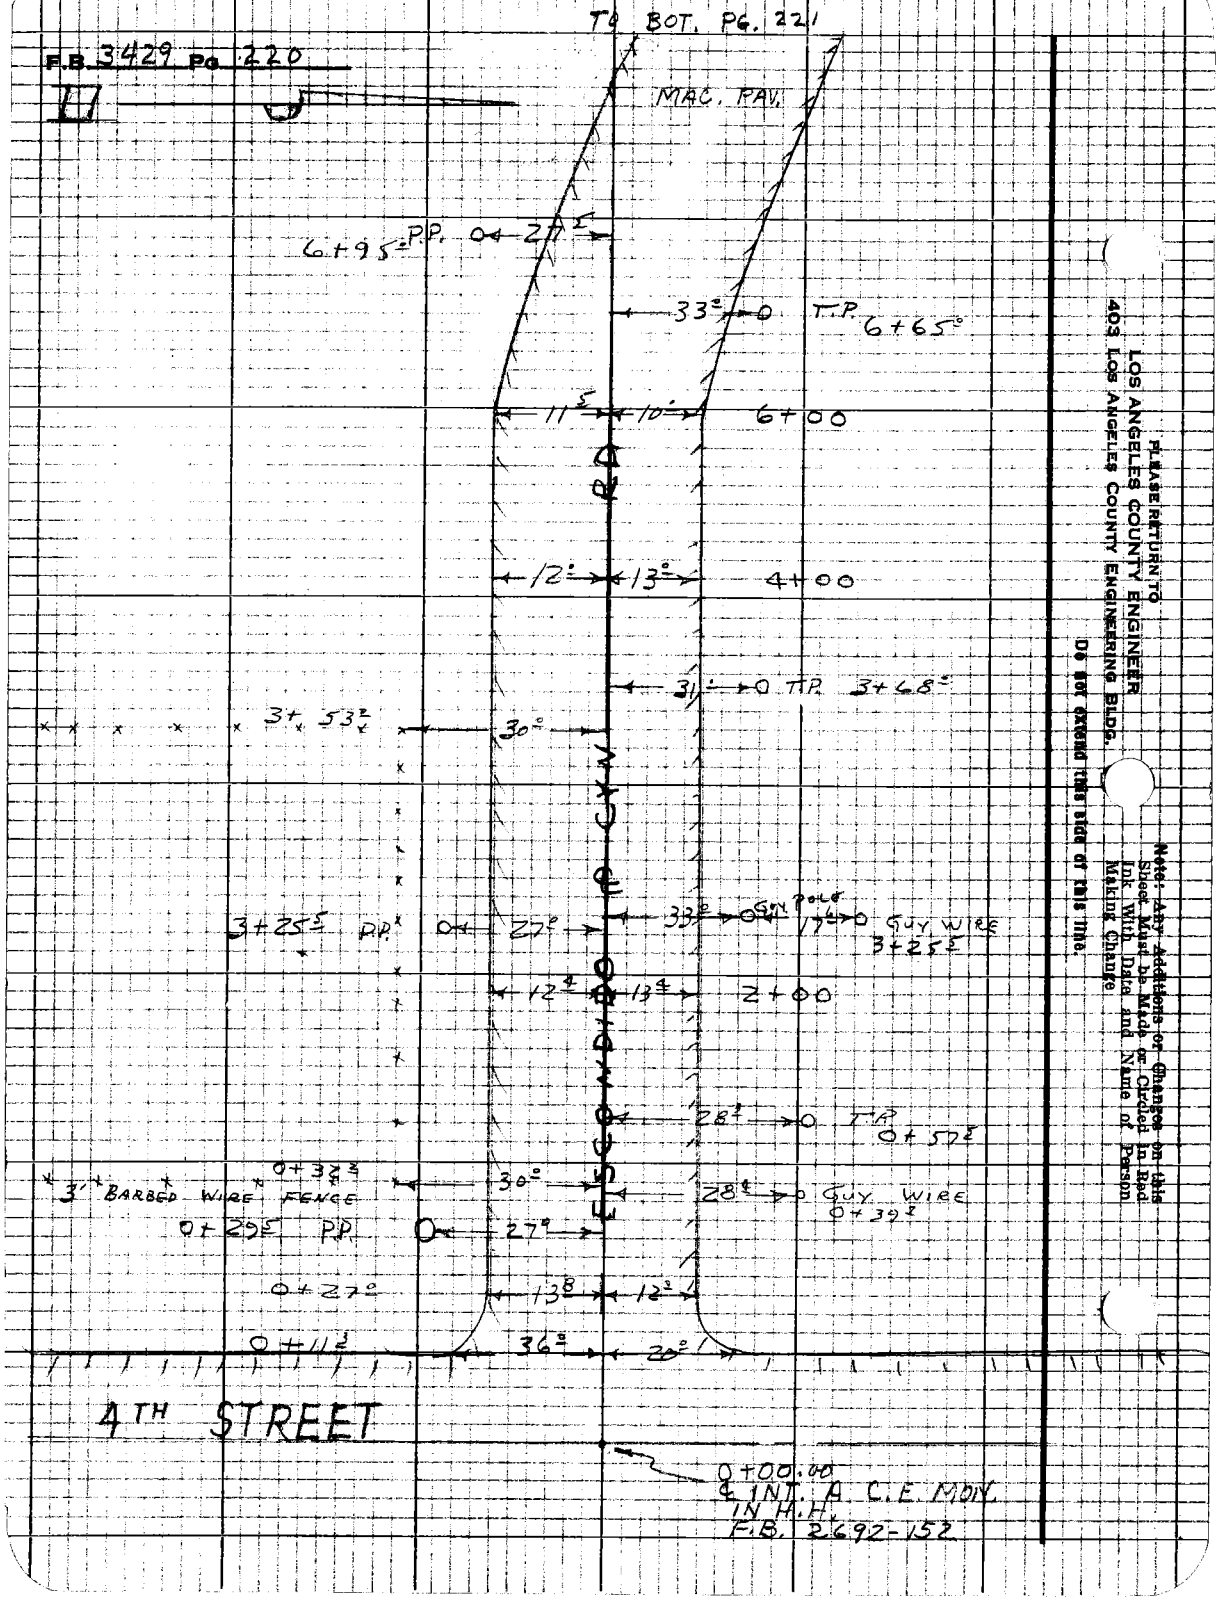
TO BOT. PG. 221
F.B. 3429 Pg. 220
MAC. PAV.
6+95± P.P. 0◁ 27°
33° → 0 T.P. 6+65±
11° 10° 6+00
12° 13° 4+00
31° → 0 T.P. 3+68±
3+53± 30°
3+25± P.P. 0◁ 27° 33° Sign Pole 4 → 0 Guy Wire 3+25±
12° 13° 2+00
28° → 0 T.P. 0+57±
3' BARBED WIRE FENCE
0+39± 30° 28° → Guy Wire 0+39±
0+29± P.P. 0◁ 27°
0+27±
13° 12°
0+11½ 36° 20°
4TH STREET
0+00.00
℄ INT. A.C.E. MON.
IN H.H.
F.B. 2692-152
PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.
DO NOT ERASE THIS SIDE OF THIS MAP.
Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Notes Ck'd by		Survey of W.W. DIST. #37	F.B. 3429 Pg. 221
Office Work		Surveyed by J.C. PIERCE	
Checked		Notes KING Date 8-15-47	
Date		Indexed H. E. OTT	

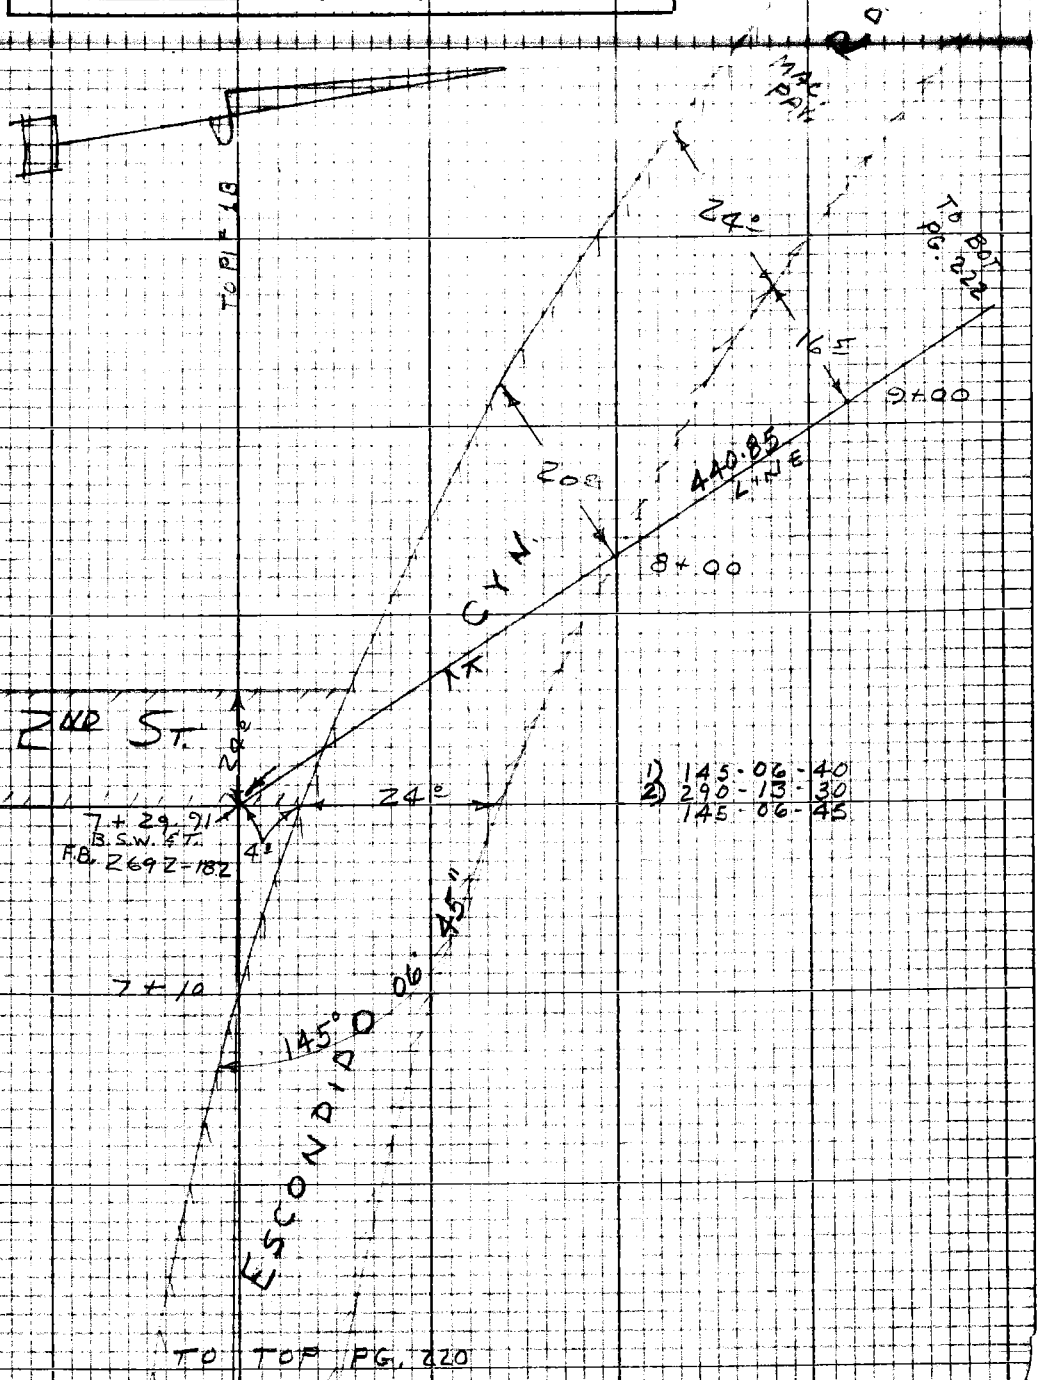

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Johnson Cat #310 Refs

F.B. 3429 Pg. 222

TO BOT PG. 223

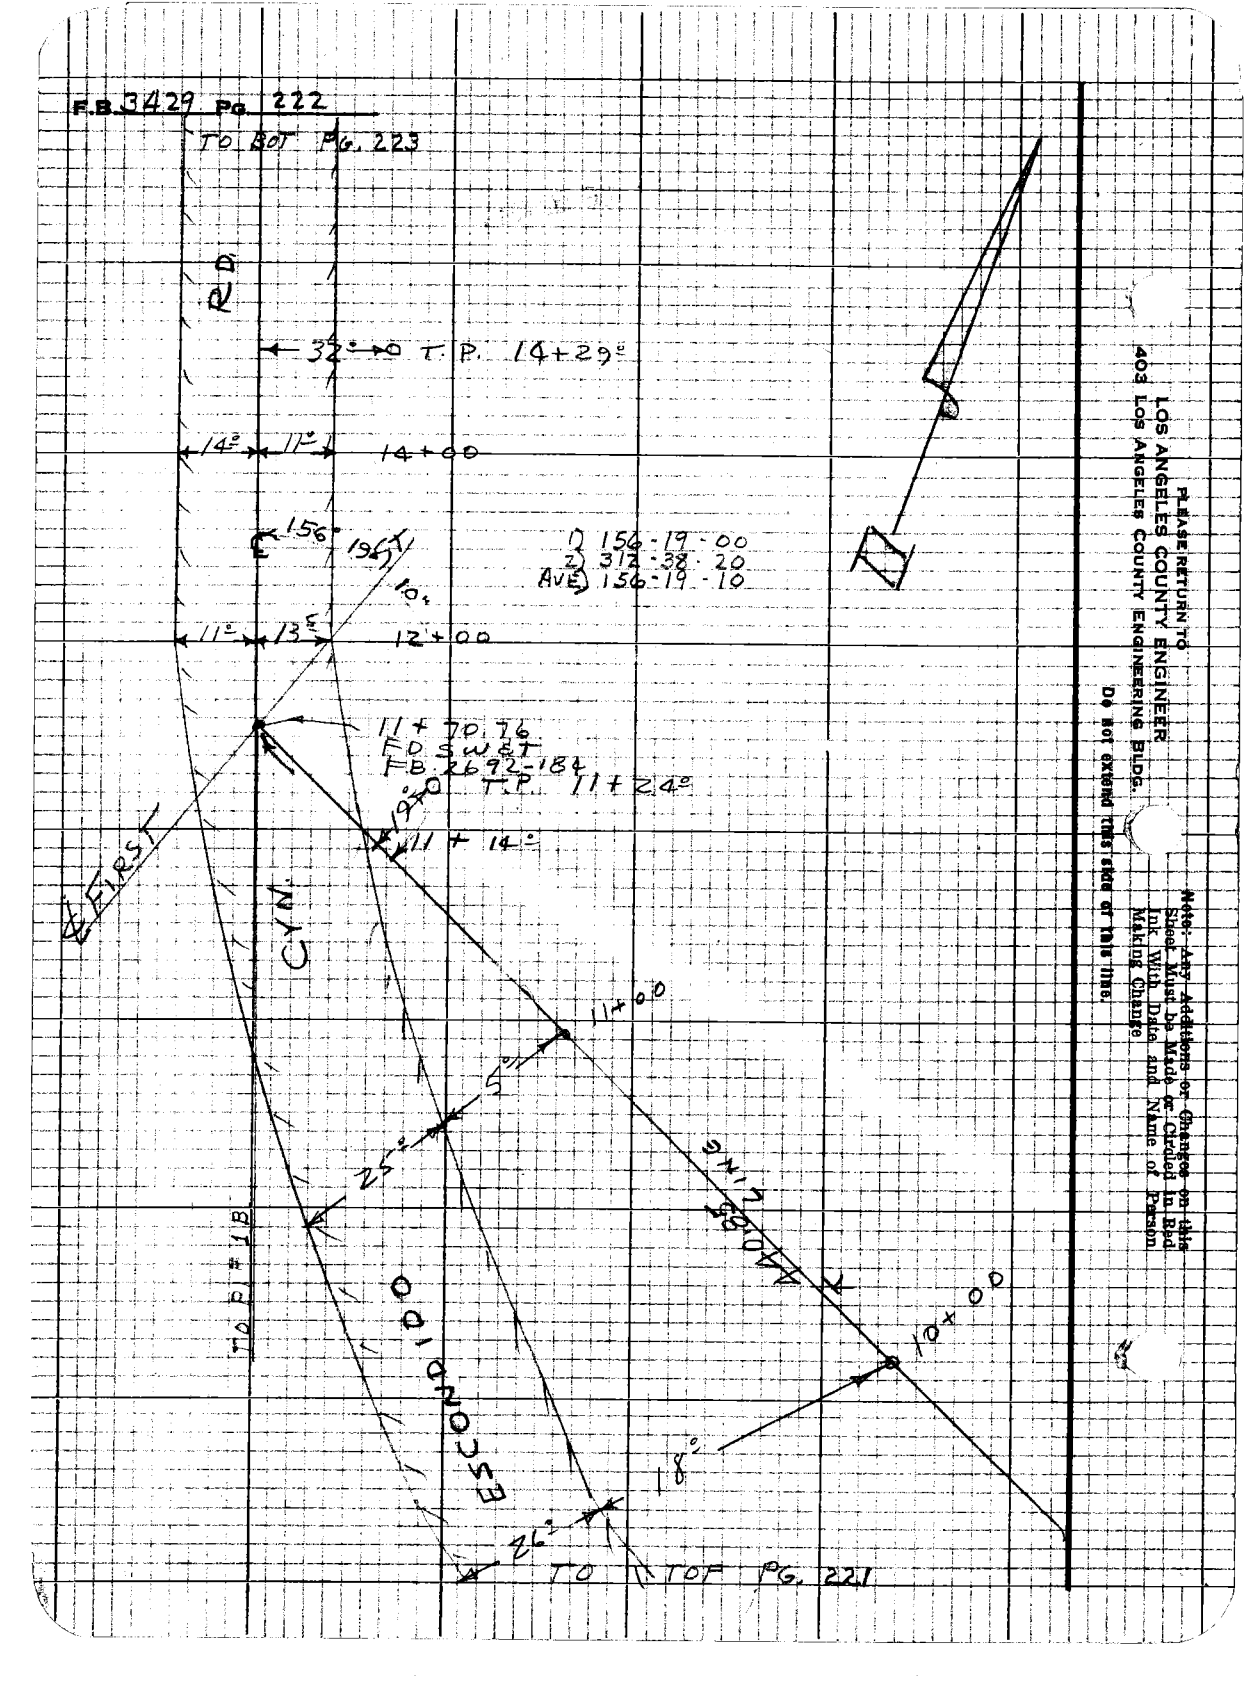

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this side of this line.

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Notes Ck'd by	Survey of W.W. DIST. #37
Map No.	F.B. 3429 Pg. 222
Office Work	Surveyed by J.C. PIERCE
Checked	Notes HWG Date 8-16-67
Date	Indexed H.E.O.

TO BOOK PG. 1224

Notes: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

7SP3098 CE #310 E-65

D.I.
D.I.
4'
14'
18+87
CONC. DRAIN
4'
14'
18+74 E
35"
18+61
12'
11'
18+00
13'
36" CONC. DRAIN
17+98
25 E
17+62
28'
T.P. 17+30
CONC. HD. WALL
24.5'
26'
16+90
24" CULV.
16+53
13.5'
40'
TYPICAL
HUBBARD Rd.
CYN.
CONDUIT
16+4.4.63
FD. CE MON
F.B. 2622 - 185
16+17
13.5'
13'
13'
16+00
TO TOP PG. 1222

F.B. 3429 Pg. 224

TO BOT PG. 225

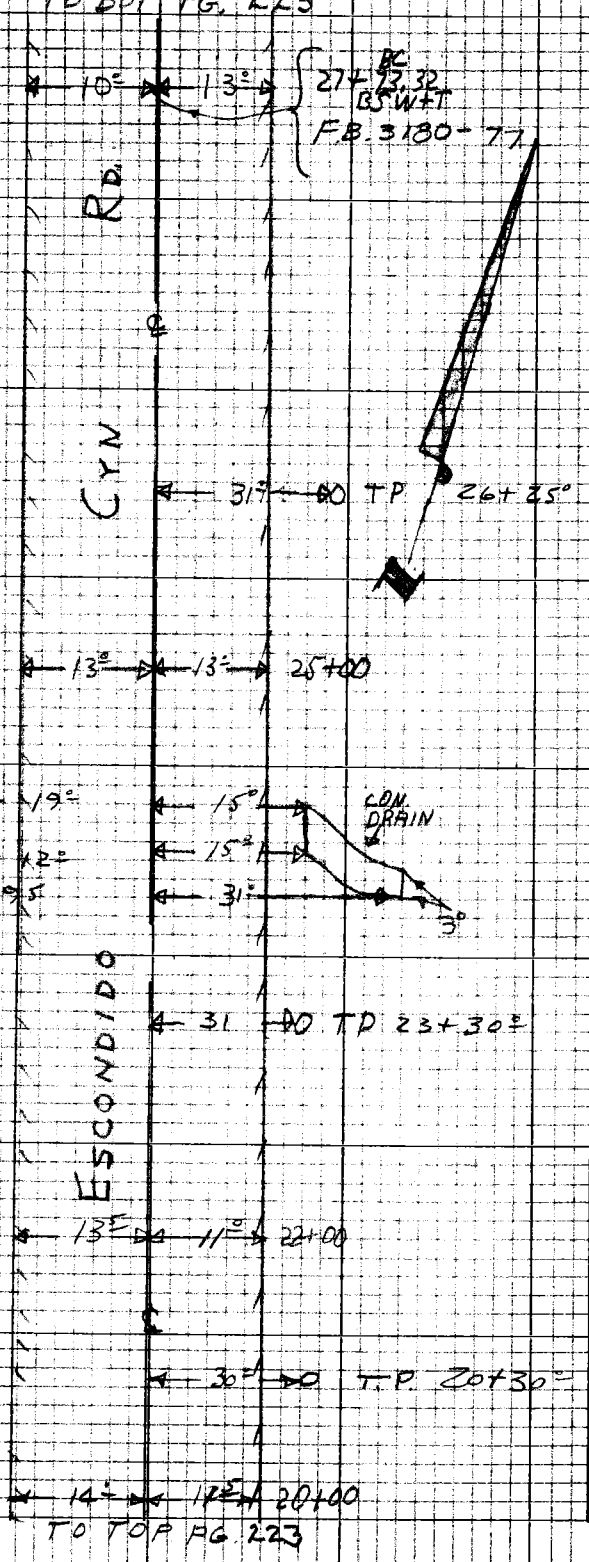

TO TOP PG 223

RELEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

DO not extend this side of this line.

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Notes Ck'd by _____
Map No. _____
Office Work _____
Checked _____
Date _____

Survey of [illegible] 67
Surveyed by J.C. PIERCE
Notes J.C.P. Date 8-17-67
Indexed H.E.L.

F.B. 3429 Pg. 225

TO EOT PG 226

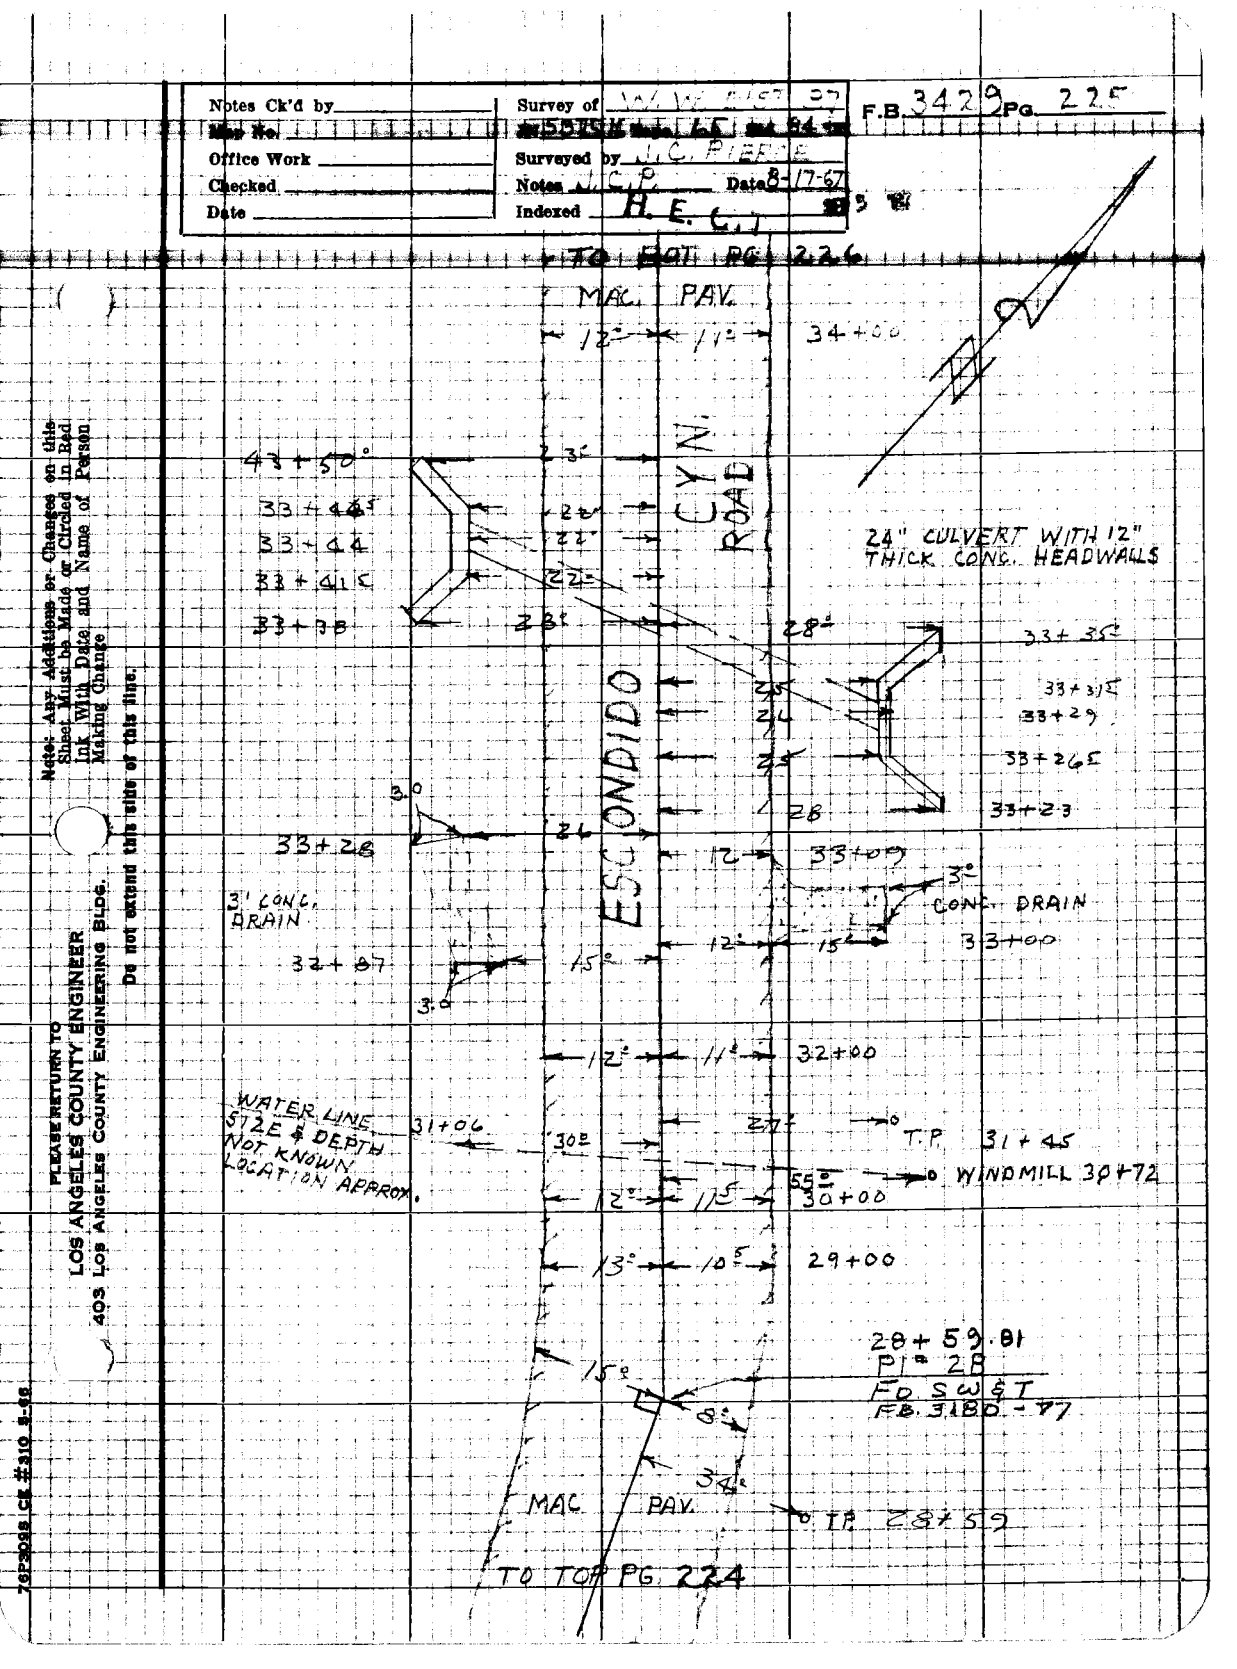

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

76P3098 CE #310 5-66

F.B. 3429 Pg. 226

TO BOT. PG. 227

Pt of B.R.
42+54.81

MAC. PAV.

12' 10'

42+00

41+80 14

5°

CONC. DRAIN

4 +73 14

41+59 27'

3°

3°

41+02 15'

ESCONDIDO ROAD

CONC. DRAIN.

41+06 30' 8' DIRT DRIVE

40+78 24'

3°

28.5' TR 40+43

11' 12.5' 40+00

11' 12' 38+00

27' TR 37+43

36+84

36+68 ELCYN

30'

10' WIDE DIRT DRIVE

36+46

12' 11' 36+00

MAC. PAV.

24' TR 34+46

TO TOR PG. 225

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

DO not detach this page of this map.

Enter any Additions or Changes on this Sheet. Must be Made or Circled in Red ink With Date and Name of Person Making Change

Notes Ck'd by _____
Map No. _____
Office Work _____
Checked _____
Date _____

Survey of W. W. DIST. # 27
Surveyed by J.C. PIERCE
Notes J.C.P. Date 8-17-67
Indexed H. E. OTT

F.B. 3127 Pg. 227

TO ASP. FB. 2787

49+13.77 P.C.

S.W. & T. IN PAV. F.B. 3180-79

CEM. DRAIN

17'

MAC. PAV.

49+35

25'

29'

49+10

16'

13'

48+25

48+89

48+06

48+04.5

48+03

48+00

28'

24'

27'

26'

28.5'

ESCONDIDO CYN. ROAD

24" CULVERT WITH 12" THICK CONC. HEADWALLS

29'

28'

27'

47+80'

47+78.5'

47+77

47+75.5'

47+73

12.5'

46+00

8'

OIL DIRT DRIVE WAY 18' WIDE

12.5'

9'

12'

44+00

10.5'

10'

43+00

MAC. PAV.

42+54.81

P.I. # 3B

S.W. & T. IN PAV.

F.B. 3180-78

TO TOP PG. 1226

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Do not extend this title of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

7SP3098 ICK #310 8-66

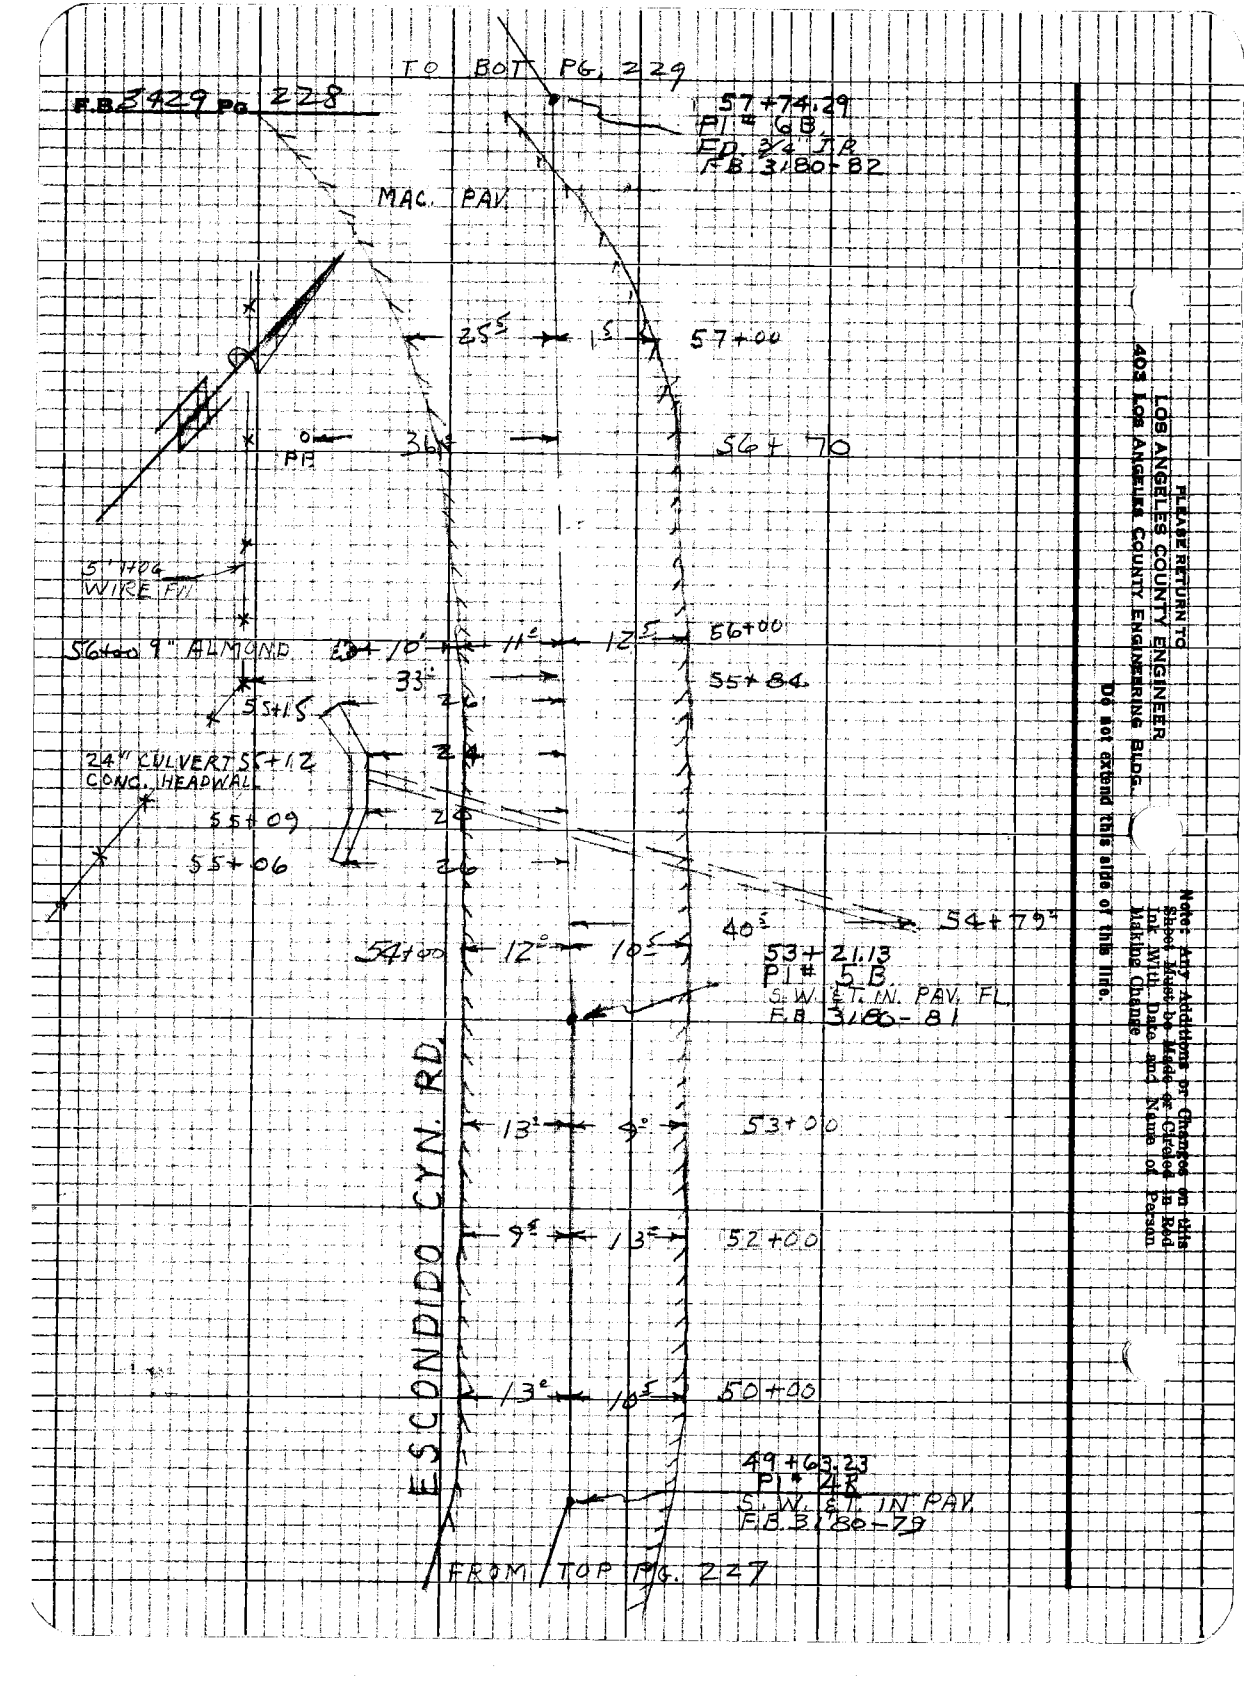

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this side of this line.

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Notes Ck'd by _____
Map No. _____
Office Work _____
Checked _____
Date _____

Survey of ESCONDIDO DIST #2
Surveyed by J. C. PIERCE
Notes J.C.P. Date 8-18-67
Indexed H. E. O.

F.B. 3195 Pg. _____

TO B.F. PG. 230

MAC. PAV.

TO B.F. PG.

62+00

55°

61+00

23°

7°

60+00

9°

15°

DIRT RD.

59+62.9

59+00

59+60

31°

18°

5°

ESCONDIDO CYN. ROAD

14°

27°

10°

58+00

57+74.29
P.I. ⊙ B
FD 34 I.P.
FB 3190-82

MAC. PAV.

TO TOP PG. 228

Notes: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

7SRSOS CK #310 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

Do not detach this side of this Title.

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

F.B. 3429 Pg. 230

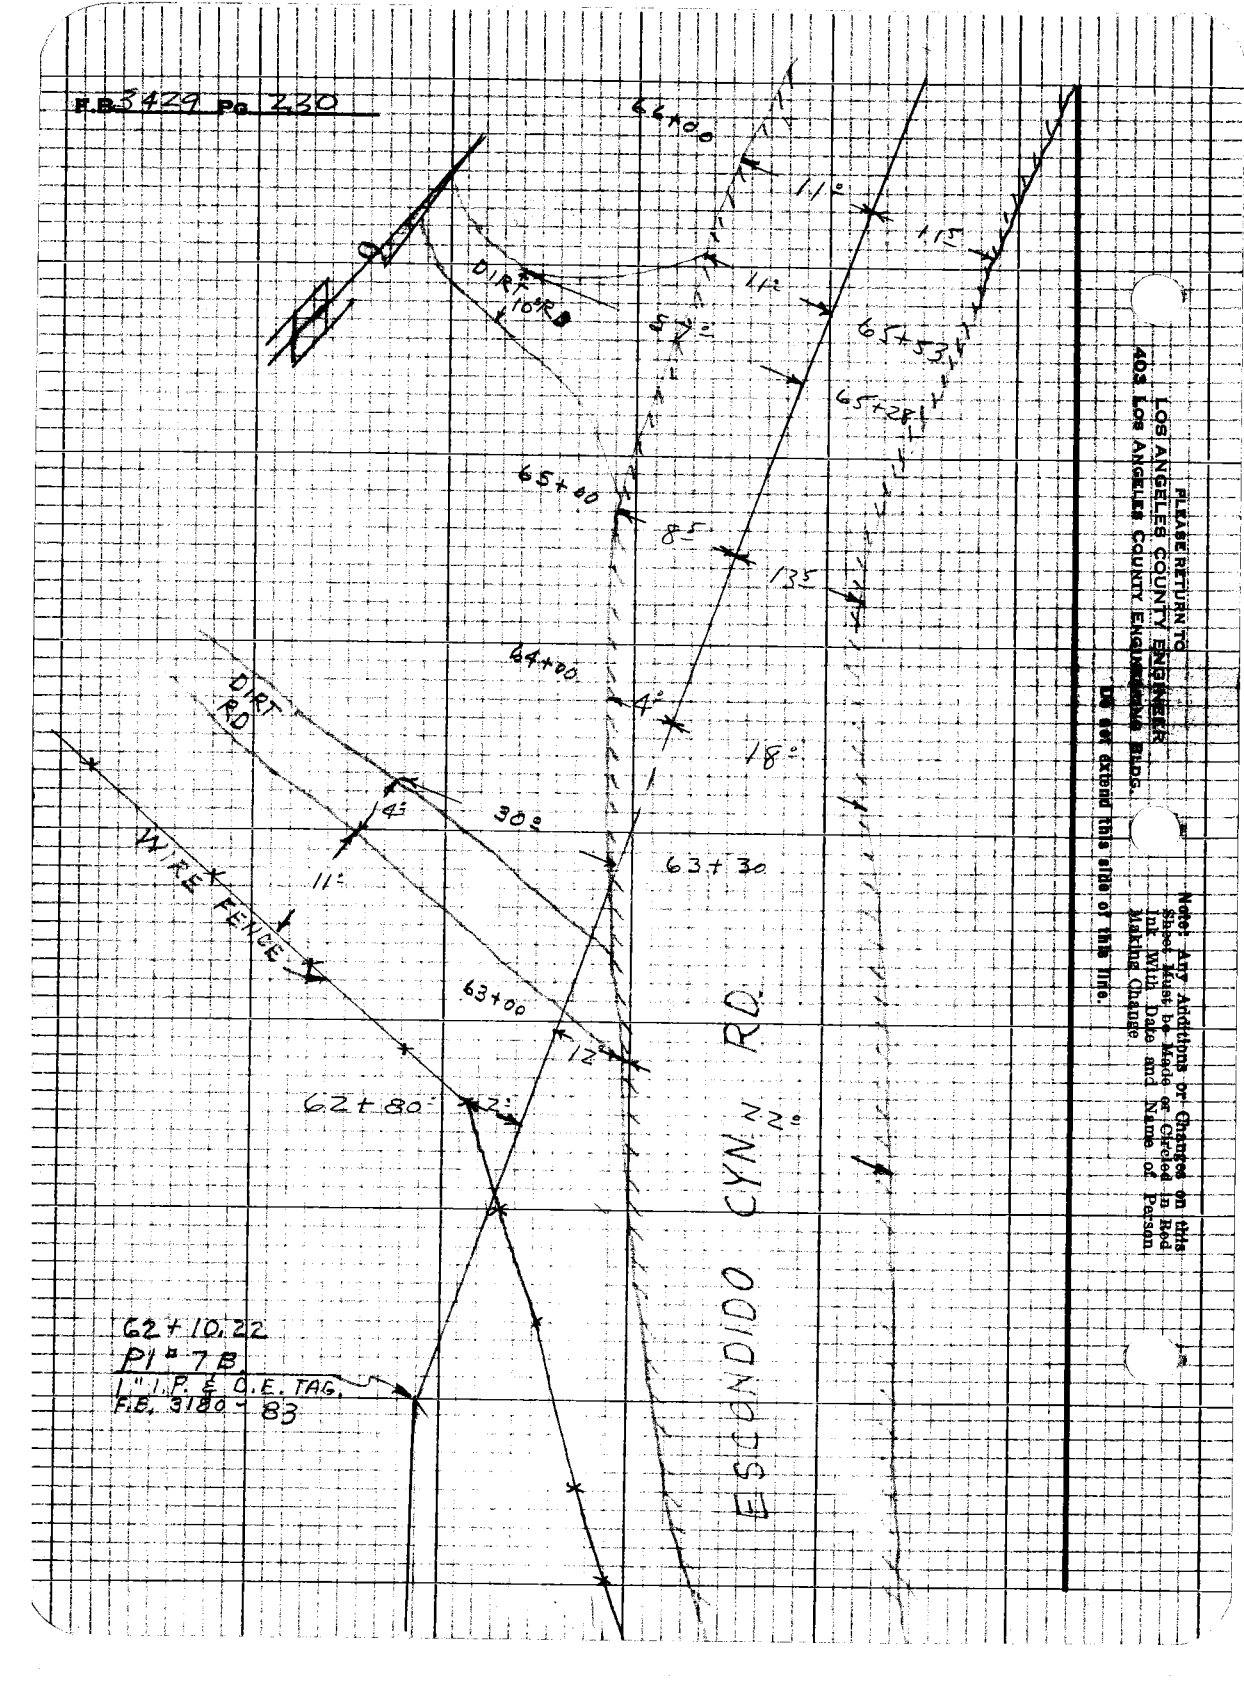

Notes Ck'd by _____
Map No. _____
Office Work _____
Checked _____
Date _____

Survey of W. W. DIST. # 37
Surveyed by D. G. PIERCE
Notes J. C. P. Date 8-21-67
Indexed H. E. OTT

F.B. 3427 Pg. 231

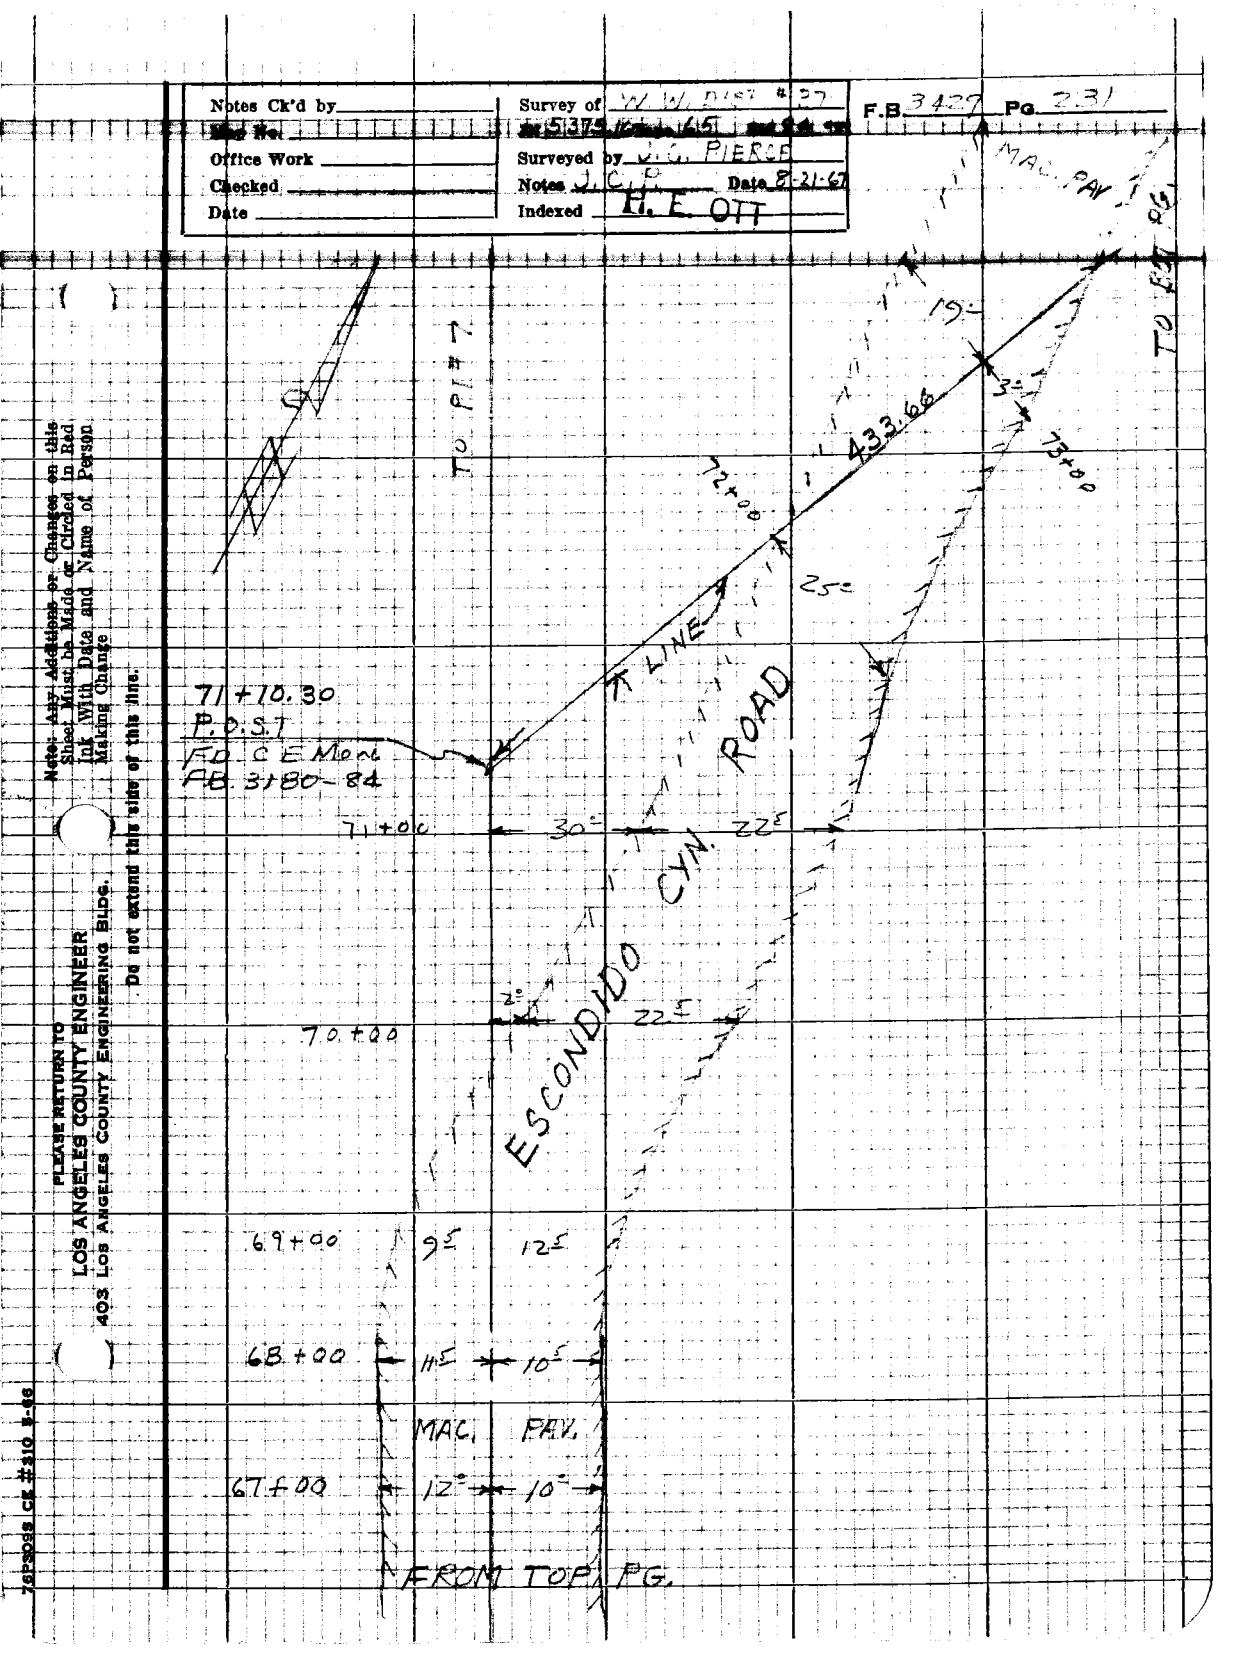

Notes: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

Do not extend this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

7835058 CK #310 8-68

F.B. 3429 Pg. 052

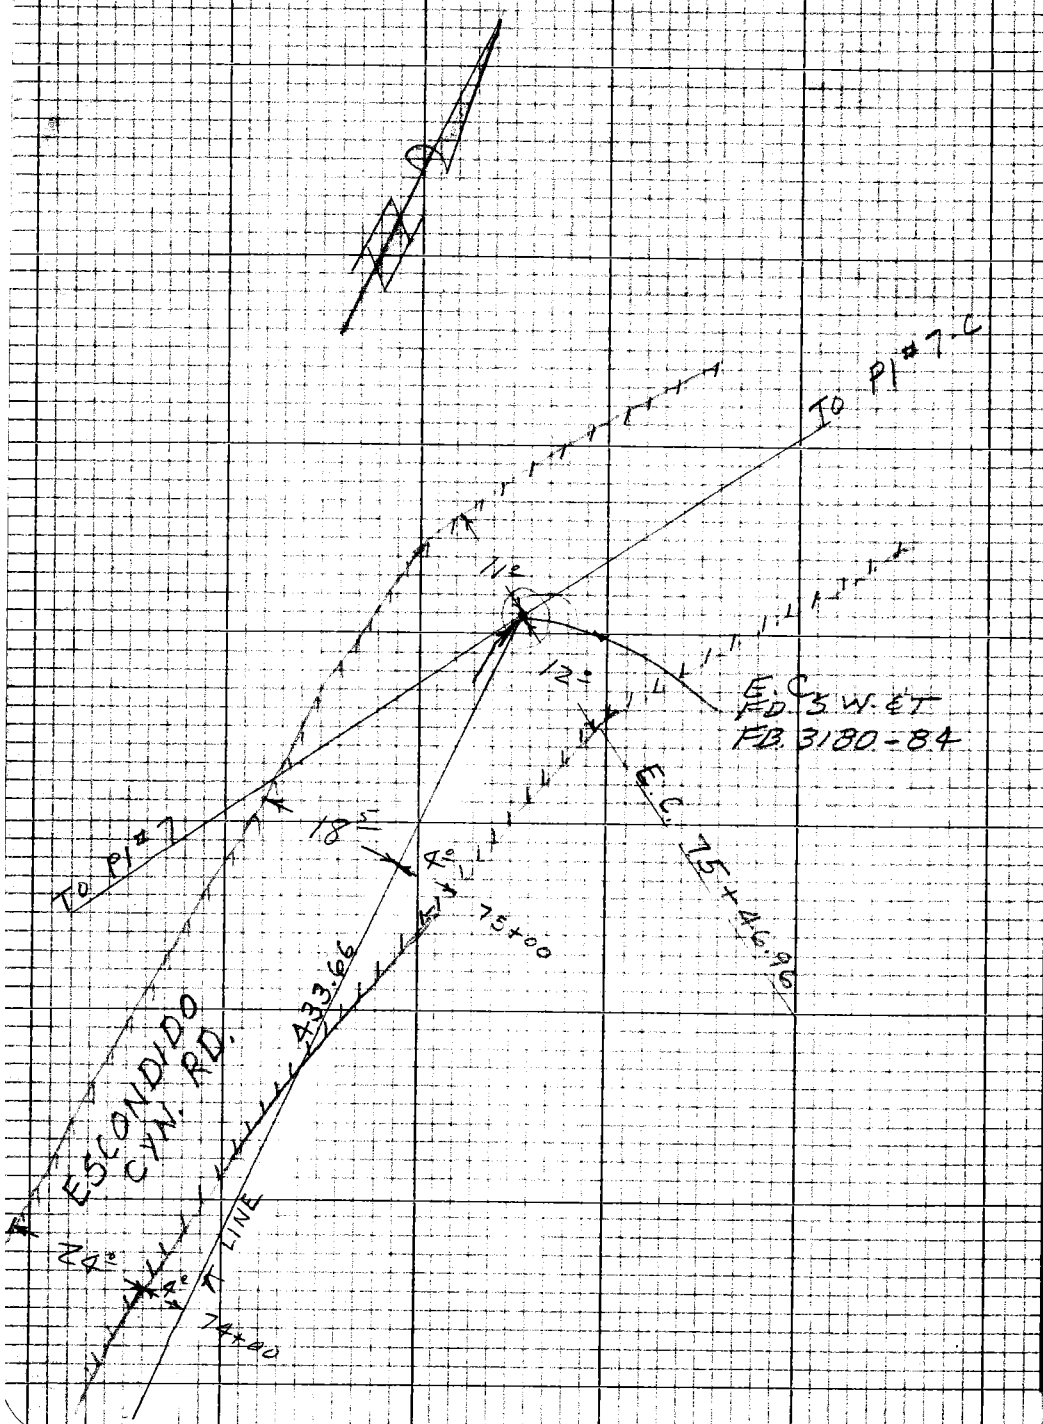

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

Do not extend this side of this file.

Note: Any Additions or Changes on this Sheet Must be Made or Circled in Red Ink With Date and Name of Person Making Change

F. B. 3[illegible] PG. [illegible]

Profile No. ____ Notes Red ____ Date ____ Plotted ____ Date ____ Job No. ____ Survey of W.W. # 37 ACTON

X-Sec. No. ____ Notes Chk'd. ____ Date ____ Checked ____ Date ____ Survey by PIERCE Notes JCP Date A[illegible] 7-7 Map No. ____ Indexed H. E. OTT Date [illegible]

J.N. 5375.16

WATERWORKS # 37 IN ACTON

ESCONDIDO CYN. RD.

CROSS-SECTIONS

FROM: 4TH STREET

TO: E.C. AT P.I. # 7 (1.5 MI. ±)

PARTY:
PIERCE
KING
TALBOT
McDONOUGH

STATION	B. S.	H. I.	F. S.	ELEV.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

76-L-296 CE 307 5-66

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 3429 PG. 234 | Job No. 5375(6) Division No. 11 Notes Red ____ Plotted ____ Profile ____
Survey of W.W. DIST #37 Date ____ Date ____ No. ____
Survey by PIGNEY Notes K.L.S. Notes Chk'd. ____ Checked ____ X-Sec. ____
Indexed ____ Date ____ Date ____ Date ____ No. ____

STATION	B. S.	H. I.	F. S.	ELEV.	ESCONDIDO CYN. ROAD
B.M. M.S. 19-A				2708.214	BM # M.S 19-A EL. = 2708.214
					FD. C.S.MON. 2" I.P. BRASS CAP SET CONC.
					FLUSH @ S.W. COR. SOLEDAD-AGUA DULCE
					UNION SCHOOL. ELEV. TAKEN ON N.W. RIM.
					STAMPED "SCHOOL LOT" R.E. 2177.
					AS PER F.B. 2631 - 202
0+00				0851	℄ PALM
0+11.3				0508	℄ "
				0870	30' R E.P.
				0752	30' L E.P. & GUTTER
0+27				0824	12' R E.P.
				0826	13.8' L E.P.
1+00				0912	℄
				0891	13' R E.P.
				102	30' R TOP BRK
				0905	13' L E.P.
				296	30' L FACE & TOP BRK
2+00				0992	℄
				0967	13.4' R E.P.
				2710.7	30' R TOP BRK

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. 5575 Division No. 11
No.____ Date____ Date____ Survey of W.W. Dist. #37
X-Sec. Notes Chk'd.____ Checked____ Survey by____ Notes____ Date
No.____ Date____ Date____ Map No.____ Indexed H. E. Ortf

F. B. 3[illegible] Pg. 2[illegible]

STATION	B. S.	H. I.	F. S.	ELEV.	ESCONDIDO CYN. RD.	
2+00				2710.05	12' L E.P.	
				10 8	30' L Top Bnk & Fnce	
3+00				10 92		℄
				10 61		13.2' R E.P.
				11 4		30' R Top Bk
				11 14	12.2' L E.P.	
				11 7	30' L Top Bnk & Fnce	
4+00				11 94		℄
				11 72		13' R E.P.
				12 5		30' R Top Bnk
				12 1.5	12' L E.P.	
				12 2	30' L Top Bnk & Fnce	
5+00				12 98		℄
				12 88		12' R E.P.
				14 0		30' R Top Bnk
				13 26	11.5' L E.P.	
				13 2	30' L Top Bnk	
6+00				14 02		℄
				13 69		10' R E.P.
				14 9		30' R Top Bnk
				14 31	11.5' L E.P.	

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 3429 Pg. 236
Job No 53757 Division No. 11 Notes Red Plotted Profile
Survey of W.W. Dist # 37 Date No.
Survey by PIERCE Notes KING Notes Chk'd. Checked X-Sec.
Indexed Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	ESCONDIDO CYN. RD.
6+00				27146	30'L TOP BRK
7+00				1550	℄
				1426	17'R E.P.
				156	30'R SIDE HILL
				1565	2'L E.P.
				167	16'L TOP BRK
				146	30'L BOT BRK
7+10				1584	℄ E.P.
8+00				1524	℄ E.P.
				177	22'R TOP BRK
				180	30'R P/L
				1715	20'L E.P.
				176	28'L TOP BRK
				169	30'L BEG. FILL
9+00				185	℄
				186	10'R FLAT
				1682	16.51 L E.P.
				1898	40'L E.P.
				194	47'L TOP FILL
				171	55'L BOT FILL
10+00				27199	℄

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. 3776 Division No. 11
No.____ Date____ Date____ Survey of W. Bell Canyon Rd.
X-Sec. Notes Chk'd____ Checked____ Survey by____ Notes
No.____ Date____ Date____ Map No.____ Indexed H. E. OTT Date____ Date____

F. B. - - Pg. -

STATION	B. S.	H. I.	F. S.	ELEV.	ESCONDIDO CYN RD.	
10+00				2720 0		10' R FLAT
				19 13	18' L E.P.	
				21 46	44' L E.P.	
				22 0	49' L TOP FILL	
				19 2	57' L BOT "	
11+00				22 10		
				21 7		12.5' R FLAT
				22 14	5' L E.P.	
				24 20	30' L E.P.	
				24 8	38' L TOP FILL	
				22 8	45' L BOT FILL	
12+00				24 83		
				24 10		13.5' R E.P.
				23 1		24.5' R GUTTER
				23 6		31' R FLAT
				25 42	11' L E.P.	
				26 2	18' L END FILL	
				25 7	24' L BOT "	
13+00				25 91		
				25 75		12' R E.P.
				2724 9		22' R GUTTER

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 3429 PG. 238 | Job No. 52516 Division No. 11 Notes Red Plotted Profile No.
Survey of W. W. DIST #37 Date Date No. X-Sec.
Survey by Pierce Notes KING Notes Chk'd. Checked
Indexed Date Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	ESCONDIDO CYN. RD.
13+00				27255	30'R FLAT
				2630	12.5'L E.P.
				266	30'L FLAT
14+00				2824	℄
				2800	11'R E.P.
				275	30'R P/L
			005	2850	14'L E.P.
				286	30'L P/L
15+00				3066	℄
				3024	12'R E.P.
				290	30'R P/L
				3077	13'L E.P.
				307	30'L P/L
16+00				3300	℄
				3283	13'R E.P.
				327	23'R Top Begin Fill
				305	30'R Bot " "
				3298	13'L E.P.
				320	30'L P/L
16+90				3075	26'R 24" Culvert
				3185	24.5'L 24" Culvert

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 5375-16 Division No. 11
No. ____ Date ____ Date ____ Survey of W.W. DIST. #1
X-Sec. Notes Chk'd. ____ Checked ____ Survey by ____ Notes ____ Date
No. ____ Date ____ Date ____ Map No. ____ Indexed H. E. OTT Date

F. B. [illegible] Pg. [illegible]

STATION	B. S.	H. I.	F. S.	ELEV.	ESCONDIDO CYN. RD.
17+00				2735 32	℄
				35 12	12' R E.P.
				36 0	18' R Top Fill
				30 9	32' R Bot Fill
				35 26	12' L E.P.
				35 7	20' L Top Fill
				32 5	30' L Bot Fill
17+62				35 32	26' R Conc. Drain
17+98				37 18	14' R "
18+00				37 48	℄
				37 02	14' R E.P. & Bot Fill
				39 7	21' R Top Fill
				39 0	30' R P/L
				37 40	12' L E.P.
				37 4	19' L Top Fill
				32 3	30' L Bot Fill
18+62				36 92	35' L Conc Drain
18+87				3881	16' L " "
19+00				39 43	℄
				39 24	12' R E.P.
				39 2	15' R Bot 8'

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 3429 PG. 240 | Job No. 5375-1 Division No. 11 Notes Red Date Plotted Date No. Profile
Survey of W. W. DIST # 37 Notes Chk'd. Date Checked Date No. X-Sec.
Survey by PIERCE Notes KINGS
Indexed

STATION	B. S.	H. I.	F. S.	ELEV.	ESCONDIDO CYN. RD.
19+00				739 19	13'L E.P.
				39 2	15'L Bot 6' Cut
20+00				41 65	℄
				41 50	11'L E.P.
				41 5	15' R Bot 10' Cut
				41 27	14'L E.P.
				41 3	16'L Bot 8' Cut
21+00				43 94	℄
				43 76	11'R E.P.
				43 8	14'R Bot Cut
				43 64	14'L E.P.
				43 6	16'L Bot Cut
21+40				46 2	19'R END CUT BEG. FILL
22+00				46 70	℄
				46 52	11'R EP & Gutter
				47 7	19'R Top Fill
				46 40	13.5'L E.P.
				47 2	21.5'L End Cut
				46 1	30'L P/L
23+00				49 70	℄
				749 45	11'R E.P.

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	ESCONDIDO	CYN. RD.
23+00				2750 2		18'R TOP FIL
				49 50	13'L E.P.	
				48 5	30'L P/L	
23+95				50 30		31'R Conc. I
24+00				52 87		
				52 70		12'R E.P.
				53 7		19'R TOP FIL
				52 75	13'L E.P.	
				52 6	25'L TOP BKL	
				51 0	30'L P/L	
24+19				53 10		15'R Conc. I
				55 6		20'R Beg. C
25+00				56 16		
				56 16		12'R E.P.
				56 1		18'R Bot Cut
				55 84	12'L E.P.	
				56 3	19'L TOP BKL	
				53 3	27'L Bot "	
26+00				59 63		
				59 51		13'R E.P.
				596		19'R Bot Cut

Profile Notes Red____ Plotted____ Job No. 5215-16 Division No. 11
No.____ Date____ Date____ Survey of W.O. 5215
X-Sec. Notes Chk'd.____ Checked____ Survey by____ Notes____ Date____
No.____ Date____ Date____ Map No.____ Indexed H. E. Ott Date____
F. B. Pg. 2011

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 3429 PG. 242 | Job No 53516 Division No. 11 Notes Red Plotted Profile No.
Survey of W. W. DIST # 37 Date Date X-Sec. No.
Survey by PIERCE Notes KING Notes Chk'd. Checked
Indexed Date Date

STATION	B. S.	H. I.	F. S.	ELEV.	ESCONDIDO CYN. RD.
26+00				2761 7	24' R END CUT
				61 7	30' R P/L
				59 50	11'L E.P.
				59 6	21'L TOP BRK
				58 0	29'L BOT BRK
27+00 *				62 01	℄
				62 40	13' R E.P.
				62 6	24' R TOP FILL
				61 7	30' R P/L
				61 70	9¾'L E.P.
				62 2	18'L TOP BRK
				62 0	30'L P/L
~~BM~~ #MS-19				2765 70	

~~BM~~ #MS-19 EL. 2765.454
Found C.E. Button Mon 2"IP Brass Cap IN Conc. UP 6" 30'± East of ℄ Escondido Rd. 0.51 MI.± N.W. From Town of Acton. Found 2" I.P. MARKER PIPE 2'± East of Mon.
PER F.B. 2631 - 204

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 Los Angeles County Engineering Bldg.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 537[illegible] Division No. ____
No. ____ Date ____ Date ____ Survey of W. IV [illegible]
X-Sec. Notes Chk'd. ____ Checked ____ Survey by [illegible] Notes
No. ____ Date ____ Date ____ Map No. ____ Indexed H. E. Ott Date 2-16-61

F. B. 3[illegible] Pg. [illegible]

STATION	B. S.	H. I.	F. S.	ELEV.	Escondido Cyn. Rd.
B.M.# M.S.-19					B.M.# M.S.-19 ELEV.= 2765.454 F.B. 263-204.
					FOR DESCRIPTION SEE PRECEDING PG.
27+35				2763 9	27' R BEGIN CUT
28+00				63 00	℄
				63 85	12.5' R EDGE PAV.
				64 2	22' R BOT 6' CUT
				62 31	9.5' L EDGE PAV.
				63 0	30' L P/L
28+20				63 0	23' L BEGIN 6' CUT
28+81				63 8	35' L END 6' CUT
29+00				62 78	℄
				63 45	10' R EDGE PAV.
				64 0	20' R BOT 6' CUT
				62 05	12.5' L EDGE PAV
				63 5	30' L SLOPE
29+48				63 2	17' R BEGIN FILL
				63 4	30' R END CUT
29+72				62 2	20' L BEGIN FILL
30+00				61 80	℄
				62 17	12.5' R EDGE P[illegible]
				63 0	18' R TOP [illegible]

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 3429 PG. 244 | Job No. 5375.16 Division No. 11 Notes Red ____ Plotted ____ Profile ____
Survey of W.W. DIST # 37 Date ____ No. ____
Survey by PIERCE Notes ____ Notes Chk'd. ____ Checked ____ X-Sec. ____
Indexed ____ Date ____ Date ____ No. ____

STATION	B. S.	H. I.	F. S.	ELEV.	ESCONDIDO CYN. RD.
30+00				2761 25	12' L EDGE PAV.
				61 5	20' L TOP FILL
				58 0	29' L BOT "
30+91				61 2	20' L END FILL BEGIN CUT
31+00 *				60 57	℄
				60 75	11.5' R EDGE PAV.
				61 6	18' R TOP FILL
				60 12	11.9' L EDGE PAV
				61 2	16' L BOT CUT
32+00				59 77	℄
				59 76	10.5' R E.P.
				61 3	20' R TOP FILL
				59 15	12' L E.P. & BOT CUT
32+87				58 78	18' L CONC. DRAIN END CUT
33+28				57 60	29' L BOT DRAIN
33+04				59 35	12' R CONC. DRAIN
				57 30	27' R " "
33+29				55 62	26' R F/L CULVERT
33+44				56 95	22' L F/L CULVERT
34+00				60 20	℄
				60 02	10.5' R E.P.

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. 5375.16 Division No. 11
No.____ Date____ Date____ Survey of W.W. Dist. #37
X-Sec. Notes Chk'd.____ Checked____ Survey by____ Notes____ Date____
No.____ Date____ Date____ Map No.____ Indexed H. E. OTT Date____

F. B. [illegible] Pg. [illegible]

STATION	B. S.	H. I.	F. S.	ELEV.	ESCONDIDO CYN RD.	
34+00				2760 5		19' R TOP FILL
				579	12' L E.P.	
				601	21' L TOP FILL	
35+00				6162		℄
				6153		10½' R E.P.
				620		20' L TOP FILL
				6125	11½' L E.P.	
				614	19' L TOP FILL	
36+00*				6344		℄
				6323		10½' R E.P.
				637		21' R TOP FILL
				6328	11' L E.P.	
				638	20' L TOP FILL	
37+00				6524		℄
				6512		11³' R E.P.
				655		21' R TOP
				6492	11' L E.P.	
				655	22' L END FILL	
				649	30' L P/L	
38+00				6700		℄
				6688		12' R E.P.

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 3429 PG. 246 | Job No. 53516 Division No. 11 Notes Red Date Plotted Profile
Survey of W. W. DIST # 37 Date No. X-Sec.
Survey by Pierce Notes Kraus Notes Chk'd. Checked
Indexed Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	ESCONDIDO CYN. RD.
38+00				2767.2	22' R TOP FILL
				667	12' L E.P.
				675	20' L TOP FILL
				667	30' L P/L
39+00				6871	℄
				6855	11.5' R E.P.
				687	21' R TOP FILL
				6825	11' L E.P.
				690	20' L TOP FILL
				660	27' L BOT "
40+00 *				7047	℄
				7026	12.5' R E.P.
				708	24' R TOP FILL
				7010	10' L EP
				704	19.5' L TOP FILL
				680	25' L BOT FILL
40+78				7050	26' L CONC. DRAIN
41+02				7203	17' L " "
41+00				7261	℄
				7245	12' R E.P.
				729	30' R P/L

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red____ Plotted____ Job No. 5335-16 Division No. 11
No.____ Date____ Date____ Survey of Yd W. Dist. # 37
X-Sec. Notes Chk'd.____ Checked____ Survey by Hence Notes Date____ Date____
No.____ Date____ Date____ Map No.____ Indexed H. E. OTT Date____ F. B. Pg.

STATION	B. S.	H. I.	F. S.	ELEV.	ESCONDIDO CYN RD.
41+00				2772 15	11' L E.P.
				726	20' L Beg. Cut
				732	30' L P/L
41+59				7241	28' R Conc. D
41+80				7370	16' R " Beg. C
42+00				7484	℄
				7442	10' R E.P.
				744	13' R Gutter
				7444	11.5' L E.P.
				744	15' L Gutter
T.P. PI # 38				7627	℄ B.S.W. & T
43+00				7750	℄
				7706	10' R E.P.
				771	12' R Gutter
				7728	10.3' L E.P.
				774	15' L Gutter
43+80				811	21' R End Cut Fill
44+00				8045	℄
				8012	12' R E.P.
				815	23' R Top Fill
				8122	9' L E.P.

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

F. B. 3429 PG. 248 | Job No. 533516 Division No. 11 Notes Red Date Plotted Date No. Profile
Survey of N.W. DIST # 37 Date No. X-Sec.
Survey by PIERCE Notes KING Notes Chk'd. Checked
Indexed Date Date

Do not extend notes this side of this line.

ESCONDIDO CYN RD.

STATION	B. S.	H. I.	F. S.	ELEV.		
44+00				8781 2	13' L BOT CUT	
45+00				8357		℄
				8349		13^{5}' R E.P.
				843		24' R TOP FILL
				8346	8^{3}' L E.P.	
			465	832	14' L END CUT	
45+91				8600		12^{5}' R E.P.
				8590		30' R E.P.
46+00				8645		℄
				8625	8' L E.P.	
				879	22' L TOP BANK	
				871	30' L P/L	
46+09				8658		12^{5}' R E.P.
				8625		30' R E.P.
47+00				8980		℄
				8930		14^{5}' R E.P.
				904		21^{5}' R TOP FILL
				8956	8' L E.P.	
				900	16' L GUTTER	
				940	27' L P/L	
47+77				8680		28' R P/L Culvert

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 5525-E Division No. H
X-Sec. No. ____ Date ____ Date ____ Survey of ESCONDIDO CYN RD. No. 37
Notes Chk'd. ____ Date ____ Checked ____ Date ____ Survey by ____ Date ____ Map No. ____ Date ____ Indexed ____ Date ____ Notes H. E. Ott
F. B. ____ PG. ____

STATION	B. S.	H. I.	F. S.	ELEV.	ESCONDIDO CYN RD.
47 80				27932	17'L Beg. Fill
48+00 *				9324	
				9315	12.5'R E.P.
				934	21'R Top Fill
				930	10'L E.P.
				941	19'L Top Fill
48+04.5				894	27'L F/L Culvert
49 ± 00				9638	℄
				9642	10.5'R E.P.
				972	19'R Top Fill
				9625	11.5'L E.P.
				975	21'L Top Fill
49+10				9502	29'L Conc. Drain
49+35				9649	17'L Conc. Drn. End Fill
50+00				9960	℄
				9965	10'R E.P.
				28010	29'R Top Fill
				9910	13'L E.P.
				990	19'L Bot. Cut
51 ± 00				28057	℄
				0280	12'R E.P.

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 3429 PG. 250 | Job No. 5375.16 Division No. 4 Notes Red ____ Plotted ____ Profile
Survey of W.W. DIST # 37 Date ____ No. ____
Survey by PIERCE & NOTES KINGS Notes Chk'd. ____ Checked ____ X-Sec.
Indexed ____ Date ____ Date ____ No.

STATION	B. S.	H. I.	F. S.	ELEV.	ESCONDIDO CYN RD.
51+00				28030	23' R TOP FILL
				0200	10' L E.P.
				020	13' L BOT CUT
52+00				0494	℄
				0547	13.5' R E.P.
				068	24' R TOP FILL
				442	9' L E.P.
				44	19' L BOT CUT
53+00 *				688	℄
				735	9' R E.P.
				94	25' R TOP FILL
				615	12' L E.P.
				62	16' L BOT CUT
54+00				816	℄
				871	9.5' R E.P.
				096	21' R BOT BKK
				124	30' R TOP FILL
				0748	11' L E.P.
				873	18' L BOT CUT
54+80				9740	1 R F/L CULVERT
				091	19' L END CUT

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile Notes Red ____ Plotted ____ Job No. 5315 Division No. ((
No. ____ Date ____ Date ____ Survey of N.W. District
X-Sec. Notes Chk'd. ____ Checked ____ Survey by ____ Notes ____ Date ____
No. ____ Date ____ Date ____ Map No. ____ Indexed H. E. O. Date ____

F. B. ____ Pg. ____

STATION	B. S.	H. I.	F. S.	ELEV.	ESONDIDO CYN RD.
55+00				2809 03	℄
				09 40	13' R E.P.
				09 8	19' R TOP FILL
				0855	10' L E.P.
				09 11	18' L TOP FILL
BM NC #1136				2807 05	BM NC #1236 ELEV = 2807.105 F.B. 2180-35 ESCONDIDO CYN ROAD S. SIDE 320'± NWLY OF HUBBARD RD 165'± SELY PI #6B BT SPK IN CONC. HEADWALL
55+10				042	'L F/L CULVERT
56+00				0983	℄
				1061	12' R E.P.
				119	20' R TOP FILL
				0908	11'± L E.P.
				096	18' L TOP FILL
56+40				089	22' L END FILL
57+00				1144	℄
				1154	15' R E.P.
				130	10'± R TOP FILL

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 3429 PG. 252 Job No. 5225-16 Division No. 11 Notes Red Plotted Profile
Survey of W. W. DIST # 37 Date Date No.
Survey by PIERCE & NOTES KINGS Notes Chk'd. Checked X-Sec.
Indexed Date Date Date No.

STATION	B. S.	H. I.	F. S.	ELEV.	ESCONDIDO CYN. RD.
57+00				2809 40	23 'L E.P.
				080	33 'L Flow Line
58+00				139	℄ Top Fill
				12 72	9 'L E.P.
				10 77	34 'L E.P.
				092	44 'L Gutter
59+00				1364	℄
				1388	7 'R E.P.
				141	15 'R End Fill
				1305	17.5 'L E.P.
				116	28. 'L Gutter
E.C T.P.				14.54	
60+00				1615	℄
				1588	14.5 'R E.P.
				158	24 'R Bot Brk
				171	30 'R Top "
				1637	8.5 'L E.P.
				168	14 'L Bot Brk
				178	17 'L Top "
				158	24 'L Bot "
61+00				2070	℄ Top Brk

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

Profile No.____ Notes Red____ Plotted____ Job No. 5313 Division No. 1
X-Sec. No.____ Notes Chk'd.____ Date____ Checked____ Date____ Survey of W.W. DIST # 37
Date____ Survey by____ Notes Date____
Map No.____ Indexed H.E. Date____
F. B.____ Pg.____

STATION	B. S.	H. I.	F. S.	ELEV.	ESCONDIDO	CYN RD
61+00				281.965		6' R E.P.
				1811		27' R E.P.
				174		37' R GUTTER
				195		44' R TOP BK
				185	7' L BOT BRK	
62+00				2160		℄
				213		15' R FLAT
				213		22' R BOT BK
				233		29' R TOP "
				2271		33' R E.P.
				2100		58' R E.P.
				196		67' R BOT B
				220		73' R TOP
PI# 7B T.P.#				2169		
62+80				231		℄ BOT BRK
62+91				261		℄ TOP "
63+00				255		℄
				2477		125' R E.P.
				2353		34' R E.P.
				231		54' R FLAT
				256	11' L TOP BRK	

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 3429 PG. 25

Job No. 5275-16 Division No. 11 Notes Red Date Plotted Date Profile No.
Survey of W. W. DIST # 37 Date Checked Date X-Sec. No.
Survey by PIERCE Notes KING Notes Chk'd. Date
Indexed Date

STATION	B. S.	H. I.	F. S.	ELEV.	ESCONDIDO CYN RD.
64+00				2825.08	℄
				24.40	18' R E.P.
				24.6	34' R TOP BKK.
				25.12	3.5' L E.P.
				25.8	14' L TOP BKK.
				26.5	25' L FLAT
65+00				27.18	℄
				26.85	13' R E.P.
				26.5	23' R BOT BKK.
				26.8	31' R TOP BKK.
				27.30	8.5' L E.P.
				28.4	30' L P/L
65+40				28.8	40' L BEGIN CUT
66+00				28.93	℄
				28.58	11' R E.P.
				29.1	20.5' R TOP FILL BEGIN FILL
				25.9	29' R BOT FILL
				29.02	10.5' L E.P.
				29.0	17' L BOT CUT
67+00				30.35	℄
				29.85	9.5' R E.P.

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

STATION	B. S.	H. I.	F. S.	ELEV.	ESCONDIDO CYN RD.
67+00				28303	
				3055	11.5' L E.P.
				305	17' L BOT. CUT
68+00				3133	℄
				3068	9.5' R E.P.
				310	20' R TOP FILL
				3164	11' L E.P.
				316	16' L BOT CUT
69+00				3226	℄
				3113	12.5' R E.P.
				318	21.5' R TOP B[illegible]
				3281	9' L E.P.
				328	14.5' L BOT CUT
69+45				337	9.5' L END CUT
70+00 *				3454	℄
				3447	2' R E.P.
				3255	24' R E.P.
				327	32' R TOP FILL
				349	4.5' L BEGIN TOP FILL
				332	9' L BOT FILL
				28342	20' L SLOPE

Profile Notes Red ____ Plotted ____ Job No. 53516 Division No. 11
No. ____ Date ____ Date ____ Survey of W. Ltr. Dist. Notes
X-Sec. Notes Chk'd. ____ Checked ____ Survey by [illegible] Notes
No. ____ Date ____ Date ____ Map No. ____ Indexed H. E. Date ____ Date

F. B. [illegible] Pg. [illegible]

76-L-298 CE 307 5-66

PLEASE RETURN TO
LOS ANGELES COUNTY ENGINEER
403 LOS ANGELES COUNTY ENGINEERING BLDG.

NOTE: ANY ADDITIONS OR CHANGES ON THIS SHEET MUST BE MADE OR CIRCLED IN RED INK, WITH DATE AND NAME OF PERSON MAKING CHANGE.

Do not extend notes this side of this line.

F. B. 3429 PG. 256 | Job No. 5315/6 Division No. 11 Notes Red Date Plotted Profile
Survey of W. W. Dist #37 Date No. X-Sec.
Survey by PIERCE Notes KING Notes Chk'd. Date Checked Date No.
Indexed Date

STATION	B. S.	H. I.	F. S.	ELEV.	ESCONDIDO CYN RD.
70+33				28355	℄ TOP BRK
70+43				342	℄ BOT "
71+00				3805	℄
				366	19'R BOT FILL
				370	24'R TOP "
				3633	30'R E.P.
				3448	51'R E.P.
				321	60'R TOP FILL
72+00				3835	℄ E.P.
				3630	24'R E.P.
				365	34'R TOP FILL
				391	8'L END FILL
				404	20'L BOT BRK.
72+20				391	17'L BEGIN CUT
73+00				3808	℄
				3778	31'R E.P.
				377	18'R TOP FILL
				3985	19'L E.P.
				404	24'L BOT CUT
74+00				3925	℄
				396	11'R END FILL

STATION	B. S.	H. I.	F. S.	ELEV.	ESCONDIDO CYN RD.
74+00				2837.1	17' R Bot Fill
				39.15	5' L E.P.
				41.24	26' L E.P.
				41.7	32' L Bot Cut
75+00				40.57	℄
				40.20	4' R E.P.
				39.1	23' R E.P.
				41.65	18' L E.P.
				42.0	32' L End Cut
75+47 E.C.				41.76	℄
				41.00	12' R E.P.
				40.4	30' R P/L
				42.12	10' L E.P.
				42.1	30' L P/L
BMNC 1237				2838.84	BMNC 1237 Elev 2838.838 FB.3180-3 Escondido Canyon Rd (W'ly ... 1.0 mi. N.W'ly of E Hubbard Rd A C.E.Mon on semi-tan 11 4" I.S. of R.L.#7

Red ____ Plotted ____ Job No. 53[illegible] Division No. 11 F. B. 3429 Pg. 52

X-Sec ____ Date ____ Survey of [illegible] Date [illegible]

Notes ____ Chk'd. ____ Checked ____ Survey by [illegible] Notes [illegible]

No. ____ Date ____ Date ____ Map No. ____ Indexed H. E. C. Date ____
