PERMIT NEEDED

Pole located across street from 4372 VERONA

LACO / E.LA

HERBERT 4kV O/O BELVEDERE SUB

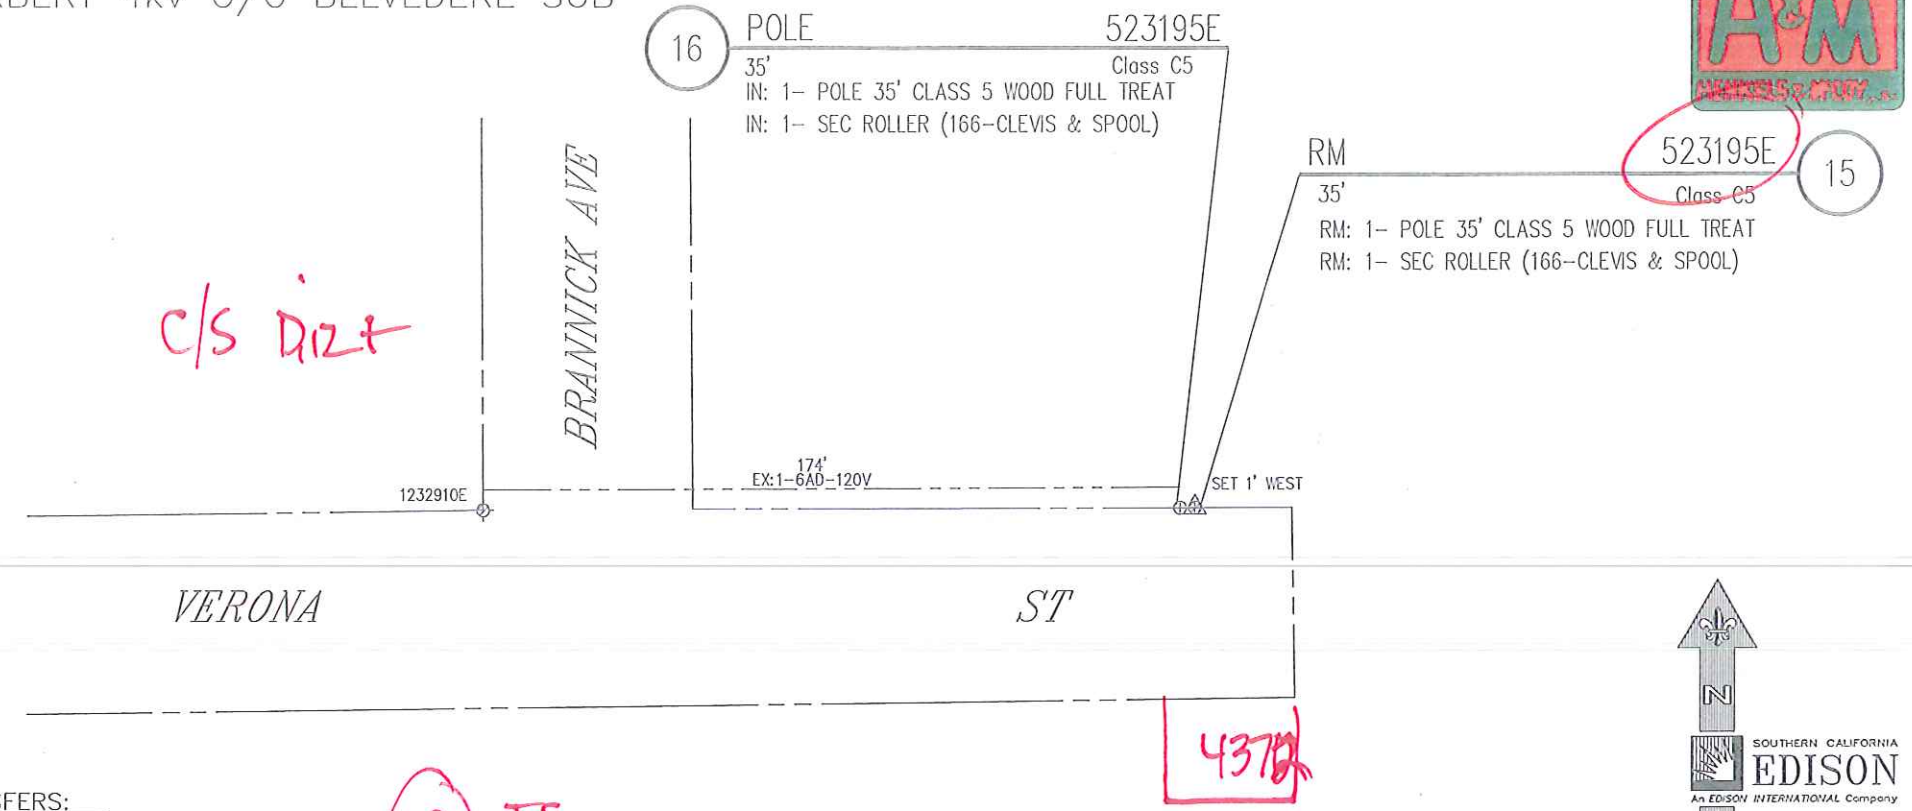

TRANSFERS:

1- 6AD 120V (W)
1- ST/LT
1- PH ATTACH

(P) JS 5.23

GPS
34°-01'-20.3"
118°-10'-38.9"

NOT TO SCALE

SET IN SAME HOLE N OR SET 1' W HARD SET N

ENVIRO REVIEW	N	HAND SET	N	SPECIAL EQUIP NEEDED	N
JOINT MEET	N	PERMIT NEEDED	Y	IF YES WHAT IS NEEDED?	
TRUCK ACCESS	Y	NETCOMM SHEET	N		
PAVEMENT REPAIR	N	RIGHTS CHECK	N	EST. TIME TO REPLACE	
ASPHALT		PED TRAFFIC CONTROL	Y	16 MH	
CONCRETE		OUTAGE	N	CONTACT CATV	N
REPAIR SIZE		CSD-140	N	MITC POLE	N

DISTRICT 22 - MONTEBELLO	PROJ. MGR. RODRIGUEZ, JOHN T PHONE 909-469-0219	PLANNER RAMIREZ, MIKE PHONE 909-517-2220	
FOREMAN	TRUCK NO. / P/E / INVENTORY MAP NO. 120-4233-1	THOMAS GUIDE 675 E1 / GRID NO.	DESIGN NO. 490360_0.01
CSD 140 Y___ N___ / BY-PASS CODE / EXISTING ___ CHANGE TO ___	TLM CHECKED ___ %LOAD	J.P.A. NO. E6022-000405865037	ASSOCIATED DESIGN NO.
PRODUCT/SAP NO. 698631- DETERIORATED POLE	PRODUCT/SAP NO.	PRODUCT/SAP NO.	

TYPE	APPROVED BY	DATE	CHECKED BY	DRAWN BY	PAX #

Southern California Edison Company

PROPOSED CONSTRUCTION (LOCATION)

4373 VERONA ST
EAST LOS ANGELES

SHEET ___ OF ___

JOB NO. 490360_0.01

PAGE NO. 4 J.P. AUTH. NO. E6022-000405865037

POLE NO.	Pole Length / Anchor Size	Year Set	Pole Trt / Class / Anchor Direct.	Record 16KV E	Record HLA	Record	Record	Proposed 16KV E	Proposed HLA	Proposed	Proposed	Proposed	Item No.	LOCATION AND NATURE OF WORK If not in accordance with Joint Pole agreement and routine-state reasons.	
														E TO REPLACE PER SEC. 7.11, 19.6, 14.3, 7.4	1
92073E	45	1928	FT 4	.50	23'			C-10 PB	LTD					WHITTIER BL A/S S/S 128' W/O ARIZONA AV, EAST LOS ANGELES	2
								1/2(1)					5C	TOP POLE	3
								1/2(1)				2X2	10B	ASPHALT REPAIR	4
															5
92073E	50		FT 1					43-14	23-5					WHITTIER BL A/S S/S 128' W/O ARIZONA AV, EAST LOS ANGELES	6
								TN 23							7
								1						BENEFIT OF PH	8
								1/2(1)					15B	VIS STRIPS	9
															10
				120V				120V						E TO REPLACE PER SEC. 7.11, 10.8	11
523195E	35	1938	FT 5	29-6	19-1			PTD						VERONA ST N/S 134' E/O BRANNICK AV, EAST LOS ANGELES	12
															13
523195E	35		FT 5					30-5	19-1					VERONA ST N/S 133' E/O BRANNICK AV, EAST LOS ANGELES	14
								1					83	PH	15
														SET 1' WEST	16
															17
															18
															19

POLE LEGEND:
P = PULL (Item 5A)
PB = PULL BUTT
T = TRANSPORT (Item 5B)
S = SALVAGE
D = DISPOSE (item 5D)
TN = TENANT
L = LOWER TOP(Item 5E)
C(XX) = FOOTAGE CUT
SCZ = SAFETY CLEARANCE ZONE

ANCHOR/ARM LEGEND:
AR = ANCHOR/ARM REMOVED
AT = ANCHOR/ARM TRANSFERRED

Show Quantity of Items to be billed in the Column of Party to be Paid.

GEOGRAPHICAL LOCATION

EAST LA
COMMUNITY

Rev. Jul 2013
