PERMIT NEEDED

Pole CS in plants @ 421 Las Flores Dr

ALTADENA

WAPELLO 4kV O/O FAIR OAKS SUB

NOTES:
REAR LINE CLEARING REQ

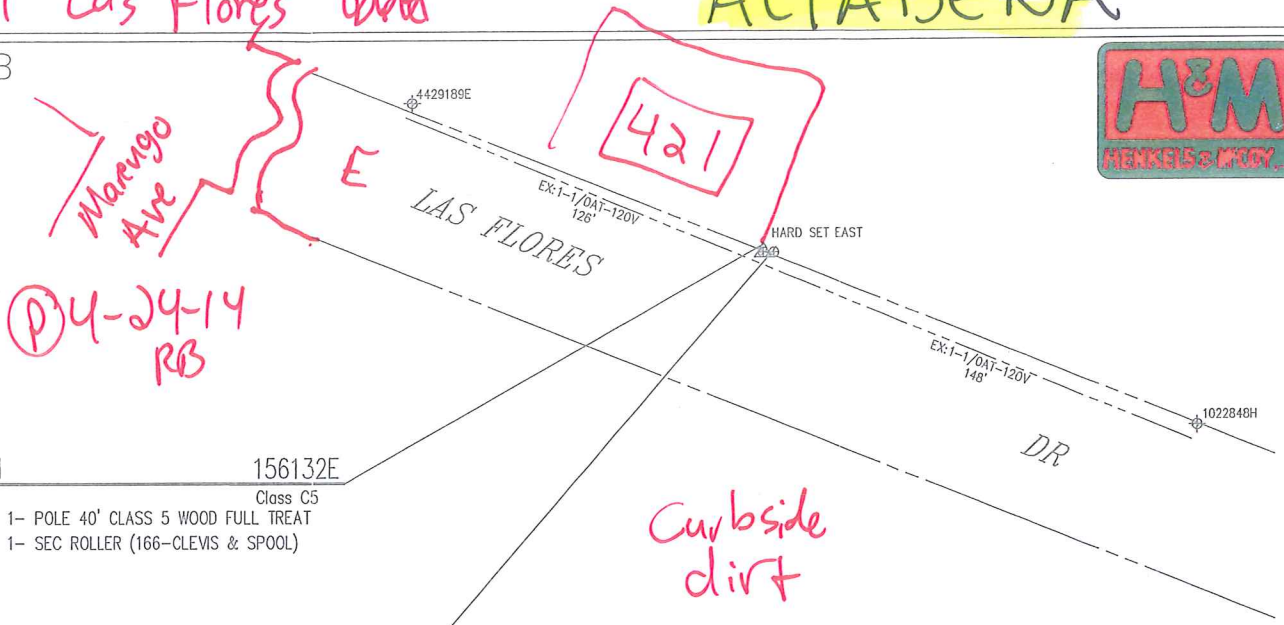

P 4-24-14 RB

1 RM 156132E
40' Class C5
RM: 1- POLE 40' CLASS 5 WOOD FULL TREAT
RM: 1- SEC ROLLER (166-CLEVIS & SPOOL)

2 POLE 156132E
40' Class C5
IN: 1- POLE 40' CLASS 5 WOOD FULL TREAT
IN: 1- SEC ROLLER (166-CLEVIS & SPOOL)

TRANSFERS:
1- 1/0AT 120V (E&W)
2- 4AT SVC
1- 6' MAST ARM ST/LT

GPS
34°-11'-48.5"
188°-08'-09.2"

NOT TO SCALE

SOUTHERN CALIFORNIA EDISON
An EDISON INTERNATIONAL Company

SET IN SAME HOLE N OR SET ___' E HARD SET Y

ENVIRO REVIEW	N	HAND SET	N	SPECIAL EQUIP NEEDED	N
JOINT MEET	N	PERMIT NEEDED	Y	IF YES WHAT IS NEEDED?	
TRUCK ACCESS	Y	NETCOMM SHEET	N		
PAVEMENT REPAIR	N	RIGHTS CHECK	N	EST. TIME TO REPLACE	
ASPHALT		PED TRAFFIC CONTROL	N	40 MH	
CONCRETE		OUTAGE	N	CONTACT CATV	Y
REPAIR SIZE		CSD-140	N	MITC POLE	N

DISTRICT 27 - MONROVIA	PROJ. MGR. RODRIGUEZ, JOHN T PHONE 909-469-0219		PLANNER CARRILLO, CHRIS PHONE 909-517-2211		
FOREMAN	TRUCK NO.	P/E	INVENTORY MAP NO. 81-77D	THOMAS GUIDE 535 J4	GRID NO.
DESIGN NO. 519755_0.01					
CSD 140 Y___ N___	BY-PASS CODE	EXISTING ___ CHANGE TO ___	TLM CHECKED ___	%LOAD	J.P.A. NO. E 6027 000405839792
ASSOCIATED DESIGN NO.					
PRODUCT/SAP NO. 739705- DETERIORATED POLE	PRODUCT/SAP NO.		PRODUCT/SAP NO.		

TYPE	APPROVED BY	DATE	CHECKED BY	DRAWN BY	PAX #

Southern California Edison Company

PROPOSED CONSTRUCTION (LOCATION)
421 LAS FLORES DR
ALTADENA

SHEET ___ OF ___

JOB NO. 519755_0.01

PAGE NO. 4 J.P. AUTH. NO. E6027-000405839792

POLE NO.	Pole Length / Anchor Size	Year Set	Pole Trt / Class / Anchor Direct.	Record 120V E	Record HLA	Record	Record	Proposed 120V E	Proposed HLA	Proposed	Proposed	Proposed	Item No.	LOCATION AND NATURE OF WORK If not in accordance with Joint Pole agreement and routine-state reasons.	
														E TO REPLACE PER SEC. 7.11, 19.4, 14.3	1
156132E	40	1931	FT 5	33-11	22-4			C-5	PTD					LOS FLORES DR N/S 375' E/O MARENGO AVE, ALTADENA	2
								1/2(1)					5C	TOP POLE	3
								1/2(1)					13B	SHRUBS	4
															5
156132E	40		FT 5					34-5	22-4					LOS FLORES DR N/S 376' E/O MARENGO AVE, ALTADENA	6
								25-1						HARD SET EAST	7
								TN 25							8
								1/2(1)					15B	VIS STRIPS	9
															10
														E TO REPLACE PER SEC. 7.11, 7.4	11
411071H	25	1938	FT 5	.50	.50			C-5	LTD					RAYMOND AV P/P 110' E 290' N/O PALM ST, ALTADENA	12
								1/2(1)					5C	TOP POLE	13
															14
4469012E	35		FT 5					30-2	23-6					RAYMOND AV P/P 110' E 290' N/O PALM ST, ALTADENA	15
								1/2(1)					19C		16
															17
															18
															19

POLE LEGEND:
P = PULL (Item 5A)
PB = PULL BUTT
T = TRANSPORT (Item 5B)
S = SALVAGE
D = DISPOSE (Item 5D)
TN = TENANT
L = LOWER TOP(Item 5E)
C(XX) = FOOTAGE CUT
SCZ = SAFETY CLEARANCE ZONE

ANCHOR/ARM LEGEND:
AR = ANCHOR/ARM REMOVED
AT = ANCHOR/ARM TRANSFERRED

Show Quantity of Items to be billed in the Column of Party to be Paid.

GEOGRAPHICAL LOCATION

ALTADENA
COMMUNITY

Rev. Jul 2013
