PERMIT NEEDED

Pole located R/Alley of address 5641 E. Beverly BLVD

East Los Angeles / LA County

CERVEZA 16kV O/O MESA SUB

(1) RM 514844E
45' Class C4
RM: 1- POLE 45' CLASS 4 WOOD FULL TREAT
RM: 2- XA SNGL FB 10' STEEL PINS SECONDARY
RM: 4- SEC ROLLER (166-CLEVIS & SPOOL)
RM: 1- SEC DE 4/0 ACSR TRI OR QUAD AUTO BAIL
RM: 8- SEC STEEL PIN & INS - PHASE
RM: 5- SEC STEEL PIN & INS - NEUTRAL
RM: 60- CD ALL SIZES AL/CU 3/C
RM: 1- GR OH #6 SOL WP SECONDARY W/ROD
RM: 2- AG SPAN GUY 9/32" - 200'
TR: 1- XA SNGL VB 10' STEEL PINS
TR: 3- INS POLY W/PIN 16KV CLMP #4-653 ACSR
TR: 3- FE CO OPEN 100A 16KV 1-EA
TR: OH 2-37KVA 16KV 120/240 OD 3P
SN:_____

(2) POLE 514844E
45' Class H1
IN: 1- POLE 45' CLASS H1 WOOD FULL TREAT
IN: 1- XA SNGL FB 10' STEEL PINS SECONDARY
IN: 2- SEC ROLLER (166-CLEVIS & SPOOL)
IN: 1- SEC DE 4/0 ACSR TRI OR QUAD AUTO BAIL
IN: 1- SEC 2" PVC FOR UNDER ARM W/#2 TW
IN: 6- SEC STEEL PIN & INS - PHASE
IN: 1- SEC STEEL PIN & INS - NEUTRAL
IN: 60- CD #4 STR AL TRIPLEX W/ACSR NEUTRAL
IN: 1- GR OH #6 SOL WP SECONDARY W/ROD
IN: 2- AG SPAN GUY 9/32" - 200'

P JS 5.3.14

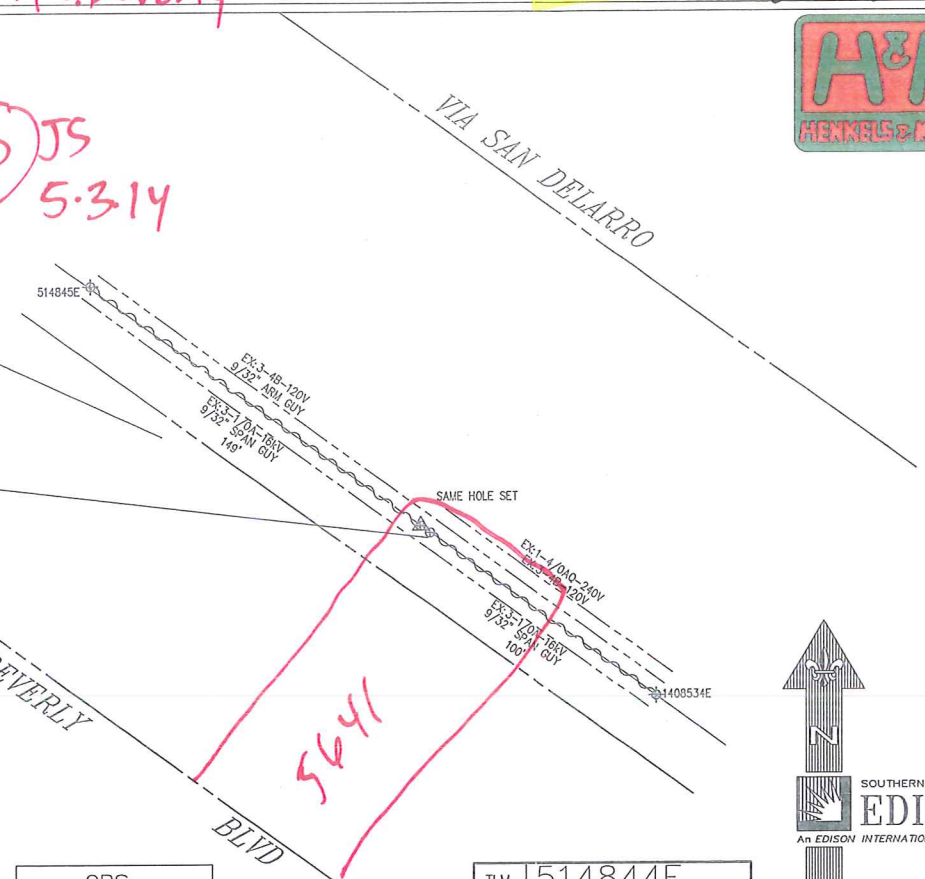

TRANSFERS:
1- 10' XARM W/ 3- 1/0A 16kV
3- 4B 120V (N&S)
1- 4/0AQ 240V (SE)
1- 9/32" A/G (NW)
1- 2/37.5/16 3P-4PW XFMR BANK W/ FUSES
1- ST/LT
2- 4AT SVC
1- 6AT SVC
1- 4/0AQ SVC

Alley CONCRETE

*SAME HOLE SET DUE TO TELCO CONNECTIONS

SET IN SAME HOLE Y OR SET___ ___ HARD SET N

ENVIRO REVIEW	N	HAND SET	N	SPECIAL EQUIP NEEDED	N
JOINT MEET	N	PERMIT NEEDED	Y	IF YES WHAT IS NEEDED?	
TRUCK ACCESS	Y	NETCOMM SHEET	N		
PAVEMENT REPAIR	Y	RIGHTS CHECK	N	EST. TIME TO REPLACE	
ASPHALT	Y	PED TRAFFIC CONTROL	N	48 MH	
CONCRETE		OUTAGE	Y	CONTACT CATV	N
REPAIR SIZE	3x3	CSD-140	N	MITC POLE	N

GPS
34°-01'-40.8"
118°-08'-44.4"

TLM DATA:	514844E			
	SIZE	kVA	CUST	%LOAD
EXIST:	75	18.3	3	24.40
PROP:	75	18.3	3	24.40
VD= N/A		FLICKER= N/A		

NOT TO SCALE

SOUTHERN CALIFORNIA EDISON
An EDISON INTERNATIONAL Company

DISTRICT 22 - MONTEBELLO	PROJ. MGR. RODRIGUEZ, JOHN T PHONE 909-469-0219		PLANNER RODRIGUEZ, LYNETTE PHONE 909-517-2177		
FOREMAN	TRUCK NO.	P/E	INVENTORY MAP NO. 122-4242-1	THOMAS GUIDE 635 J7	GRID NO.
DESIGN NO. 535747_0.01					
CSD 140 Y___ N___	BY-PASS CODE	EXISTING CHANGE TO	TLM CHECKED 24.40 %LOAD	J.P.A. NO. E6022-000405861255	ASSOCIATED DESIGN NO.
PRODUCT/SAP NO. 762534- DETERIORATED POLE		PRODUCT/SAP NO.		PRODUCT/SAP NO.	

PROPOSED CONSTRUCTION (LOCATION)
R/O 5641 BEVERLY BLVD
EAST LOS ANGELES

TYPE	APPROVED BY	DATE	CHECKED BY	DRAWN BY	PAX #

SHEET ___ OF ___ JOB NO. 535747_0.01

Southern California Edison Company

AUTHORIZATION FOR JOINT POLE TRANSACTION

J.P. FORM 2-1 Preliminary 1/95

This authorization is in accordance with Joint Pole Agreement and Routine. The undersigned have agreed on joint work as specified hereon.

Date Prepared: 2/6/2014

Date Sent:

Confirming Agreement:

In Field ☐ By Telephone ☐

Est. Const. Start:

No. of Pages: 6

J.P. Auth.No.: E6022-000405861255

UTILITY	REPRESENTATIVE	DISTRICT-DIVISION-EXCHANGE	APPROVED	TAXING INSTRUCTIONS	ACCOUNTING DATA
E	J. T. RODRIGUEZ	MONTEBELLO	J. T. RODRIGUEZ	MONTEREY PARK	TD 762534
HLA					
H&M	J. KOHLER				909-517-2205

POLE NO.	Pole Length / Anchor Size	Year Set	Pole Trt / Class / Anchor Direct.	Record 16KV E	Record HLA	Record	Record	Proposed 16KV E	Proposed HLA	Proposed	Proposed	Proposed	Item No.	LOCATION AND NATURE OF WORK If not in accordance with Joint Pole agreement and routine-state reasons.	
														E TO REPLACE PER SEC. 7.11, 7.4, 14.3, 19.4, 19.6	1
514844E	45	1937	FT 4	38-15	23-5			C-15 PB	LTD					BEVERLY BL A/N N/S 496' E/O SADLER ST, MONTEBELLO	2
								1/2(1)					5C	TOP POLE	3
								1/2(1)				3X3	10B	ASPHALT REPAIR	4
								1/2(1)					13B	SHRUBS	5
															6
514844E	45		FT H1					39-10	23-5					BEVERLY BL A/N N/S 496' E/O SADLER ST, EAST LOS ANGELES	7
									TN 23						8
								1/2(1)					15B	VIS STRIPS	9
								1					19A	BENEFIT OF PH	10
															11
															12
															13

VP/J.P.-03

Rev. Jul 2013

POLE LEGEND:
P = PULL (Item 5A)
PB = PULL BUTT
T = TRANSPORT (Item 5B)
S = SALVAGE
D = DISPOSE (Item 5D)
TN = TENANT
L = LOWER TOP(Item 5E)
C(XX) = FOOTAGE CUT
SCZ = SAFETY CLEARANCE ZONE

ANCHOR/ARM LEGEND:
AR = ANCHOR/ARM REMOVED
AT = ANCHOR/ARM TRANSFERRED

Show Quantity of Items to be billed in the Column of Party to be Paid.

GEOGRAPHICAL LOCATION

EAST LA

COMMUNITY

COPY
ORIGINAL SENT TO
JPA ORGANIZATION
DATE SENT 2/12/14
