Hankels & McCoy

00000838538

ELECTRICAL CONTRACTOR DAILY TIMESHEET and WORK REPORT

Work Location: Covina 26
Date: 5/9/14
Day: Friday
Military Start Time: 0600
Military Finish Time: 1630
SAP Contract No.: 4600003988
SAP P.O. No.: 4500582085
SAP P.O. Item No.: 10
Contractor Job No.: ELCSTE

SAP Order No. / Cost Center No.	—							Work Type	
	902204						Total hours	$ In Lieu of Meals	Subsistence

EMPLOYEE NAME	Classification		1	2	3	4	5	6	Total hours	$ In Lieu of Meals	Subsistence
James Yolinski	FM	ST	8						8		
	OT X	PT	2						2		50
Employee No.: 608713	In Lieu of Meals										
Dale Rourk	JL	ST	8						8		
	OT X	PT	2						2		50
Employee No.: 622210	In Lieu of Meals										
Richard Stephens	GM	ST	8						8		
	OT X	PT	2						2		50
Employee No.: 668522	In Lieu of Meals										
		ST									
	OT	PT									
Employee No.:	In Lieu of Meals										
		ST									
	OT	PT									
Employee No.:	In Lieu of Meals										
		ST									
	OT	PT									
Employee No.:	In Lieu of Meals										
Totals Per SAP Order / Cost Center No.		ST	24						24		
		OT									
		PT	6						6		150
	In Lieu of Meals										

Equipment Numbers	Equipment Description	Do not include hours for in lieu of meals						
TC48	Pick-up Truck	10						10
SC800	Flat bed Truck	10						10

Provide the following detail for each work assignment: Description of work performed; Meter Order number(s); Passport work order number(s); Street location; Station and/or structure numbers; FCO log number; Unusual occurrences or working conditions; Weather status; Total manhours.

1 Brea 12KV o/o Merced Sub
Cable life testing Inspection
- Take detailed pictures of each location
- Remove debris and water as needed
- Shoot each location for hot spots
- Clean cable tags and name plates and take pictures
- Verify circ or duct and its size and take pictures
- Tag locations as needed
- Identify source for each tap line for outage purposes
This work performed at each of the following locations:

B5126370

X5127585

Contract Employee or Foreman's Signature:
SCE Authorized Field Reviewer Printed Name and Date:
SCE Authorized Field Reviewer Signature:
SCE Approver Printed Name and Date:
SCE Approver Signature:

COPY DISTRIBUTION: White - Contract Administration, Canary - Contractor, Pink - Field Copy

SCE TDBU 1-A REV 10/08 (CW)

PERMIT NEEDED

Pole located ON SIDE OF 392 GERHART IN Alley.

East Los Angeles / LA County

HILLVIEW 4kV O/O AMALIA SUB

(2) POLE 542468E
40' Class C1
IN: 1- POLE 40' CLASS 1 WOOD FULL TREAT
IN: 1- XA DBLE FB 10' STEEL PINS SECONDARY
IN: 6- SEC ROLLER (166-CLEVIS & SPOOL)
IN: 1- SEC 2" PVC FOR UNDER ARM W/#2 TW
IN: 1- AG DOWN GUY 7/16" - 50' LESS THAN 22.5KV

Alley CONCRETE

(1) RM 542468E
40' Class C5
RM: 1- POLE 40' CLASS 5 WOOD FULL TREAT
RM: 1- XA DBLE FB 10' STEEL PINS SECONDARY
RM: 6- SEC ROLLER (166-CLEVIS & SPOOL)
RM: 1- SEC 2" PVC FOR UNDER ARM W/#2 TW
RM: 1- AG DOWN GUY 9/32" - 50' LESS THAN 22.5KV

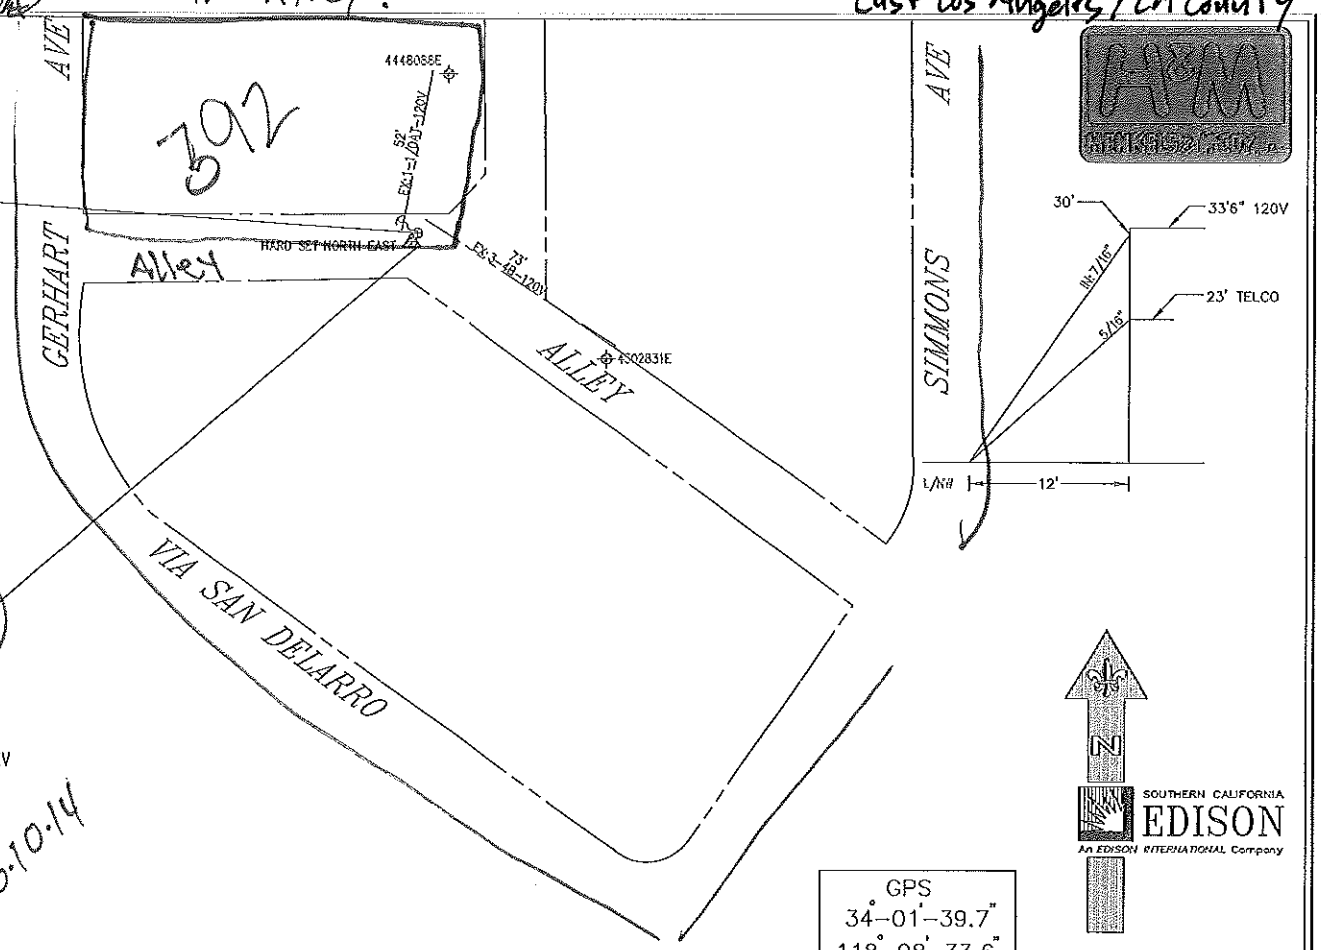

GPS
34°-01'-39.7"
118°-08'-33.6"

TRANSFERS:
3- 4B 120V (E)
1- 1/0AT 120V (N)
6- 4AT SVC
1- 6' MAST ARM ST/LT

JS 5.10.14

SET IN SAME HOLE N OR SET ' NE HARD SET Y

ENVIRO REVIEW	N	HAND SET	N	SPECIAL EQUIP NEEDED	N
JOINT MEET	N	PERMIT NEEDED	N	IF YES WHAT IS NEEDED?	
TRUCK ACCESS	Y	NETCOMM SHEET	N		
PAVEMENT REPAIR	Y	RIGHTS CHECK	N	EST. TIME TO REPLACE	
ASPHALT	Y	PED TRAFFIC CONTROL	N	40 MH	
CONCRETE		OUTAGE	Y	CONTACT CATV	N
REPAIR SIZE	2x2	CSD-140	N	MITC POLE	N

DISTRICT 22 - MONTEBELLO	PROJ. MGR. RODRIGUEZ, JOHN T PHONE 909-469-0219		PLANNER CARRILLO, CHRIS PHONE 909-517-2211		
FOREMAN	TRUCK NO.	P/E	INVENTORY MAP NO. 122-4242-1	THOMAS GUIDE 635 J7	GRID NO.
DESIGN NO. 535753_0.01					
CSD 140 Y___ N___	BY-PASS CODE	EXISTING CHANGE TO	TLM CHECKED	%LOAD	J.P.A. NO. E 6022 000405857497
ASSOCIATED DESIGN NO.					
PRODUCT/SAP NO. 762540- DETERIORATED POLE	PRODUCT/SAP NO.		PRODUCT/SAP NO.		
PROPOSED CONSTRUCTION (LOCATION) VIA SAN DELARRO A/N 120' E/O GERHART AVE EAST LOS ANGELES					
TYPE	APPROVED BY	DATE	CHECKED BY	DRAWN BY	PAX #
SHEET ___ OF ___	JOB NO. 535753_0.01				

Southern California Edison Company

AUTHORIZATION FOR JOINT POLE TRANSACTION

J.P. FORM 2-1 Preliminary 1/95

This authorization is in accordance with Joint Pole Agreement and Routine. The undersigned have agreed on joint work as specified hereon.

Date Prepared: 2/10/214

Date Sent: _____ Confirming Agreement: _____ In Field ☐ By Telephone ☐ Est. Const. Start: _____ No. of Pages: 6 J.P. Auth.No.: E6022-000405857497

UTILITY	REPRESENTATIVE	DISTRICT-DIVISION-EXCHANGE	APPROVED	TAXING INSTRUCTIONS	ACCOUNTING DATA
E	J. T. RODRIGUEZ	MONTEBELLO	J. T. RODRIGUEZ	MONTEREY PARK	TD 762540
HLA					
H&M	J. KOHLER				909-517-2205

POLE NO.	Pole Length / Anchor Size	Year Set	Pole Trt / Class / Anchor Direct.	Record 120V E	Record HLA	Record	Record	Proposed 120V E	Proposed HLA	Proposed	Proposed	Proposed	Item No.	LOCATION AND NATURE OF WORK (If not in accordance with Joint Pole agreement and routine-state reasons.)	
														E TO REPLACE PER SEC. 7.11, 12.12, 19.6	1
542468E	40	1938	FT 5	34-11	23-5			C-5	PTD					VIA SAN DE LARRO A/N N/S 120' E/O GERHART AV, MONTEBELLO	2
								1/2(1)					5C	TOP POLE	3
	1"	1940	W	.50	.50			AT							4
								1/2(1)				2X2	10B	ASPHALT REPAIR	5
															6
542468E	40		FT 1					34-5	23-5					VIA SAN DE LARRO A/N N/S 121' E/O GERHART AV, EAST LOS ANGELES	7
									TN 23					HARD SET NORTH EAST	8
								1/2(1)					15B	VIS STRIPS	9
															10
															11
															12
															13

POLE LEGEND:
P = PULL (Item 5A)
PB = PULL BUTT
T = TRANSPORT (Item 5B)
S = SALVAGE
D = DISPOSE (Item 5D)
TN = TENANT
L = LOWER TOP(Item 5E)
C(XX) = FOOTAGE CUT
SCZ = SAFETY CLEARANCE ZONE

ANCHOR/ARM LEGEND:
AR = ANCHOR/ARM REMOVED
AT = ANCHOR/ARM TRANSFERRED

Show Quantity of Items to be billed in the Column of Party to be Paid.

GEOGRAPHICAL LOCATION

EAST LA

COMMUNITY

VP/J.P.-03

Rev. Jul 2013

COPY
ORIGINAL SENT TO
JPA ORGANIZATION
DATE SENT 2/10/2014
