PERMIT NEEDED

POLE LOCATED C/S AT ADDRESS 334 MARGARET AVE

MONTEBELLO / LA COUNTY

CERVEZA 16kV O/O MESA SUB

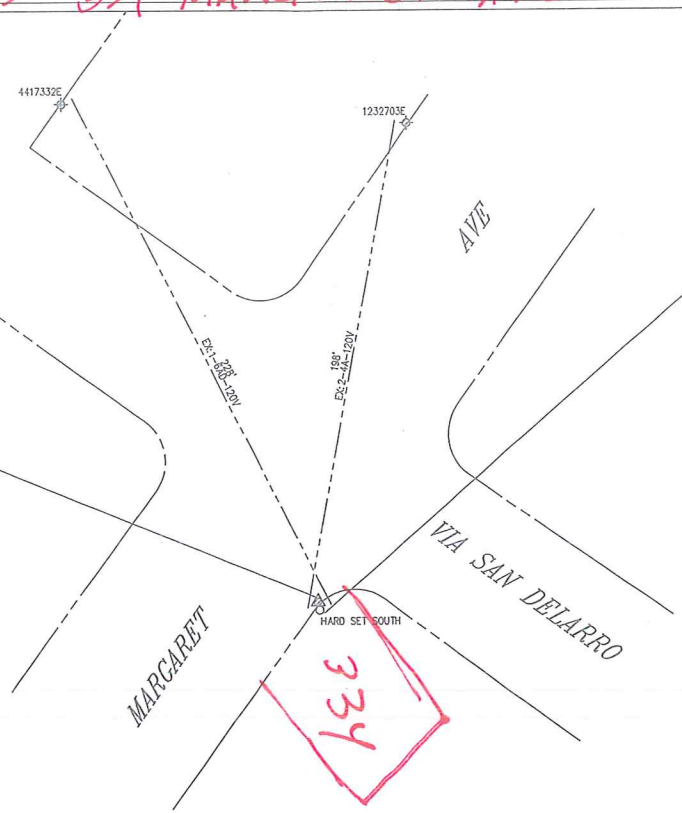

5 RM 567169E
40' Class C5
RM: 1- POLE 40' CLASS 5 WOOD FULL TREAT
RM: 1- XA SNGL FB 8' STEEL PINS SECONDARY
RM: 2- INS POLY DE 4KV COLD SHOE #4 ACSR
RM: 2- SEC STEEL PIN & INS - PHASE

POLE 567169E 6
40' Class H2
IN: 1- POLE 40' CLASS H2 WOOD FULL TREAT
IN: 1- XA SNGL FB 10' STEEL PINS SECONDARY
IN: 3- SEC ROLLER (166-CLEVIS & SPOOL)
IN: 1- SEC 2" PVC FOR UNDER ARM W/#2 TW
IN: 1- AG BLOCK & POLE KEY

JS 4.29.14

TRANSFERS:
2-4A 120V (N)
1-6AD (N/W)
1-ST LIGHT

C/S DIRT

GPS
34°-01'-48.9"
118°-08'-55.8"

NOT TO SCALE

SOUTHERN CALIFORNIA EDISON
An EDISON INTERNATIONAL Company

SET IN SAME HOLE N OR SET ' S HARD SET Y

ENVIRO REVIEW	N	HAND SET	N	SPECIAL EQUIP NEEDED	N
JOINT MEET	N	PERMIT NEEDED	Y	IF YES WHAT IS NEEDED?	
TRUCK ACCESS	Y	NETCOMM SHEET	N		
PAVEMENT REPAIR	N	RIGHTS CHECK	N	EST. TIME TO REPLACE	
ASPHALT		PED TRAFFIC CONTROL	Y	16 MAN HRS	
CONCRETE		OUTAGE	N	CONTACT CATV	N
REPAIR SIZE		CSD-140	N	MITC POLE	N

DISTRICT 22 - MONTEBELLO	PROJ. MGR. RODRIGUEZ, JOHN T. PHONE 909-469-0219		PLANNER RAMIREZ, MIKE PHONE 909-217-2806		
FOREMAN	TRUCK NO.	P/E	INVENTORY MAP NO. 122-4242-1	THOMAS GUIDE 635 J6	GRID NO.
DESIGN NO. 540432_0.01					
CSD 140 Y___ N___	BY-PASS CODE	EXISTING ___ CHANGE TO ___	TLM CHECKED ___ %LOAD	J.P.A. NO. N/A	ASSOCIATED DESIGN NO.
PRODUCT/SAP NO. 769585 - DET POLE REPLACEMENT		PRODUCT/SAP NO.		PRODUCT/SAP NO.	

TYPE	APPROVED BY	DATE	CHECKED BY	DRAWN BY	PAX #

PROPOSED CONSTRUCTION (LOCATION)
334 MARGARET
EAST LOS ANGELES

SHEET ___ OF ___ JOB NO. 540432_0.01

Southern California Edison Company
