NAZOMETB-500

NOTIFICATIONS:
406424443
400969539

SCOPE OF WORK:
REPLACE O/L XFMR &
REPAIR TOP PORTION OF
MOLDING

SOUTHERN CALIFORNIA EDISON
An EDISON INTERNATIONAL Company

SCALE: 1" = 50'

0 50 100

NEW YORK-4KV O/O ALLEN SUB

"1485"

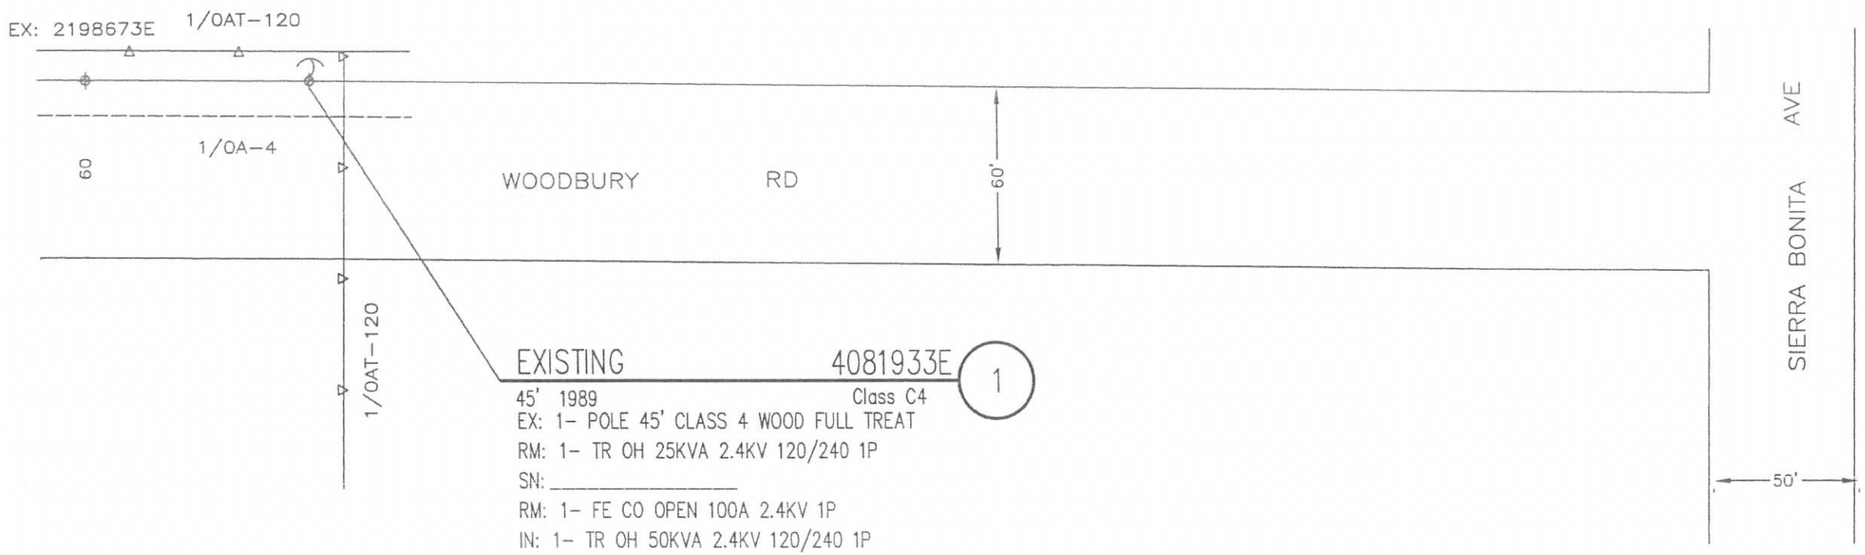

TLM DATA:	SIZE	KVA	#CUST	%LOAD
EXIST	25.0	52.9	10	211.63
PROP	50.0	52.9	10	105.8
	VD =		FLICKER =	

DISTRICT 27 - MONROVIA	PROJ. MGR. SOLIS, SANDRA C PHONE		PLANNER SOLIS, SANDRA C PHONE 626-688-4792		
FOREMAN	TRUCK NO.	P/E	INVENTORY MAP NO. 78-78B	THOMAS GUIDE LAC 536C-7	GRID NO.
DESIGN NO. 640545_0.01					
CSD 140 Y___ N___	BY-PASS CODE	EXISTING _____ CHANGE TO _____	TLM CHECKED _____ %LOAD	J.P.A. NO.	ASSOCIATED DESIGN NO.
PRODUCT/SAP NO. 920707-PREVENTIVE MAINT (INSPECTION DRIVEN)	PRODUCT/SAP NO.			PRODUCT/SAP NO.	

TYPE	APPROVED BY	DATE	CHECKED BY	DRAWN BY	PAX #

PROPOSED CONSTRUCTION (LOCATION)

1485 E WOODBURY RD.
PASADENA, CA 91104

SHEET 1 OF 1

JOB NO. 640545_0.01

Southern California Edison Company
